



PEARL GTL PROJECT
C8
EFFLUENT TREATMENT PLANT
Client: SHELL / QS GTL



Weekly Project Progress Report

KEN-187-WPR-037
(Cut off Date: 14/09/2008)

PEARL GTL PROJECT C8 EFFLUENT TREATMENT PLANT

CONTRACT No. - QT-02P-187

Client: SHELL / QS GTL

Prepared By :

Gomu Subramanian
Planning Engineer

Approved By :

Gerry Linnane
Project Manager

Week - (From 08th Sep - 14th Sep 08)



PEARL GTL PROJECT
C8
EFFLUENT TREATMENT PLANT
SECTION-1- INDEX



Week - (From 08th Sep - 14th Sep 08)

CONTENTS

SECTION

- 1a PMT
- 1b HSSE
- 1c QUALITY
- 1d ENGINEERING
- 2a PROCUREMENT
- 2b CONSTRUCTION
- 2c PRE-COMMISSIONING/COMISSIONING - NONE
- 2d AREAS OF CONCERN
- 3 HSSE STATISTICS
- 4 MANHOURS REPORT
- 5 ENGINEERING DELIVERABLES SUMMARY
- 6 QUANTITY MARKUPS
 - a) FIREWATER MARKUP
 - b) EARTHING CABLES MARKUP
 - c) EQUIPMENT POSITION MARKUP
 - d) SUPPORTS & TRAY MARKUP
- 7 SCHEDULES:
 - a) ENGINEERING SCHEDULE
 - b) 6 WEEKS LOOK AHEAD SCHEDULE
 - c) UPDATED FIRE WATER SCHEDULE
 - d) UPDATED EARTHING SCHEDULE
 - e) UPDATE F1 TRENCH SCHEDULE



PEARL GTL PROJECT
C8
EFFLUENT TREATMENT PLANT
SECTION 2(a)



PROJECT PLANNING & CONTROL:

Baseline Weightage submitted, To Be Finalized in separate meeting with VSA on W38
Finalised work schedule for next two weeks for laying earthing grids on going-On Hold (Damages)
Commence with prep work for OSS 200 Supports.
Other updates are as per schedules enclosed with this report
Engineering Schedule Revision Incorporated with VSA Comments

HSSE

HSSE Statistics dated 14th September 2008 is enclosed.
Documentation summary is enclosed with this report.
Regular extreme weather conditions Red flags envisaged.

QUALITY

Documentation summary is enclosed with this report.
Quality surveillance for ongoing earthing, FAR 7- Cabinet supports, OSS-Hanger Support,
HV / MV Transformer Installation
Preparation of ITP for HV Transformer Assembly and installation
Preparation of Method Statement for No. 25 & 26
NCR Issued for improper unloading of cable drums
Method Statement approved 11 out of 16
ITP Approved 9 out of 12
Cathodic protection-Sweet COC Tank

ENGINEERING

Overview of Engineering Drawings under progress:

FAR7:

HVAC In Line Equipment GA
A/G cable containment routings
Electrical Equipment Support Frames
Electrical Equipment Earthing
ACU support frames
Instrument Equipment Support Frames

OSS200:

Substation Building Cable Void Cable Routing Layout
HVAC Duct Supports
HVAC Data Book
HVAC Piping
HVAC DAMPER DATA BOOK received with code 2 comments

CWBD:

HVAC Data Book received with code 2 comments

CDF Tank:

A/G Cable Routing under progress

Guard House:

HVAC piping under progress



PEARL GTL PROJECT
C8
EFFLUENT TREATMENT PLANT
SECTION 2 (b)



PROCUREMENT

FAR7 cable trays have been ordered and partially delivered
OSS Cable void supports for plinth mounting have been ordered
OSS 200 cable trays for cable void - awaiting vendor approval by SHELL.
Temporary AC/s for FAR 7 installed and to be commissioned by 10/9/08.
General consumables and equipment ordering is ongoing.

CONSTRUCTION

Fire Water system:

North side fire water line being aligned and fixed in position
West side spools under prefabrication
Fire water Valve Chambers for West Side Trench (Below F1 trench) being installed
Shifting Of North & South Side Trenches under progress

Earthing Grids:

Earthing grids near OSS 200 layed.
Earthing grids around CDF tank being layed.
Earthing grids near AOC tank being laid
Earthing grids near IWT
Earthing cable installation around RFSU3 & 4 under progress
Earthing grids along Pipe supports being laid. (PT9, 10,11, 1 and 2)
Repair work on damaged earth cable insulation and defective cadwelds.
Installation of earth rods at OSS200 and FAR 7.

FAR7 Lighting Supports:

Lighting supports installation completed & Cable Tray fixing under progress
Cabinet Supports prefabrication complete and awaiting additional materials for extras.

U/G Cabling:

Cable Tagging & Testing Completed in Trenches A2,A2a & A2b

OSS200:

Drilling Of Holes For Cable void Hanger Support.
Dimensional measurements in cable void under progress for trapeze hangers.
Prep work for cable void hanger supports.
Installation of Cable void hanger supports
Installation of Power and Distribution transformers completed.

SWEET COC TANK - CATHODIC PROTECTION

Completed Installation oc Undertank CP Installation and pre-testing.

HVAC

Duct manufacturer revisited

COMMISSIONING

Nil

AREA OF CONCERN

Anticipated shortage of storage space for cable drums (new arrival)
Shortage of office space at O2P offices.
Vendor approval - SS Cable Tray supplier and HVAC Ducting supplier
Trenches to be opened on time to avoid ideling by Cable Pullers
Fire water trenches are not being opened up to suffice laying of available pipe spools
Non availability of cables for trench A3b. Onus shifts to laying cables for later RFSU's
Damages caused to Earthing cables by others a continuous occurrence.
Plotting & Printing facilities for larger than A3 size drawings to be addressed.
Copier facility provided is inadequate to cope with requirement for Kentech's new offices.
Exposure to damage of earth cable already installed.Stopped further Installation
Completion of warehouses and new offices.
Delay in approval of Method statement and ITP, posting in VDR/Nexus is impacting
PMC inspection and approval of site activity
Fire Water no frotes ,Activity will not complete end of October '08
Trenching progress of Earth Grids.

**SAFETY STATISTICS
KENTECH - WEEK NO. 37**

Sl.No	KENTECH-STATISTICS (25th Aug ~31st Aug 08) ----- Health	Unit	WTD
			8th ~14th Sep 08
1	Number of occupational diseases contracted	No.	0
2	Total Recordable Occupational Illness Frequency (TROIF) per million man Hrs.	Freq.	0
3	TROI – Infectious and parasitic diseases	No.	0
11	TROI – Noise induced hearing loss	No.	0
12	TROI – Other illnesses and disorders including heat stress	No.	0
Safety			
13a	Hours worked (Exposure hours)	No.	6420
14a	Number of total workforce	No.	95
14b	Total workforce	No.	95
15	Number of first aid cases (FAC)	No.	0
16	Number of records entered in First Aid book (Non Occupational)	No.	0
17	Maximize First Aid Cases (FAC's) reported: Audit medical clinics – measure disparity of actual clinic/medic records vs. reported FAC's (KPI = 75%)	%	0.00%
18	Number of cases requiring medical treatment (MTC)	NO	0
19	Number of cases resulting in restricted work (RWC)	No.	0
20	Number of cases resulting in lost workdays (LWC)	No.	0
21	Number of cases resulting in disability	No.	0
22	Number of cases resulting in fatality (KPI = 0)	No.	0
23	Total Reportable Case Frequency (TRCF) (KPI = <3)	No.	0
24	Lost Time Injuries (LTI)	No.	0
25	Lost Time Injury Frequency (LTIF)	No.	0
26	Number of cases resulting in damage to project or property	No.	0
27	Near misses- Potential incidents reported (unsafe conditions)	No.	0
28	Near misses – Number identified during Unsafe Act/STOP or SAFE audits	No.	0
29	Ratio (KPI = 1:3)	Ratio 1:3	0
30	Number of audit actions outstanding after original date for close-out	No.	2
31	Close-out of High / Medium audit and/or inspection findings on time (KPI)	No./H/M actions overdue	0
32	Number of Safety Observation Card	No.	4
33	Number of supervisors (carrying out audits during week)	No.	0
34	Number of Safety Observation Cards per supervisor per week (requirement is one SOC per supervisor per week (KPI = 80%))	% Note A	0.00%
35	Number of people receiving secondary training	No.	20
36	No.of people due to receive secondary Trg. as per Contractors training Programme	No.	20
37	Number of people receiving secondary training (i.e. over and above basic training induction, SAFE & TSTI.) - as % reported in training records (KPI = 75%)	%	0.00%
38	Number of investigation-actions outstanding after original date for close-out	No.	0
39	Number of people who have had HSSE induction	No.	97
40	Number of toolbox talks held	No.	6
41	Number of Management site inspections planned	No.	1
42	Number of Management site inspections carried out	No.	1
43	Number of activities identified in Contractors HSSE plan for action	No.	1
44	Number actions completed	No.	1
Environmental			
45	Volumes of Hazardous waste generated	Tonnes	0
46	Hazardous waste stored/dispose on site	Tonnes	0
47	Hazardous waste stored/dispose off site	Tonnes	0
48	Volumes of Non-hazardous waste generated	Tonnes	0
49	Waste disposed in RLC waste cell	Tonnes	0
50	Waste disposed off site	Tonnes	0
51	Diesel Fuel consumption - for all plant, equipment and vehicles	Litres	125
52	Gasoline Fuel consumption - for all cars	Litres	87
53	Energy consumption	GJ	0
54	Net fresh water consumption	M³	0
55	Archaeological findings	No.	0
56	Number of oil spills to water > 100 kg (KPI = 0)	No.	0
57	Quantity of oil spills to water > 100 kg	Kg	0
58	Number of oil spills to land > 100 kg (KPI = 0)	No.	0
59	Quantity of oil spills to land > 100 kg	Kg	0
60	Cases of environmental damage	No.	0
61	Metal recycled	Tonnes	0
62	Wood recycled	Tonnes	0
63	Paper recycled	Tonnes	0
64	Oil recycled	Tonnes	0
65	Plastic recycled	Tonnes	0
Transportation			
66	Kilometers driven:	Km	1533
67	No. of passenger vehicle KM's driven:	No.	940
68	No of passengers carried:	No.	99
69	No of freight vehicles KM's driven:	No.	0
70	No of freight vehicle journeys:	No.	0
71	Number of times maximum speed exceeded (IVMS)	No.	0
72	Number of Road Traffic Incident	No.	0
73	Police Violations	No.	0
74	Vehicle defects	No.	0
75	Number of occasions rest breaks were taken (IVMS)	No.	0
76	Duration of rest breaks (IVMS)	Hours	0
Security			
77	Number of security related incidents (within any 24 hours period)	No.	0
Social Performance			
78	Social Incidents	No.	0
79	Number of total workforce	No.	98
80	Number of workers taking trips	No.	98
81	Percent utilization of transport of Contractor's workforce taking up the bus service on day off for return visit to Doha (or Al Khor)	%	0
82	Number of local (Qatari) contracts	No.	0
83	Number of jobs for locals	No.	0
84	Number of installed and operational telephones	No.	0
85	Number of installed and operational internet connections	No.	0
86	Measured usage of telephones	No. of Calls	0
87	Measured usage of internet connections	No. of Connections	11



PEARL GTL PROJECT
C8
EFFLUENT TREATMENT PLANT



SECTION-4

PLANNED

Descr		Last Weeks Cumulative	THIS WEEK	Cumulative Total @ Cut-off	Cumulative Total @ End of Project
Management		10704	420	11124	139360
Engineering		14317	721	15038	
Procurement		7278	480	7758	
Construction					
Electrical	Direct	24105	2677	26782	313407
	Indirect	4890	400	5290	12756
Instrumentation	Direct	6800	680	7480	194879
	Indirect	620	80	700	7932
HVAC	Direct	10400	1680	12080	47471
	Indirect	1580	200	1780	1932
Fire Water	Direct	12992	2480	15472	5280
	Indirect	1700	200	1900	480
Total		95386	10018	105404	723497

ACTUAL

Descr		Last Weeks Cumulative	THIS WEEK	Cumulative Total @ Cut-off
Management		11314	800	12114
Engineering		17379	1440	18819
Procurement		3610	420	4030
Construction				
Electrical	Direct	13880	2320	16200
	Indirect	4069	240	4309
Instrumentation	Direct	0	0	0
	Indirect	0	0	0
HVAC	Direct	0	120	120
	Indirect	0	0	0
Fire Water	Direct	11440	920	12360
	Indirect	1740	160	1900
Total		63432	6420	69852

STATUS OF ENGINEERING DELIVERABLES

SECTION-5

LEGEND			DELETED	ADDITION	SUMMARY				
DATE:14/09/8			All Documents Status		363	153	151	105	35
Document	Rev No.	Submittal Code	TITLE		Client Number	Forecast	Started	ICC/MDR	IFL/Nexus
TOTAL COUNT			CERTIFICATES		4	0	0	0	0
TOTAL COUNT			DATA BOOKS		8	3	3	3	3
TOTAL COUNT			DATA SHEETS		2	0	0	0	0
TOTAL COUNT			DRAWINGS		164	54	54	28	3
TOTAL COUNT			INSTRUCTIONS		1	0	0	0	0
TOTAL COUNT			LISTS		22	4	4	4	1
TOTAL COUNT			MANUALS		1	1	1	1	0
TOTAL COUNT			METHOD STATEMENTS		31	21	21	14	9
TOTAL COUNT			PLANS		36	22	20	14	5
TOTAL COUNT			PROCEDURES		49	38	38	38	14
TOTAL COUNT			RECOMMENDATIONS		1	0	0	0	0
TOTAL COUNT			REGISTERS		1	0	0	0	0
TOTAL COUNT			REPORTS		41	9	9	3	0
TOTAL COUNT			SCHEDULES		2	1	1	0	0

Archives from Personal Files



PEARL GTL PROJECT
C8
EFFLUENT TREATMENT PLANT
SECTION-6




QUANTITY MARKUPS

Archives from Personal Files

FIRE WATER SYSTEM


FIREWATER
MARKUP REPORT

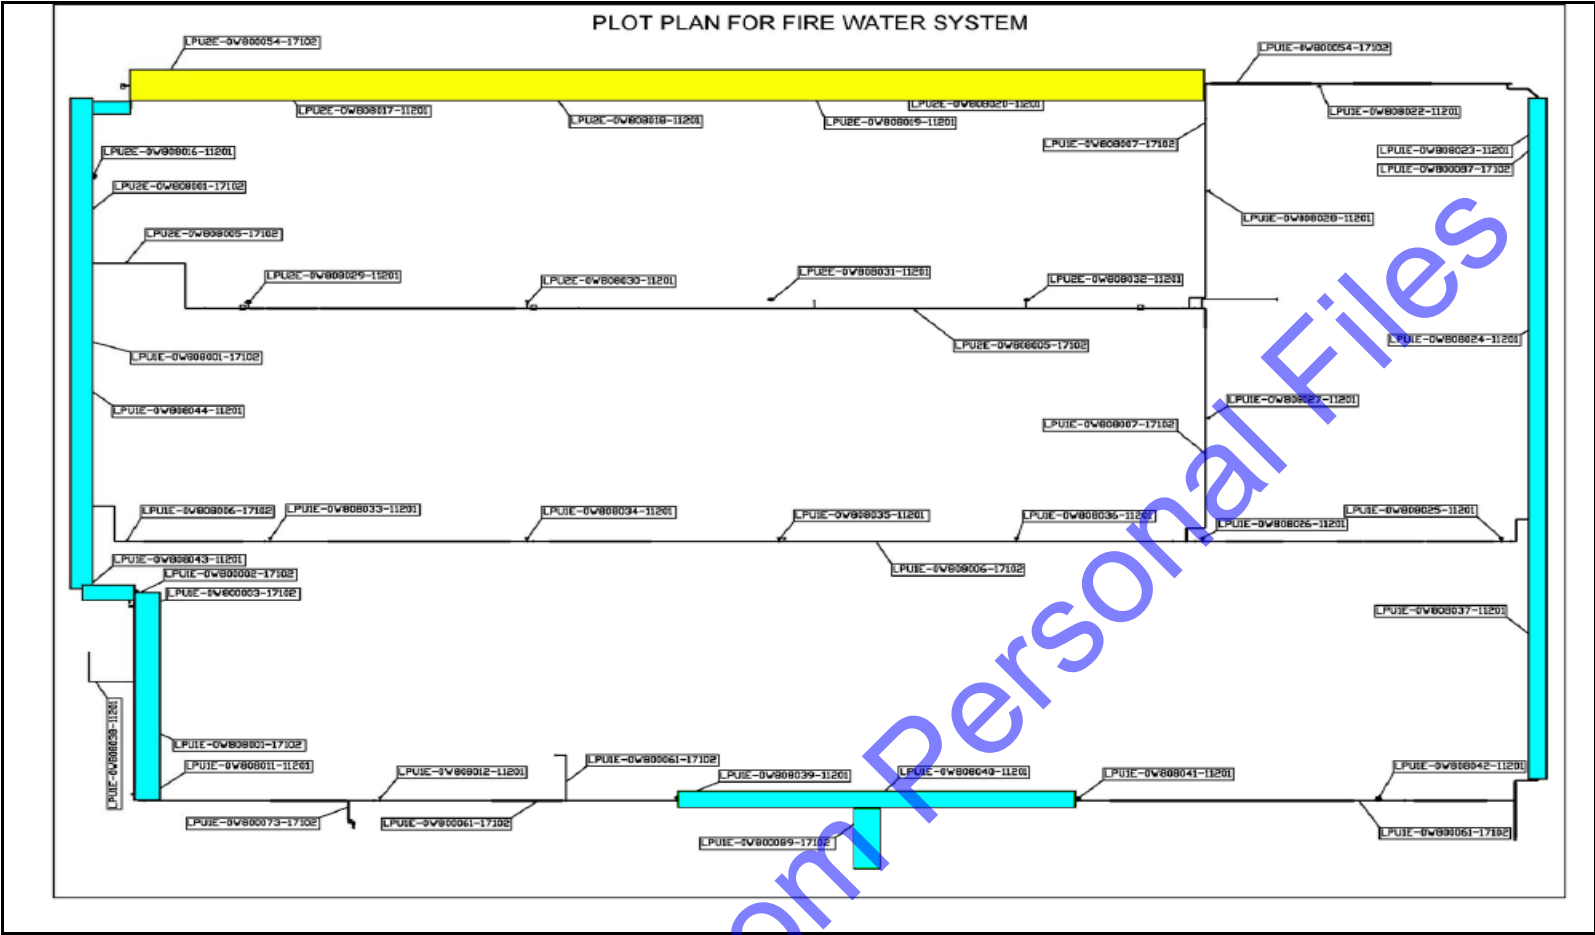

QUANTITY REPORT

Pipe Dia.	Pipe Material	Unit of Measure	Qty. (Contract)	Qty. (Revised)	Qty. (Prefab)	Qty. (Installed)	Qty. (Tested)	Qty. (Backfilled)
4"	GRE	m	12	36		12	12	12
6"	GRE	m	2			0	0	0
10"	GRE	m	1030			0	0	0
14"	GRE	m	1550			753	338	438


EARTHING GRIDS

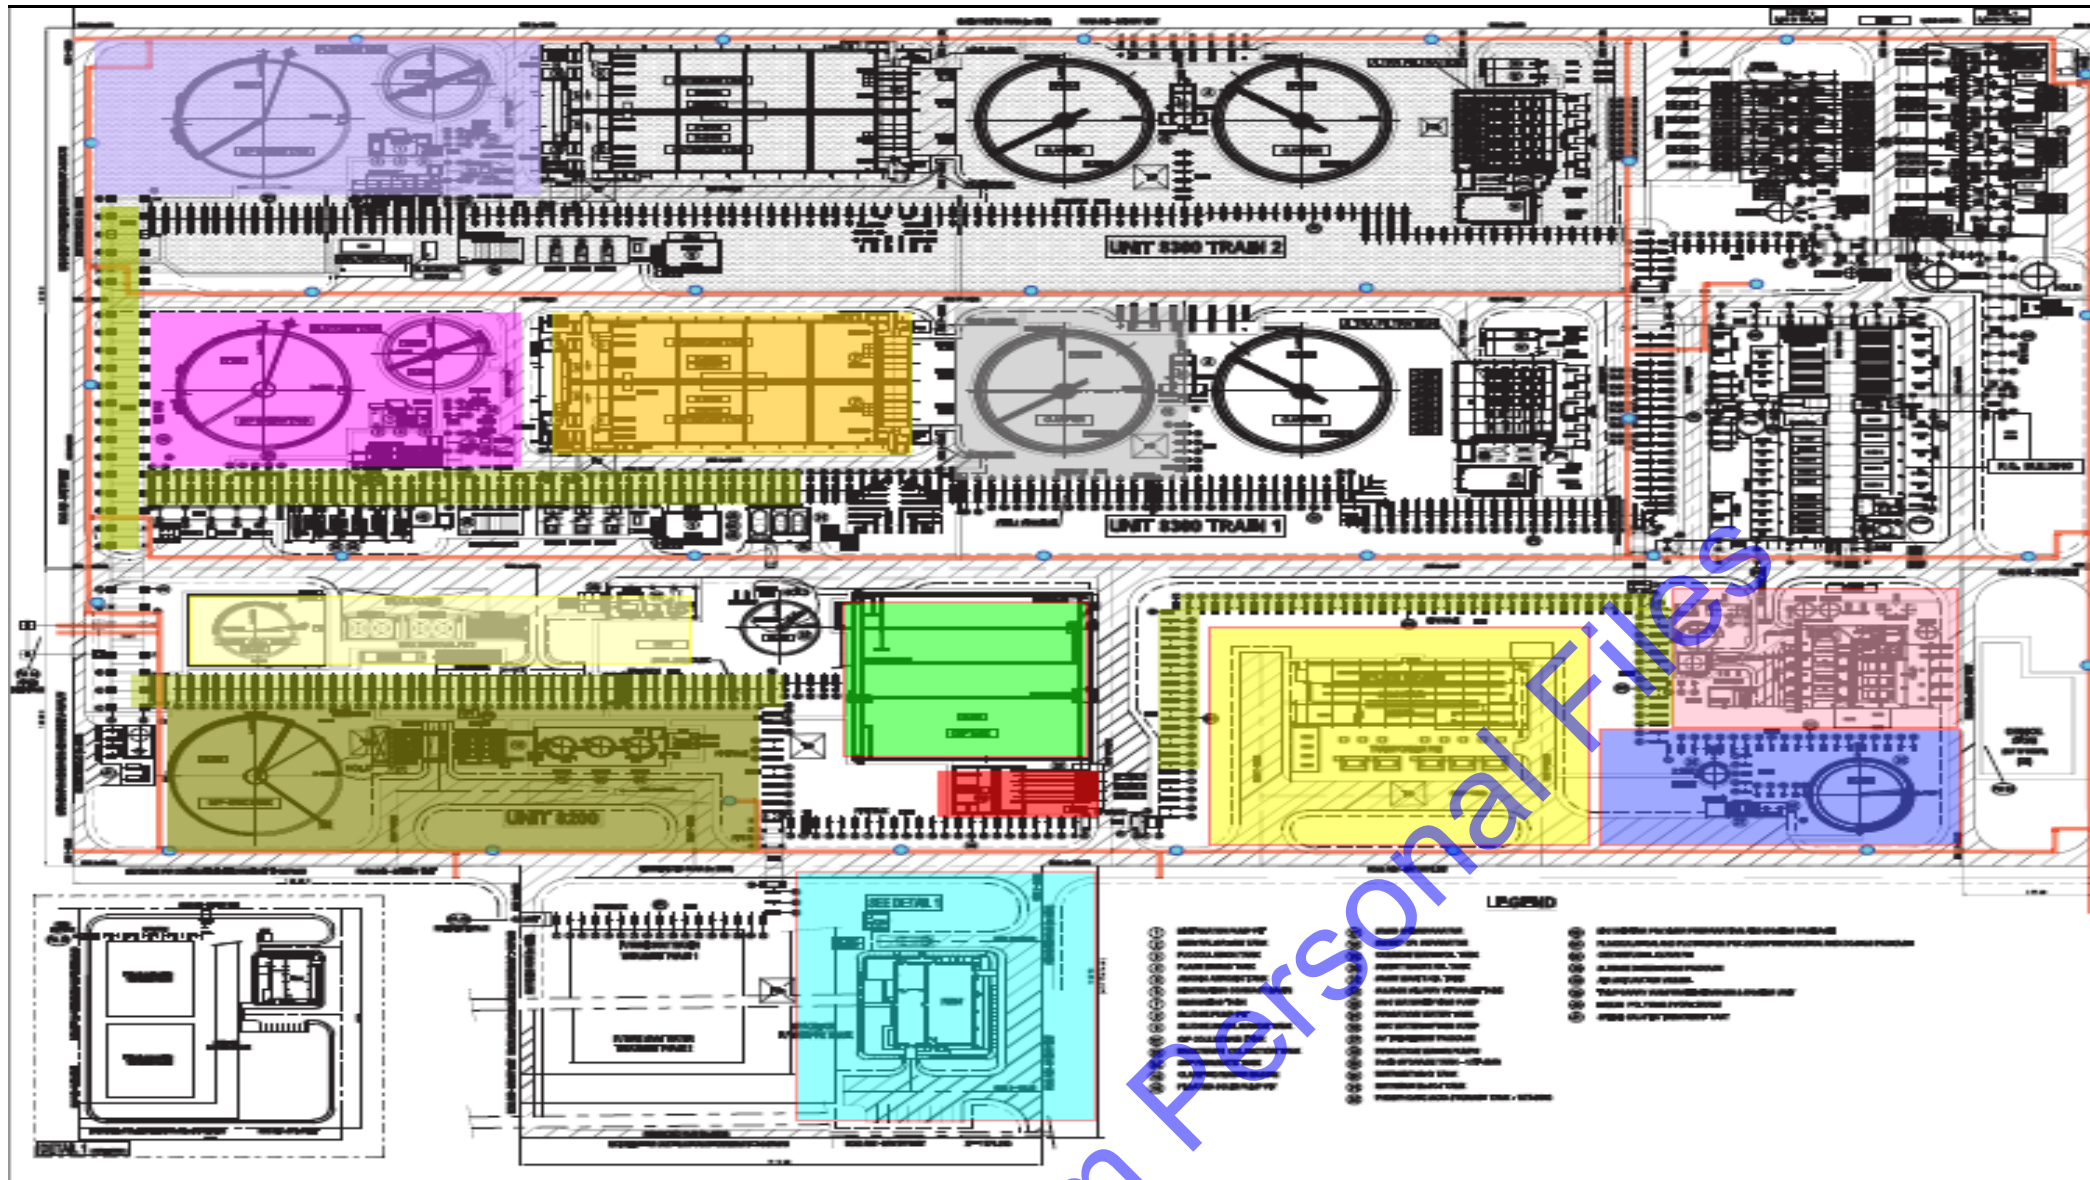EARTHING
MARKUP REPORT

QUANTITY REPORT

UNIT NAME	UNIT	FAR7	OSS200	CDF	CWBD	IWT	AOC	COC	OFF-SPEC TANK	ETPBT-1	ETPBT-2	CLARFI ER-1	Pipe Rack	BIO-Tank-1	TOTAL
HOLES	NOS	4	18	3	3	5	0	0	0	0	0	0			33
EXCAVATION	m	0	100	100	0	0	20	0	0	0	0	0			220
CABLES	m	403	955	100	320	472	50	237	175	75	216	298	367	372	4040
JOINTS	NOS	60	98	20	72	31	4	31	13	8	12	26	8	16	399
RODS	NOS	5	6	0	0	0	0	0	0						11
GRID	%	0%	0%	0%	0%	0%	0%	0%	0%						0
TARGET	DATE	30-Sep-08	30-Sep-08	15-Sep-08	15-Sep-08	20-Sep-08	15-Oct-08	15-Sep-08	15-Sep-08	15-Oct-08	30-Oct-08	15-Oct-08	15-Oct-08	15-Oct-08	


EQUIPMENT-OSS MARKUP REPORT

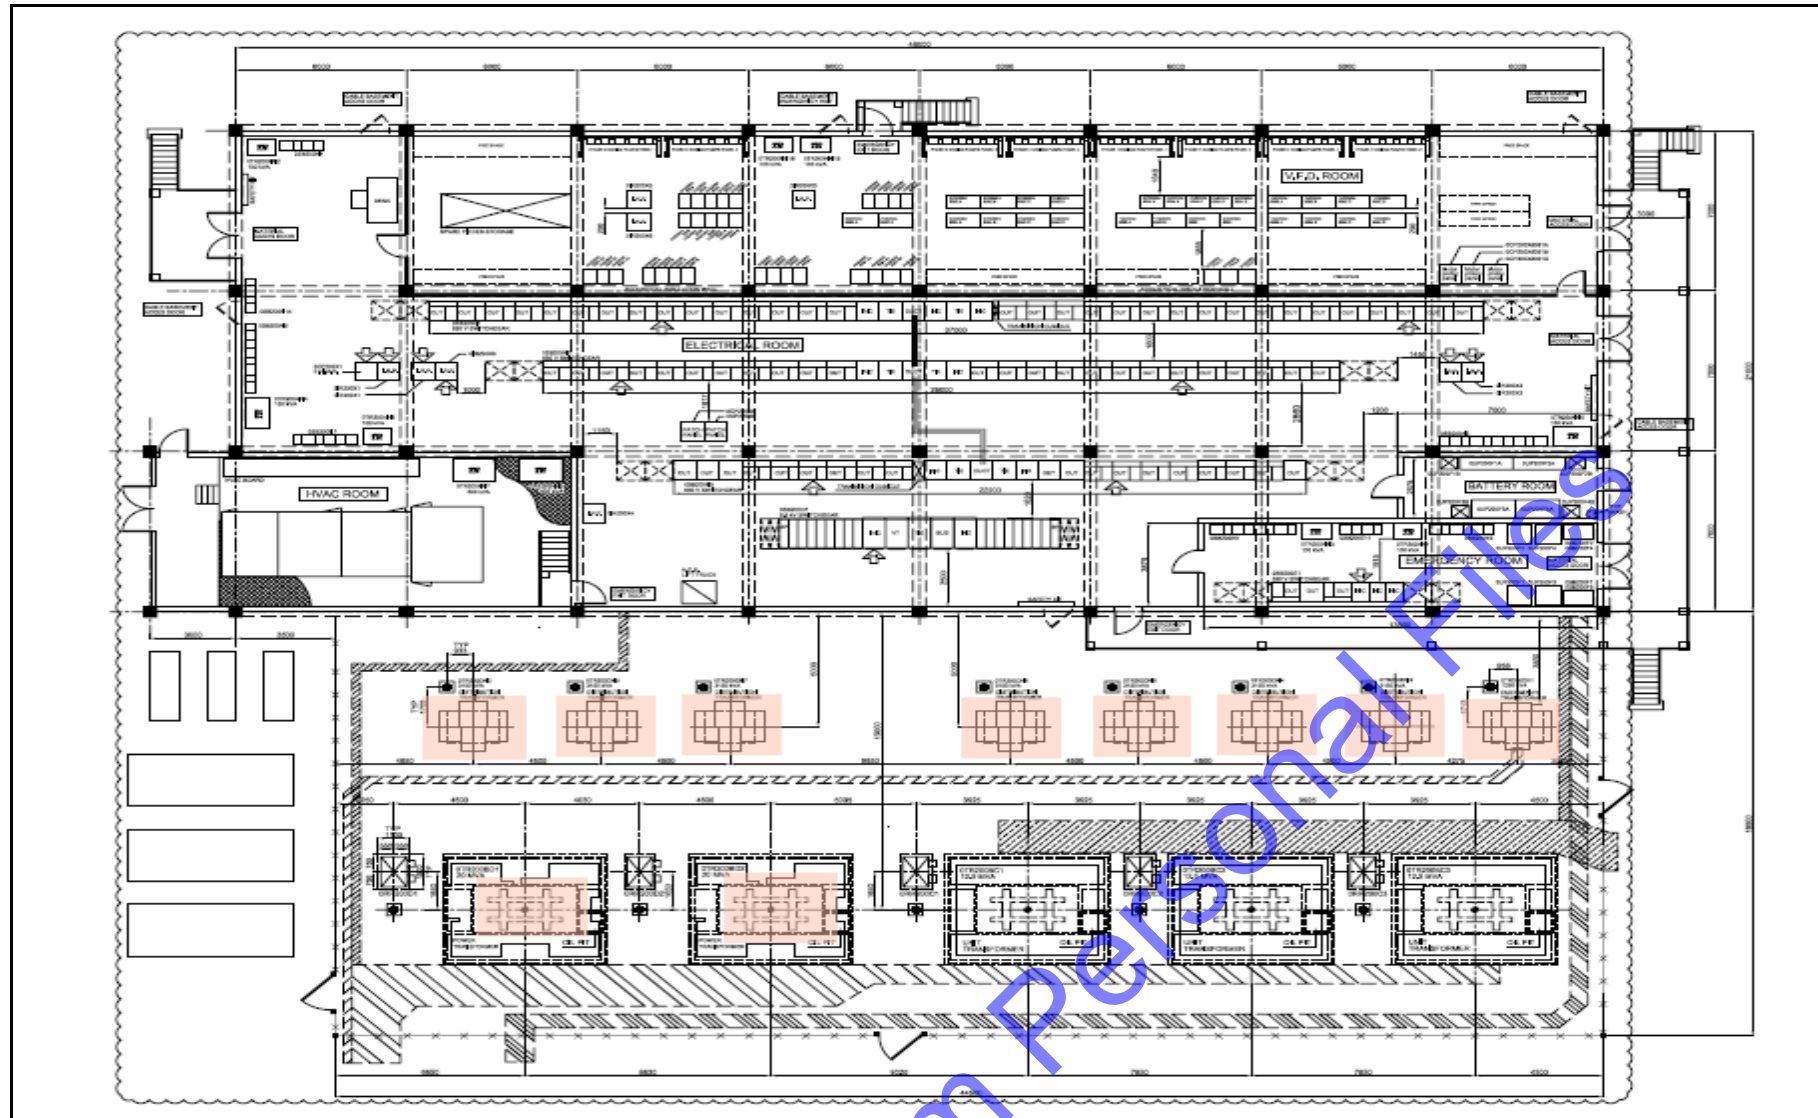

QUANTITY REPORT

Area	Unit	Actual Qty	Revised Qty.	Equipment Positioned	Equipment Terminated	Equipment Tested	Equipment Commissioned	% Completed	Target Completion
OSS200	Nos	143		10	0	0	0	2%	

TRAY'S & LIGHTS
MARKUP REPORT

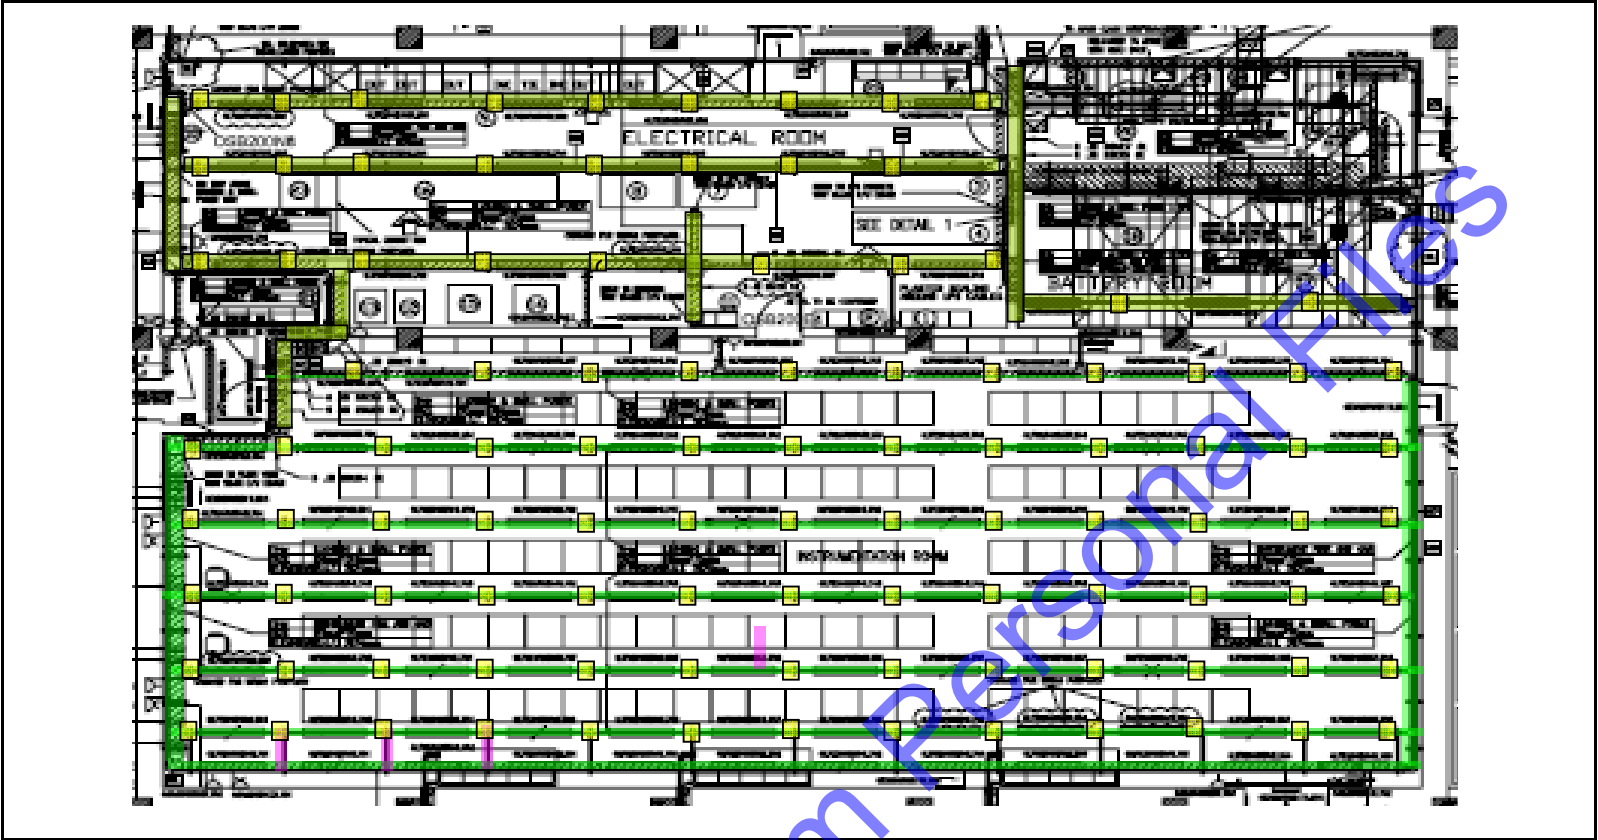

QUANTITY REPORT

Support Type	Unit	Order Qty	Revised Qty	Supplied Qty	Installed Qty	Balance Qty	% Completed	Target Completion
Hanger	nos		189	189	177	12	94%	30-Sep
Bracket	nos							
Trays	m		492	474	71	421	14%	30-Sep
Lighting	nos		154		0	154	0%	



PEARL GTL PROJECT
C8
EFFLUENT TREATMENT PLANT
SECTION-7



SCHEDULES


Archives from Personal Files

 UNDER ICC STAGE
 UNDER IFL STAGE


x	SCHEDULE (START TO COMPLETE)
	SUMMARY

[illegible]

[illegible]

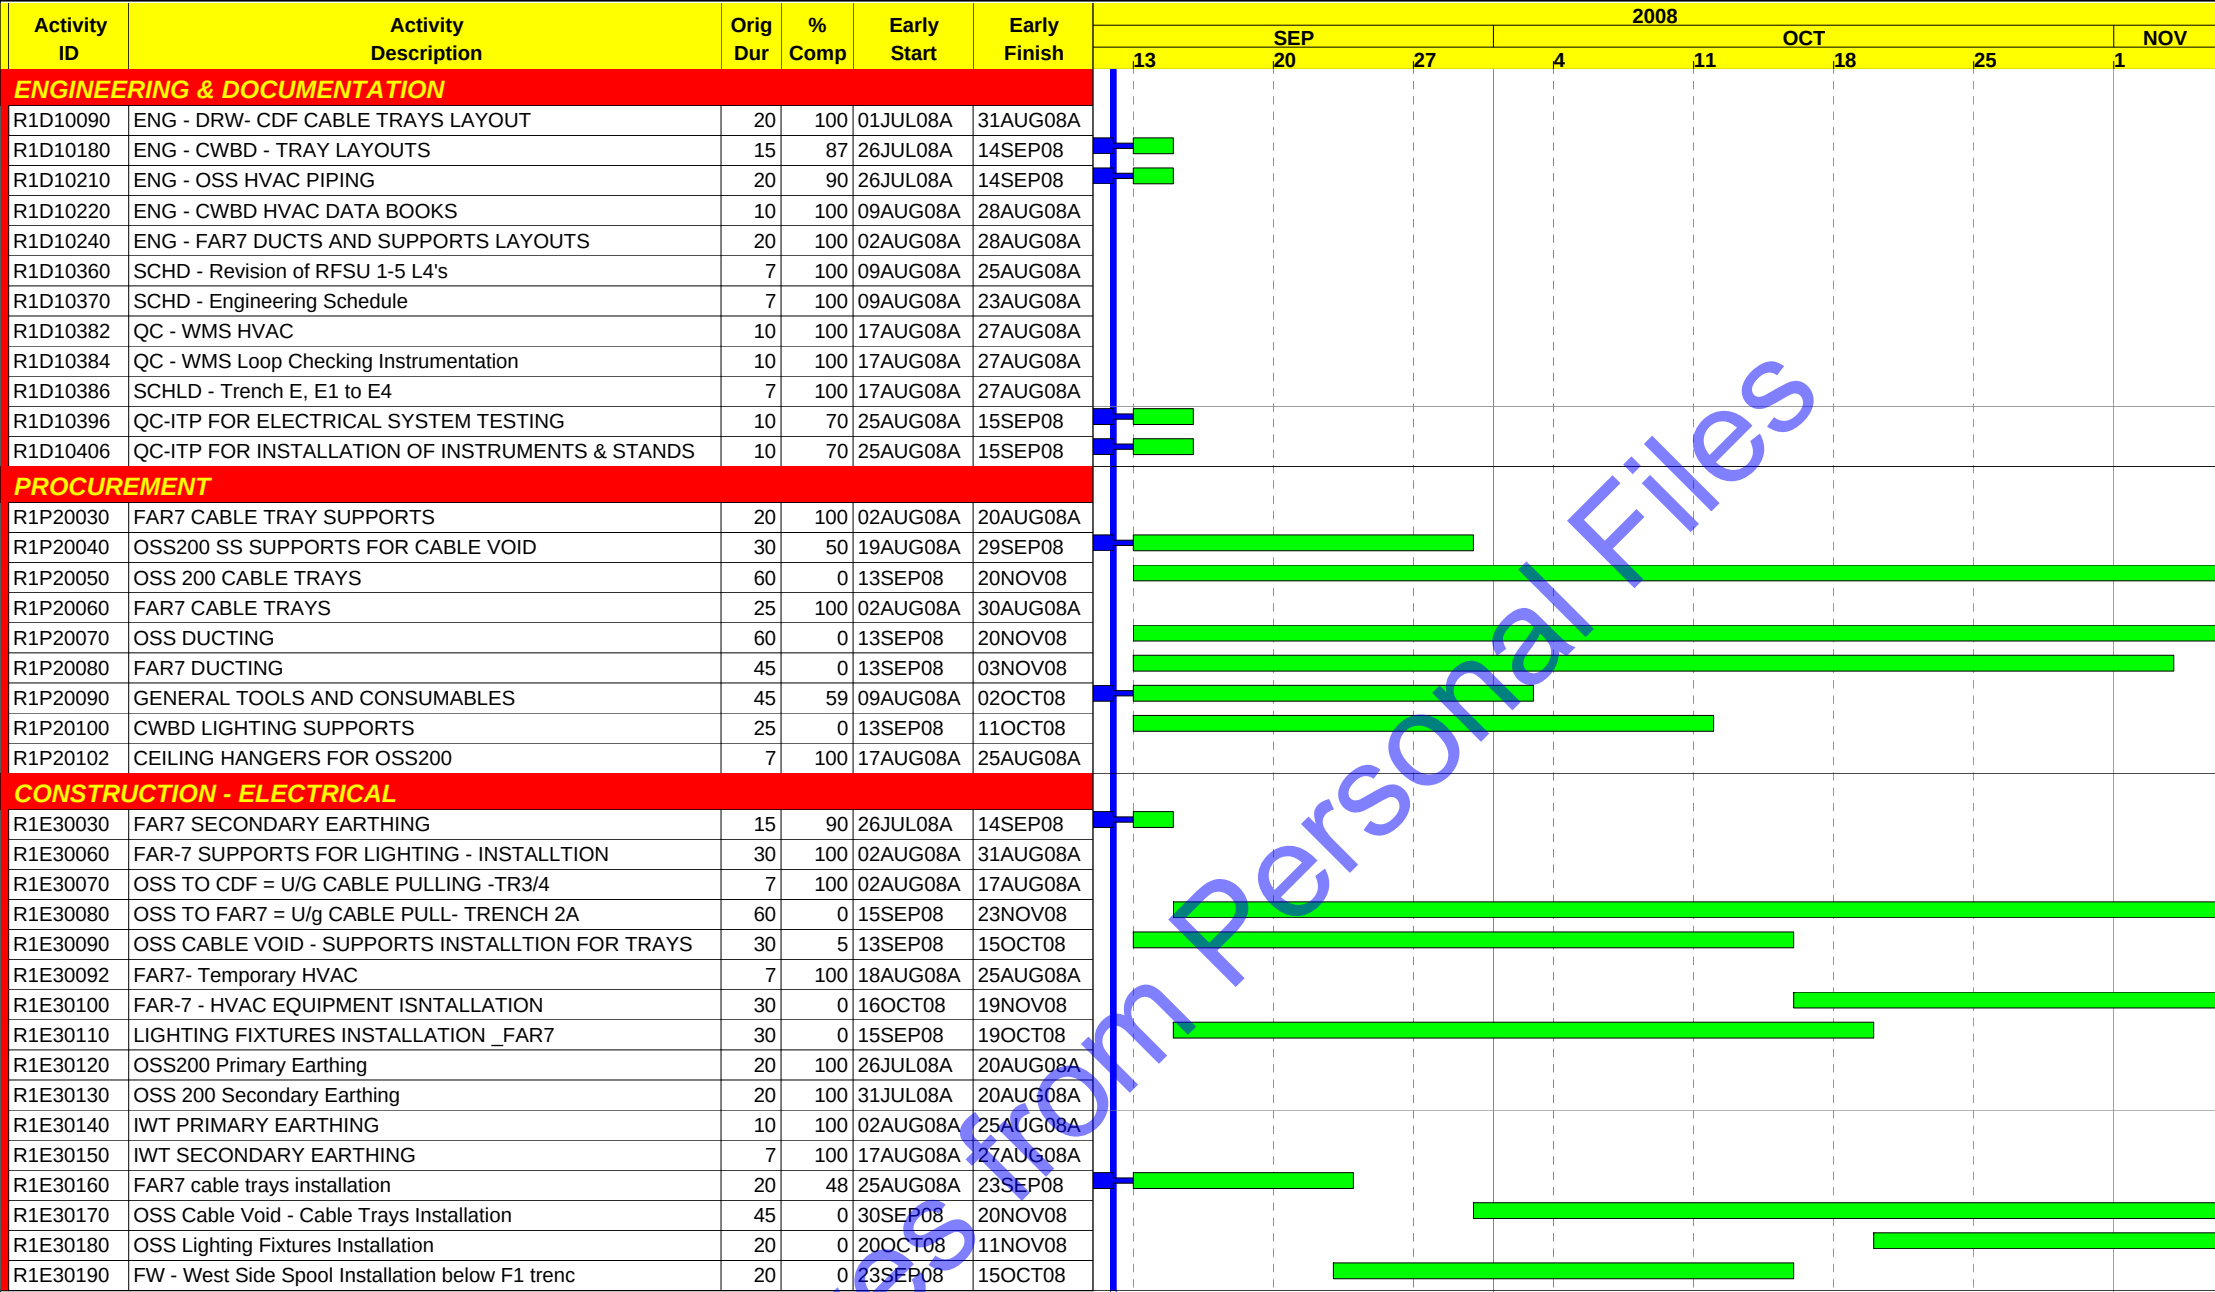

Activity ID	Activity Description	Orig Dur	% Comp	Early Start	Early Finish	2008											
						SEP			OCT						NOV		
						13	20	27	4	11	18	25	1				
R1E30200	F1 trench excavation by Al- Jaber	15	55	25AUG08A	20SEP08												
R1E30210	HILTI Supports installation inside FAR7	45	65	13AUG08A	30SEP08												
R1E30220	CDF Area - Earthing Cables - Primary	7	70	28AUG08A	14SEP08												
R1E30230	CDF Area - Earthing Cables - Secondary	15	5	10SEP08A	30SEP08												
R1E30240	FW - South side trench completion	15	100	04AUG08A	27AUG08A												
R1E30250	FW - North Side Trench Completion	20	85	16AUG08A	15SEP08												
R1E30252	Cathodic Protection for Sweet COC	20	100	25AUG08A	10SEP08A												
R1E30254	OSS200- Ceiling Hangers in basement	10	55	26AUG08A	17SEP08												
R1E30256	OSS 200 1st Floor Ceiling Hangers	20	0	18SEP08	11OCT08												
R1E30258	33kV Transformers assembly	20	0	24SEP08	16OCT08												
R1E30260	8 nos Distr. Transformers Assembly	15	100	09SEP08A	11SEP08A												
R1E30262	Ducting Installation inside OSS	20	0	29OCT08	20NOV08												
R1E30272	Laying of cables inside F1 trench - first layer	10	0	21SEP08	01OCT08												
R1E30282	Excavation of Trench E by Al Jaber	7	0	21SEP08	28SEP08												
R1E30292	U/G cables installation in Trench E - Start	10	0	29SEP08	09OCT08												

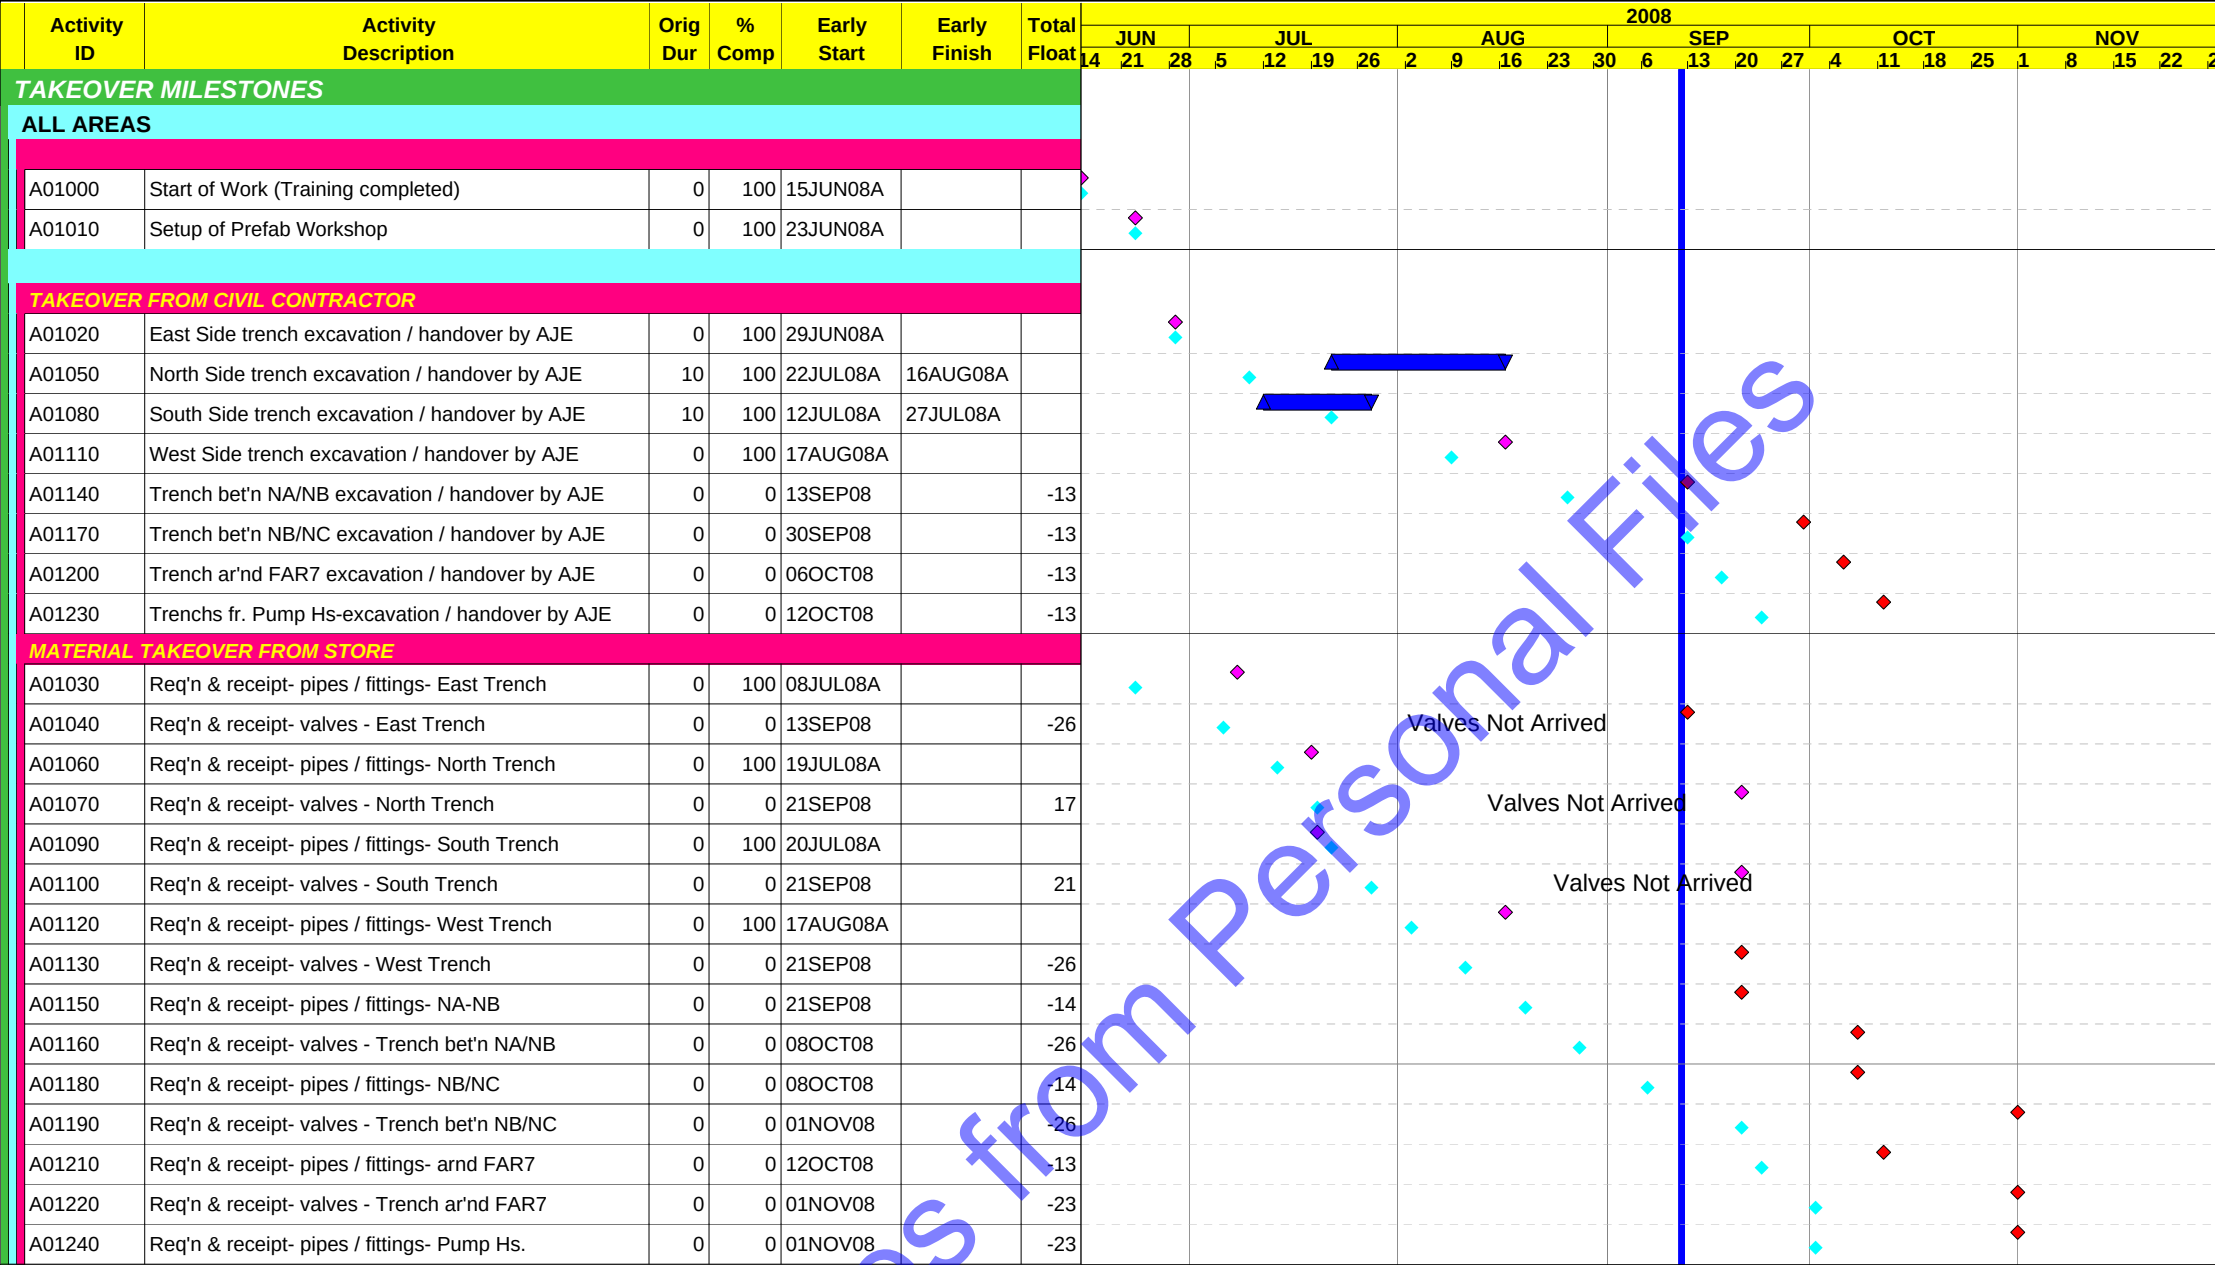

Start Date15JUN08

Finish Date11DEC08

Data Date12SEP08

Run Date13SEP08 14:58

Early Bar

Target

Progress Bar

Critical Activity

FW02

VSA / KENTECH

UPDATED CONSTRUCTION SCHEDULE

INSTALLATION OF FIRE WATER SYSTEM

Sheet 1 of 7

Date	Revision	Checked	Approved
24AUG08	SEVENTH UPDATE	RISHI	
31AUG08	EIGHTH UPDATE	SUBBU	
07SEP08	NINETH UPDATE	SUBBU	
12SEP08	TENTH UPDATE	SUBBU	

© Primavera Systems, Inc.


Activity ID	Activity Description	Orig Dur	% Comp	Early Start	Early Finish	Total Float	2008																											
							JUN				JUL				AUG				SEP				OCT				NOV							
SHOP - PREFABRICATION							14	21	28	5	12	19	26	2	9	16	23	30	6	13	20	27	4	11	18	25	1	8	15	22	29			
EAST SIDE TRENCH																																		
HEADER																																		
A02010	Shift Material from Stores to W/shop	7	100	23JUN08A	10JUL08A																													
A02020	Prefab spools	7	100	24JUN08A	15JUL08A																													
BRANCHES																																		
A02140	Prefab spools for FH 2-7	2	80	10JUL08A	11SEP08	-43																									Except for CS Spools, All Completed			
A02150	Prefab spools for FH 2-8	2	80	10JUL08A	11SEP08	-43																									Except for CS Spools, All Completed			
A02160	Prefab spools for FH 2-9	2	80	10JUL08A	11SEP08	-43																									Except for CS Spools, All Completed			
A02170	Prefab spools for FH 2-10	2	80	12JUL08A	11SEP08	-43																									Except for CS Spools, All Completed			
A02180	Prefab spools for FH 2-12	2	80	12JUL08A	11SEP08	-43																												
NORTH SIDE TRENCH																																		
HEADER																																		
AO3010	Shift Material from Stores to W/shop	4	100	20JUL08A	05AUG08A																													
AO3020	Prefab spools	4	100	22JUL08A	09AUG08A																													
BRANCHES																																		
AO3140	Prefab spools for FH 2-6	2	82	28JUL08A	20SEP08	19																									AWAITING CS MATERIAL			
AO3150	Prefab spools for FH 2-5	2	82	28JUL08A	20SEP08	23																									AWAITING CS MATERIAL			
AO3160	Prefab spools for FH 2-4	2	82	29JUL08A	20SEP08	23																									AWATING CS MATERIAL			
AO3170	Prefab spools for Additional Hydrant	2	82	30JUL08A	20SEP08	23																									AWAITING CA MATERIAL			
SOUTH SIDE TRENCH																																		
HEADER																																		
AO4010	Shift Material from Stores to W/shop	4	100	12JUL08A	04AUG08A																													
AO4020	Prefab spools	4	100	13JUL08A	07AUG08A																													
BRANCHES																																		
AO4040	Prefab spools for FH 2-13	2	80	19JUL08A	20SEP08	24																									Except for CS Spools, All Completed			
AO4050	Prefab spools for FH 2-14	2	80	20JUL08A	20SEP08	24																									Except for CS Spools, All Completed			
AO4060	Prefab spools for FH 2-27	2	80	21JUL08A	20SEP08	24																									Except for CS Spools, All Completed			
WEST SIDE TRENCH																																		
HEADER																																		
A05010	Shift Material from Stores to W/shop	7	100	14AUG08A	20AUG08A																													
A05020	Prefab spools	7	55	16AUG08A	23SEP08	-22																												
BRANCHES																																		
A05030	25Prefab spools for FH 2-1	2	28	18AUG08A	24SEP08	-22																												
A05040	Prefab spools for FH 2-2	2	28	19AUG08A	25SEP08	-22																												
A05050	Prefab spools for FH 2-3	2	28	20AUG08A	27SEP08	-22																												
A05060	Prefab spools for FH 4-1	2	28	23AUG08A	28SEP08	-22																												
A05070	Prefab spools for FH 4-2	2	0	29SEP08	30SEP08	-22																												



Activity ID	Activity Description	Orig Dur	% Comp	Early Start	Early Finish	Total Float	2008																							
							JUN			JUL				AUG				SEP				OCT				NOV				
A02230	Test all Socket / Spigot Joints	6	100	10JUL08A	19AUG08A																									
VALVES																														
A02320	Install Valve #1 / Hydrotest Header	2	90	15JUL08A	11SEP08	30																								
A02330	Install Valve #2 / Hydrotest Header	2	90	16JUL08A	11SEP08	30																								
A02340	Install Valve #3 / Hydrotest Header	2	90	19JUL08A	11SEP08	30																								
A02350	Install Valve #4 / Hydrotest Header	2	90	21JUL08A	11SEP08	30																								
BRANCHES																														
A02370	Install & join / Hydrotest FH 2-7	1	80	12AUG08A	11SEP08	-43																								
A02380	Install & join / Hydrotest FH 2-8	1	80	13AUG08A	11SEP08	-43																								
A02390	Install & join / Hydrotest FH 2-9	1	80	14AUG08A	11SEP08	-43																								
A02400	Install & join / Hydrotest FH 2-10	1	80	16AUG08A	11SEP08	-43																								
A02410	Install & join / Hydrotest FH 2-12	1	80	19AUG08A	11SEP08	-43																								
MONITORS & HYDRANTS																														
A02430	Install Hydrants & Monitors	3	0	03DEC08	06DEC08	-43																								
NORTH SIDE TRENCH																														
HEADER																														
A03210	Check Top of Trench Levels	1	100	03AUG08A	03AUG08A																									
A03220	Install & join pipes and spools	5	100	04AUG08A	18AUG08A																									
A03230	Test all Socket / Spigot Joints	3	100	11AUG08A	20AUG08A																									
VALVES																														
A03320	Install Valve #1 / Hydrotest Header	2	60	13AUG08A	21SEP08	17																								
A03330	Install Valve #2 / Hydrotest Header	2	60	17AUG08A	22SEP08	17																								
BRANCHES																														
A03350	Install & join / Hydrotest FH 2-6	1	0	23SEP08	23SEP08	17																								
A03360	Install & join / Hydrotest FH 2-5	1	0	24SEP08	24SEP08	17																								
A03370	Install & join / Hydrotest FH 2-4	1	0	25SEP08	25SEP08	17																								
A03380	Install & join / Hydrotest Additional Hydrant	1	0	27SEP08	27SEP08	17																								
MONITORS & HYDRANTS																														
A03410	Install Hydrants & Monitors	1	0	07DEC08	07DEC08	-43																								
SOUTH SIDE TRENCH																														
HEADER																														
A04210	Check Top of Trench Levels	1	100	27JUL08A	31JUL08A																									
A04220	Install & join pipes and spools	5	100	02AUG08A	17AUG08A																									
A04230	Test all Socket / Spigot Joints	3	100	09AUG08A	18AUG08A																									
VALVES																														
A04250	Install Valve #1 / Hydrotest Header	2	80	11AUG08A	20SEP08	21																								
A04260	Install Valve #2 / Hydrotest Header	2	80	11AUG08A	20SEP08	21																								

Activity ID	Activity Description	Orig Dur	% Comp	Early Start	Early Finish	Total Float	2008																											
							JUN			JUL				AUG					SEP				OCT				NOV							
							14	21	28	5	12	19	26	2	9	16	23	30	6	13	20	27	4	11	18	25	1	8	15	22	29			
BRANCHES																																		
A04280	Install & join / Hydrotest FH 2-13	1	0	21SEP08	21SEP08	21																												
A04290	Install & join / Hydrotest FH 2-14	1	0	22SEP08	22SEP08	21																												
A04300	Install & join / Hydrotest FH 2-27	1	0	23SEP08	23SEP08	21																												
MONITORS & HYDRANTS																																		
A04330	Install Hydrants & Monitors	1	0	08DEC08	08DEC08	-43																												
WEST SIDE TRENCH																																		
HEADER																																		
A05210	Check Top of Trench Levels	1	0	13SEP08	13SEP08	-24																												
A05220	Install & join pipes and spools	5	0	14SEP08	18SEP08	-24																												
A05230	Test all Socket / Spigot Joints	3	0	17SEP08	20SEP08	-24																												
VALVES																																		
A05250	Install Valve #1 / Hydrotest Header	2	0	21SEP08	22SEP08	-24																												
A05260	Install Valve #2 / Hydrotest Header	2	0	23SEP08	24SEP08	-24																												
A05270	Install Valve #3 / Hydrotest Header	2	0	25SEP08	27SEP08	-24																												
A05340	Install Valve #4 / Hydrotest Header	2	0	28SEP08	29SEP08	-24																												
BRANCHES																																		
A05280	Install & join / Hydrotest FH 2-1	1	0	30SEP08	30SEP08	-24																												
A05290	Install & join / Hydrotest FH 2-2	1	0	01OCT08	01OCT08	-24																												
A05300	Install & join / Hydrotest FH 2-3	1	0	02OCT08	02OCT08	-24																												
A05310	Install & join / Hydrotest FH 4-1	1	0	04OCT08	04OCT08	-24																												
A05360	Install & join / Hydrotest FH 4-2	1	0	05OCT08	05OCT08	-24																												
A05370	Install & join / Hydrotest FH 4-3	1	0	06OCT08	06OCT08	-24																												
A05380	Install & join / Hydrotest FH 4-4	1	0	07OCT08	07OCT08	-24																												
MONITORS & HYDRANTS																																		
A05320	Install Hydrants & Monitors	1	0	09DEC08	09DEC08	-43																												
TRENCH BETWEEN AREAS NA & NB																																		
HEADER																																		
A06210	Check Top of Trench Levels	1	0	13SEP08	13SEP08	-9																												
A06220	Install & join pipes and spools	8	0	14SEP08	22SEP08	-9																												
A06230	Test all Socket / Spigot Joints	6	0	17SEP08	23SEP08	-9																												
VALVES																																		
A06250	Install Valve #1 / Hydrotest Header	2	0	08OCT08	09OCT08	-21																												
A06260	Install Valve #2 / Hydrotest Header	2	0	11OCT08	12OCT08	-21																												
A06270	Install Valve #3 / Hydrotest Header	2	0	13OCT08	14OCT08	-21																												
A06280	Install Valve #4 / Hydrotest Header	2	0	15OCT08	16OCT08	-21																												
A06290	Install Valve #5 / Hydrotest Header	2	0	18OCT08	19OCT08	-21																												

Activity ID	Activity Description	Orig Dur	% Comp	Early Start	Early Finish	Total Float	2008																											
							JUN			JUL				AUG					SEP				OCT				NOV							
							14	21	28	5	12	19	26	2	9	16	23	30	6	13	20	27	4	11	18	25	1	8	15	22	29			
A08260	Install Valve #2 / Hydrotest Header	2	0	03NOV08	04NOV08	-16																												
SUPPLY & RETURN FROM PUMP HOUSE																																		
HEADER																																		
A08270	Check Top of Trench Levels	1	0	08NOV08	08NOV08	-23																												
A08280	Install & join pipes and spools	2	0	09NOV08	10NOV08	-23																												
A08290	Test Supply Header	1	0	11NOV08	11NOV08	-23																												
A08300	Test Return Header	1	0	12NOV08	12NOV08	-23																												
HANDOVER MILESTONES																																		
A09010	Release East Trench for Backfilling	0	0		11SEP08	42																												
A09020	Release North trench for backfilling	0	0		27SEP08	29																												
A09030	Release South trench for backfilling	0	0		23SEP08	32																												
A09040	Release West Trench for Backfilling	0	0		11SEP08*	-2																												
A09050	Release Trench between NA&NB for Backfilling	0	0		02OCT08*	0																												
A09060	Release trench between NB & NC for Backfilling	0	0		21OCT08*	0																												
A09070	Release Trenches North & South of FAR7 for backf	0	0		16OCT08*	0																												
A09080	Release trenches from Pump House for backfilling	0	0		16OCT08*	0																												
A09090	Complete installation of all Hydrants & Monitors	0	0		22OCT08*	0																												
A09100	Charge and Handover system to COMPANY	0	0		30OCT08*	0																												

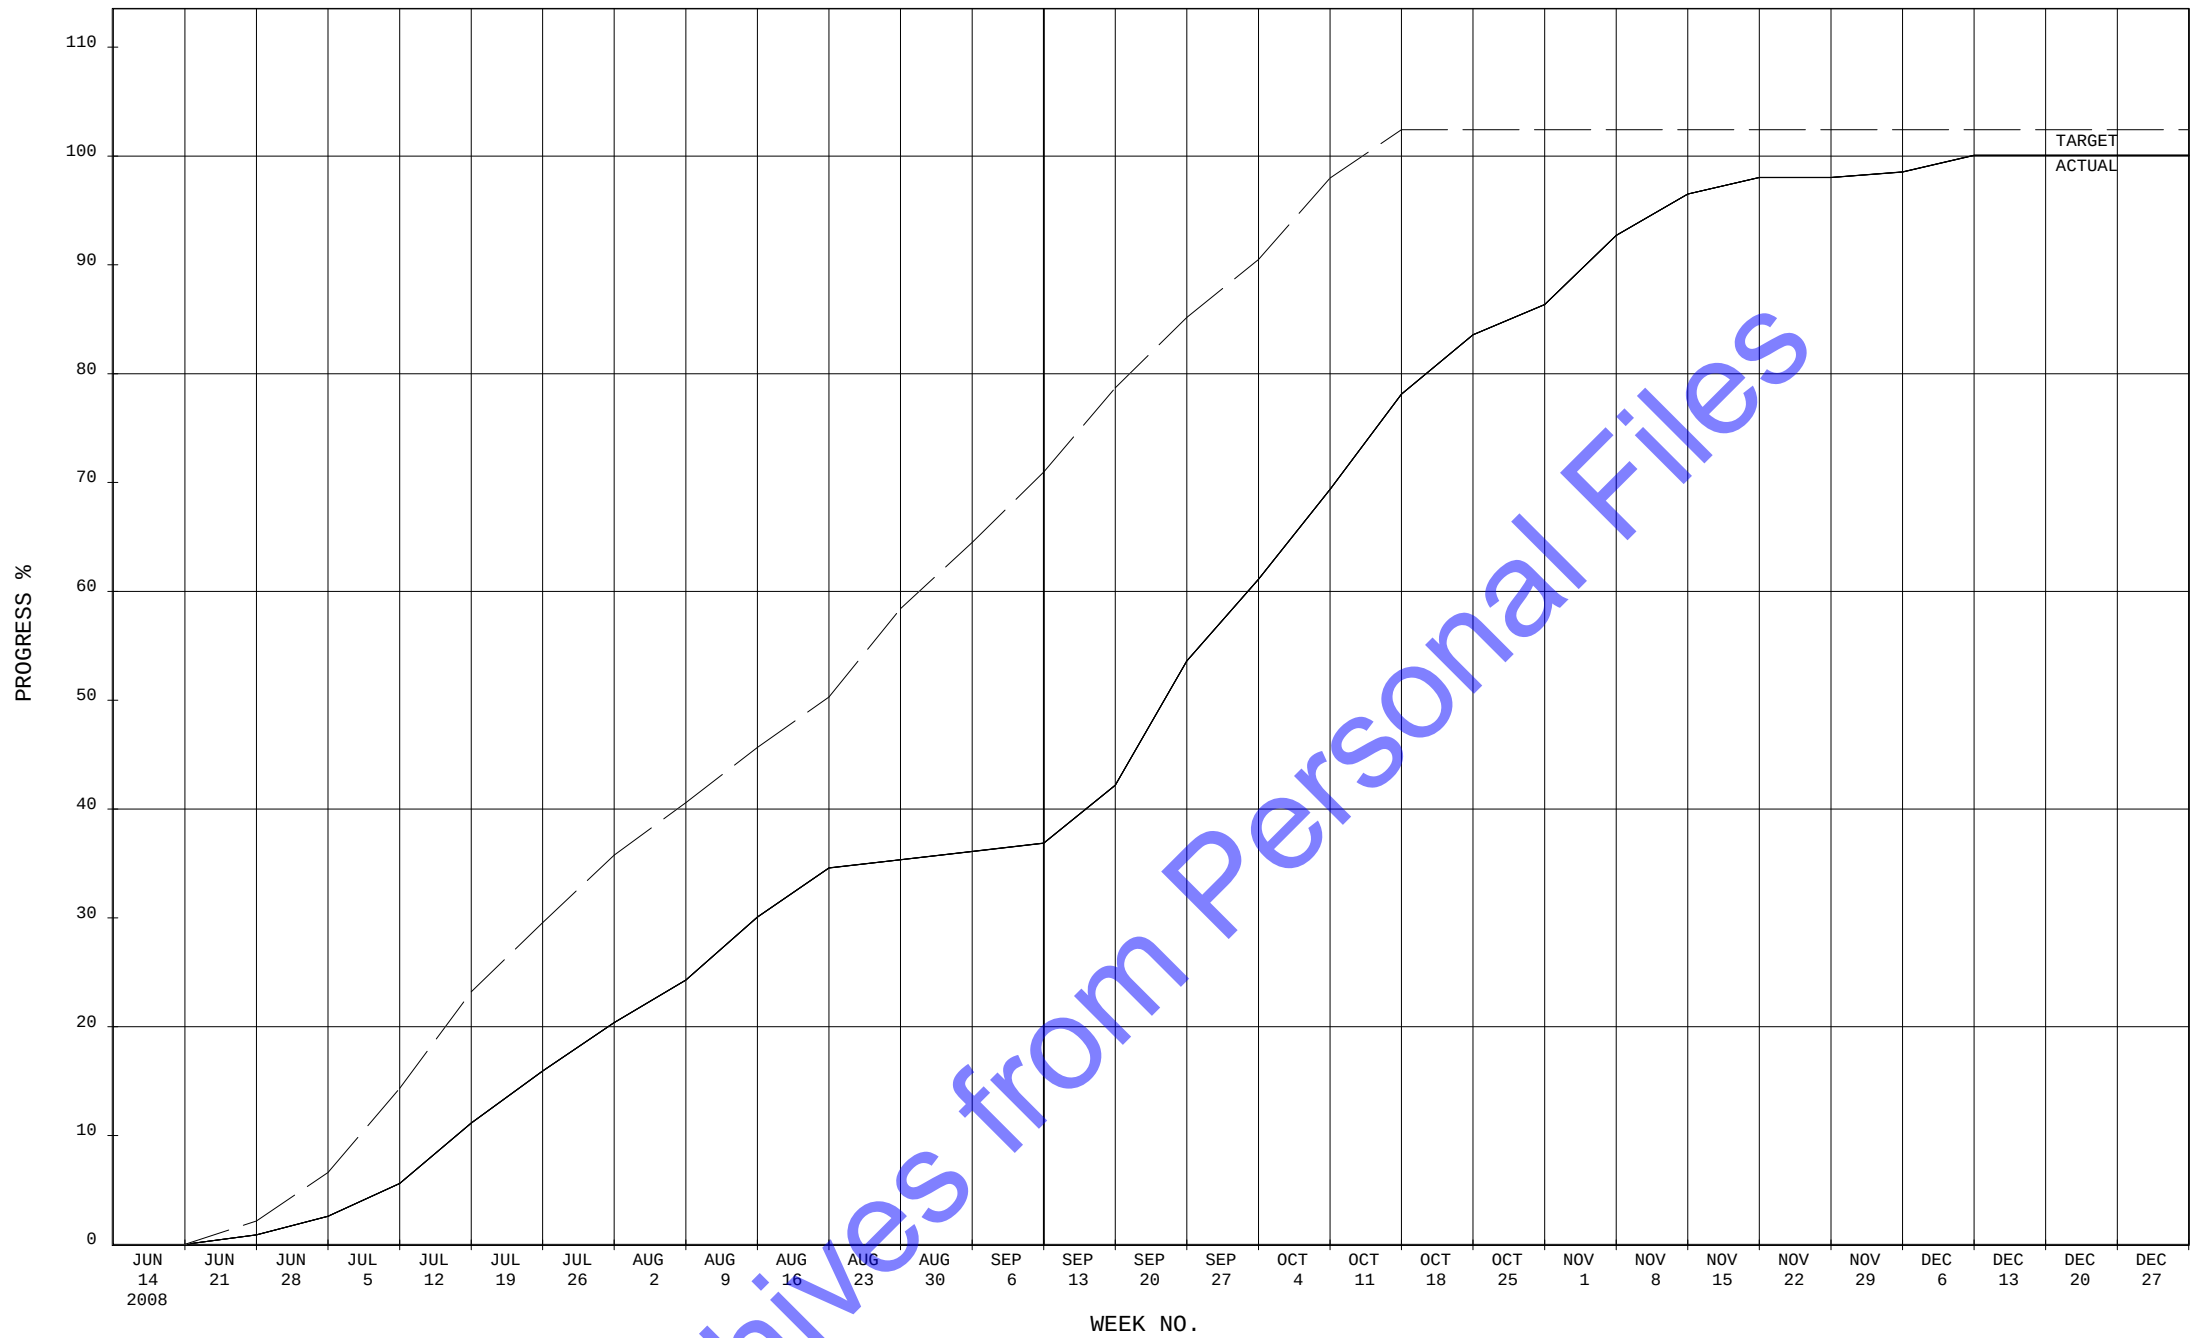

Project Start 15JUN08
Project Finish 31OCT08*
Data Date 12SEP08
Plot Date 13SEP08

Schedule dates
Target 1 dates as of: 15JUN08

FW02

VSA / KENTECH
FIRE WATER WORKS FOR ETP AT 02P
FIRE WATER WORKS PROGRESS

Sheet 1 of 1

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	% Comp	Early Start	Early Finish	2008						2009									
						JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL			
RFSU-1																					
8200 CDF Tank																					
E013010	Study / Req'n / Shift cables / Drums	2	100	11AUG08A	12AUG08A																
E013020	Cut To Length - Connector Cables	3	100	13AUG08A	17AUG08A																
E013030	Prepare / Roll / Shift - Primary mesh	3	100	18AUG08A	20AUG08A																
E013070	Prepare / receive / lay -secondary mesh	7	70	18AUG08A	15SEP08																
E013050	Connect Primary Mesh to Earthing Bosses	4	100	21AUG08A	07SEP08A																
E013090	Install earthing rods and copper bars	4	0	24SEP08	28SEP08																
E013100	Interconnect connectors to bars	5	0	29SEP08	04OCT08																
E013110	Test / check / insulate interconnections	3	0	05OCT08	07OCT08																
E013120	QC / Documentation	7	0	08OCT08	15OCT08																
Substation OSS200																					
E012010	Study / Req'n / Shift cables / Drums	2	100	20JUL08A	24JUL08A																
E012020	Cut To Length - Connector Cables	3	100	27JUL08A	04AUG08A																
E012030	Prepare / Roll / Shift - Primary mesh	3	100	27JUL08A	06AUG08A																
E012050	Connect Primary Mesh to Earthing Bosses	4	100	30JUL08A	10AUG08A																
E012070	Prepare / receive / lay -secondary mesh	7	100	31JUL08A	21AUG08A																
E012090	Install earthing rods and copper bars	4	100	07SEP08A	09SEP08A																
E012100	Interconnect connectors to bars	5	0	14SEP08	18SEP08																
E012110	Test / check / insulate interconnections	3	0	20SEP08	22SEP08																
E012120	QC / Documentation	7	0	23SEP08	30SEP08																
FAR7																					
E011010	Study / Req'n / Shift cables / Drums	2	100	16JUL08A	19JUL08A																
E011020	Cut To Length - Connector Cables	3	100	17JUL08A	20JUL08A																
E011030	Prepare / Roll / Shift - Primary mesh	3	100	19JUL08A	21JUL08A																
E011050	Connect Primary Mesh to Earthing Bosses	4	100	21JUL08A	22JUL08A																
E011070	Prepare / receive / lay -secondary mesh	7	100	17AUG08A	09SEP08A																
E011090	Install earthing rods and copper bars	4	100	10SEP08A	14SEP08A																
E011100	Interconnect connectors to bars	5	0	14SEP08	18SEP08																
E011110	Test / check / insulate interconnections	3	0	20SEP08	22SEP08																

Start Date	01JAN08		Early Bar	EART	Sheet 1 of 3					
Finish Date	05MAY09									
Data Date	14SEP08		Target							
Run Date	16SEP08 07:36		Progress Bar							
			Critical Activity							
C8 - VSA / SAIPEM / KENTECH										
EFFLUENT TREATMENT PLANT - O2 PEARL										
SCHEDULE FOR EARTHING GRIDS INSTALLATION										

Activity ID	Activity Description	Orig Dur	% Comp	Early Start	Early Finish	2008						2009						
						JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL
E011120	QC / Documentation	7	0	23SEP08	30SEP08													
RFSU-2																		
7100 CWBD																		
E010010	Study / Req'n / Shift cables / Drums	2	100	05JUL08A	10JUL08A													
E010020	Cut To Length - Connector Cables	3	100	06JUL08A	24JUL08A													
E010030	Prepare / Roll / Shift - Primary mesh	3	100	07JUL08A	26JUL08A													
E010050	Connect Primary Mesh to Earthing Bosses	4	100	08JUL08A	27JUL08A													
E010070	Prepare / receive / lay -secondary mesh	7	100	05AUG08A	18AUG08A													
E010090	Install earthing rods and copper bars	4	100	27AUG08A	10SEP08A													
E010100	Interconnect connectors to bars	5	0	14SEP08	18SEP08													
E010110	Test / check / insulate interconnections	3	0	20SEP08	22SEP08													
E010120	QC / Documentation	7	0	23SEP08	30SEP08													
RFSU-3																		
8200 Off-spec Tank																		
E026010	Study / Req'n / Shift cables / Drums	2	100	08SEP08A	09SEP08A													
E026020	Cut To Length - Connector Cables	3	100	08SEP08A	10SEP08A													
E026030	Prepare / Roll / Shift - Primary mesh	3	100	09SEP08A	11SEP08A													
E026050	Connect Primary Mesh to Earthing Bosses	4	100	10SEP08A	10SEP08A													
E026070	Prepare / receive / lay -secondary mesh	7	100	10SEP08A	14SEP08A													
E026090	Install earthing rods and copper bars	4	0	22SEP08	25SEP08													
E026100	Interconnect connectors to bars	5	0	27SEP08	01OCT08													
E026110	Test / check / insulate interconnections	3	0	02OCT08	05OCT08													
E026120	QC / Documentation	7	0	06OCT08	13OCT08													
8200 Wax Removal																		
E015010	Study / Req'n / Shift cables / Drums	2	100	10SEP08A	11SEP08A													
E015020	Cut To Length - Connector Cables	3	100	10SEP08A	13SEP08A													
E015030	Prepare / Roll / Shift - Primary mesh	3	0	14SEP08	16SEP08													
E015050	Connect Primary Mesh to Earthing Bosses	4	0	17SEP08	21SEP08													
E015070	Prepare / receive / lay -secondary mesh	7	0	30SEP08	07OCT08													
E015090	Install earthing rods and copper bars	4	0	16OCT08	20OCT08													
E015100	Interconnect connectors to bars	5	0	21OCT08	26OCT08													
E015110	Test / check / insulate interconnections	3	0	27OCT08	29OCT08													
E015120	QC / Documentation	7	0	30OCT08	06NOV08													
8301 Buffer Tank																		
E016010	Study / Req'n / Shift cables / Drums	2	0	22SEP08	23SEP08													

Activity ID	Activity Description	Orig Dur	% Comp	Early Start	Early Finish	2008						2009											
						JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL					
E016020	Cut To Length - Connector Cables	3	0	24SEP08	27SEP08																		
E016030	Prepare / Roll / Shift - Primary mesh	3	0	28SEP08	30SEP08																		
E016050	Connect Primary Mesh to Earthing Bosses	4	0	01OCT08	05OCT08																		
E016070	Prepare / receive / lay -secondary mesh	7	0	14OCT08	21OCT08																		
E016090	Install earthing rods and copper bars	4	0	28OCT08	01NOV08																		
E016100	Interconnect connectors to bars	5	0	02NOV08	06NOV08																		
E016110	Test / check / insulate interconnections	3	0	08NOV08	10NOV08																		
E016120	QC / Documentation	7	0	11NOV08	18NOV08																		
8340 Biotreater																							
E017010	Study / Req'n / Shift cables / Drums	2	0	06OCT08	07OCT08																		
E017020	Cut To Length - Connector Cables	3	0	08OCT08	11OCT08																		
E017030	Prepare / Roll / Shift - Primary mesh	3	0	12OCT08	14OCT08																		
E017050	Connect Primary Mesh to Earthing Bosses	4	0	15OCT08	19OCT08																		
E017070	Prepare / receive / lay -secondary mesh	7	0	28OCT08	04NOV08																		
E017090	Install earthing rods and copper bars	4	0	13NOV08	17NOV08																		
E017100	Interconnect connectors to bars	5	0	18NOV08	23NOV08																		
E017110	Test / check / insulate interconnections	3	0	24NOV08	26NOV08																		
E017120	QC / Documentation	7	0	27NOV08	04DEC08																		
8340 Clarifier 1																							
E018010	Study / Req'n / Shift cables / Drums	2	0	20OCT08	21OCT08																		
E018020	Cut To Length - Connector Cables	3	0	22OCT08	25OCT08																		
E018030	Prepare / Roll / Shift - Primary mesh	3	0	26OCT08	28OCT08																		
E018050	Connect Primary Mesh to Earthing Bosses	4	0	29OCT08	02NOV08																		
E018070	Prepare / receive / lay -secondary mesh	7	0	11NOV08	18NOV08																		
E018090	Install earthing rods and copper bars	4	0	27NOV08	01DEC08																		
E018100	Interconnect connectors to bars	5	0	02DEC08	07DEC08																		
E018110	Test / check / insulate interconnections	3	0	08DEC08	10DEC08																		
E018120	QC / Documentation	7	0	11DEC08	18DEC08																		

