


February 23, 2020

 أدنوك للتكرير
ADNOC Refining
ADNOC

 Plan 34.43% Act 32.35% Var -2.08%
SHUTDOWN PROGRESS MONITOR


NEWSLETTER

RRWs CBDC-WSD & CDU/UTILITIES/OFFSITE T/As 2020

HIGHLIGHTS

BLOCK WISE

BLOCK-1 (Units 1100, 1110, 1120, 1130, 1510, 1690) Running Behind Sched

1510-D-053 buffing i/p, C-001 segment 13 and 24 removal complete, D-012/13 internal fixing completed, D-005 dome dropped, EA-001C2/D1/D2 air blowing completed, EA-001D1/003 A1/A2 hydro-jetting completed.

1130-E-002A/B manual cleaning and inspection completed D-003 manway boxup done, /004 A/B / 001 A/B buffing completed, NDT

1120-D-010 cleaning, D-111 manway boxup, D-112 buffing completed, E-100 hydrojetting, F-001 boxup done, D-010 buffing complete, 228/274CVs and 214/296 PSVs dropped, 23CVs & 48 PSVs reinstalled

BLOCK-2 (UNITS 1210, 1400, 1520, 1530) Running Ahead of Schedule

1210-D-54 boxup, D-005 boxup and deblending, B-002 blinding completed

1400- D-054 boxup done, D-111 blinding completed and manway opened, D-001 buffing and cleaning, D-003 internal cleaning i/p, EA-002 B1/B2 Cleaning done

290 CVs & 85PSVs removed, 4 CVs installed

BLOCK-3 (UNITS 1300, 1800, 1810, 1700, 1900, 1036) Running Ahead of Sch

1900- E-402C internal cleaning, E-201 cover open/202/203 dome cover removal, E-402A/B bundle installed, E-502C shell hydrotest, E-501 A/B bundle installed, C-501/502 all Tray m/ways open, EA 500A/B / 502 plug removal, B-601 ventilation, D-600 i/ scaffolding, E-101 dome cover fixing, D-601 blinding, C-401 i/scaffolding

1700-C-01 tray manway opening, internal scaffolding, EA-012/22 boxup, E-021B buffing completed, 21A buffing i/p, EA-001A/B/C/D hydro-jetting completed

1800-EA 101A/B/012/022 hydrojetting completed, EA-001A/B/C/D/101A/B air blowing completed, D-001 internal scaffolding i/p

1036-ME-001D2 ready for boxup, ME-001D3 buffing, ME-001E1/E2 hydrojetting

Total 212CVs removed 95 PSVs removed, 12 CVs and 22 PSVs installed

BLOCK-4 (UNITS 1023, 1024, 1041, 1045, 1060) Running Ahead of Schedule

Unit -1060 (Jetty) 10 Boxups completed
All concentration on Flare Jobs this week. Preparing for Tip replacement

7CVs / 21PSVs removed & 17 PSVs reinstalled

HSE Message—Shamsudeen H (Logistics Co'ordinator STS)

Safe Work Practice & Habits desired from Drivers & Operators on TA :

- ◆ Be Safety Trained and Safe to work
- ◆ Competent by training, experience and knowledge
- ◆ Be fit and healthy
- ◆ Obtain authorization by Site / Plant Safety Department
- ◆ Site Induction and Permit to Drive in place with latest validation
- ◆ Understood the route and traffic plan prevailing inside the plant
- ◆ Obtained training in language they understand not limited to english

TRAFFIC LIGHT REPORTS

Block wise STATUS BY COUNT

	TOE	Scope	BL	OP	PI	CLE	NDT	REP	FIS	Box	DBL
BLOCK-1	Columns	18	15	15	15	7					
	Exchanger	146	125	85	77	19	6				
	FinFan	170	149	149	149	40	13	4	4	4	
	Heaters	3	3	3	3	1					
	Vessels	83	65	61	61	32	15	15	15	10	
	Heater Aux	8	6	6	4						
	Ejector & De Sup	8	2	2	2						
	Filter/ mixer	3	3	3							
	Tank	14	9	8	5	5	5	5	5	4	1
	Silencer	2									
BLOCK-2	Columns	8	8	8	8						
	Exchanger	84	58	47	41	13	2	2	2	2	
	FinFan	126	126	126	126	16					
	Heaters	7	7	7	7	4					
	Vessels	64	61	57	57	24	16	16	16	16	5
	Heater Aux	4									
	Ejector & De Sup	3	2	2							
	Filter	2	2	2	2	2	2	2	1	1	
	Tank	10	2	2	2	1	1	1	1	1	1
	Silencer	2	1	1							
BLOCK-3	Columns	16	16	15	15	2					
	Exchanger	103	101	93	84	42	19	13	7	7	3
	FinFan	70	66	62	62	36	5	5	4	4	
	Heaters	5	3	3	3	2	2	1			
	Vessels	80	72	72	72	43	38	38	38	31	
	Heater Aux	16	14	13	12	9	8	7	7	1	
	Ejector & De Sup	11	5	4	3	3	3	3	3	3	
	Seal legs	9	6	6	2	2	2	2	2	2	2
	Tank	4	1	1	1	1	1	1	1		
	Silencer	6	4	4	4	3	3	3	3		
BLOCK-4	Exchanger	8	2	2	2	2					
	FinFan	6									
	Vessels	25	16	16	16	12	12	12	12	12	11
	Flare	2									
	Stack	1	1	1	1	1	1	1	1	1	1
	Tank	10	10	10	10	10	10	10	10	10	10
	Mixer	3	3	3	3	3	3	3	3	3	3
CCU/SHT	Exchanger	6	6	6	6	6	5	3	3	3	3
	Heaters	3	3	3	3	3	3	3	3	3	3
	Vessels	2	2	2	2	2	2	2	2	2	2
	Heater Aux	7	7	7	7	4	4	4	4	4	4
	Piping / Line Repla	1	1	1	1						

BL- Blinding

OP- Opening

PI- Priliminary Inspection

CLE- Cleaning

REP- Repair

FIS- Final inspection

BOX- Boxup

DBL - Deblinding


NEWSLETTER

RRWs CBDC-WSD & CDU/UTILITIES/OFFSITE T/As 2020

SAFE MHRs TO DATE PRE TA = 773,718 CBDC(WSD) = 227,612 CDU(TA)= 804,720 GRAND TOTAL = 1,806,050

CRITICAL UNITS PERFORMANCE


TARGET V/S CURRENT PROGRESS

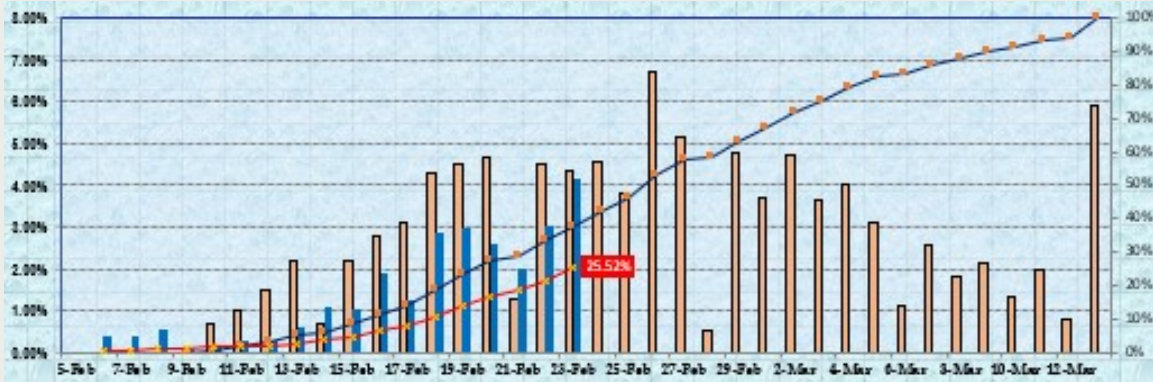

UNIT 1100—BLOCK 1

- Further slipped & Running Behind schedule by **12.28%**


1100-C-002 Cleaning in progress in Zone1, Tray removal in progress in Zone8., 1100-B-001B: Burners cleaning by steam in progress, Cleaning & Scaffolding erection in progress., 1100-B-001A: Burners cleaning by steam in progress, Scaffolding erection completed., 1100-E-004E/F pullout done.1100-E-015G/H Back cover dropped., 1100-E-21 hydrojetting of shell & tube done&1100-E-007E-2 Hydrojetting done., 1100-E-3A,2A,2C Shell cleaning in-progress., 1100-EA-006-D hydrotest Completed., 1100-D-101,102 blinding completed., 1100-D-006 Cleaning in-progress., 1100-D-007-D1,D2,D3 Cleaning completed&offered for inspection., 1100-EA-005F,G,H Plug installation is in progress.,

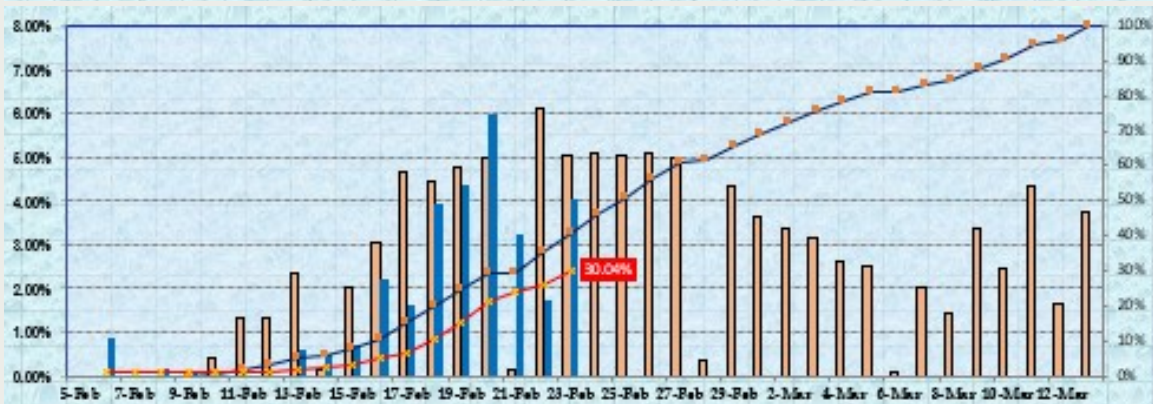

UNIT 1110—BLOCK 1

- Further slipped & Running Behind Schedule by **10.66%**


E-002A/B/17A/B/06 shell water washing completed, E-005A/B /007 Domes dropped, C-002 pall rings water washing, ME-001D1 Air blowing, E-008 Dome dropped, E-015 shell cleaning, EA-005A1/004B1/B2 hydrojetting, E-014 C/H dropped, D-008/009 buffing completed,

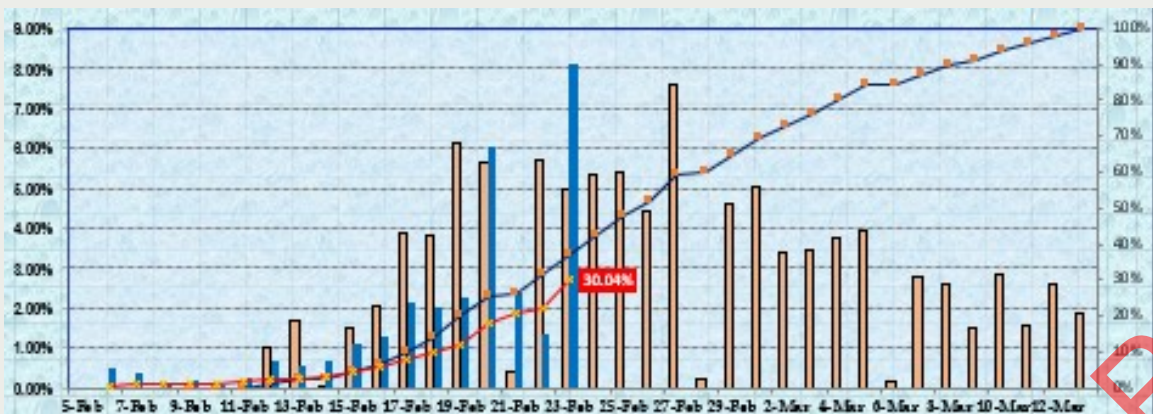

UNIT 1520—BLOCK 2

- Good intra day progress but Running behind schedule by **6.84%**


D-031/32 ventilation, D-033/34/53/54 cleaning completed, D-001 cleaning & inspection, D-005 blinding done, D-014/15 cleaning completed, E-013A/B/031A/B bundles pulled out, K-001E1A/B bundle pulled out, EA-035A-E hydrojetting i/p, EA-035 F-J Jetting done, 003 -G/H Jetting done., E-09A/B Neutralization completed.

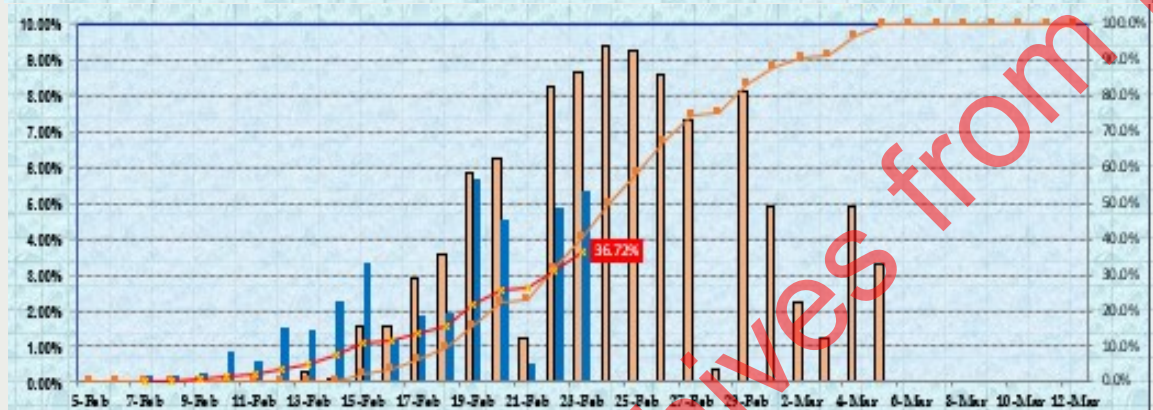

UNIT 1300—BLOCK 3

- Slipped further and Running behind by **3.48%**


B-001 94 tubes catalyst unloaded out of 350. WHB-002 water filling, D-007 Final inspection completed, EA-112/001C1/C2/B2 plugs installation, E-051 A/B Tube bundle pulled out, D-009 manway torqueing , E-004 all convection covers fixed back, D-009 manway torqueing completed, E-009/10 shell hydrojetting, EA-001 A/B/C/112 hydro-jetting, D-003 buffing, D110/111 internal cleaning, E-002 covers fixed

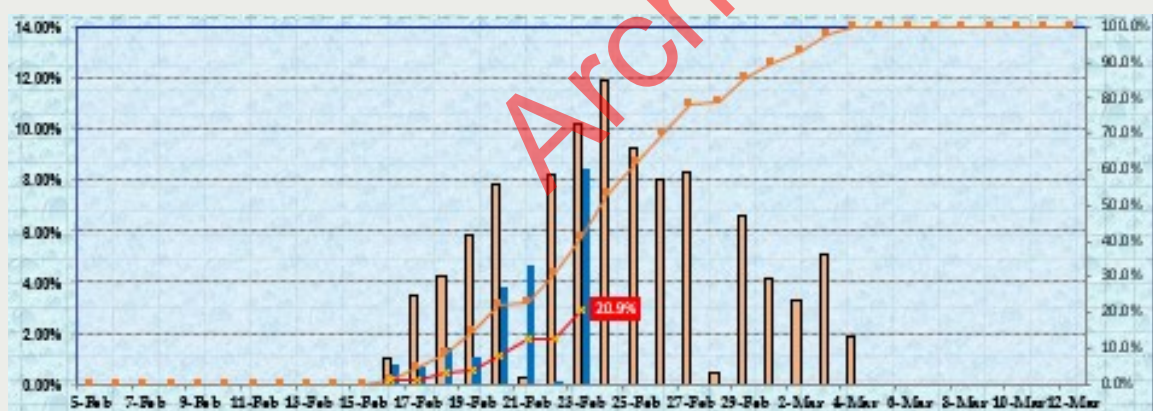

UNIT 1810—BLOCK 3

- Slipped further & Running behind schedule presently by **20.2%**

D-012/22 Preliminary inspection completed, C-021 tray manway opening, E-012 bundle removed, shell and tube preliminary inspection done

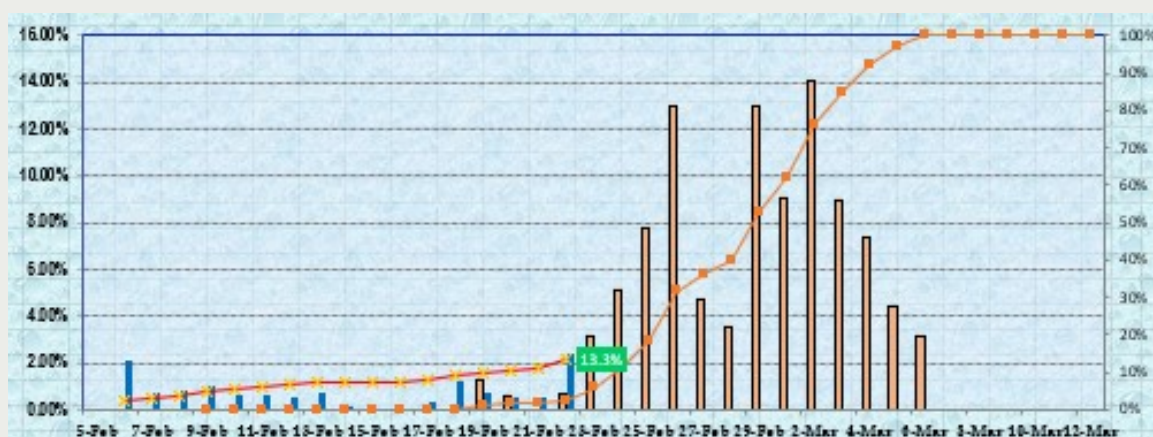

UNIT 1045/1021/22/26/27/29/1040/47/49/1053—BLOCK 4



- Ahead of schedule due to early start
- Crane assembly for Flare tip lifting completed
- 1045-ME-008 D1 deblinding, 013 deblinding
- 1045-D-001A/B manway opening and ventilation
- 1045-ME-001D1/D2 manway opening and ventilation
- 1045-D-013 deblinding

NEWSLETTER

RRWs CBDC-WSD & CDU/UTILITIES/OFFSITE T/As 2020

EQUIPMENT TYPE FOCUS WITH NARRATIVE

BY COUNT AND PERCENT (BY NUMBERS)



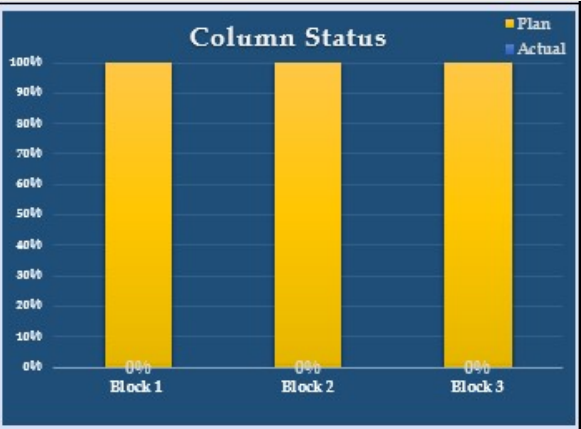
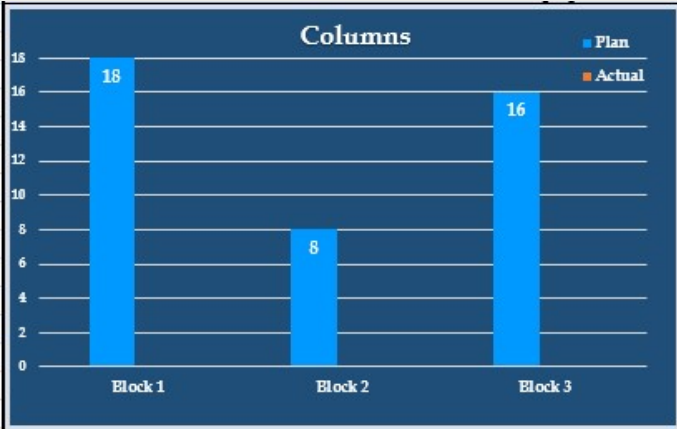


Columns are behind schedule Overall

	Blinding	Manway Opening	Prilliminary Inspection	Obtain CSE Permit	Erect Internal Scaffolding	Distribute r Removal
P	41	41	38	38	33	28
A	39	38	38	37	15	13
	Trays Removal	Tray Manways Removal	Packing Removal	Cleaning	Inspection as per QA/QC Requirements	Packing Loading
P	3	25	1	21	12	0
A	13	20	12	10	1	1

Vessels are ahead of schedule Overall

	Blinding	Manway Opening	Demister Removal	Cleaning	Inspection as per QA/QC Requireme	Install Demister	Remove Internal Scaffolding	Boxup Manway	Deblinding
P	170	167	33	119	112	17	36	71	58
A	216	208	113	113	91	75	84	71	19

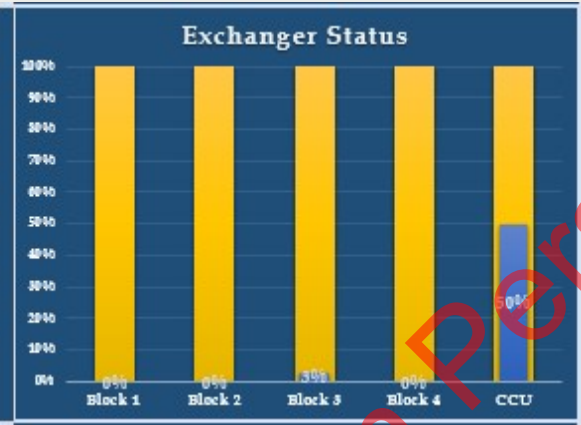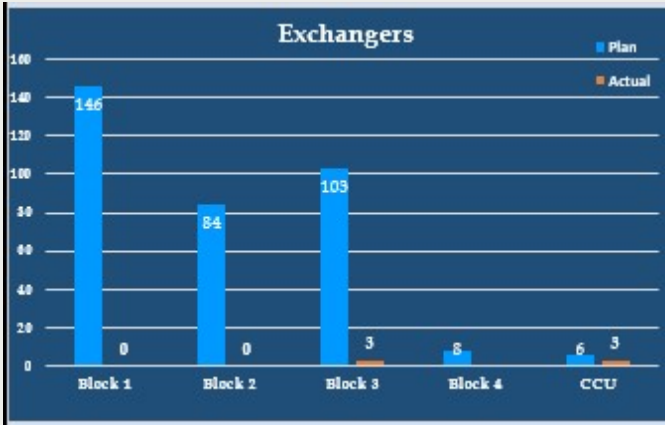
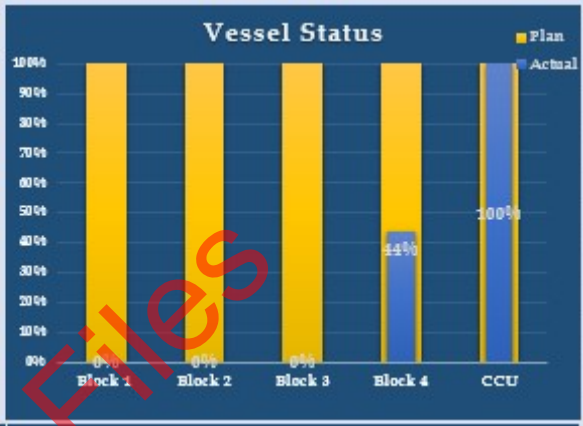
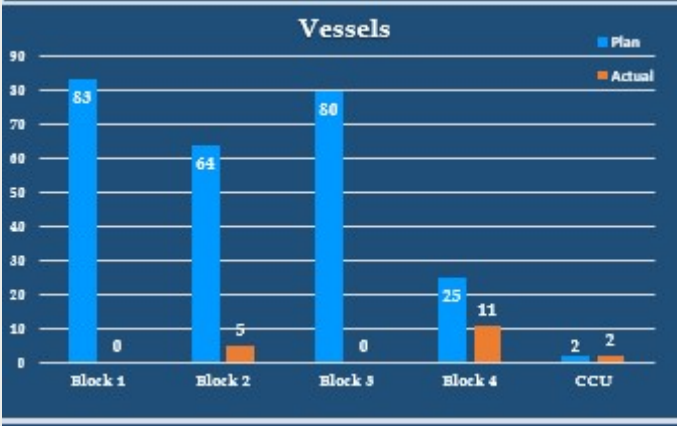


Exchangers are behind schedule Overall
Hydrojetting needs to speed up

	Blinding	Bundle Removal	Hydrojetting of Tubes	Inspection NDT - Tube	Hydrojetting of Shell & Component	Bundle Installation	Shell Test	Covers Boxup	Tube Test
P	212	183	168	76	170	107	103	87	80
A	292	210	82	42	68	36	26	15	10

AFCs are behind schedule over all
Hydrojetting needs to speed up

	Blinding	Plug Removal	Prilliminary Inspection	Hydrojetting of Tubes	Air Blowing of tubes	Inspection as per QA/QC Requirement	Plug Installation	Hydrotest	Final Inspection
P	177	170	168	150	150	145	121	113	103
A	347	337	337	92	62	37	29	9	8

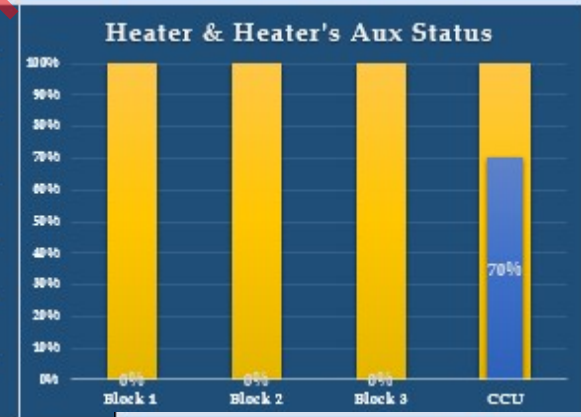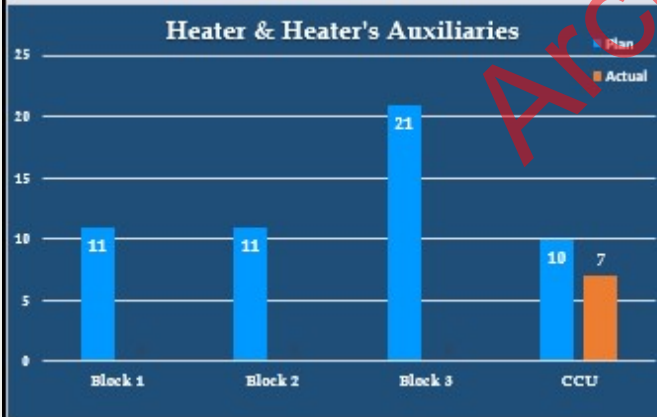
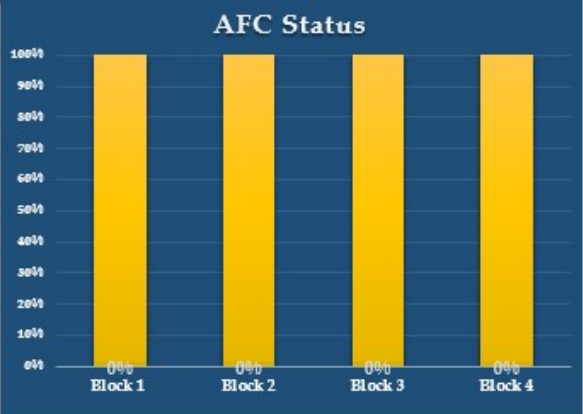


Heaters are almost on Schedule Overall

	Blinding	Manway Opening	Open Convection Panels	Prilliminary Inspection	Erect Internal Scaffolding	Cleaning
P	17	17	4	17	14	10
A	16	16	16	16	10	9

Tanks are just Ahead of Schedule Overall

	Blinding	Manway Opening	CSE Permit	Prilliminary Inspection	Erect Internal Scaffolding	Cleaning	Inspection/ NDT - Tube
P	19	19	18	6	15	15	12
A	22	21	18	18	17	17	17



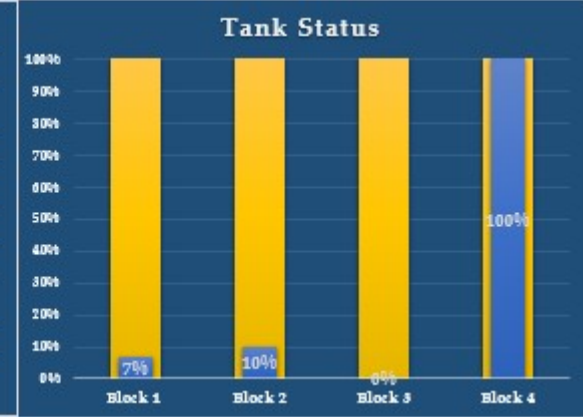
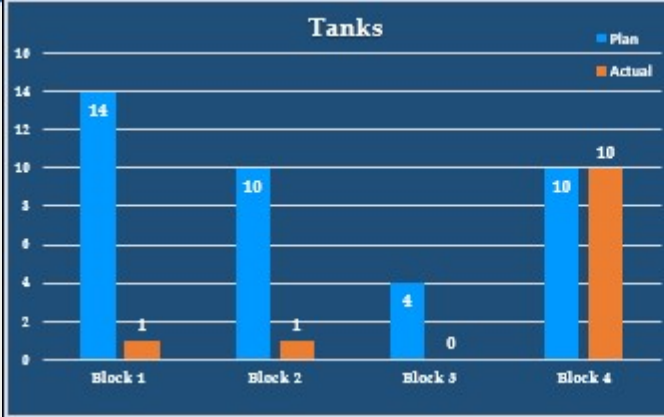


NEWSLETTER

RRWs CBDC-WSD & CDU/UTILITIES/OFFSITE T/As 2020

Ahead of schedule

	Blinding	Disconnect Flange	Remove Ejector/Venturi/Injection Nozzle	Cleaning	Inspection as per QA/QC Requirement	Repair if any
P	5	5	4	4	4	3
A	9	9	9	5	5	4

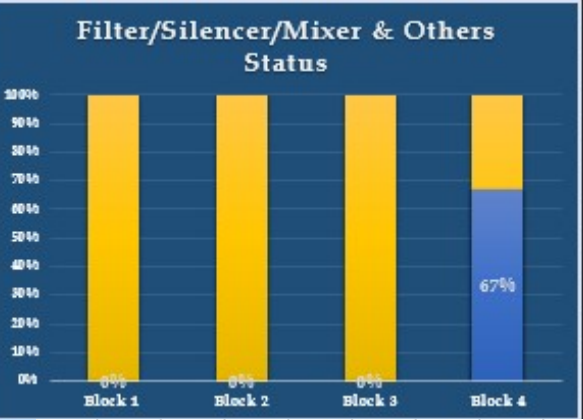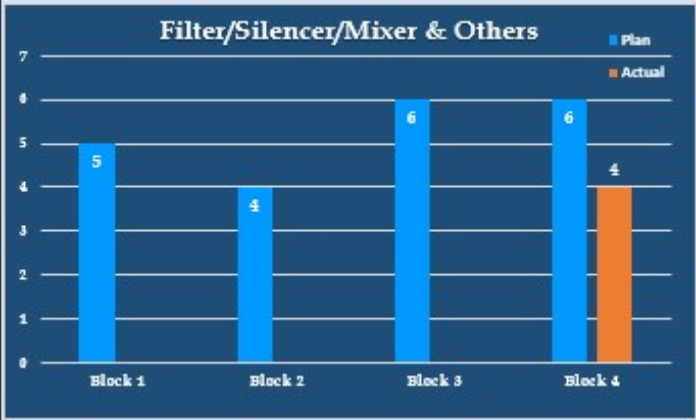
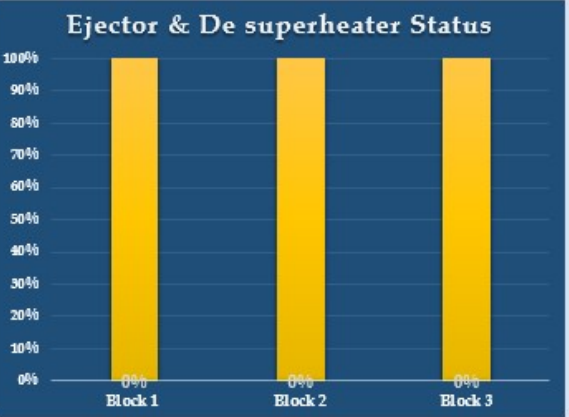
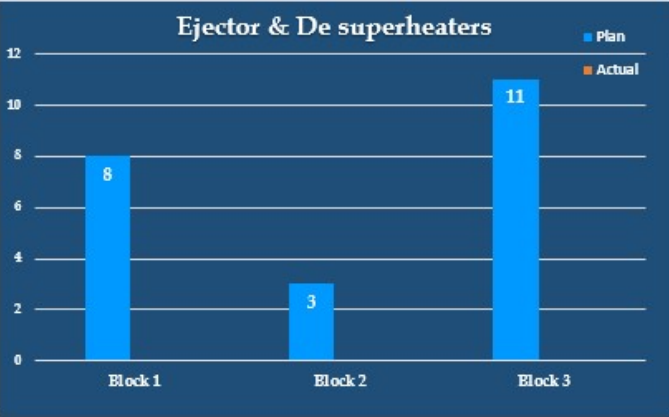


Ahead of schedule

	Blinding	Flange/cover opening	Remove filter	Clean shell/filter	Shell NDT	Inspection as per QA/QC
P	0	0	0	0	0	0
A	8	8	8	5	5	5

Running behind schedule over all

PLAN/ACTUAL	REMOVED	SHIFTED TO W/S	RECONDITIONED	SHIFTED TO SITE	INSTALLED
Plan	686	639	267	218	171
Actual	757	709	257	105	57

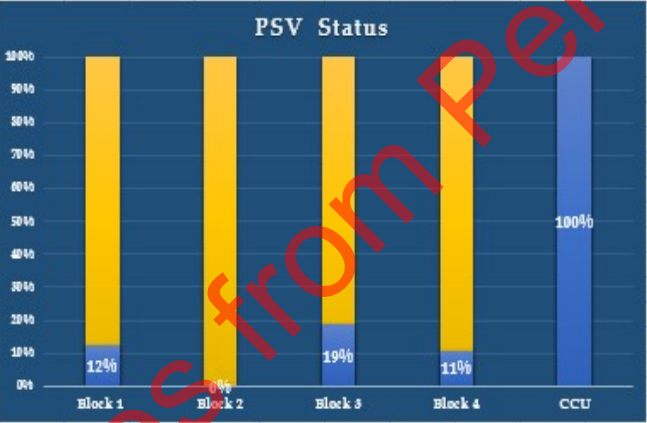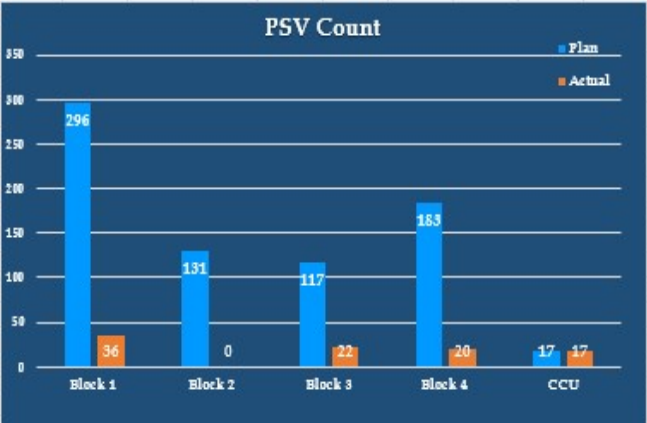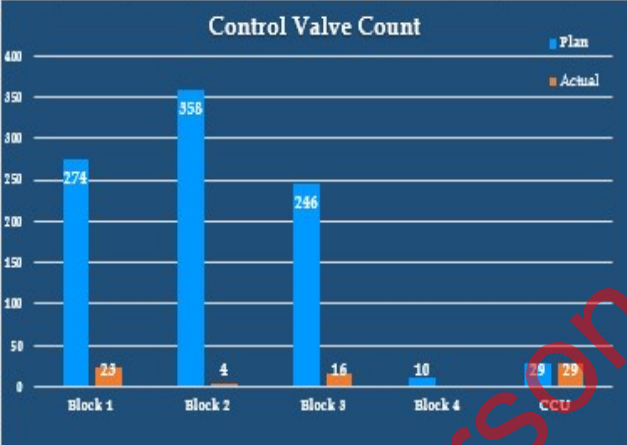

Running behind schedule overall

PLAN/ACTUAL	REMOVED	SHIFTED TO W/S	RECONDITIONED	SHIFTED TO SITE	INSTALLED
Plan	468	452	113	78	48
Actual	466	387	208	151	95

CRITICAL PATH SPOTLIGHT (EXCHANGERS' RISING ASKING RATES)

