



**ABU DHABI GAS INDUSTRIES LTD.
(GASCO)**

PROJECT TITLE:

**BuHasa Replacement of Valves and Actuators for EPC Works
Agreement No. 14562101**

REPORT NO:

5621-MPR-012

DOCUMENT TITLE:

**MONTHLY PROGRESS REPORT-012
(25-Sep-15 to 29-Oct-15)**

DOCUMENT NO:

5621-RT-00-AA-0001

			Saad Zaman	Rishi Chadda		
			(Prepared By)	(Checked By)	GASCO	GASCO
			AHEC	AHEC	APPROVED	

INDEX

Sr.No	Description	Page no
1	Monthly Narrative Report	3
2	HSE Statistics	4
3	Overall Progress Summary - <u>Attachment-1</u>	
4	Overall Progress S-Curve - <u>Attachment-1A</u>	
5	Engineering Document Deliverable Register (EDDR) - <u>Attachment-2</u>	
6	Engineering Progress S-Curve - <u>Attachment-2A</u>	
7	Procurement Status Register - <u>Attachment-3</u>	
8	Procurement Progress S-Curve - <u>Attachment-4</u>	
9	DCA Register - <u>Attachment-5</u>	
10	CTN Register - <u>Attachment-6</u>	
11	Manpower Deployment - <u>Attachment-7</u>	
12	Manpower Mobilization Histogram - <u>Attachment-8</u>	
13	Equipment Deployments - <u>Attachment-9</u>	
14	Updated Schedule - <u>Attachment-10</u>	
15	4 Month Lookahead Schedule - <u>Attachment-11</u>	
16	Project Document Deliverable Register - <u>Attachment-12</u>	
17	Construction Register - <u>Attachment-13</u>	
18	Construction S Curve - <u>Attachment-14</u>	
19	Milestone Summary - <u>Attachment-15</u>	
20	Vendor Document Deliverable Register - <u>Attachment-16</u>	
Attachments		
Sr.No	Description	Page no



BuHasa Replacement of Valves and Actuators for EPC Works
Project No: 5621



MONTHLY NARRATIVE REPORT

Monthly Progress Report No.: MPR-012

Cut-Off Date: 30-Oct-15

PROGRESS SUMMARY:	% Progress (as of 29-Oct-15)
Cumulative Baseline Planned Progress Percentage (%)	53.75%
Cumulative Revised Baseline Progress Percentage (%)	44.35%
Cumulative Actual Progress Percentage (%)	46.26%
Cumulative Variance (%) [Actual Progress - Revised Baseline Progress]	1.91%

Major Activities Performed During This Period	Major Activities Planned for Next Month
HOME OFFICE ENGINEERING & PROJECT MANAGEMENT 1. Submission of Scope of Work for Existing DCS & ESD Modifications 2. Submission of I/O LIST - DCS 3. Submission of Instrument Cable Routing Layout 4. Submission of Instrument Bulk Material Take Off 5. Submission of AHEC commented Buffer Vessel Drawings with Design Calculations 6. Submission of Inspection & Test Plan - Actuators 7. Submission of Welding Repair Procedure 8. Submission of Drawings for CAI Actuators	1. Submission of PG Data sheet from MSA/ROTORK 2. Submission of PSV Data sheet from MSA/ROTORK 3. Submission of Solenoid valve catalogue
PROCUREMENT 1. Machining in Progress for MSA Valves 2. Manufacturing in Progress for ROTORK Actuators 3. MPI/DPT after Machining is in Progress 4. P.O for Junction Boxes Released 5. Inspection was done in ROTORK Factory on 29 Oct 2015 6. P.O for Pressure Switches Released	1. Issue Purchase Order for Instrument Glands 2. Issue Purchase Order for Instrument Tubing 3. Cables Delivery at Site 4. Inspection Report from ROTORK to be Submitted
CONSTRUCTION 1. Construction Completed for all Foundations for Buffer Vessels for TRAIN - 1 & TRAIN - 2 2. Piping Fabrication Completed in AHEC Work shop - Radiography of Joints also completed - Report Submitted to BuHasa Inspection Dpt. 3. Completion of 11 Oct, 2015 One Day S/D Replacements - 11 Actuators were installed 4. Site Survey from 2 Crane Vendors & AHEC Construction Team Done 5. Site Survey Conducted regarding Obstruction and Valves Dimensions 6. Site Survey Conducted by Instrumentation Team for Tubing Modifications 7. Site Survey Conducted for CAI Actuators Installation for NOV' 15 S/D 8. Site Survey Conducted for Fire Box Dimensions against each TAG	1. Submission of Work Packs to Company for Review (Discussions and Preparations are in Progress) 2. November ' 2015 S/D to be carried out 3. Piping Painting to be Carried out 4. Work Packs Compilation for 23 Nos. of SDT Valves and Actuators 5. Work Permit Certificates Approval from GASCO 6. Discussion on Valves Replacement Schematics 7. Joint Survey Planned with TME and ROTORK for Revised G.As 8. Completion of all Foundations for Buffer Vessels 9. Draft Plan Submission for PRE S/D Activities 10. Revised Rigging Plans Submission for Major S/D

Remark/Area of Concerns:			
Sr.No	Description	Action By	Remark
1	Following Important Documents are still not commented by TME: System Interconnection cable schedule, Marshalling cabinet Drawings, Method of statement for DCS modification, I/O List DCS, Vendor BOM, Vendor Hardware specification and technical data, DCS IO list & FTA details.	TEBODIN	
2	Close Follow Up needed for Manufacturing and Delivery for MSA/ROTORK Valves	AHEC / MSA / ROTORK	
3	CAI Actuators Response Commissioning Spares	CAI	

HSE Statistics

Date 30-Oct-15

Sr. No	Safety Statistics	Up to Last Month	In This Period	Cumulative
1	Man-Hours Worked Without LTI (Home Office)	15790	720	16510
2	Total No Of Days Worked Without LTI	0	0	0
3	Man-Hours Worked Without LTI, Site	51210	12480	63690
4	Number of Lost Time Injuries (LTI's)	0	0	0
5	Fatalities (Nos)	0	0	0
6	Restricted Work Cases (RWC)	0	0	0
7	Medical Treatment Cases (MTC)	0	0	0
8	First Aid Cases Reported	0	0	0
9	Reported Near Misses	3	0	3
10	Reported Unsafe Observations	1	0	1
11	Reported Loss of Containment	0	0	0
12	Vehicle Accident	0	0	0
13	Safety Inductions (Nos)	54	0	54
14	Total HSE Supervisors (Nos.)	2	0	2
15	Ratio of HSE Supervisor Vs Employees	32:1	37:2	43:2
16	Total Man-Hours Worked	67000	13200	80200
17	Tool Box Talks	23	23	46
MANPOWER STATUS				
1	Total Manpower Mobilized at Site	45		
2	Total Mnapower Mobilized at Home Office	4		
TOTAL		49		

Progress for Month Ending : 30-Oct-15

SI No.	Activity Description	Weight Factors		Cumulative Progress (%)			Progress during Reporting			Completion Date		
		Level-1	Level-2	Base Plan	Revised Baseline	Actual	Base Plan	Revised Baseline	Actual	Early Plan	Forecast	Actual
1. Detailed Engineering												
a)	Genaral	1.19%	23.88%	100.00%	100.00%	100.00%	0.00%	0.00%	0.00%	08-Apr-15	-	21-Apr-15
b)	Process	0.22%	4.49%	100.00%	100.00%	100.00%	0.00%	0.00%	0.00%	15-Apr-15	15-May-15	-
c)	Mechanical / Piping	1.26%	25.19%	100.00%	100.00%	100.00%	0.00%	0.00%	0.00%	01-Apr-15	-	22-Apr-15
d)	Instrumentation	1.26%	25.19%	100.00%	100.01%	97.07%	0.00%	0.00%	0.00%	08-Apr-15	30-May-15	-
e)	HSE	0.24%	4.71%	100.00%	100.00%	90.51%	0.00%	0.00%	0.00%	08-Apr-15	27-May-15	-
f)	Civil / Structure	0.83%	16.54%	100.00%	100.00%	100.00%	0.00%	0.00%	0.00%	15-Apr-15	30-May-15	-
Sub-Total (Detail Engineering)		5.00%	100.00%	100.00%	100.00%	98.82%	0.00%	0.00%	0.00%	15-Apr-15		
2. Procurement												
a)	Long Lead Items	19.20%	48.00%	100.00%	66.79%	62.43%	0.00%	5.00%	1.46%	04-Sep-15	-	-
b)	Bulk Materials	16.00%	40.00%	100.00%	91.60%	75.86%	0.00%	31.06%	14.36%	11-Sep-15		
c)	Operating Spares	4.80%	12.00%	100.00%	40.00%	40.00%	0.00%	0.00%	0.00%	04-Sep-15	-	-
d)	Vendor Documents	2.00%	5.00%	90.00%	90.00%	40.00%	10.00%	10.00%	0.00%			
Sub-Total (Procurement)		40.00%	100.00%	99.50%	76.00%	65.11%	0.50%	15.32%	6.45%	11-Sep-15		
3. Construction & Commissioning												
a)	Construction & Pre-commissioning	50.08%	90.00%	17.88%	17.88%	30.52%	9.93%	9.93%	22.38%	18-Dec-16	-	-
b)	Commissioning & As-Built Drawings	4.92%	10.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	08-Feb-17	-	-
Sub-Total (Construction & Commissioning)		55.00%	100.00%	16.27%	16.27%	27.77%	9.04%	9.04%	20.36%	08-Feb-17		
Overall Progress %		100.00%		53.75%	44.35%	46.26%	5.17%	11.10%	13.78%			


Note : 1. Above details shall be consistent with the agreed WBS, Progress Measurement and Progress Reporting Systems.

2. Weight % details wherever not specified, shall be developed by Contractor during EPC execution and submitted to COMPANY for review / approval.

ATTACHMENT - 1A

OVERALL PROGRESS S-CURVE

Archives from Personal Files

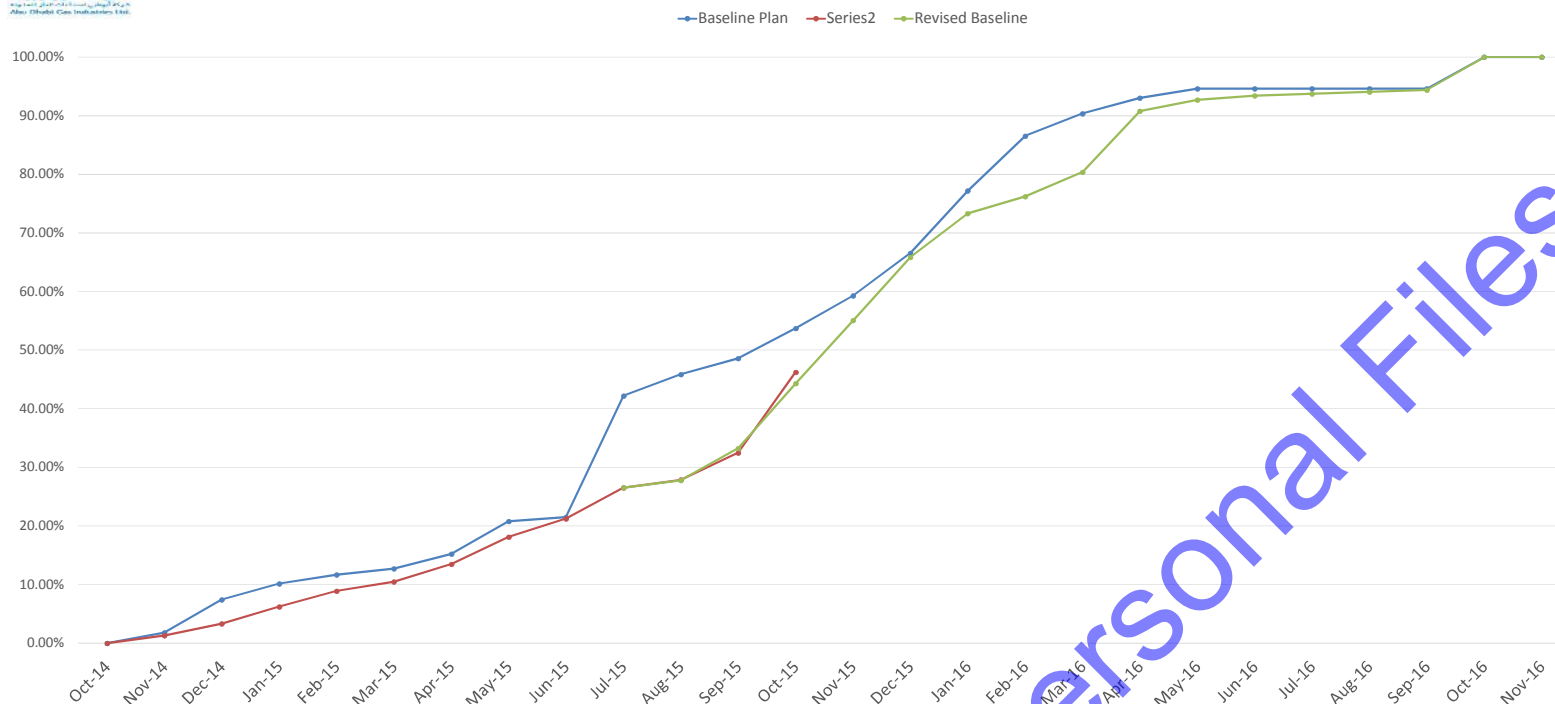[illegible]

ATTACHMENT - 2

**ENGINEERING DOCUMENT
DELIVERABLE REGISTER
EDDR**

Archives from Personal Files



BuHasa Replacement of Valves & Actuators for EPC Works																																
GASCO PROJECT NO: 5621																																
Engineering Document Deliverables Register																																
																				Document Title:	Engineering Document Deliverables Register (EDDR)											
																				Document No:	5621-SCH-00-AA-0003											
																				Rev:	1											
																				Date:	30-Oct-15											
SI No.	TME Doc No.	GASCO Drawing / Document Title	Activity ID (Baseline Plan)	Drawing/Document No.	Drawing/Document Class	Rev No.	Rev Date	Level 1 %Wt	Est. Man-Hours /wt %	P A F	Started 5%	Drafting Complete 25%	ISC Complete 40%	Submission / Review Status				Issue as IFC				Status as on 30-Oct-15				Earned Man-Hours		Remarks				
														Issue-1 (ICR)		Issue-2		Issue-3 (FD/IFA)								% Plan	% Revised		% Actual	% Variance	Plan	Actual
														Submitted 50%	Receive Comments 50%	Submitted 50%	Receive Comments 50%	Submitted 75%	Approved 85%	First Issue 95%	Final Issue 100%											
		DETAILED ENGINEERING Overall						100%	100%		5%	20%	15%	10%	0%	0%	0%	25%	10%	10%	5%	100.00%	100.00%	99.82%	-1.19%							
		General							23.88%	P												23.88%	23.88%	23.88%	0.00%							
			A																													
			F																													
2	7141001	Document Control Register	A1060-A1070	5621-SCH-00-AA-V102	1					P	21-Oct-14	30-Oct-14	01-Nov-14	03-Nov-14	17-Nov-14			01-Dec-14	08-Dec-14	15-Dec-14	29-Dec-14		0.00%	0.00%	0.00%	0.00%						
										A	30-Oct-14	30-Oct-14	30-Oct-14	30-Oct-14	11-Dec-14			02-Feb-15	02-Feb-15	02-Feb-15	02-Feb-15											
										F																						
3	7191001	Site Visit Report (TOTAL # 12)	A1050	5621-RT-00-AA-V101	1			11.94%	50.00%	P	04-Nov-14	06-Nov-14	08-Nov-14	10-Nov-14	24-Nov-14			08-Dec-14	15-Dec-14	22-Dec-14	05-Jan-15	11.94%	11.94%	11.94%	0.00%							
										A	16-Nov-14	17-Nov-14	17-Nov-14	17-Nov-14	07-Dec-14			26-Feb-15	11-Mar-15	21-Apr-15	21-Apr-15											
										F																						
4	7176001	Design Basis Memorandum	A1080-A1085	5621-SP-00-AA-V101	1			10.70%	44.80%	P	21-Oct-14	13-Nov-14	15-Nov-14	17-Nov-14	01-Dec-14			15-Dec-14	22-Dec-14	29-Dec-14	12-Jan-15	10.70%	10.70%	10.70%	0.00%							
										A	04-Nov-14	11-Nov-14	12-Nov-14	16-Nov-14	03-Dec-14			30-Dec-14	09-Feb-15	11-Feb-15	11-Feb-15											
										F																						
6		Miscellaneous Deliverables (Not identified at this stage)			1			1.24%	5.20%	P	22-Jan-15	25-Jan-15	27-Jan-15	29-Jan-15	12-Feb-15			26-Feb-15	05-Mar-15	12-Mar-15	26-Mar-15	1.24%	1.24%	1.24%	0.00%		NO FURTHER GENERAL MISC DELIVERABLES ARE IDENTIFIED					
										A	20-Mar-15	20-Mar-15	20-Mar-15	20-Mar-15	20-Mar-15			20-Mar-15	20-Mar-15	20-Mar-15	20-Mar-15											
										F																						
		Process							4.49%	P												4.49%	4.49%	4.49%	0.00%							
			A																													
			F																													
1	3143001	P&ID for Gas Compr'n- Common Facilities Plant 2 Sht-1	A1100,A1105,A1106	5621-58-BD-V101	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	13-Nov-14	08-Dec-14	08-Dec-14	08-Dec-14			08-Dec-14	08-Dec-14	08-Dec-14	08-Dec-14											
										F																						
2	3143002	P&ID for Gas Compr'n- Common Facilities Plant 2 Sht-2	A1100,A1105,A1106	5621-58-BD-V102	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	13-Nov-14	08-Dec-14	08-Dec-14	08-Dec-14			08-Dec-14	08-Dec-14	08-Dec-14	08-Dec-14											
										F																						
3	3143003	P&ID for Gas Compression Plant-2 (TR-1) Sht-3	A1100,A1105,A1106	5621-51-BD-V102	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	13-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15											
										F																						
4	3143004	P&ID for Gas Compression Plant-2 (TR-2) Sht-4	A1100,A1105,A1106	5621-52-BD-V102	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	13-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15											
										F																						
5	3143005	P&ID for Gas Compression Plant-2 (TR-2) Sht-5	A1100,A1105,A1106	5621-52-BD-V103	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	13-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15											
										F																						
6	3143006	P&ID for Pump Station Plant-3 Sht-6	A1100,A1105,A1106	5621-58-BD-V103	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	13-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15											
										F																						
7	3143007	P&ID for Buhasa Pump Station Sht-7	A1100,A1105,A1106	5621-58-BD-V104	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	13-Nov-14	08-Dec-14	08-Dec-14	08-Dec-14			08-Dec-14	08-Dec-14	08-Dec-14	08-Dec-14											
										F																						
8	3143008	P&ID for Extraction Train-1, Buhasa Plant-3 Sht-8	A1100,A1105,A1106	5621-51-BD-V103	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	13-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15											
										F																						
9	3143009	P&ID for Extraction Plant-3 (TR-1) Sht-9	A1100,A1105,A1106	5621-51-BD-V104	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15											
										F																						
10	3143010	P&ID for Extraction Plant-3 (TR-1) Sht-10	A1100,A1105,A1106	5621-51-BD-V105	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15											
										F																						
11	3143011	P&ID for Refrigeration Plant-3 (TR-1) Sht-11	A1100,A1105,A1106	5621-51-BD-V106	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15											
										F																						
12	3143012	P&ID for Extraction Plant-3 (TR-2) Sht-12	A1100,A1105,A1106	5621-52-BD-V104	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15											
										F																						
13	3143013	P&ID for Extraction Plant-3 (TR-2) Sht-13	A1100,A1105,A1106	5621-52-BD-V105	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15											
										F																						
14	3143014	P&ID for Extraction Plant-3 (TR-2) Sht-14	A1100,A1105,A1106	5621-52-BD-V106	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%							
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15											
										F																						
										P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15											



Sl No.	TME Doc No.	GASCO Drawing / Document Title	Activity ID (Baseline Plan)	Drawing/Document No.	Drawing Document Class	Rev No.	Rev Date	Level 1 %WT	Est. Man-Hours %wt	P A F	Started %	Drafting Complete 25%	ISC Complete 40%	Submission / Review Status						Issue as IFC		Status as on				Earned Man-Hours		Remarks
														Issue-1 (ICR)		Issue-2		Issue-3 (IFD/IFA)				30-Oct-15		Plan	Actual			
														Submitted 50%	Receive Comments 50%	Submitted 50%	Receive Comments 50%	Submitted 75%	Approved 85%	First Issue 95%	Final Issue 100%	% Plan	% Revised			% Actual	% Variance	
15	3143015	P&ID for Refrigeration Plant-3 (TR-2)- Sht-15	A1100,A1105,A1106	5621-52-BD-V107	1			0.07%	1.46%	A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15	0.07%	0.07%	0.07%	0.00%			
										F																		
16	3143016	P&ID for Residue Gas Distribution System Utilities- Sht-16	A1100,A1105,A1106	5621-58-BD-V105	1			0.07%	1.46%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.07%	0.07%	0.07%	0.00%			
										A	04-Nov-14	27-Nov-14	08-Dec-14	08-Dec-14	08-Dec-14			08-Dec-14	08-Dec-14	08-Dec-14	08-Dec-14							
										F																		
17	3143017	P&ID for Gas Compression Plant-2 (TR-1)- Sht-17	A1100,A1105,A1106	5621-51-BD-V107	1			0.09%	1.95%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15							
										F																		
18	3143018	P&ID for Refrigeration Plant-3 (TR-1)- Sht-18	A1100,A1105,A1106	5621-51-BD-V108	1			0.09%	1.95%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15							
										F																		
19	3143019	P&ID for Refrigeration Plant-3 (TR-2)- Sht-19	A1100,A1105,A1106	5621-52-BD-V108	1			0.09%	1.95%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15							
										F																		
20	3143020	P&ID for Liquid Dehydration Package (TR-1)- Sht-20	A1100,A1105,A1106	5621-51-BD-V109	1			0.09%	1.95%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15							
										F																		
21	3143021	P&ID for Utility Fuel Gas System-Common Facilities- Sht-21	A1100,A1105,A1106	5621-58-BD-V106	1			0.09%	1.95%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15							
										F																		
22	3143022	P&ID for Extraction Train-1 Buhasa Plant-3- Sht-22	A1100,A1105,A1106	5621-51-BD-V110	1			0.09%	1.95%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	08-Dec-14	08-Dec-14	08-Dec-14			08-Dec-14	08-Dec-14	08-Dec-14	08-Dec-14							
										F																		
23	3143023	P&ID for Extraction Plant-3 (TR-2)- Sht-23	A1100,A1105,A1106	5621-52-BD-V109	1			0.09%	1.95%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	08-Dec-14	08-Dec-14	08-Dec-14			08-Dec-14	08-Dec-14	08-Dec-14	08-Dec-14							
										F																		
24	3143024	P&ID for Vapor Dehydration Package (TR-1)- Sht-24	A1100,A1105,A1106	5621-51-BD-V111	1			0.09%	1.95%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15							
										F																		
25	3143025	P&ID for Vapor Dehydration Package (TR-2)- Sht-25	A1100,A1105,A1106	5621-52-BD-V110	1			0.09%	1.95%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15							
										F																		
26	3143026	P&ID for Liquid Dehydration Package (TR-2)- Sht-26	A1100,A1105,A1106	5621-52-BD-V111	1			0.09%	1.95%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	04-Dec-14	09-Dec-14	21-Dec-14			14-Jan-15	14-Jan-15	14-Jan-15	14-Jan-15							
										F																		
27	3143027	P&ID for Gas Compr'n- Common Facilities Plant-2 Cover Sheet- Sht-27	A1100,A1105,A1106	5621-58-BD-V107	1			0.09%	1.95%	P	04-Nov-14	09-Nov-14	11-Nov-14	13-Nov-14	27-Nov-14			11-Dec-14	18-Dec-14	25-Dec-14	15-Apr-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	08-Dec-14	08-Dec-14	08-Dec-14			08-Dec-14	08-Dec-14	08-Dec-14	08-Dec-14							
										F																		
28	3143028	P&ID for Gas Compr'n- Common Facilities Plant-2 (Demolition)- Sht-28	A1110-A1115	5621-58-BD-V101D	1			0.09%	1.95%	P	16-Nov-14	11-Dec-14	13-Dec-14	15-Dec-14	29-Dec-14			12-Jan-15	19-Jan-15	26-Jan-15	09-Feb-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	08-Dec-14	08-Dec-14	08-Dec-14			08-Dec-14	08-Dec-14	08-Dec-14	08-Dec-14							
										F																		
29	3143029	P&ID for Gas Compr'n- Common Facilities Plant-2 (Demolition)- Sht-29	A1110-A1115	5621-58-BD-V102D	1			0.09%	1.95%	P	16-Nov-14	11-Dec-14	13-Dec-14	15-Dec-14	29-Dec-14			12-Jan-15	19-Jan-15	26-Jan-15	09-Feb-15	0.09%	0.09%	0.09%	0.00%			
										A	04-Nov-14	27-Nov-14	08-Dec-14	08-Dec-14	08-Dec-14			08-Dec-14	08-Dec-14	08-Dec-14	08-Dec-14							
										F																		
30	3143030	P&ID for Gas Compression Plant-2 (TR-1) (Demolition)- Sht-30	A1110-A1115	5621-51-BD-V102D	1			0.09%	1.95%	P	16-Nov-14	11-Dec-14	13-Dec-14	15-Dec-14	29-Dec-14			12-Jan-15	19-Jan-15	26-Jan-15	09-Feb-15	0.09%	0.09%	0.09%	0.00%			
										A	07-Dec-14	11-Dec-14	15-Dec-14	15-Dec-14	09-Feb-15			09-Feb-15	09-Feb-15	10-Feb-15	26-Feb-15							
										F																		
31	3143031	P&ID for Gas Compression Plant-2 (TR-2) (Demolition)- Sht-31	A1110-A1115	5621-52-BD-V102D	1			0.09%	1.95%	P	16-Nov-14	11-Dec-14	13-Dec-14	15-Dec-14	29-Dec-14			12-Jan-15	19-Jan-15	26-Jan-15	09-Feb-15	0.09%	0.09%	0.09%	0.00%			
										A	07-Dec-14	11-Dec-14	15-Dec-14	15-Dec-14	09-Feb-15			09-Feb-15	09-Feb-15	10-Feb-15	26-Feb-15							
										F																		
32	3143032	P&ID for Gas Compression Plant-2 (TR-2) (Demolition)- Sht-32	A1110-A1115	5621-52-BD-V103D	1			0.09%	1.95%	P	16-Nov-14	11-Dec-14	13-Dec-1															



Sl No.	TME Doc No.	GASCO Drawing / Document Title	Activity ID (Baseline Plan)	Drawing/Document No.	Drawing /Document Class	Rev No.	Rev Date	Level 1 %WT	Est. Man-Hours /wt %	P A F	Started %	Drafting Complete 25%	ISC Complete 40%	Submission / Review Status				Issue as IFC				Status as on				Earned Man-Hours		Remarks		
														Issue-1 (ICR)		Issue-2		Issue-3 (FD/IFA)		First Issue 95%		Final Issue 100%		% Plan	%Revised	% Actual	% Variance		Plan	Actual
														Submitted 50%	Receive Comments 50%	Submitted 50%	Receive Comments 50%	Submitted 75%	Approved 85%	First Issue 95%	Final Issue 100%									
41	3143041	P&ID for Extraction Plant-3 (TR-2) (Demolition)- Sht-41	A1110-A1115	5621-52-BD-V106D	1			0.09%	1.95%	P A F	16-Nov-14 07-Dec-14 16-Nov-14	11-Dec-14 11-Dec-14 11-Dec-14	13-Dec-14 15-Dec-14 13-Dec-14	15-Dec-14 15-Dec-14 15-Dec-14	29-Dec-14 09-Feb-15 29-Dec-14			12-Jan-15 09-Feb-15 12-Jan-15	19-Jan-15 09-Feb-15 19-Jan-15	26-Jan-15 10-Feb-15 26-Jan-15	09-Feb-15 26-Feb-15 09-Feb-15	0.09%	0.09%	0.09%	0.00%					
42	3143042	P&ID for Refrigeration Plant-3 (TR-2) (Demolition)- Sht-42	A1110-A1115	5621-52-BD-V107D	1			0.09%	1.95%	P A F	16-Nov-14 07-Dec-14 16-Nov-14	11-Dec-14 11-Dec-14 11-Dec-14	13-Dec-14 15-Dec-14 13-Dec-14	15-Dec-14 15-Dec-14 15-Dec-14	29-Dec-14 09-Feb-15 29-Dec-14			12-Jan-15 09-Feb-15 12-Jan-15	19-Jan-15 09-Feb-15 19-Jan-15	26-Jan-15 10-Feb-15 26-Jan-15	09-Feb-15 26-Feb-15 09-Feb-15	0.09%	0.09%	0.09%	0.00%					
43	3143043	P&ID for Residue Gas Distribution System Utilities (Demolition)- Sht-43	A1110-A1115	5621-58-BD-V105D	1			0.09%	1.95%	P A F	16-Nov-14 08-Dec-14 16-Nov-14	11-Dec-14 08-Dec-14 11-Dec-14	13-Dec-14 08-Dec-14 13-Dec-14	15-Dec-14 08-Dec-14 15-Dec-14	29-Dec-14 08-Dec-14 29-Dec-14			12-Jan-15 08-Dec-14 12-Jan-15	19-Jan-15 08-Dec-14 19-Jan-15	26-Jan-15 08-Dec-14 26-Jan-15	09-Feb-15 08-Dec-14 09-Feb-15	0.09%	0.09%	0.09%	0.00%					
44	3143044	P&ID for Gas Compression Plant-2 (TR-1) (Demolition)- Sht-44	A1110-A1115	5621-51-BD-V107D	1			0.09%	1.95%	P A F	16-Nov-14 15-Dec-14 16-Nov-14	11-Dec-14 15-Dec-14 11-Dec-14	13-Dec-14 15-Dec-14 13-Dec-14	15-Dec-14 15-Dec-14 15-Dec-14	29-Dec-14 12-Jan-15 29-Dec-14			12-Jan-15 12-Jan-15 12-Jan-15	19-Jan-15 12-Jan-15 19-Jan-15	26-Jan-15 12-Jan-15 26-Jan-15	09-Feb-15 12-Jan-15 09-Feb-15	0.09%	0.09%	0.09%	0.00%					
45	3143045	P&ID for Refrigeration Plant-3 (TR-1) (Demolition)- Sht-45	A1110-A1115	5621-51-BD-V108D	1			0.09%	1.95%	P A F	16-Nov-14 07-Dec-14 16-Nov-14	11-Dec-14 11-Dec-14 11-Dec-14	13-Dec-14 15-Dec-14 13-Dec-14	15-Dec-14 15-Dec-14 15-Dec-14	29-Dec-14 09-Feb-15 29-Dec-14			12-Jan-15 09-Feb-15 12-Jan-15	26-Jan-15 09-Feb-15 26-Jan-15	02-Feb-15 10-Feb-15 02-Feb-15	16-Feb-15 26-Feb-15 16-Feb-15	0.09%	0.09%	0.09%	0.00%					
46	3143046	P&ID for Refrigeration Plant-3 (TR-2) (Demolition)- Sht-46	A1110-A1115	5621-52-BD-V108D	1			0.09%	1.95%	P A F	16-Nov-14 07-Dec-14 16-Nov-14	11-Dec-14 11-Dec-14 11-Dec-14	13-Dec-14 15-Dec-14 13-Dec-14	15-Dec-14 15-Dec-14 15-Dec-14	29-Dec-14 09-Feb-15 29-Dec-14			12-Jan-15 09-Feb-15 12-Jan-15	26-Jan-15 09-Feb-15 26-Jan-15	02-Feb-15 10-Feb-15 02-Feb-15	16-Feb-15 26-Feb-15 16-Feb-15	0.09%	0.09%	0.09%	0.00%					
47	3143047	P&ID for Liquid Dehydration Package (TR-1) (Demolition)- Sht-47	A1110-A1115	5621-51-BD-V109D	1			0.09%	1.95%	P A F	16-Nov-14 07-Dec-14 16-Nov-14	11-Dec-14 11-Dec-14 11-Dec-14	13-Dec-14 15-Dec-14 13-Dec-14	15-Dec-14 15-Dec-14 15-Dec-14	29-Dec-14 09-Feb-15 29-Dec-14			12-Jan-15 09-Feb-15 12-Jan-15	26-Jan-15 09-Feb-15 26-Jan-15	02-Feb-15 10-Feb-15 02-Feb-15	16-Feb-15 26-Feb-15 16-Feb-15	0.09%	0.09%	0.09%	0.00%					
48	3143048	P&ID for Utility Fuel Gas System-Common Facilities (Demolition)- Sht-48	A1110-A1115	5621-58-BD-V106D	1			0.09%	1.95%	P A F	16-Nov-14 07-Dec-14 16-Nov-14	11-Dec-14 11-Dec-14 11-Dec-14	13-Dec-14 15-Dec-14 13-Dec-14	15-Dec-14 15-Dec-14 15-Dec-14	29-Dec-14 09-Feb-15 29-Dec-14			12-Jan-15 09-Feb-15 12-Jan-15	26-Jan-15 09-Feb-15 26-Jan-15	02-Feb-15 10-Feb-15 02-Feb-15	16-Feb-15 26-Feb-15 16-Feb-15	0.09%	0.09%	0.09%	0.00%					
49	3143049	P&ID for Extraction Train-1 Buhasa Plant-3 (Demolition)- Sht-49	A1110-A1115	5621-51-BD-V110D	1			0.09%	1.95%	P A F	16-Nov-14 08-Dec-14 16-Nov-14	11-Dec-14 08-Dec-14 11-Dec-14	13-Dec-14 08-Dec-14 13-Dec-14	15-Dec-14 08-Dec-14 15-Dec-14	29-Dec-14 08-Dec-14 29-Dec-14			12-Jan-15 08-Dec-14 12-Jan-15	26-Jan-15 08-Dec-14 26-Jan-15	02-Feb-15 08-Dec-14 02-Feb-15	16-Feb-15 08-Dec-14 16-Feb-15	0.09%	0.09%	0.09%	0.00%					
50	3143050	P&ID for Extraction Plant-3 (TR-2) (Demolition)- Sht-50	A1110-A1115	5621-52-BD-V109D	1			0.09%	1.95%	P A F	16-Nov-14 08-Dec-14 16-Nov-14	11-Dec-14 08-Dec-14 11-Dec-14	13-Dec-14 08-Dec-14 13-Dec-14	15-Dec-14 08-Dec-14 15-Dec-14	29-Dec-14 08-Dec-14 29-Dec-14			12-Jan-15 08-Dec-14 12-Jan-15	26-Jan-15 08-Dec-14 26-Jan-15	02-Feb-15 08-Dec-14 02-Feb-15	16-Feb-15 08-Dec-14 16-Feb-15	0.09%	0.09%	0.09%	0.00%					
51	3143051	P&ID for Vapor Dehydration Package (TR-1) (Demolition)- Sht-51	A1110-A1115	5621-51-BD-V111D	1			0.09%	1.95%	P A F	16-Nov-14 07-Dec-14 16-Nov-14	11-Dec-14 11-Dec-14 11-Dec-14	13-Dec-14 15-Dec-14 13-Dec-14	15-Dec-14 15-Dec-14 15-Dec-14	29-Dec-14 09-Feb-15 29-Dec-14			12-Jan-15 09-Feb-15 12-Jan-15	26-Jan-15 09-Feb-15 26-Jan-15	02-Feb-15 10-Feb-15 02-Feb-15	16-Feb-15 26-Feb-15 16-Feb-15	0.09%	0.09%	0.09%	0.00%					
52	3143052	P&ID for Vapor Dehydration Package (TR-2) (Demolition)- Sht-52	A1110-A1115	5621-52-BD-V110D	1			0.09%	1.95%	P A F	16-Nov-14 07-Dec-14 16-Nov-14	11-Dec-14 11-Dec-14 11-Dec-14	13-Dec-14 15-Dec-14 13-Dec-14	15-Dec-14 15-Dec-14 15-Dec-14	29-Dec-14 09-Feb-15 29-Dec-14			12-Jan-15 09-Feb-15 12-Jan-15	26-Jan-15 09-Feb-15 26-Jan-15	02-Feb-15 10-Feb-15 02-Feb-15	16-Feb-15 26-Feb-15 16-Feb-15	0.09%	0.09%	0.09%	0.00%					
53	3143053	P&ID for Liquid Dehydration Package (TR-2) (Demolition)- Sht-53	A1110-A1115	5621-52-BD-V111D	1			0.04%	0.98%	P A F	16-Nov-14 07-Dec-14 16-Nov-14	11-Dec-14 11-Dec-14 11-Dec-14	13-Dec-14 15-Dec-14 13-Dec-14	15-Dec-14 15-Dec-14 15-Dec-14	29-Dec-14 09-Feb-15 29-Dec-14			12-Jan-15 09-Feb-15 12-Jan-15	26-Jan-15 09-Feb-15 26-Jan-15	02-Feb-15 10-Feb-15 02-Feb-15	16-Feb-15 26-Feb-15 16-Feb-15	0.04%	0.04%	0.04%	0.00%					
54	3185001	Shutdown Requirement & Philosophy	A1120-A1130	5621-GEN-AA-V101	1			0.09%	1.95%	P A F	02-Dec-14 15-Dec-14 02-Dec-14	04-Dec-14 18-Dec-14 04-Dec-14	06-Dec-14 14-Jan-15 06-Dec-14	08-Dec-14 14-Jan-15 08-Dec-14	22-Dec-14 02-Mar-15 25-Mar-15			05-Jan-15 04-Apr-15 08-Apr-15	19-Jan-15 21-May-15 15-Apr-15	26-Jan-15 21-May-15 15-Apr-15	09-Feb-15 21-May-15 15-Apr-15	0.09%	0.09%	0.09%	0.00%			GASCO COMMENTS SENT TO TIME		
55		Incorporation of comments from Vendor Review			1			0.04%	0.98%	P A F	04-Mar-15 20-Mar-15 04-Mar-15	06-Mar-15 20-Mar-15 06-Mar-15	08-Mar-15 20-Mar-15 08-Mar-15	11-Mar-15 20-Mar-15 11-Mar-15	25-Mar-15 26-Mar-15 25-Mar-15			08-Apr-15 20-Mar-15 15-Apr-15	15-Apr-15 20-Mar-15 15-Apr-15	15-Apr-15 20-Mar-15 15-Apr-15	15-Apr-15 20-Mar-15 15-Apr-15	0.04%	0.04%	0.04%	0.00%			ALL COMMENTS HAVE BEEN INCORPORATED		
56		Miscellaneous Deliverables (Not identified at this stage)			1			0.11%	2.44%	P A F	22-Jan-15 20-Mar-15 22-Jan-15	25-Jan-15 20-Mar-15 25-Jan-15	27-Jan-15 20-Mar-15 27-Jan-15	29-Jan-15 20-Mar-15 29-Jan-15	12-Feb-15 20-Mar-15 12-Feb-15			26-Feb-15 20-Mar-15 26-Feb-15	05-Mar-15 20-Mar-15 05-Mar-15	12-Mar-15 20-Mar-15 12-Mar-15	26-Mar-15 20-Mar-15 26-Mar-15	0.11%	0.11%	0.11%	0.00%			NO FURTHER GENERAL MISC. DELIVERABLES ARE IDENTIFIED		
		Mechanical/Piping							25.19%	P A F												25.19%	25.19%	25.19%	0.00%					
1	2671001	Isometrics drawings (Demolition and Construction)	A1360-A1365	5621-00-LD-V101	1			2.45%	9.74%	P A F	14-Dec-14 07-Dec-14 16-Nov-14	21-Dec-14 11-Dec-14 16-Nov-14	23-Dec-14 07-Jan-15 18-Nov-14	25-Dec-14 13-Jan-15 20-Nov-14	08-Jan-15 28-Jan-15 04-Dec-14			22-Jan-15 28-Jan-15 18-Dec-14	29-Jan-15 28-Jan-15 25-Dec-14	05-Feb-15 28-Jan-15 01-Jan-15	19-Feb-15 28-Jan-15 15-Jan-15	2.45%	2.45%	2.45%	0.00%					
2	2647001	Tie-in Schedule	A1370-A1375	5621-SCH-AA-V102	1			4.93%	19.57%	P A F	09-Nov-14 15-Nov-14 16-Nov-14	16-Nov-14 20-Nov-14 16-Nov-14	18-Nov-14 20-Nov-14 18-Nov-14	20-Nov-14 23-Dec-14 20-Nov-14	04-Dec-14 29-Dec-14 04-Dec-14			18-Dec-14 15-Feb-15 18-Dec-14	25-Dec-14 17-Feb-15 25-Dec-14	01-Jan-15 17-Feb-15 01-Jan-15	15-Jan-15 17-Feb-15 15-Jan-15	4.93%	4.93%	4.93%	0.00%					
3	2632001	Piping GA (Demolition and Construction)	A1380-A1390	5621-00-LD-V102	1			2.48%	9.83%	P A F	14-Dec-14 07-Dec-14 23-Nov-14	21-Dec-14 11-Dec-14 30-Nov-14	23-Dec-14 29-Dec-14 02-Dec-14	25-Dec-14 31-Dec-14 04-Dec-14	08-Jan-15 15-Jan-15 18-Dec-14			22-Jan-15 15-Jan-15 01-Jan-15	29-Jan-15 15-Jan-15 08-Jan-15	05-Feb-15 15-Jan-15 15-Jan-15	19-Feb-15 28-Jan-15 29-Jan-15	2.48%	2.48%	2.48%	0.00%					
4	2632001	Pipe stress analysis report	A1380-A1390	5621-RT-00-AA-V102	1			4.93%	19.57%	P A F	23-Nov-14 11-Dec-14 28-Dec-14	30-Nov-14 07-Jan-15 04-Jan-15	02-Dec-14 04-Feb-15 06-Jan-15	04-Dec-14 17-Feb-15 08-Jan-15	18-Dec-14 17-Feb-15 22-Jan-15			01-Jan-15 28-Mar-15 05-Feb-15	08-Jan-15 06-Apr-15 12-Feb-15	15-Jan-15 22-Apr-15 19-Feb-15	29-Jan-15 22-Apr-15 05-Mar-15	4.93%	4.93%	4.93%	0.00%					
4	2953001	Piping Material take off	A1400-A1405	5621-MTO-00-AA-V101	1			4.82%	19.13%	P A F	28-Dec-14 04-Jan-15 04-Jan-15	04-Jan-15 07-Jan-15 07-Jan-15	06-Jan-15 14-Jan-15 14-Jan-15	08-Jan-15 02-Feb-15 08-Feb-15	22-Jan-15 08-Feb-15 08-Feb-15			05-Feb-15 15-Feb-15 15-Feb-15	12-Feb-15 15-Feb-15 15-Feb-15	19-Feb-15 15-Feb-15 15-Feb-15	05-Mar-15 15-Feb-15 15-Feb-15	4.82%	4.82%	4.82%	0.00%					
5	2981001	Piping Material Specification	A1410-A1560	5621-SP-00-AA-V102	1	A	6-Nov-14	4.38%	17.39%	P A F	04-Nov-14 04-Nov-14 22-Jan-15	05-Nov-14 05-Nov-14 25-Jan-15	05-Nov-14 06-Nov-14 27-Jan-15	06-Nov-14 11-Nov-14 29-Jan-15	20-Nov-14 19-Nov-14 12-Feb-15			04-Dec-14 19-Nov-14 26-Feb-15	11-Dec-14 19-Nov-14 05-Mar-15	18-Dec-14 07-Dec-14 12-Mar-15	01-Jan-15 07-Dec-14 26-Mar-15	4.38%	4.38%	4.38%	0.00%					
6		Miscellaneous Deliverables (Not identified at this stage)			1			1.20%	4.78%	P A F	22-Jan-15 27-Mar-15 22-Jan-15	25-Jan-15 27-Mar-15 25-Jan-15	27-Jan-15 27-Mar-15 27-Jan-15	29-Jan-15 27-Mar-15 29-Jan-15	12-Feb-15 27-Mar-15 12-Feb-15			26-Feb-15 03-Apr-15 03-Apr-15	05-Mar-15 03-Apr-15 03-Apr-15	12-Mar-15 03-Apr-15 03-Apr-15	26-Mar-15 03-Apr-15 03-Apr-15	1.20%	1.20%	1.20%	0.00%					

[illegible]


Sl No.	TME Doc No.	GASCO Drawing / Document Title	Activity ID (Baseline Plan)	Drawing/Document No.	Drawing /Document Class	Rev No.	Rev Date	Level 1 %Wt	Est. Man-Hours %wt	P A F	Started 5%	Drafting Complete 25%	ISC Complete 40%	Submission / Review Status						Issue as IFC		Status as on				30-Oct-15		% Variance	Plan	Actual	Remarks
														Issue-1 (ICR)		Issue-2		Issue-3 (FD/IFA)		First Issue 95%	Final Issue 100%	% Plan	%Revised	% Actual	Plan	Actual					
														Submitted 50%	Receive Comments 50%	Submitted 50%	Receive Comments 50%	Submitted 75%	Approved 85%												
23	4375001	Interpanel Wiring Diagrams	A1600-A1601	5621-00-JD-V107	1			0.99%	3.91%	P A F	11-Jan-15 27-Mar-15 27-Mar-15	11-Jan-15 27-Mar-15 27-Mar-15	13-Jan-15 27-Mar-15 27-Mar-15	15-Jan-15 27-Mar-15 27-Mar-15	29-Jan-15 27-Mar-15 27-Mar-15			12-Feb-15 27-Mar-15 27-Mar-15	19-Feb-15 27-Mar-15 27-Mar-15	26-Feb-15 27-Mar-15 27-Mar-15	12-Mar-15 27-Mar-15 27-Mar-15	0.99%	0.99%	0.99%	0.00%				THIS DELIVERABLE HAS BEEN DISCUSSED WITH TME AND IS A PART OF HONEYWELL DELIVERABLES		
24	4376003	Instrument Installation Diagrams	A1610-A1611	5621-00-JD-V108	1			0.99%	3.91%	P A F	11-Jan-15 13-Jan-15 13-Jan-15	11-Jan-15 15-Jan-15 15-Jan-15	13-Jan-15 27-Jan-15 27-Jan-15	15-Jan-15 29-Jan-15 29-Jan-15	29-Jan-15 22-Feb-15 22-Feb-15			12-Feb-15 06-May-15 10-May-15	19-Feb-15 25-May-15 25-May-15	26-Feb-15 25-May-15 25-May-15	12-Mar-15 25-May-15 25-May-15	0.99%	0.99%	0.99%	0.00%						
25	4376002	Pneumatic Instrument Hook-Up Diagrams	A1620-A1621	5621-00-JD-V109	1			0.99%	3.91%	P A F	11-Jan-15 13-Jan-15 13-Jan-15	11-Jan-15 14-Jan-15 14-Jan-15	13-Jan-15 15-Jan-15 15-Jan-15	15-Jan-15 27-Jan-15 27-Jan-15	29-Jan-15 01-Feb-15 01-Feb-15			12-Feb-15 19-Mar-15 24-Jun-15	19-Feb-15 24-Jun-15 24-Jun-15	26-Feb-15 24-Jun-15 24-Jun-15	12-Mar-15 24-Jun-15 24-Jun-15	0.99%	0.99%	0.99%	0.00%						
26	4324001	Instrument Bulk Material Take Off	A1630-A1660	5621-MTO-00-AA-V102	1			0.99%	3.91%	P R A F	18-Jan-15 15-Jan-15 15-Jan-15	01-Feb-15 18-Feb-15 18-Feb-15	03-Feb-15 19-Feb-15 19-Feb-15	05-Feb-15 19-Mar-15 19-Mar-15	19-Feb-15 22-Apr-15 22-Apr-15			05-Mar-15 02-Jul-15 25-Aug-15	12-Mar-15 25-Aug-15 25-Aug-15	19-Mar-15 25-Aug-15 25-Aug-15	02-Apr-15 16-Sep-15 25-Aug-15	0.99%	0.99%	0.99%	0.00%						
27		General Instrument Specifications		5621-SP-00-AA-V107	1			1.07%	4.26%	P A F	22-Jan-15 04-Feb-15 04-Feb-15	25-Jan-15 04-Feb-15 04-Feb-15	27-Jan-15 19-Mar-15 19-Mar-15	29-Jan-15 19-Mar-15 19-Mar-15	12-Feb-15 22-Apr-15 22-Apr-15			26-Feb-15 20-May-15 27-May-15	05-Mar-15 27-May-15 27-May-15	12-Mar-15 27-May-15 27-May-15	26-Mar-15 27-May-15 27-May-15	1.07%	1.07%	1.07%	0.00%						
28		Miscellaneous Deliverables (Not identified at this stage)			1			0.18%	0.70%	P A F	22-Jan-15 19-Feb-15 19-Feb-15	25-Jan-15 19-Feb-15 19-Feb-15	27-Jan-15 19-Feb-15 19-Feb-15	29-Jan-15 19-Mar-15 19-Mar-15	12-Feb-15 19-Mar-15 19-Mar-15			26-Feb-15 03-Apr-15 03-Apr-15	05-Mar-15 03-Apr-15 03-Apr-15	12-Mar-15 03-Apr-15 03-Apr-15	26-Mar-15 03-Apr-15 03-Apr-15	0.18%	0.18%	0.18%	0.00%						
		Safety and Loss Prevention							4.71%	P R A F												4.71%	4.71%	4.26%	-0.45%						
1	3415001	HSE Plan	A1640-A1641	5621-PP-00-AA-V101	1			0.66%	13.95%	P A F	02-Dec-14 20-Nov-14 20-Nov-14	11-Dec-14 26-Nov-14 26-Nov-14	13-Dec-14 27-Nov-14 27-Nov-14	15-Dec-14 29-Dec-14 29-Dec-14	29-Dec-14 29-Jan-15 29-Jan-15			12-Jan-15 02-Feb-15 22-Feb-15	19-Jan-15 22-Feb-15 22-Feb-15	26-Jan-15 22-Feb-15 22-Feb-15	09-Feb-15 22-Feb-15 22-Feb-15	0.66%	0.66%	0.66%	0.00%						
2	3415002	HSE Philosophy	A1650-A1651	5621-PP-00-AA-V102	1			0.66%	13.95%	P A F	16-Dec-14 10-Jan-15 10-Jan-15	25-Dec-14 11-Jan-15 11-Jan-15	27-Dec-14 12-Jan-15 12-Jan-15	29-Dec-14 03-Feb-15 03-Feb-15	12-Jan-15 22-Feb-15 22-Feb-15			26-Jan-15 04-Mar-15 04-Mar-15	02-Feb-15 04-Mar-15 04-Mar-15	09-Feb-15 04-Mar-15 04-Mar-15	23-Feb-15 04-Mar-15 04-Mar-15	0.66%	0.66%	0.66%	0.00%						
3	3415003	HAZID/ENVID/OHRA Procedure	A1660-A1661	5621-PP-00-AA-V103	1			0.66%	13.95%	P A F	30-Dec-14 27-Nov-14 27-Nov-14	08-Jan-15 05-Jan-15 05-Jan-15	10-Jan-15 06-Jan-15 06-Jan-15	12-Jan-15 14-Jan-15 14-Jan-15	26-Jan-15 29-Jan-15 29-Jan-15			09-Feb-15 03-Feb-15 22-Feb-15	16-Feb-15 22-Feb-15 04-Mar-15	23-Feb-15 04-Mar-15 04-Mar-15	09-Mar-15 04-Mar-15 04-Mar-15	0.66%	0.66%	0.66%	0.00%						
4	3415004	HAZID/ENVID/OHRA Report	A1670-A1671	5621-RT-00-AA-V103	1			0.88%	18.60%	P A F	11-Jan-15 23-Feb-15 23-Feb-15	11-Jan-15 24-Feb-15 24-Feb-15	13-Jan-15 25-Feb-15 25-Feb-15	15-Jan-15 03-Mar-15 03-Mar-15	29-Jan-15 19-Mar-15 19-Mar-15			12-Feb-15 20-Apr-15 23-Apr-15	19-Feb-15 23-Apr-15 23-Apr-15	26-Feb-15 23-Apr-15 23-Apr-15	12-Mar-15 23-Apr-15 23-Apr-15	0.88%	0.88%	0.88%	0.00%						
5	3415005	HAZID/ENVID/OHRA Close Out Report	A1680-A1681	5621-RT-00-AA-V104	1			0.74%	15.81%	P R A F	18-Jan-15 26-Feb-15 26-Feb-15	18-Jan-15 26-Feb-15 26-Feb-15	20-Jan-15 12-Mar-15 12-Mar-15	22-Jan-15 03-Sep-15 03-Sep-15	05-Feb-15 03-Sep-15 03-Sep-15			19-Feb-15 05-Sep-15 12-Sep-15	26-Feb-15 12-Sep-15 14-Sep-15	05-Mar-15 14-Sep-15 16-Sep-15	19-Mar-15 16-Sep-15 16-Sep-15	0.74%	0.74%	0.30%	-0.45%						
6	3415006	HSE Action Tracking Register	A1690-A1870	5621-RT-00-AA-V105	1			0.88%	18.60%	P R A F	25-Jan-15 26-Feb-15 26-Feb-15	01-Feb-15 26-Feb-15 26-Feb-15	03-Feb-15 12-Mar-15 12-Mar-15	05-Feb-15 05-Apr-15 05-Apr-15	19-Feb-15 09-Apr-15 09-Apr-15			05-Mar-15 29-Jul-15 06-Sep-15	12-Mar-15 06-Sep-15 06-Sep-15	19-Mar-15 06-Sep-15 06-Sep-15	02-Apr-15 08-Sep-15 06-Sep-15	0.88%	0.88%	0.88%	0.00%						
7		Miscellaneous Deliverables (Not identified at this stage)			1			0.24%	5.12%	P A F	22-Jan-15 19-Feb-15 19-Feb-15	25-Jan-15 19-Feb-15 19-Feb-15	27-Jan-15 19-Feb-15 19-Feb-15	29-Jan-15 19-Feb-15 19-Feb-15	12-Feb-15 19-Feb-15 19-Feb-15			26-Feb-15 09-Apr-15 09-Apr-15	05-Mar-15 09-Apr-15 09-Apr-15	12-Mar-15 09-Apr-15 09-Apr-15	26-Mar-15 09-Apr-15 09-Apr-15	0.24%	0.24%	0.24%	0.00%						
		Civil Engineering							16.54%	P A F												16.54%	16.54%	16.54%	0.00%						
1	1181001	Project specifications (including all Addendums to Civil and Structural DGS)	A1700-A1701	5621-SP-00-AA-V105	1			0.99%	5.96%	P A F	18-Nov-14 10-Nov-14 10-Nov-14	27-Nov-14 16-Nov-14 16-Nov-14	29-Nov-14 17-Nov-14 17-Nov-14	01-Dec-14 19-Nov-14 19-Nov-14	15-Dec-14 03-Dec-14 03-Dec-14			29-Dec-14 07-Dec-14 07-Dec-14	05-Jan-15 07-Dec-14 07-Dec-14	12-Jan-15 15-Dec-14 15-Dec-14	26-Jan-15 15-Dec-14 15-Dec-14	0.99%	0.99%	0.99%	0.00%						
2	1120001	Adequacy study of existing structures & their foundations and modifications as necessary for additional loading	A1710-A1711	5621-RT-00-AA-V106	1			0.70%	4.24%	P A F	07-Dec-14 04-Jan-15 04-Jan-15	14-Dec-14 07-Jan-15 07-Jan-15	16-Dec-14 12-Feb-15 12-Feb-15	18-Dec-14 12-Mar-15 12-Mar-15	01-Jan-15 24-Mar-15 24-Mar-15			15-Jan-15 16-Jun-15 23-Jun-15	22-Jan-15 23-Jun-15 23-Jun-15	29-Jan-15 23-Jun-15 23-Jun-15	12-Feb-15 23-Jun-15 23-Jun-15	0.70%	0.70%	0.70%	0.00%						
3	1173001	G.A. and reinforcement details of Foundations.	A1720-A1721	5621-00-CD-V101	1			0.88%	5.30%	P A F	21-Dec-14 04-Jan-15 04-Jan-15	28-Dec-14 07-Jan-15 07-Jan-15	30-Dec-14 19-Feb-15 19-Feb-15	01-Jan-15 16-Jun-15 16-Jun-15	15-Jan-15 29-May-15 29-May-15			29-Jan-15 24-May-15 29-May-15	05-May-15 24-May-15 29-May-15	12-Feb-15 29-May-15 29-May-15	26-Feb-15 29-May-15 29-May-15	0.88%	0.88%	0.88%	0.00%						
4	1190001	Civil/ Structural Design Criteria	A1730-A1731	5621-SP-00-AA-V106	1			0.88%	5.30%	P A F	02-Dec-14 26-Nov-14 26-Nov-14	11-Dec-14 27-Nov-14 27-Nov-14	13-Dec-14 21-Dec-14 21-Dec-14	15-Dec-14 20-Mar-15 20-Mar-15	29-Dec-14 20-Mar-15 20-Mar-15			12-Jan-15 20-Mar-15 20-Mar-15	19-Jan-15 20-Mar-15 20-Mar-15	26-Jan-15 20-Mar-15 20-Mar-15	09-Feb-15 20-Mar-15 20-Mar-15	0.88%	0.88%	0.88%	0.00%				THIS PART IS ALREADY INCLUDED IN DESIGN BASIS MEMORANDUM		
5	1349001	Modified Structural steel layout plan, elevations and details - where required.	A1740-A1741	5621-00-CD-V102	1			0.88%	5.30%	P A F	21-Dec-14 04-Jan-15 04-Jan-15	28-Dec-14 07-Jan-15 07-Jan-15	30-Dec-14 19-Feb-15 19-Feb-15	01-Jan-15 29-Apr-15 15-May-15	15-Jan-15 06-May-15 22-May-15			29-Jan-15 07-May-15 24-May-15	05-Feb-15 08-Jun-15 26-May-15	12-Feb-15 08-Jun-15 28-May-15	26-Feb-15 08-Jun-15 30-May-15	0.88%	0.88%	0.88%	0.00%				NOT REQUIRED		
6	1119001	Demolition Layout Plan as required.	A1750-A1751	5621-00-CD-V103	1			0.55%	3.31%	P A F	06-Jan-15 07-Jan-15 07-Jan-15	15-Jan-15 19-Feb-15 19-Feb-15	17-Jan-15 26-Feb-15 27-Mar-15	19-Jan-15 02-Feb-15 27-Mar-15	02-Feb-15 27-Mar-15 27-Mar-15			16-Feb-15 27-Mar-15 27-Mar-15	23-Feb-15 27-Mar-15 27-Mar-15	02-Mar-15 27-Mar-15 27-Mar-15	16-Mar-15 27-Mar-15 27-Mar-15	0.55%	0.55%	0.55%	0.00%				NO FOUNDATION TO BE DEMOLISHED AS PER ADEQUACY STUDY REPORT		
7	1173002	GA and Reinf. Detail of Pipe Support Foundations (as required)	A1760-A1761	5621-00-CD-V104	1			0.55%	3.31%	P A F	04-Jan-15 19-Feb-15 05-Feb-15	11-Jan-15 19-Feb-15 14-Feb-15	13-Jan-15 26-Feb-15 16-Feb-15	15-Jan-15 20-Mar-15 18-Feb-15	29-Jan-15 20-Mar-15 04-Mar-15			12-Feb-15 20-Mar-15 18-Mar-15	19-Feb-15 20-Mar-15 25-Mar-15	26-Feb-15 20-Mar-15 01-Apr-15	12-Mar-15 20-Mar-15 15-Apr-15	0.55%	0.55%	0.55%	0.00%				NOT REQUIRED AS PER CALCULATIONS		
																														NO CHANGES IN THE PLATEWORK	

Sl No.	TME Doc No.	GASCO Drawing / Document Title	Activity ID (Baseline Plan)	Drawing/Document No.	Drawing /Document Class	Rev No.	Rev Date	Level 1 %WT	Est. Man-Hours /wt %	P A F	Started 5%	Drafting Complete 25%	ISC Complete 40%	Submission / Review Status						Issue as IFC		Status as on				Earned Man-Hours		Remarks
														Issue-1 (ICR)		Issue-2		Issue-3 (FD/IFA)		% Plan	% Revised	% Actual	% Variance	Plan	Actual			
														Submitted 50%	Receive Comments 50%	Submitted 50%	Receive Comments 50%	Submitted 75%	Approved 85%							First Issue 95%	Final Issue 100%	
8	1173003	G.A. and Reinr. Details Foundation for Platforms and Crossovers (as required)	A1770-A1772	5621-00-CD-V105	1			0.55%	3.31%	A F	19-Feb-15	19-Feb-15	26-Feb-15	20-Mar-15	20-Mar-15			20-Mar-15	20-Mar-15	20-Mar-15	20-Mar-15	0.55%	0.55%	0.55%	0.00%		FOUNDATION AS PER ADEQUACY STUDY REPORT	
9	1349002	Pipe Supports Details	A1780-A1781	5621-00-CD-V106	1			1.10%	6.62%	A F	14-Dec-14 04-Jan-15	21-Dec-14 07-Jan-15	23-Dec-14 19-Feb-15	25-Dec-14 20-Mar-15	08-Jan-15 20-Mar-15			22-Jan-15 20-Mar-15	29-Jan-15 20-Mar-15	05-Feb-15 20-Mar-15	19-Feb-15 20-Mar-15	1.10%	1.10%	1.10%	0.00%		NO CHANGES IN THE PLATFORM FOUNDATION AS PER ADEQUACY STUDY REPORT	
10	1172001	Foundation Layout Plan	A1800-A1801	5621-00-CD-V107	1			1.10%	6.62%	P A F	07-Dec-14 04-Jan-15	14-Dec-14 07-Jan-15	16-Dec-14 15-Jan-15	18-Dec-14 02-Jun-15	01-Jan-15 16-Jun-15			15-Jan-15 16-Jun-15	22-Jan-15 26-Jun-15	29-Jan-15 26-Jun-15	12-Feb-15 26-Jun-15	1.10%	1.10%	1.10%	0.00%			
11	1181002	General Notes Civil Works	A1810-A1811	5621-00-CD-V108	1			1.10%	6.62%	P A F	16-Dec-14 16-Nov-14	18-Dec-14 17-Nov-14	20-Dec-14 17-Nov-14	22-Dec-14 20-Nov-14	05-Jan-15 10-Dec-14			19-Jan-15 11-Dec-14	26-Jan-15 24-Dec-14	02-Feb-15 24-Dec-14	16-Feb-15 24-Dec-14	1.10%	1.10%	1.10%	0.00%			
12	1181003	General Notes Structural Works	A1820-A1821	5621-00-CD-V109	1			1.10%	6.62%	P A F	23-Dec-14 16-Nov-14	25-Dec-14 17-Nov-14	27-Dec-14 17-Nov-14	29-Dec-14 20-Nov-14	12-Jan-15 10-Dec-14			26-Jan-15 11-Dec-14	02-Feb-15 24-Dec-14	09-Feb-15 24-Dec-14	23-Feb-15 24-Dec-14	1.10%	1.10%	1.10%	0.00%			
13	1163001	Roads and Paving Details	A1830-A1831	5621-00-CD-V110	1			1.10%	6.62%	P A F	30-Dec-14 16-Nov-14	01-Jan-15 17-Nov-14	03-Jan-15 17-Nov-14	05-Jan-15 20-Nov-14	19-Jan-15 10-Dec-14			02-Feb-15 11-Dec-14	09-Feb-15 24-Dec-14	16-Feb-15 24-Dec-14	02-Mar-15 24-Dec-14	1.10%	1.10%	1.10%	0.00%			
14	1344001	Ladder Standard Details and Foundation	A1840-A1841	5621-00-CD-V111	1			1.10%	6.62%	P A F	06-Jan-15 16-Nov-14	15-Jan-15 17-Nov-14	17-Jan-15 17-Nov-14	19-Jan-15 20-Nov-14	02-Feb-15 10-Dec-14			16-Feb-15 11-Dec-14	23-Feb-15 24-Dec-14	02-Mar-15 24-Dec-14	16-Mar-15 24-Dec-14	1.10%	1.10%	1.10%	0.00%			
15	1145001	Standard Details Concrete Protection	A1850-A1880	5621-00-CD-V112	1			1.10%	6.62%	P A F	20-Jan-15 16-Nov-14	22-Jan-15 17-Nov-14	24-Jan-15 17-Nov-14	26-Jan-15 20-Nov-14	09-Feb-15 10-Dec-14			23-Feb-15 11-Dec-14	02-Mar-15 24-Dec-14	09-Mar-15 24-Dec-14	23-Mar-15 24-Dec-14	1.10%	1.10%	1.10%	0.00%			
16		Adequacy study of affected structures	5621-RT-00-CA-V101	1				0.55%	3.31%	P A F	04-Jan-15 14-Jan-15	11-Jan-15 15-Jan-15	13-Jan-15 12-Feb-15	15-Jan-15 27-Mar-15	29-Jan-15 27-Mar-15			12-Feb-15 27-Mar-15	19-Feb-15 27-Mar-15	26-Feb-15 27-Mar-15	12-Mar-15 27-Mar-15	0.55%	0.55%	0.55%	0.00%		As per Approval of latest Pipe Stress Report/Weight of new valve is less than the existing valve- refer stress report page 4 of 24- hence Not required this deliverables	
17		Updating Civil General Arrangement Drawings (as required)	5621-00-CD-V113	1				0.55%	3.31%	P A F	06-Jan-15 14-Jan-15	15-Jan-15 15-Jan-15	17-Jan-15 27-Mar-15	19-Jan-15 27-Mar-15	02-Feb-15 27-Mar-15			16-Feb-15 27-Mar-15	23-Feb-15 27-Mar-15	02-Mar-15 27-Mar-15	16-Mar-15 27-Mar-15	0.55%	0.55%	0.55%	0.00%		No updation required of civil drawings as per calculation report	
18		Modification of Cable Trenches Drawings (as required)	5621-00-CD-V114	1				0.55%	3.31%	P A F	05-Feb-15 14-Jan-15	14-Feb-15 19-Feb-15	16-Feb-15 26-Feb-15	18-Feb-15 09-Apr-15	04-Mar-15 09-Apr-15			18-Mar-15 09-Apr-15	25-Mar-15 09-Apr-15	01-Apr-15 09-Apr-15	15-Apr-15 09-Apr-15	0.55%	0.55%	0.55%	0.00%		Deleted: No modification is required – Instrument drawing number 5621-00-JD-V103 is sufficient as reference. 02-Mar	
19		Incorporation of comments from Vendor Review		1				0.44%	2.65%	P A F	04-Mar-15 19-Feb-15	06-Mar-15 19-Feb-15	08-Mar-15 25-Feb-15	11-Mar-15 27-Mar-15	25-Mar-15 27-Mar-15			06-Apr-15 27-Mar-15	15-Apr-15 27-Mar-15	15-Apr-15 27-Mar-15	15-Apr-15 27-Mar-15	0.44%	0.44%	0.44%	0.00%			
20		Miscellaneous Deliverables (Not identified at this stage)		1				0.83%	5.03%	P A F	22-Jan-15 19-Feb-15	25-Jan-15 19-Feb-15	27-Jan-15 19-Feb-15	29-Jan-15 19-Feb-15	12-Feb-15 19-Feb-15			19-Feb-15 03-Apr-15	05-Mar-15 03-Apr-15	12-Mar-15 03-Apr-15	26-Mar-15 03-Apr-15	0.83%	0.83%	0.83%	0.00%			

ATTACHMENT - 2A

**ENGINEERING PROGRESS
S-CURVE**

Archives from Personal Files

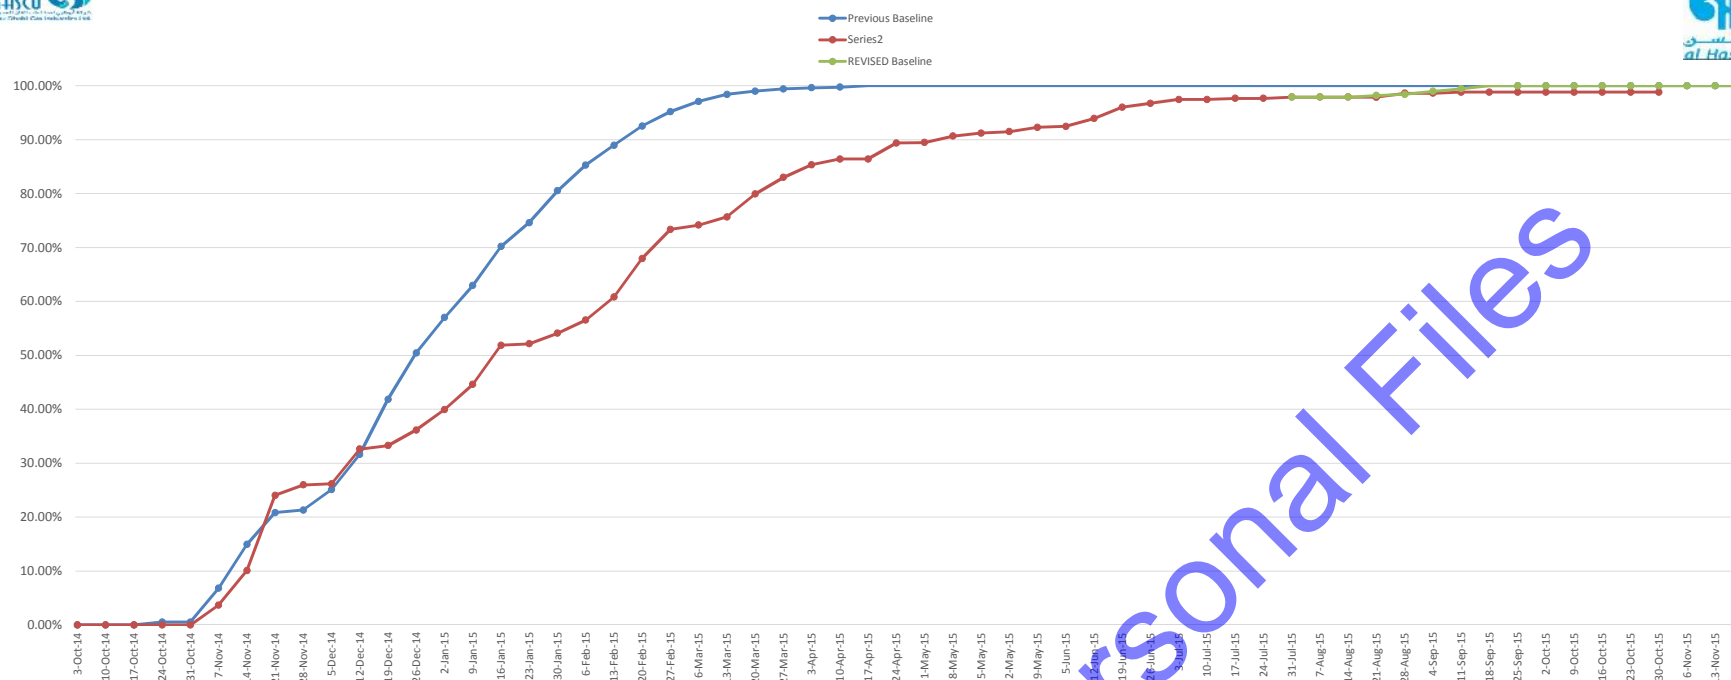

WEEKS	WEEKS																													
	3-Oct-14	10-Oct-14	17-Oct-14	24-Oct-14	31-Oct-14	7-Nov-14	14-Nov-14	21-Nov-14	28-Nov-14	5-Dec-14	12-Dec-14	19-Dec-14	26-Dec-14	2-Jan-15	9-Jan-15	16-Jan-15	23-Jan-15	30-Jan-15	6-Feb-15	13-Feb-15	20-Feb-15	27-Feb-15	6-Mar-15	13-Mar-15	20-Mar-15	27-Mar-15	3-Apr-15	10-Apr-15	17-Apr-15	24-Apr-15
	W01	W02	W03	W04	W05	W06	W07	W08	W09	W10	W11	W12	W13	W14	W15	W16	W17	W18	W19	W20	W21	W22	W23	W24	W25	W26	W27	W28	W29	W30
PLAN FOR THE WEEK	0.00%	0.00%	0.00%	0.53%	0.00%	6.26%	8.13%	5.92%	0.47%	3.79%	6.52%	10.21%	8.60%	6.59%	5.92%	7.23%	4.42%	5.93%	4.76%	3.70%	3.56%	2.65%	1.92%	1.28%	0.61%	0.41%	0.20%	0.12%	0.28%	0.00%
PLAN CUMM	0.00%	0.00%	0.00%	0.53%	0.53%	6.80%	14.93%	20.84%	21.32%	25.11%	31.63%	41.83%	50.43%	57.02%	62.94%	70.17%	74.59%	80.52%	85.28%	88.97%	92.54%	95.18%	97.11%	98.39%	98.99%	99.40%	99.61%	99.73%	100.00%	100.00%
REVISED PLAN FOR THE WEEK																														
REVISED PLAN CUMM																														
ACTUAL FOR THE WEEK	0.00%	0.00%	0.00%	0.00%	0.00%	3.70%	6.38%	13.95%	1.93%	0.22%	6.44%	0.64%	2.90%	3.70%	4.67%	7.25%	0.26%	1.98%	2.41%	4.28%	7.15%	5.41%	0.81%	1.51%	4.23%	3.11%	2.34%	1.05%	0.00%	2.97%
ACTUAL CUMM	0.00%	0.00%	0.00%	0.00%	0.00%	3.70%	10.08%	24.03%	25.96%	26.19%	32.62%	33.26%	36.16%	39.95%	44.62%	51.87%	52.13%	54.11%	56.52%	60.80%	67.96%	73.36%	74.17%	75.68%	79.91%	83.02%	85.35%	86.41%	86.41%	89.37%
WEEKS	WEEKS																													
	1-May-15	8-May-15	15-May-15	22-May-15	29-May-15	5-Jun-15	12-Jun-15	19-Jun-15	26-Jun-15	3-Jul-15	10-Jul-15	17-Jul-15	24-Jul-15	31-Jul-15	7-Aug-15	14-Aug-15	21-Aug-15	28-Aug-15	4-Sep-15	11-Sep-15	18-Sep-15	25-Sep-15	2-Oct-15	9-Oct-15	16-Oct-15	23-Oct-15	30-Oct-15	6-Nov-15	13-Nov-15	20-Nov-15
	W31	W32	W33	W34	W35	W36	W37	W38	W39	W40	W41	W42	W43	W44	W45	W46	W47	W48	W49	W50	W51	W52	W53	W54	W55	W56	W57	W58	W59	W60
PLAN FOR THE WEEK	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%
PLAN CUMM	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%
REVISED PLAN FOR THE WEEK															0.00%	0.00%	0.00%	0.32%	0.19%	0.57%	0.47%	0.58%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%
REVISED PLAN CUMM															97.88%	97.88%	97.88%	98.21%	98.39%	98.96%	99.43%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%
ACTUAL FOR THE WEEK	0.09%	1.20%	0.54%	0.29%	0.78%	0.20%	1.45%	2.09%	0.72%	0.71%	0.00%	0.22%	0.00%	0.22%	0.00%	0.00%	0.00%	0.71%	0.00%	0.22%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%
ACTUAL CUMM	89.46%	90.67%	91.21%	91.50%	92.28%	92.48%	93.93%	96.02%	96.73%	97.45%	97.45%	97.67%	97.67%	97.88%	97.88%	97.88%	97.88%	98.60%	98.60%	98.82%	98.82%	98.82%	98.82%	98.82%	98.82%	98.82%	98.82%	98.82%	98.82%	98.82%

ATTACHMENT - 3

PROCUREMENT STATUS REGISTER

Archives from Personal Files



BuHasa Replacement of Valves & Actuators for EPC Works

GASCO PROJECT NO: 5621

Procurement Status Report



Document Title	Procurement Status Report (PSR)
Document No.	5621 SCH 00-AA-0011
Rev.	1
Date	30-Oct-15

Sr. No.	Item Description	ITEM TYPE	ITEM QTY	RFQ NUMBER	Activity ID (Baseline Plan)	WL % LEVEL - 1	WL % LEVEL - 2	P / F / A	Prepare MR / PR	Issue RFQ	Receive Offers	Complete Vendor Clarifications	Complete Eval & Submit TBE to COMPANY	Receive COMPANY Approval	Commit / Issue P.O.	Receive & Approve Vendor Docs (Major)	Place Sub-Orders (Major)	Receive Sub-ordered Materials (Major)	Compl. Mfg.	Compl. Final Inspection	Compl. Mfg. Dispatch	Receive MRV at Site (Complete)	Prepare MRV	Receive Material in Baseline Site	ROS Date*	Weightage Achieved			Remarks / Status							
									PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA	PIFA		PIFA	PIFA	PIFA	PIFA	PLAN	REVISED	ACTUAL
									0%	2%	3%	6%	8%	8%	10%	15%	20%	40%	80%	90%	95%	98%	100%													
COMPLETE PROCUREMENT																											99.94%	76.00%	66.11%	34.82%						
LONG LEAD ITEMS																											99.99%	64.79%	62.43%							
																											48.00%	32.06%	29.37%							
TRAIN - 1 SDT VALVES AND ACTUATORS FOR REPLACEMENT																											17.00%	8.90%	9.01%							
1	10" X 10" - #300 QTY 01 Nos.			5621-RFQ-00-AA-V001		0.65%	1.62%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	1.62%	0.86%	0.86%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
2	12" X 12" - #300 QTY 03 Nos.			5621-RFQ-00-AA-V001		1.94%	4.85%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	4.85%	2.57%	2.57%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
3	14" X 14" - #300 QTY 02 Nos.			5621-RFQ-00-AA-V001		1.29%	3.23%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	3.23%	1.78%	1.71%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
4	30" X 30" - #300 QTY 03 Nos.			5621-RFQ-00-AA-V001		1.94%	4.85%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	4.85%	2.47%	2.57%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
5	36" X 36" - #300 QTY 01 Nos.			5621-RFQ-00-AA-V001		1.00%	2.46%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	2.46%	1.30%	1.30%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
TRAIN - 2 SDT VALVES AND ACTUATORS FOR REPLACEMENT																										17.00%	8.90%	6.96%								
6	10" X 10" - #300 QTY 01 Nos.			5621-RFQ-00-AA-V001		0.50%	1.24%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	1.24%	0.66%	0.50%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
7	12" X 12" - #300 QTY 03 Nos.			5621-RFQ-00-AA-V001		1.49%	3.73%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	3.73%	1.98%	1.49%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
8	14" X 14" - #300 QTY 02 Nos.			5621-RFQ-00-AA-V001		0.98%	2.48%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	2.48%	1.37%	0.99%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
9	16" X 16" - #150 QTY 01 Nos.			5621-RFQ-00-AA-V001		0.50%	1.24%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	1.24%	0.66%	0.50%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
10	16" X 16" - #300 QTY 01 Nos.			5621-RFQ-00-AA-V001		0.50%	1.24%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	1.24%	0.68%	0.66%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
11	20" X 20" - #300 QTY 01 Nos.			5621-RFQ-00-AA-V001		0.50%	1.24%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	1.24%	0.66%	0.50%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
12	30" X 30" - #300 QTY 03 Nos.			5621-RFQ-00-AA-V001		1.49%	3.73%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15	3.73%	1.98%	1.49%								
								F	18-Nov-14	28-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	28-Feb-15	21-Apr-15	13-May-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
								R	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15	28-Jul-15	7-Aug-15	29-Aug-15	29-Aug-15	31-Aug-15	5-Dec-15	2-Sep-15											
13	36" X 36" - #300 QTY 01 Nos.			5621-RFQ-00-AA-V001		0.84%	2.09%	P	24-Oct-14	9-Dec-14	15-Dec-14	22-Dec-14	22-Dec-14	24-Dec-14	31-Dec-14	7-Jan-15	13-Jan-15	18-Jul-15																		



																									Document Title	Procurement Status Report (PSR)				
																									Document No.	5621-SCH-00-AA-0011				
																									Rev.	1				
																									Date	30 Oct 15				
Sr. No.	Item Description	ITEM TYPE	ITEM QTY	RFQ NUMBER	Activity ID (Baseline Plan)	WL % LEVEL - 1	WL % LEVEL - 2	P F A	Prepare MR / PR	Issue RFQ	Receive Offers	Complete Vendor Clarifications	Complete Eval. & Submit TBE to COMPANY	Receive COMPANY Approval	Comm't / Issue P.O.	Receive & Approve Vendor Docs (Major)	Place Sub-Orders (Major)	Receive Sub-ordered Materials (Major)	Compl. Mfg.	Compl. Final Inspection	Compl. Mtr'l Dispatch	Receive Mtr'l at Site (Complete)	Prepare MOV	Receive Material in Baseline Site	ROS Date*	Weightage Achieved	Remarks / Status			
									PRFA	PRFA	PRFA	PRFA	PRFA	PRFA	PRFA	PRFA	PRFA	PRFA	PRFA	PRFA	PRFA	PRFA	PRFA	PRFA		PLAN	REVISED	ACTUAL		
24	QTY 04 Nos.							F	18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	6-Dec-14	14-Dec-14	15-Dec-14	14-Jan-15	16-Jan-15	29-Jan-15	19-Feb-15	31-Mar-15	6-Apr-15	9-Apr-15	12-Apr-15							
OPERATING SPARES						4.80%	12.80%																			86.84%	88.82%	40.80%		
TRAIN - 1 & 2 OPERATING SPARES & VENDOR DOCUMENTS						4.80%	12.80%																			11.55%	7.33%	4.85%		
23	OPERATING SPARES	-	-	5621-RFQ-00-AA-V002		2.80%	7.00%	P R	24-Oct-14 18-Nov-14	9-Dec-14 29-Nov-14	15-Dec-14 2-Dec-14	22-Dec-14 4-Dec-14	22-Dec-14 6-Dec-14	24-Dec-14 29-Jan-15	31-Dec-14 29-Jan-15	7-Jan-15 29-Jan-15	13-Jan-15 29-Jan-15	19-Jul-15 30-Aug-15	28-Jul-15 4-Nov-15	7-Aug-15 8-Nov-15	29-Aug-15 14-Nov-15	29-Aug-15 14-Dec-15	31-Aug-15 15-Dec-15	29-Aug-15 14-Dec-15	2-Sep-15 15-Mar-16	7.00%	2.80%	2.80%		
24	VENDOR DOCUMENTS	-	-			2.00%	5.00%	P R	25-Dec-14 28-Dec-15	2-Feb-15 10-Apr-15	27-Feb-15 18-Apr-15	3-Apr-15 9-May-15	17-Apr-15 10-May-15	17-Apr-15 10-May-15	1-May-15 30-May-15	16-May-15 27-Jun-15	26-Jun-15 30-Jun-15	24-Jul-15 29-Jul-15	18-Sep-15 18-Sep-15	16-Oct-15 16-Oct-15	20-Nov-15 20-Nov-15	18-Dec-15 18-Dec-15	6-May-16 6-May-16	18-Dec-15 18-Dec-15	6-May-16 6-May-16	4.50%	4.50%	2.00%		
BULK MATERIALS						16.00%	40.00%																			100.00%	91.86%	75.86%		
PIPEWORK BULK MATERIAL						6.00%	16.00%																				40.65%	36.65%	30.33%	
25	PIPE	TBA	TBA	5621-RFQ-00-AA-100X		2.85%	7.13%	P R	18-Dec-14 8-Feb-15	2-Mar-15 12-Feb-15	7-Mar-15 16-Feb-15	14-Mar-15 1-Mar-15	14-Mar-15 3-Mar-15	16-Mar-15 5-Mar-15	26-Mar-15 13-May-15	28-Mar-15 13-May-15	4-Apr-15 20-May-15	2-Aug-15 20-May-15	7-Aug-15 3-Jun-15	9-Aug-15 23-Jun-15	9-Aug-15 25-Jun-15	6-Sep-15 7-Sep-15	7-Sep-15 15-Feb-16	6-Sep-15 1-Mar-16	7-Sep-15 1-Mar-16	7.13%	7.13%	6.77%		
26	FLANGES	TBA	TBA	5621-RFQ-00-AA-100X		1.42%	3.56%	P R	18-Dec-14 8-Feb-15	2-Mar-15 12-Feb-15	7-Mar-15 16-Feb-15	14-Mar-15 1-Mar-15	14-Mar-15 3-Mar-15	16-Mar-15 5-Mar-15	26-Mar-15 13-May-15	28-Mar-15 13-May-15	4-Apr-15 20-May-15	2-Aug-15 20-May-15	7-Aug-15 11-Jun-15	9-Aug-15 23-Jun-15	9-Aug-15 25-Jun-15	6-Sep-15 7-Sep-15	7-Sep-15 15-Feb-16	6-Sep-15 1-Mar-16	7-Sep-15 1-Mar-16	3.56%	3.56%	3.38%		
27	GASKETS	TBA	TBA	5621-RFQ-00-AA-100X		0.71%	1.78%	P R	18-Dec-14 8-Feb-15	2-Mar-15 12-Feb-15	7-Mar-15 16-Feb-15	14-Mar-15 1-Mar-15	14-Mar-15 3-Mar-15	16-Mar-15 5-Mar-15	26-Mar-15 13-May-15	28-Mar-15 13-May-15	4-Apr-15 20-May-15	2-Aug-15 20-May-15	7-Aug-15 11-Jun-15	9-Aug-15 23-Jun-15	9-Aug-15 25-Jun-15	6-Sep-15 7-Sep-15	7-Sep-15 15-Feb-16	6-Sep-15 1-Mar-16	7-Sep-15 1-Mar-16	1.78%	1.69%	0.71%		
28	STUD BOLTS	TBA	TBA	5621-RFQ-00-AA-100X		1.01%	2.53%	P R	18-Dec-14 8-Feb-15	2-Mar-15 12-Feb-15	7-Mar-15 16-Feb-15	14-Mar-15 1-Mar-15	14-Mar-15 3-Mar-15	16-Mar-15 5-Mar-15	26-Mar-15 13-May-15	28-Mar-15 13-May-15	4-Apr-15 20-May-15	2-Aug-15 20-May-15	7-Aug-15 11-Jun-15	9-Aug-15 23-Jun-15	9-Aug-15 25-Jun-15	6-Sep-15 7-Sep-15	7-Sep-15 15-Feb-16	6-Sep-15 1-Mar-16	7-Sep-15 1-Mar-16	2.53%	2.40%	2.02%		
INSTRUMENTATION BULK MATERIAL						6.00%	16.00%																			16.96%	11.96%	7.45%		
29	PNEUMATIC TUBING	TBA	TBA	5621-RFQ-00-AA-200X		0.57%	1.42%	P R	20-Dec-14 10-Mar-15	5-Jan-15 12-Mar-15	15-Jan-15 9-Jun-15	25-Jan-15 25-Jun-15	25-Jan-15 27-Jul-15	31-Jan-15 15-Aug-15	10-Feb-15 30-Aug-15	14-Feb-15 4-Sep-15	21-Feb-15 6-Sep-15	12-May-15 11-Sep-15	22-May-15 1-Nov-15	28-May-15 1-Nov-15	27-Jun-15 1-Nov-15	28-Jun-15 27-Nov-15	28-Jun-15 25-Nov-15	30-Jun-15 15-Jan-16	1.42%	1.14%	1.14%			
30	JUNCTION BOXES	TBA	TBA	5621-RFQ-00-AA-200X		0.86%	2.14%	P R	20-Dec-14 10-Mar-15	5-Jan-15 12-Mar-15	15-Jan-15 9-Jun-15	25-Jan-15 25-Jun-15	25-Jan-15 27-Jul-15	31-Jan-15 15-Aug-15	10-Feb-15 30-Aug-15	14-Feb-15 4-Sep-15	21-Feb-15 6-Sep-15	12-May-15 11-Sep-15	22-May-15 1-Nov-15	28-May-15 1-Nov-15	27-Jun-15 1-Nov-15	28-Jun-15 27-Nov-15	28-Jun-15 25-Nov-15	30-Jun-15 15-Jan-16	2.14%	0.86%	0.86%			
31	DCS CABLES	TBA	TBA	5621-RFQ-00-AA-200X		2.00%	4.99%	P R	20-Dec-14 10-Mar-15	5-Jan-15 12-Mar-15	15-Jan-15 9-Jun-15	25-Jan-15 25-Jun-15	25-Jan-15 27-Jul-15	31-Jan-15 15-Aug-15	10-Feb-15 30-Aug-15	14-Feb-15 4-Sep-15	21-Feb-15 6-Sep-15	12-May-15 11-Sep-15	22-May-15 1-Nov-15	28-May-15 1-Nov-15	27-Jun-15 1-Nov-15	28-Jun-15 27-Nov-15	28-Jun-15 25-Nov-15	30-Jun-15 15-Jan-16	4.99%	4.49%	3.99%			
32	CABLE TRAYS	TBA	TBA	5621-RFQ-00-AA-200X		0.86%	2.14%	P R	20-Dec-14 10-Mar-15	5-Jan-15 12-Mar-15	15-Jan-15 9-Jun-15	25-Jan-15 25-Jun-15	25-Jan-15 27-Jul-15	31-Jan-15 15-Aug-15	10-Feb-15 30-Aug-15	14-Feb-15 4-Sep-15	21-Feb-15 6-Sep-15	12-May-15 11-Sep-15	22-May-15 1-Nov-15	28-May-15 1-Nov-15	27-Jun-15 1-Nov-15	28-Jun-15 27-Nov-15	28-Jun-15 25-Nov-15	30-Jun-15 15-Jan-16	2.14%	1.92%	0.17%			
33	COMPRESSION FITTINGS	TBA	TBA	5621-RFQ-00-AA-200X		0.40%	1.00%	P R	20-Dec-14 10-Mar-15	5-Jan-15 12-Mar-15	15-Jan-15 9-Jun-15	25-Jan-15 25-Jun-15	25-Jan-15 27-Jul-15	31-Jan-15 15-Aug-15	10-Feb-15 30-Aug-15	14-Feb-15 4-Sep-15	21-Feb-15 6-Sep-15	12-May-15 11-Sep-15	22-May-15 1-Nov-15	28-May-15 1-Nov-15	27-Jun-15 1-Nov-15	28-Jun-15 27-Nov-15	28-Jun-15 25-Nov-15	30-Jun-15 15-Jan-16	1.00%	0.80%	0.80%			
34	INSTRUMENT PRESSURE SWITCHES	TBA	TBA	5621-RFQ-00-AA-200X		1.33%	3.31%	P R	20-Dec-14 10-Mar-15	5-Jan-15 12-Mar-15	15-Jan-15 9-Jun-15	25-Jan-15 25-Jun-15	25-Jan-15 27-Jul-15	31-Jan-15 15-Aug-15	10-Feb-15 30-Aug-15	14-Feb-15 4-Sep-15	21-Feb-15 6-Sep-15	12-May-15 11-Sep-15	22-May-15 1-Nov-15	28-May-15 1-Nov-15	27-Jun-15 1-Nov-15	28-Jun-15 27-Nov-15	28-Jun-15 25-Nov-15	30-Jun-15 15-Jan-16	3.31%	2.65%	0.50%			
CIVIL BULK MATERIAL						4.80%	16.80%																			16.86%	16.86%	16.86%		
35	CIVIL PRE CAST FOUNDATIONS	TBA	TBA	5621-RFQ-00-AA-300X		1.55%	3.88%	P R	12-Dec-14 28-Jun-15	18-Dec-14 29-Jun-15	28-Dec-14 6-Jul-15	7-Jan-15 21-Jul-15	7-Jan-15 21-Jul-15	13-Jan-15 21-Jul-15	23-Jan-15 6-Aug-15	27-Jan-15 13-Sep-15	3-Feb-15 6-Sep-15	14-May-15 16-Sep-15	3-Jun-15 9-Sep-15	9-Jun-15 22-Sep-15	19-Jul-15 22-Sep-15	20-Jul-15 22-Sep-15	21-Jul-15 22-Sep-15	20-Jul-15 21-Jul-15	21-Jul-15 21-Jul-15	3.88%	3.88%	3.88%		
36	STEEL STRUCTURE	TBA	TBA	5621-RFQ-00-AA-300X		1.49%	3.72%	P R	12-Dec-14 28-Jun-15	18-Dec-14 29-Jun-15	28-Dec-14 6-Jul-15	7-Jan-15 21-Jul-15	7-Jan-15 21-Jul-15	13-Jan-15 21-Jul-15	23-Jan-15 6-Aug-15	27-Jan-15 13-Sep-15	3-Feb-15 6-Sep-15	14-May-15 16-Sep-15	3-Jun-15 9-Sep-15	9-Jun-15 22-Sep-15	19-Jul-15 22-Sep-15	20-Jul-15 22-Sep-15	21-Jul-15 21-Jul-15	21-Jul-15 21-Jul-15	3.72%	3.72%	3.72%			
37	ANCHOR BOLTS	TBA	TBA	5621-RFQ-00-AA-300X		0.96%	2.40%	P R	12-Dec-14 28-Jun-15	18-Dec-14 29-Jun-15	28-Dec-14 6-Jul-15	7-Jan-15 21-Jul-15	7-Jan-15 21-Jul-15	13-Jan-15 21-Jul-15	23-Jan-15 6-Aug-15	27-Jan-15 13-Sep-15	3-Feb-15 6-Sep-15	14-May-15 16-Sep-15	3-Jun-15 9-Sep-15	9-Jun-15 22-Sep-15	19-Jul-15 22-Sep-15	20-Jul-15 22-Sep-15	21-Jul-15 21-Jul-15	21-Jul-15 21-Jul-15	2.40%	2.40%	2.40%			
Overall Weightage%						100.00%																								
GENERAL NOTES: ROS Date* ROS Date is as per Project Requirement																									Overall (Plan%)					

DETAILED PSR SUMMARY	
----------------------	--

Prepare MR / PR	Issue RFQ	Receive Offers	Complete Vendor Clarifications	Complete Eval. & Submit TBE to COMPANY	Receive COMPANY Approval	Commit / Issue P.O.	Receive & Approve Vendors (Major)	Place Sub-Orders (Major)	Receive Sub-ordered Materials (Major)	Data Sheet Approval for Manufacturing	Machining of Trunion	Machining of Seat	Machining of Stem	Machining of Body	Machining of Ball Valve	Assembly of Complete ESD VALVE	Assembly of Complete Valve With Rotork Actuator	Compl. Mfg.	Testing of Actuator	Testing of Valve + Actuator Assembly	Compl. Mat'l Dispatch	Receive Material in AUH	Valves Testing in AUH	Receive Mat'l at BuHasa	Prepare MRV	FLOAT	ROS Date		
P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A	P/F/A				
0%	2%	3%	6%	8%	8%	10%	15%	20%	40%	45%	47%	49%	51%	53%	55%	65%	75%	80%	85%	90%	95%	96%	97%	98%	100%				

18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	21-Apr-15	13-May-15	19-Jul-15	20-Aug-15	4-Sep-15	19-Sep-15	4-Oct-15	19-Oct-15	3-Nov-15	20-Nov-15	5-Dec-15	10-Dec-15	15-Dec-15	20-Dec-15	25-Dec-15	20-Jan-16	22-Jan-16	4-Feb-16	6-Feb-16	40.00	15-Mar-16
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	21-Apr-15	13-May-15	19-Jul-15	9-Aug-15	15-Sep-15	15-Sep-15	23-Sep-15	6-Oct-15													
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	21-Apr-15	13-May-15	19-Jul-15	20-Aug-15	11-Sep-15	26-Sep-15	6-Oct-15	26-Oct-15	5-Nov-15	15-Nov-15	30-Nov-15	7-Dec-15	12-Dec-15	17-Dec-15	25-Dec-15	20-Jan-16	24-Jan-16	4-Feb-16	6-Feb-16	40.00	15-Mar-16
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	21-Apr-15	13-May-15	19-Jul-15	9-Aug-15	15-Sep-15	15-Sep-15	23-Sep-15	6-Oct-15													
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	21-Apr-15	13-May-15	19-Jul-15	20-Aug-15	11-Sep-15	18-Sep-15	28-Sep-15	18-Oct-15	28-Oct-15	4-Nov-15	19-Nov-15	26-Nov-15	6-Dec-15	11-Dec-15	25-Dec-15	20-Jan-16	25-Jan-16	4-Feb-16	6-Feb-16	40.00	15-Mar-16
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	21-Apr-15	13-May-15	19-Jul-15	9-Aug-15	15-Sep-15	15-Sep-15	15-Sep-15	6-Oct-15													
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	21-Apr-15	27-May-15	28-Jul-15	20-Aug-15	11-Sep-15	3-Oct-15	13-Oct-15	2-Nov-15	12-Nov-15	22-Nov-15	27-Nov-15	4-Dec-15	14-Dec-15	19-Dec-15	25-Dec-15	20-Jan-16	28-Jan-16	4-Feb-16	6-Feb-16	40.00	15-Mar-16
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	21-Apr-15	27-May-15	28-Jul-15	9-Aug-15	15-Sep-15	23-Sep-15	6-Oct-15	20-Oct-15													
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	21-Apr-15	27-May-15	28-Jul-15	20-Aug-15	11-Sep-15	1-Oct-15	11-Oct-15	21-Oct-15	31-Oct-15	15-Nov-15	30-Nov-15	7-Dec-15	12-Dec-15	17-Dec-15	25-Dec-15	20-Jan-16	30-Jan-16	4-Feb-16	6-Feb-16	40.00	15-Mar-16
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	21-Apr-15	27-May-15	28-Jul-15	9-Aug-15	15-Sep-15	23-Sep-15	6-Oct-15	20-Oct-15													
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	11-May-15	13-May-15	19-Jul-15	27-Aug-15	18-Sep-15	8-Oct-15	18-Oct-15	28-Oct-15	7-Nov-15	22-Nov-15	7-Dec-15	14-Dec-15	19-Dec-15	24-Dec-15	25-Dec-15	20-Jan-16	22-Jan-16	4-Feb-16	6-Feb-16	40.00	15-Mar-16
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	11-May-15	13-May-15	19-Jul-15	15-Aug-15	15-Sep-15	23-Sep-15	23-Sep-15	6-Oct-15													
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	11-May-15	13-May-15	19-Jul-15	27-Aug-15	18-Sep-15	3-Oct-15	13-Oct-15	23-Oct-15	2-Nov-15	17-Nov-15	2-Dec-15	9-Dec-15	14-Dec-15	19-Dec-15	25-Dec-15	20-Jan-16	24-Jan-16	4-Feb-16	6-Feb-16	40.00	15-Mar-16
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	11-May-15	13-May-15	19-Jul-15	15-Aug-15	15-Sep-15	23-Sep-15	23-Sep-15	6-Oct-15													
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	18-May-15	22-May-15	19-Jul-15	27-Aug-15	11-Sep-15	26-Sep-15	6-Oct-15	16-Oct-15	26-Oct-15	10-Nov-15	25-Nov-15	2-Dec-15	7-Dec-15	12-Dec-15	25-Dec-15	20-Jan-16	25-Jan-16	4-Feb-16	6-Feb-16	40.00	15-Mar-16
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	18-May-15	22-May-15	19-Jul-15	15-Aug-15	15-Sep-15	23-Sep-15	23-Sep-15	6-Oct-15													
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	24-May-15	27-May-15	19-Jul-15	27-Aug-15	18-Sep-15	8-Oct-15	18-Oct-15	28-Oct-15	7-Nov-15	17-Nov-15	27-Nov-15	4-Dec-15	9-Dec-15	14-Dec-15	25-Dec-15	20-Jan-16	23-Jan-16	4-Feb-16	6-Feb-16	40.00	15-Mar-16
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	24-May-15	27-May-15	19-Jul-15	15-Aug-15	15-Sep-15	23-Sep-15	6-Oct-15	20-Oct-15													
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	24-May-15	27-May-15	19-Jul-15	27-Aug-15	18-Sep-15	28-Sep-15	8-Oct-15	18-Oct-15	28-Oct-15	7-Nov-15	17-Nov-15	24-Nov-15	29-Nov-15	4-Dec-15	25-Dec-15	20-Jan-16	23-Jan-16	4-Feb-16	6-Feb-16	40.00	15-Mar-16
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	24-May-15	27-May-15	19-Jul-15	15-Aug-15	15-Sep-15	23-Sep-15	6-Oct-15	20-Oct-15													
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	24-May-15	27-May-15	19-Jul-15	27-Aug-15	18-Sep-15	8-Oct-15	18-Oct-15	28-Oct-15	7-Nov-15	17-Nov-15	27-Nov-15	4-Dec-15	9-Dec-15	14-Dec-15	25-Dec-15	20-Jan-16	27-Jan-16	4-Feb-16	6-Feb-16	40.00	15-Mar-16
18-Nov-14	29-Nov-14	2-Dec-14	4-Dec-14	10-Feb-15	25-Feb-15	26-Feb-15	24-May-15	27-May-15	19-Jul-15	15-Aug-15	15-Sep-15	23-Sep-15	6-Oct-15	20-Oct-15													


DETAILED PSR SUMMARY

[illegible]

ATTACHMENT - 4

**PROCUREMENT PROGRESS
S-CURVE**

Archives from Personal Files

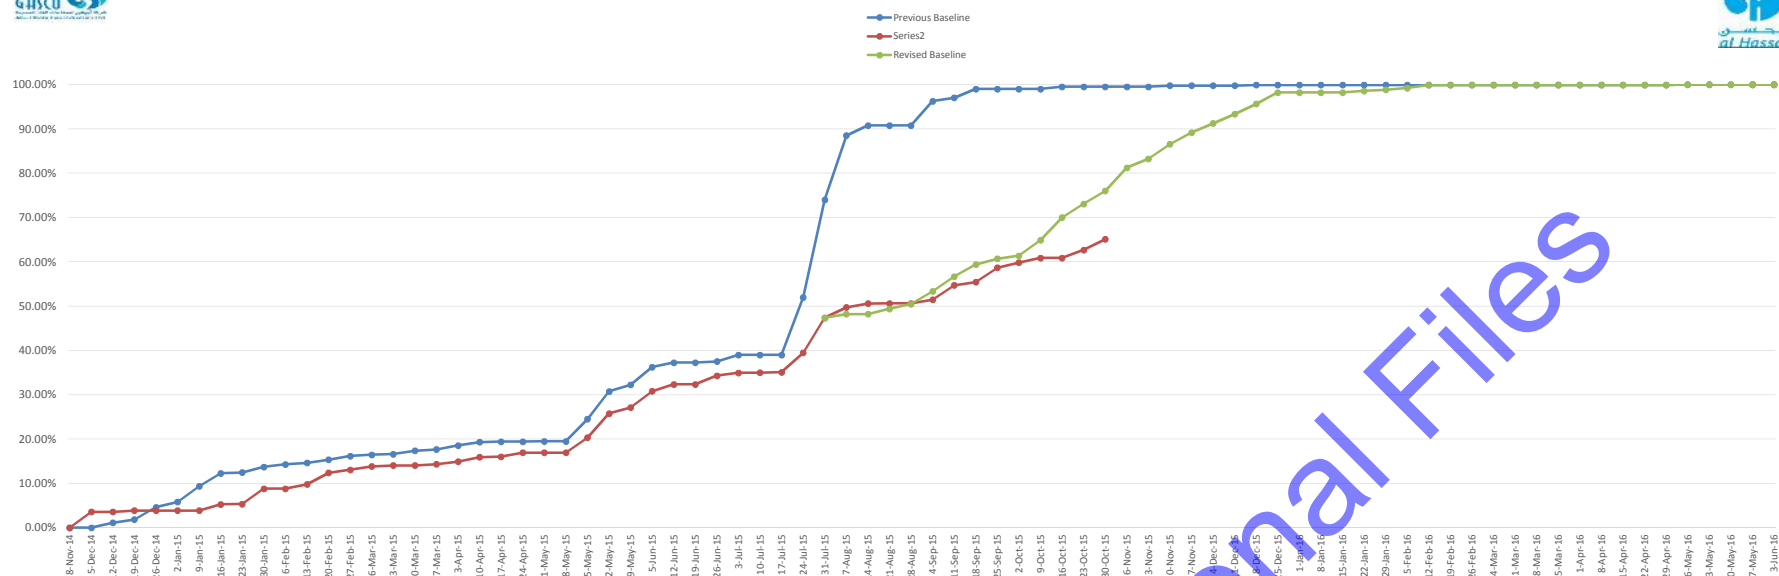[illegible]

ATTACHMENT - 5

DCA REGISTER

Archives from Personal Files



ATTACHMENT - 6

CTN REGISTER

Archives from Personal Files

LEGENDS : C = IDENTIFIED , P = PREPARED & SUBMITTED, A = APPROVED, R = REJECTED, W = AMMENDMENT TO CONTRACT DONE

ATTACHMENT - 7

MANPOWER DEPLOYMENT

Archives from Personal Files

SR No.	Designation / Title	Peak (Nos.)	2014												2015												2016												2017						Total Est. Man-days (Month)	Total Est. @25days Month																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
			Sep-14				Oct-14				Nov-14				Dec-14				Jan-15				Feb-15				Mar-15				Apr-15				May-15				Jun-15				Jul-15				Aug-15				Sep-15				Oct-15				15				16				17				18				19				20				21				22				23				24				25				26				27				28				29				30																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
			P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A			P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A

MANPOWER DEPLOYMENT SCHEDULE

 One day shutdown
 Major shutdown

SR No.	Designation / Title	Peak (Nos.)	2014				2015												2016												2017				Total Est. @26days Month	Total Est. Non-days Month						
			Sep-14	Oct-14	Nov-14	Dec-14	Jan-15	Feb-15	Mar-15	Apr-15	May-15	Jun-15	Jul-15	Aug-15	Sep-15	Oct-15	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30										
			P	A	P	A	P	A	P	A	P	A	P	A	P	A	P	A	Dec-15	Jan-16	Feb-16	Mar-16	Apr-16	May-16	Jun-16	Jul-16	Aug-16	Sep-16	Oct-16	Nov-16	Dec-16	Jan-17	Feb-17									
	24 CRANE OPERATOR	6												1	2	1	1	2	2	1	4	2	1					1				36	936									
	25 EQPT OPERATOR	3												1	1	1	1	2	1	1	1	2					2				27	702										
	26 HSE ENGINEER	2	0.5	0.5	0.5	0.5	0.5	0.5	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1									30										
	27 QHSE ENGINEER	1	0.5	0.5	0.5	0.5	0.5	0.5	0.5	0.5	0.5	0.5	0.5	0.5	1.0	0.5			0.5	1.0	0.5	1					0.5					17										
2.2	Direct Manpower (Non-supervisory Staff) (Tenderer to indicate Details separately against each discipline)																																									
	1 Civil Foreman	1												1	1		1															10	260									
	2 Bar Bender / Steel Fiaer	2												2	2		2	2	2	1	1	1										14	364									
	3 Carpenter	4												2	2		2			4	1	2										19	494									
	4 Mason	4												3	3		3			4	1	2										16	416									
	5 Helper	12												2	12	2				4	4	2										53	1,365									
	6 Structural Foreman	1																1	1	1	1											3	78									
	7 Structural Fabricator/Fitter	2																2	2	2												8	208									
	8 Structural Welder	1																1	1	1	1											4	104									
	9 Rigger	6																2	6	2	2											12	312									
	10 Mech Foreman	2												2	2		2	2	1	2												10	260									
	11 Rigging Foreman	2												1	1				2	1	1	1	2					2				23	598									
	12 Piping Foreman	4												1	1		1			4	2	1										12	312									
	13 Welder	4												1	1		2	1	2	1								1				22	572									
	14 Fitter	12												12	12					4	4	2	12					12				94	2,444									
	15 Gas Cutter	4																1	4	2	2	1										10	260									
	16 Fitter/ Fabricator	8												8	2	6	2			8	4	2	1					1				70	1,820									
	17 Helper	16												12	4	12	2			12	16	16	4	12				12				124	3,224									
	18 Riggers	16												10	10				10	16	16	4	10					10				107	2,782									
	19 Technician	8												7	7	2			7	8	2	7						7				55	1,430									
	20 General Foreman	2												1	1		1			2	1	1	1					1				10	260									
	21 Instrument Foreman	2												2	2	2	2			2	2	1	2					2				23	598									
	22 Instrument Technician	6												4	6	4	4		2		4	2	4					4				51	1,326									
	23 Instrument Electrician	4												2	2		2	2	1	2								2				31	806									
	24 Al Welder	1												7	6	7	1				1	1										3	78									
	25 Instrument Fitter	7												7	6	7	1			7	2	7						7				63	1,638									
	26 Scaffolding Foreman	2												1	1					2	1	1	1					1				10	260									
	27 Scaffolders	20												10	10				10	10	10	10	10					10				90	2,340									
	28 Auto Electrician	2												1	1		1			1	2	1	1					1				10	260									
	29 Mechanic	2												1	1		1	1	1		1	1						1				15	390									
	30 Electrician	4												4			1	1	1		1	2	1									15	390									
2.3	Subcontractor Manpower																																-	-								
	1 Fireproofing	2																		2	2	2	2									8	208									
	2 NDT Works	3																		3	3	3	3									12	312									
2.4	Other Manpower																																-	-								
	1) Commissioning & Start-up	-																															-	-								
	2) Vendor Representatives	4																		2	2	4	2									10	260									
	Sub-Total	163	1	1	1	1	1	1	1	3	3	3	3	3	3	3	3	3	3	3	3	3	3									1,435	42,882									
166	Grand Total (Monthwise)	166	9	9	14	14	14	14	16	15	14	13	14	12	16	17	114	56	106	35	4	21	4	38	11	36	9	34	9	40	111	49	111	18	76	156	163	66	104		1,661	48,572

Note:

Water:

1. Above figures are tentative only. Required Manpower deployment during construction shall be actual, based on Engineering Qty estimation at later stage.


2. AHFC INHOUSE ENGINEERING TEAM will be Active till the end of the Project and will be made available on call basis

3. Construction Deployment will be reviewed further upon finalization of Execution Plan / Constructability Review

ATTACHMENT - 8

**MANPOWER MOBILIZATION
HISTOGRAM**

Archives from Personal Files

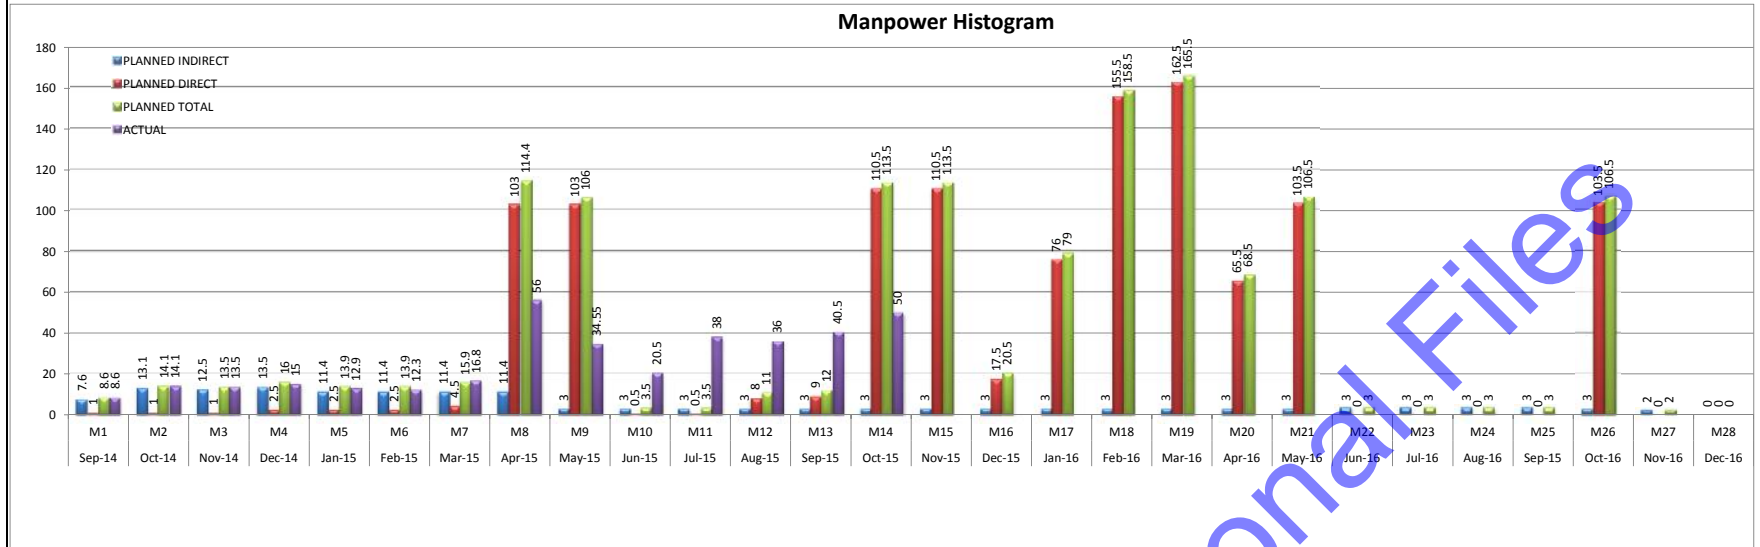

		Sep-14	Oct-14	Nov-14	Dec-14	Jan-15	Feb-15	Mar-15	Apr-15	May-15	Jun-15	Jul-15	Aug-15	Sep-15	Oct-15	Nov-15	Dec-15	Jan-16	Feb-16	Mar-16	Apr-16	May-16	Jun-16	Jul-16	Aug-16	Sep-16	Oct-16	Nov-16	Dec-16	Total Man months
Sr.	Description	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12	M13	M14	M15	M16	M17	M18	M19	M20	M21	M22	M23	M24	M25	M26	M27	M28	
	PLANNED INDIRECT	7.6	13.1	12.5	13.5	11.4	11.4	11.4	11.4	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	2		146.3
	ACTUAL INDIRECT	7.6	13.1	12.5	12.5	10.4	4.3	3.3	2.5	2.55	2.5	2.5	2.5	1	1															78.25
	PLANNED DIRECT	1	1	1	2.5	2.5	2.5	4.5	103	103	0.5	0.5	8	9	110.5	110.5	17.5	76	155.5	162.5	65.5	103.5					103.5			1144
	ACTUAL DIRECT	1	1	1	2.5	2.5	8	13.5	53.5	32	18	35.5	33.5	39.5	49															290.5
	TOTAL INDIRECT	8.6	14.1	13.5	16	13.9	13.9	15.9	114.4	106	3.5	3.5	11	12	113.5	113.5	20.5	79	158.5	165.5	68.5	106.5	3	3	3	3	106.5	2		1290.3
	TOTAL DIRECT	8.6	14.1	13.5	15	12.9	12.3	16.8	56	34.55	20.5	38	36	40.5	50															368.75

Note: Above figures are tentative only, Required Manpower deployment during construction shall be actual based on site requirement.

ATTACHMENT - 9

EQUIPMENT DEPLOYMENT

Archives from Personal Files

[illegible]

NOTE :

TENTATIVE LIST & SHALL BE FINALISED POST AWARD. HIRE ALSO INCLUDES POLICE / TARIF COMMITTEE VEHICLES

* TOOLS & CONSUMEABLES TO BE ADVISED DURING PRE-SHUTDOWN PERIOD

ATTACHMENT - 10

UPDATED SCHEDULE

Archives from Personal Files

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	REV Start	REV Finish	Start	Finish	2015												2016												2017														
									O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
5621_Revised Schedule_29 Oct 2015 Update			859	17-Sep-14	22-Jun-17	25-Sep-14	22-Jun-17	17-Sep-14 A	22-Jun-17																																					22-Jun-17	
PRELIMINARIES			7	17-Sep-14	24-Sep-14	25-Dec-14	01-Jan-15	17-Sep-14 A	24-Sep-14 A																																					24-Sep-14 A	
AH.PM.10000	Contract Award	0	17-Sep-14		25-Dec-14			17-Sep-14 A																																							
AH.PM.10020	Effective date of contract	0		24-Sep-14			01-Jan-15		24-Sep-14 A																																						
PROJECT MILESTONE COMPLETION SCHEDULE			655	21-Oct-14	13-Dec-16	15-Jan-15	13-Feb-17	15-Dec-14 A	18-Feb-17																																					18-Feb-17	
Engineering			248	21-Oct-14	09-Apr-15	31-Jan-15	07-Sep-15	15-Feb-15 A	15-Nov-15																																					15-Nov-15	
AH.EN.M1100	COMPLETE SITE SURVEY AND SUBMIT FINAL REPORT	0		21-Oct-14			28-Mar-15		28-Feb-15 A																																						
AH.EN.M1120	ISSUE DESIGN BASIS MEMORANDUM FOR ALL DISCIPLINES, AFTER COMPANY REVIEW, FINAL ISSUE	0		05-Apr-15			06-Jul-15		15-Feb-15 A																																						
AH.EN.M1125	ISSUE PLOT PLAN, PFDs & P&IDs FOR HAZOP REVIEW	0		24-Mar-15			18-Feb-15		18-Feb-15 A																																						
AH.EN.M1130	COMPLETE HAZOP / SIL REVIEW AND ISSUE FINAL REPORT TO COMPANY	0		26-Mar-15			20-Apr-15		20-Apr-15 A																																						
AH.EN.M1140	ISSUE TIE-IN AND SHUTDOWN PHILOSOPHY FOR COMPANY APPROVAL	0		15-Jan-15			31-Jan-15		15-Feb-15 A																																						
AH.EN.M1150	ISSUE STRESS ANALYSIS REPORT (FINAL)	0		09-Apr-15			22-Jul-15		28-Mar-15 A																																						
AH.EN.M1160	ISSUE GA's ISOMETRICS AND PIPE SUPPORT DRAWINGS FOR PIPING MODIFICATIONS, TIE-IN WORKS (IFC), ALSO EXISTING PLANT DWGS	0		31-Mar-15			28-May-15		25-Jun-15 A																																						
AH.EN.M1170	ISSUE ALL CIVIL / RCC DRAWINGS INCL. PAVING DETAILS AND CABLE TRENCHES (IFC), ALSO UPDATING EXISTING PLANT DWGS	0		28-Mar-15			28-May-15		23-Jun-15 A																																						
AH.EN.M1180	ISSUE STRUCTURAL STEEL FABRICATION AND INSTALLATION DETAILS FOR ALL FACILITIES (IFC)	0		11-Mar-15			23-Jun-15		23-Jun-15 A																																						
AH.EN.M1190	ISSUE E&I DWGS INCL. CABLE SCH, LAYOUTS, TRAY/SUPPORTS & IPS/DCS MODIFICATIONS, I&C INDEX FOR CONST (IFC), UPDATE	0		21-Mar-15			16-Aug-15		15-Nov-15																																						
AH.EN.M1200	ISSUE ALL HSE DELIVERABLES INCLUDING UPDATING HSE PLAN AND HSE PHILOSOPHY (IFC) AND COMP. SIMOPS & HAZID REVIEWS	0		04-Mar-15			07-Sep-15		04-Aug-15 A																																						
AH.EN.M1210	COMPLETE CONSTRUCTABILITY REVIEW AND SUBMIT FINAL REPORT AFTER INCORPORATING COMPANY COMMENTS	0		25-Mar-15			22-Jun-15		23-Jun-15 A																																						
Procurement & Delivery			398	02-Dec-14	17-Nov-15	15-Jan-15	29-Feb-16	15-Dec-14 A	24-Apr-16																																					24-Apr-16	
AH.EN.M1220	ISSUE P.O FOR ALL SDT VALVS / ACTUATORS - 23 SETS	0		18-Jan-15			08-Apr-15		28-Feb-15 A																																						
AH.EN.M1230	ISSUE P.O FOR 28 NOS. OF ACTUATORS A FOR CAI VALVES	0		02-Dec-14			15-Jan-15		15-Dec-14 A																																						
AH.EN.M1240	ISSUE P.O FOR E&I CABLES	0		27-Apr-15			05-Aug-15		27-Jul-15 A																																						
AH.EN.M1250	RECEIVE ALL SDT VALVES / ACTUATORS SET AT SITE	0		12-Oct-15			03-Feb-16		08-Feb-16																																						
AH.EN.M1260	RECEIVE ALL ACTUATORS FOR CAI VALVES	0		14-Apr-15			26-Sep-15		24-Sep-15 A																																						
AH.EN.M1270	RECEIVE ALL E&I CABLES AT SITE	0		07-Nov-15			22-Nov-15		21-Nov-15																																						
AH.EN.M1280	SUBMIT G-SPIRS TO COMPANY AND PLACE ORDERS FOR ALL ITEMS AFTER OBTAINING COMAPNY APPROVAL	0		25-Jan-15			18-Oct-15		29-Oct-15																																						

5621 - Buhasa Replacement of ESD Valves and Actuators_ Monthly Updated SCHEDULE (October, 2015)

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	REV Start	REV Finish	Start	Finish	2015												2016												2017																		
									O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N					
AH.EN.M1290	RECEIVE INSURANCE / COMMISSIONING AND OPERATING SPARES FOR EQUIPMENTS & PACKAGES AT SITE & HANDOVER TO COMPANY	0		04-Sep-15			24-Jan-16	24-Apr-16																																											
AH.EN.M1450	COMPLETE TESTING OF VALVES AFTER SHIPPING	0		17-Nov-15			29-Feb-16	29-Oct-15																																											
Construction / Commissioning Works		410	13-Feb-16	13-Dec-16	30-Jul-15	13-Feb-17	29-Oct-15	18-Feb-17																																											
AH.EN.M1300	COMPLETE CIVIL WORKS FOR ALL SLOPE PROTECTION, CABLE TRENCHES & DUCTS AND FOUNDATIONS	0		06-Apr-16			07-May-16	07-May-16																																											
AH.EN.M1310	COMPLETE FABRICATION AND INSTALLATION OF ALL STRUCTURAL STEEL WORKS	0		13-Feb-16			30-Jul-15	29-Oct-15																																											
AH.EN.M1320	COMPLETE ROADS, PAVING, ROAD SIGNAGE AND RE-HABILITATION IF DISTURBED	0		30-Jun-16			01-Aug-16	01-Aug-16																																											
AH.EN.M1330	COMPLETE RE-HABILITATION OF ANY TEMP. OR PERMANENT E&I FACILITIES IF DISTURBED	0		12-Oct-16			08-Jun-16	08-Jun-16																																											
AH.EN.M1340	COMPLETE REROUTING OF EXISTING UNDERGROUND CABLES & PIPING	0		29-Feb-16			08-Jun-16	08-Jun-16																																											
AH.EN.M1350	COMPLETE INSTALLATION OF 28 NOS. OF NEW CAI ACTUATORS DULY HOOKED UP TO THE EXISTING IPS/DCS CONTROL SYSTEM	0		15-Oct-16			16-Oct-16	15-Oct-16																																											
AH.EN.M1360	COMPLETE INSTALLATION OF 23 DOUBLE ACTING VALVES AND ACTUATORS DULY HOOKED UP TO THE EXISTING IPS/DCS CONTROL SYSTEM	0		12-Mar-16			12-Apr-16	12-Apr-16																																											
AH.EN.M1370	COMPLETE INSTALLATION OF ALL FIELD INSTRUMENTS, CABLING AND PIPING WORKS	0		12-Mar-16			12-Apr-16	12-Apr-16																																											
AH.EN.M1380	COMPLETE ALL DCS MODIFICATION WORKS	0		05-Apr-16			07-May-16	07-May-16																																											
AH.EN.M1410	ACHIEVE MECHANICAL COMPLETION FOR TRAIN - 1	0		18-Oct-16			17-Dec-16	15-Oct-16																																											
AH.EN.M1415	ACHIEVE MECHANICAL COMPLETION FOR TRAIN - 2	0		15-Oct-16			16-Oct-16	15-Oct-16																																											
AH.EN.M1420	COMPLETE DEMOLITION OF ALL OBSOLETE VALVES AND ACTUATORS AND ANY OTHER REDUNTANT MATERIAL / EQUIPMENT	0		15-Oct-16			16-Oct-16	15-Oct-16																																											
AH.EN.M1430	COMPLETE ALL COMMISSIONING, TEST RUN AND ACHIEVE PAC	0		13-Dec-16			13-Feb-17	18-Feb-17																																											
AH.EN.M1440	SUBMIT FINAL DOSSIER / AS BUILT DOCUMENTATIONS / COMMISSIONING AND OPERATING SPARES	0		22-Nov-16			23-Jan-17	07-Jan-17																																											
One Day Shutdowns		549	15-Apr-15	15-Oct-16	15-Apr-15	15-Oct-16	15-Apr-15 A	15-Oct-16																																											
AH.SD.M1000	ONE DAY SHUTDOWN FOR TRAIN - 1 No. 01	0	15-Apr-15		15-Apr-15		15-Apr-15 A																																												
AH.SD.M1010	ONE DAY SHUTDOWN FOR TRAIN - 1 No. 02	0	15-Oct-15		15-Oct-15		11-Oct-15 A																																												
AH.SD.M1030	ONE DAY SHUTDOWN FOR TRAIN - 2 No. 01	0	15-May-15		15-May-15		15-May-15 A																																												
AH.SD.M1040	ONE DAY SHUTDOWN FOR TRAIN - 2 No. 02	0	15-Nov-15		15-Nov-15		15-Nov-15																																												
AH.SD.M1050	ONE DAY SHUTDOWN FOR TRAIN - 1 No. 03	0	15-Oct-16		15-Oct-16		15-Oct-16																																												
AH.SD.M1060	ONE DAY SHUTDOWN FOR TRAIN - 2 No. 03	0	15-May-16		15-May-16		15-May-16																																												
DETAILED ENGINEERING		376	25-Sep-14	28-Apr-15	25-Sep-14	07-Sep-15	25-Sep-14 A	07-Dec-15																																											
General / Project Management		376	25-Sep-14	28-Apr-15	25-Sep-14	07-Sep-15	25-Sep-14 A	07-Dec-15																																											
A1000	Engineering Design Project Start	0	25-Sep-14		03-Jan-15		25-Sep-14 A																																												
A1010	Mobilization Engineering Design Team	10	25-Sep-14	06-Oct-14	25-Sep-14	06-Oct-14	25-Sep-14 A	06-Oct-14 A																																											

■ Actual Work
 ■ Critic...
 ■ Remaining Work
 ◆ Milest...

Page 2 of 22

Date

Revision

Checked

Approved

29-Oct-15

Monthly Updated Schedule _ October, 2015

SZ

RC

[illegible]

5621 - Buhasa Replacement of ESD Valves and Actuators_ Monthly Updated SCHEDULE (October, 2015)

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	REV Start	REV Finish	Start	Finish		O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D					
A1425	TBE for SDT Valves & Actuators	13	18-Nov-14	02-Dec-14	05-Jan-15	19-Jan-15	11-Dec-14 A	23-Mar-15 A																																													
A1428	Instrument Index Final Issue	53	10-Dec-14	09-Feb-15	27-Jan-15	29-Mar-15	04-Nov-14 A	18-Jun-15 A																																													
A1435	I/O List - DCS Final Issue	52	22-Dec-14	19-Feb-15	25-Jan-15	25-Mar-15	06-Nov-14 A	12-Nov-15																																													
A1438	I/O List - ESD Final ISSUE	52	22-Dec-14	19-Feb-15	25-Jan-15	25-Mar-15	06-Nov-14 A	11-Jun-15 A																																													
A1440	Scope of Work for Existing DCS & ESD Modifications Final Issue	60	03-Jan-15	12-Mar-15	25-Jan-15	04-Apr-15	06-Nov-14 A	15-Nov-15																																													
A1450	Addendum to Specification DGS-1543-002 ESD & On-Off valves Final Issue	45	10-Nov-14	31-Dec-14	03-Jan-15	23-Feb-15	11-Nov-14 A	14-Jan-15 A																																													
A1530	Instrument Cable Block Diagrams (DCS & ESD) Final Issue	53	09-Dec-14	08-Feb-15	24-Jan-15	25-Mar-15	13-Jan-15 A	25-May-15 A																																													
A1540	Instrument Location Layout Final Issue	54	03-Dec-14	03-Feb-15	18-Jan-15	21-Mar-15	13-Jan-15 A	25-May-15 A																																													
A1550	Main Instrument Cable Routing Layout Final Issue	54	14-Dec-14	14-Feb-15	28-Jan-15	31-Mar-15	13-Jan-15 A	25-May-15 A																																													
A1565	Instrument Loop Diagrams - DCS Final Issue	40	28-Dec-14	28-Feb-15	11-Feb-15	29-Mar-15	11-Jan-15 A	09-Nov-15																																													
A1570	Instrument Loop Diagrams - ESD Final Issue	40	28-Dec-14	28-Feb-15	11-Feb-15	29-Mar-15	13-Jan-15 A	08-Jun-15 A																																													
A1580	Instrument Cable Schedule Final Issue	50	22-Dec-14	17-Feb-15	05-Feb-15	04-Apr-15	04-Jan-15 A	11-Jun-15 A																																													
A1582	Instrument JB Schedule Final Issue	43	30-Dec-14	04-Mar-15	14-Feb-15	04-Apr-15	04-Jan-15 A	11-Jun-15 A																																													
A1590	JB Wiring Diagrams Final Issue	40	30-Dec-14	08-Mar-15	14-Feb-15	31-Mar-15	14-Jan-15 A	10-May-15 A																																													
A1600	Interpanel Wiring Diagrams Final Issue	40	30-Dec-14	08-Mar-15	14-Feb-15	31-Mar-15	05-Jan-15 A	05-Jan-15 A																																													
A1610	Instrument Installation Diagrams Final Issue	40	30-Dec-14	08-Mar-15	14-Feb-15	31-Mar-15	13-Jan-15 A	25-May-15 A																																													
A1620	Pneumatic Instrument Hook-Up Diagrams Final Issue	42	30-Dec-14	08-Mar-15	14-Feb-15	02-Apr-15	13-Jan-15 A	11-Aug-15 A																																													
A1630	Instrument Bulk Material Take Off Final Issue	25	11-Jan-15	21-Mar-15	25-Feb-15	25-Mar-15	15-Jan-15 A	10-Aug-15 A																																													
A1790	General Instrument Specifications	60	10-Dec-14	17-Feb-15	12-Mar-15	20-May-15	04-Feb-15 A	20-May-15 A																																													
HSE		139	15-Nov-14	04-Mar-15	24-Jan-15	04-Jul-15	20-Nov-14 A	10-Nov-15																																													
A1640	HSE Plan Review and Final Issue	58	15-Nov-14	20-Jan-15	24-Jan-15	31-Mar-15	20-Nov-14 A	02-Feb-15 A																																													
A1650	HSE Philosophy Review and Final Issue	63	08-Dec-14	18-Feb-15	24-Jan-15	06-Apr-15	10-Jan-15 A	04-Mar-15 A																																													
A1660	HAZID Procedure Review and Final Issue	60	20-Dec-14	26-Feb-15	04-Feb-15	14-Apr-15	27-Nov-14 A	04-Mar-15 A																																													
A1670	HAZID Report Review and Final Issue	35	30-Dec-14	03-Mar-15	30-Apr-15	09-Jun-15	03-Mar-15 A	20-Apr-15 A																																													
A1680	HAZID Close-out Report Review and Final Issue	30	06-Jan-15	09-Feb-15	30-Apr-15	03-Jun-15	28-Apr-15 A	10-Nov-15																																													
A1690	HSE Action Tracking Register and Final Issue	20	10-Feb-15	04-Mar-15	11-Jun-15	04-Jul-15	05-Apr-15 A	05-Nov-15																																													

■ Actual Work
 ■ Critic...
 ■ Remaining Work
 ◆ Milest...

Page 4 of 22

Date

29-Oct-15

Revision

Monthly Updated Schedule _ October, 2015

Checked

SZ

Approved

RC

5621 - Buhasa Replacement of ESD Valves and Actuators_ Monthly Updated SCHEDULE (October, 2015)

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	REV Start	REV Finish	Start	Finish	2015												2016												2017														
									O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
Civil/Structural									16-Jun-15 A																																						
A1700	Project specifications (including all Addendums to Civil and Structural DGS) Final Issue	60	03-Nov-14	11-Jan-15	12-Jan-15	22-Mar-15	10-Nov-14 A	07-Dec-14 A																																							
A1710	Adequacy study of existing structures & their foundations and modifications Final Issue	50	17-Nov-14	13-Jan-15	24-Jan-15	22-Mar-15	14-Jan-15 A	22-Apr-15 A																																							
A1720	G.A. and reinforcement details of Foundations Final Issue	20	02-Dec-14	09-Feb-15	30-Apr-15	23-May-15	15-May-15 A	16-Jun-15 A																																							
A1730	Civil/ Structural Design Criteria Final Issue	58	23-Nov-14	28-Jan-15	01-Feb-15	08-Apr-15	26-Nov-14 A	25-Dec-14 A																																							
A1740	Modified Structural steel layout plan, elevations and details- where required Final Issue	60	04-Dec-14	11-Feb-15	10-Feb-15	20-Apr-15	04-Jan-15 A	14-Jun-15 A																																							
A1750	Demolition Layout Plan as required Final Issue	65	06-Jan-15	22-Mar-15	15-Mar-15	28-May-15	07-Jan-15 A	23-Mar-15 A																																							
A1760	GA and Reinf. Detail of Pipe Support Foundations (as required) Final Issue	58	15-Dec-14	19-Feb-15	21-Feb-15	28-Apr-15	04-Jan-15 A	16-Jun-15 A																																							
A1770	G.A. and Reinf. Details Foundation for Platforms and Crossovers (as required) Final Issue	50	29-Jan-15	28-Mar-15	28-Feb-15	26-Apr-15	28-Feb-15 A	23-Mar-15 A																																							
A1780	Pipe Supports Details Final Issue	40	27-Nov-14	12-Jan-15	03-Feb-15	21-Mar-15	04-Jan-15 A	16-Jun-15 A																																							
A1800	Foundation Layout Plan Final Issue	57	17-Nov-14	21-Jan-15	24-Jan-15	30-Mar-15	04-Jan-15 A	16-Jun-15 A																																							
A1810	General Notes Civil Works Final Issue	53	01-Dec-14	31-Jan-15	26-Jan-15	28-Mar-15	16-Nov-14 A	25-Dec-14 A																																							
A1820	General Notes Structural Works Final Issue	53	08-Dec-14	07-Feb-15	02-Feb-15	04-Apr-15	16-Nov-14 A	25-Dec-14 A																																							
A1830	Roads and Paving Details Final Issue	53	31-Dec-14	02-Mar-15	25-Feb-15	27-Apr-15	16-Nov-14 A	25-Dec-14 A																																							
A1840	Ladder Standard Details and Foundation Final Issue	70	21-Dec-14	11-Mar-15	15-Feb-15	06-May-15	16-Nov-14 A	25-Dec-14 A																																							
A1850	Standard Details Concrete Protection Final Issue	63	03-Jan-15	16-Mar-15	28-Feb-15	11-May-15	16-Nov-14 A	25-Dec-14 A																																							
PROCUREMENT		410	10-Nov-14	07-Nov-15	03-Jan-15	19-Feb-16	18-Nov-14 A	24-Apr-16	24-Apr-16																																						
Bulk material		260	05-Jan-15	07-Nov-15	31-Jan-15	22-Nov-15	20-Jan-15 A	21-Nov-15	21-Nov-15																																						
Civil Bulk Material		71	17-Feb-15	26-Aug-15	30-Jul-15	20-Oct-15	30-Jul-15 A	21-Sep-15 A	21-Sep-15 A																																						
AH.PR.CA.1(Prepare / Issue RFQ_Bulk Civil & Structural Mat'l		6	17-Feb-15	23-Feb-15	30-Jul-15	05-Aug-15	30-Jul-15 A	05-Aug-15 A																																							
AH.PR.CA.1(Receive Bids_Bulk Civil & Structural Mat'l		6	24-Feb-15	14-Mar-15	06-Aug-15	12-Aug-15	06-Aug-15 A	12-Aug-15 A																																							
AH.PR.CA.1(Issue LOA/ FOA_Bulk Civil & Structural Mat'l		6	15-Mar-15	21-Mar-15	13-Aug-15	19-Aug-15	13-Aug-15 A	26-Aug-15 A																																							
AH.PR.CA.1(Receive & Approve Vendor drawings_Bulk Civil & Structural		10	22-Mar-15	08-Apr-15	20-Aug-15	31-Aug-15	29-Aug-15 A	15-Sep-15 A																																							
AH.PR.CA.1(Complete Manufacturing and Final inspection_Bulk Civil & Structural Mat'l		20	09-Apr-15	17-Jul-15	01-Sep-15	20-Sep-15	01-Sep-15 A	20-Sep-15 A																																							
AH.PR.CA.1(Shipping, Transportation and Receipt at Site_Bulk Civil & Structural Mat'l		10	29-Apr-15	26-Aug-15	11-Oct-15	20-Oct-15	20-Sep-15 A	21-Sep-15 A																																							
Instrumentation Bulk Material		156	26-Mar-15	07-Nov-15	28-May-15	22-Nov-15	28-May-15 A	21-Nov-15	21-Nov-15																																						
AH.PR.CI.1(Prepare / Issue RFQ_Bulk Instrumentation material		6	26-Mar-15	01-Apr-15	28-May-15	03-Jun-15	28-May-15 A	03-Jun-15 A																																							

■ Actual Work
 ■ Critic...
 ■ Remaining Work
 ◆ Milest...

Page 5 of 22

Date

29-Oct-15

Revision

Monthly Updated Schedule _ October, 2015

Checked

SZ

Approved

RC



Actual Work Remaining Work Critic... Milest...	Page 6 of 22	Date 29-Oct-15	Revision Monthly Updated Schedule _October, 2015	Checked SZ	Approved RC
--	--------------	--------------------------------------	--	----------------------------------	-----------------------------------

5621 - Buhasa Replacement of ESD Valves and Actuators_ Monthly Updated SCHEDULE (October, 2015)

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	REV Start	REV Finish	Start	Finish	2015												2016												2017																				
									O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N							
	AH.PR.CI.10 Data sheet approval for Manufacturing_SDT Valves with Actuators	10			17-Aug-15	27-Aug-15	01-Aug-15 A	09-Aug-15 A																																													
	AH.PR.CI.10 Assembly of Complete ESD Valve and Actuator_SDT Valves with Actuators	40			29-Aug-15	05-Nov-15	29-Sep-15 A	03-Dec-15																																													
	AH.PR.CI.10 Assembly of ESD Valve and Rotork Actuator_SDT Valves with Actuators	40			07-Nov-15	22-Dec-15	14-Oct-15 A	27-Dec-15																																													
	AH.PR.CI.10 Shipping, Transportation and Receipt at Site_SDT Valves with Actuators	30	16-Aug-15	29-Sep-15	23-Dec-15	21-Jan-16	28-Dec-15	26-Jan-16																																													
	AH.PR.CI.1 Valve Testing works for recieved SDT valves	16	13-Oct-15	28-Oct-15	04-Feb-16	19-Feb-16	09-Feb-16	24-Feb-16																																													
	CAI Actuators	131	10-Nov-14	11-Apr-15	03-Jan-15	03-Jun-15	18-Nov-14 A	24-Sep-15 A																																													
	AH.PR.CI.10 Prepare / Issue RFQ_Actuators for CAI Valves.	4	10-Nov-14	13-Nov-14	03-Jan-15	06-Jan-15	18-Nov-14 A	29-Nov-14 A																																													
	AH.PR.CI.10 Receive Bids_Actuators for CAI Valves.	2	12-Nov-14	13-Nov-14	05-Jan-15	06-Jan-15	02-Dec-14 A	02-Dec-14 A																																													
	AH.PR.CI.10 Submit Technical Bid Evaluation (TBE) for Company Approval	4	30-Nov-14	03-Dec-14	17-Jan-15	20-Jan-15	05-Dec-14 A	10-Dec-14 A																																													
	AH.PR.CI.10 Issue LOA/ FOA_Actuators for CAI Valves.	2	01-Dec-14	02-Dec-14	18-Jan-15	19-Jan-15	15-Dec-14 A	15-Dec-14 A																																													
	AH.PR.CI.10 Receive & Approve Vendor drawings_Actuators for CAI Valves.	7	03-Dec-14	10-Dec-14	17-Jan-15	24-Jan-15	04-Jan-15 A	21-Mar-15 A																																													
	AH.PR.CI.10 Complete Manufacturing and Final inspection_Actuators for CAI Valves.	87	11-Dec-14	07-Mar-15	22-Feb-15	19-May-15	10-Feb-15 A	18-Aug-15 A																																													
	AH.PR.CI.10 Shipping, Transportation and Receipt at Site_Actuators for CAI Valves.	35	08-Mar-15	11-Apr-15	30-Apr-15	03-Jun-15	06-Apr-15 A	24-Sep-15 A																																													
	Operating spares	338	10-Nov-14	04-Sep-15	28-Mar-15	24-Jan-16	15-Dec-14 A	24-Apr-16																																													
	AH.PR.CI.10 Prepare / Issue RFQ_Operational Spares	6	10-Nov-14	16-Nov-14	28-Mar-15	02-Apr-15	28-Feb-15 A	28-Feb-15 A																																													
	AH.PR.CI.10 Receive Bids_Operational Spares	6	17-Nov-14	23-Nov-14	04-Apr-15	09-Apr-15	28-Feb-15 A	05-Mar-15 A																																													
	AH.PR.CI.10 Submit Technical Bid Evaluation (TBE) for Company Approval	38	24-Nov-14	06-Jan-15	11-Apr-15	24-May-15	11-Apr-15 A	12-Apr-15 A																																													
	AH.PR.CI.10 Issue LOA/ FOA_Operational Spares	6	07-Jan-15	13-Jan-15	30-Apr-15	06-May-15	15-Dec-14 A	28-Feb-15 A																																													
	AH.PR.CI.10 Receive & Approve Vendor drawings_Operational Spares	16	14-Jan-15	01-Feb-15	30-Apr-15	18-May-15	30-Apr-15 A	18-May-15 A																																													
	AH.PR.CI.10 Complete Manufacturing and Final inspection_Operational Spares	180	02-Feb-15	31-Jul-15	28-May-15	23-Nov-15	28-May-15 A	20-Mar-16																																													
	AH.PR.CI.10 Shipping, Transportation and Receipt at Site_Operational Spares	35	01-Aug-15	04-Sep-15	21-Dec-15	24-Jan-16	21-Mar-16	24-Apr-16																																													
	SUB-CONTRACTING SERVICES	353	24-Sep-14	10-Nov-15	25-Dec-14	12-Jan-16	24-Sep-14 A	22-Feb-16																																													
	Design Engineering services	0	24-Sep-14	25-Sep-14	25-Dec-14	25-Dec-14	24-Sep-14 A	25-Dec-14 A																																													
	AH.PR.SC.1012 Receive Company Approval-Design Engineering Services	0		24-Sep-14		25-Dec-14		24-Sep-14 A																																													
	AH.PR.SC.1013 Issue LOA/ FOA-Design Engineering Services	0	25-Sep-14	25-Sep-14	25-Dec-14	25-Dec-14	25-Dec-14 A	25-Dec-14 A																																													
	DCS Modification	27	09-Mar-15	02-Apr-15	27-May-15	28-Jun-15	12-Feb-15 A	22-May-15 A																																													
	AH.PR.SC.1014 Prepare / Issue RFQ-DCS Modification Services	7	09-Mar-15	16-Mar-15	07-Jun-15	14-Jun-15	12-Feb-15 A	23-Feb-15 A																																													
	AH.PR.SC.1015 Receive Bids-DCS Modification Services	7	10-Mar-15	17-Mar-15	08-Jun-15	15-Jun-15	16-Feb-15 A	01-Mar-15 A																																													

■ Actual Work
 ■ Critic...
 ■ Remaining Work
 ◆ Milest...

Page 7 of 22

Date

29-Oct-15

Revision


Monthly Updated Schedule _ October, 2015

Checked

SZ


Approved

RC

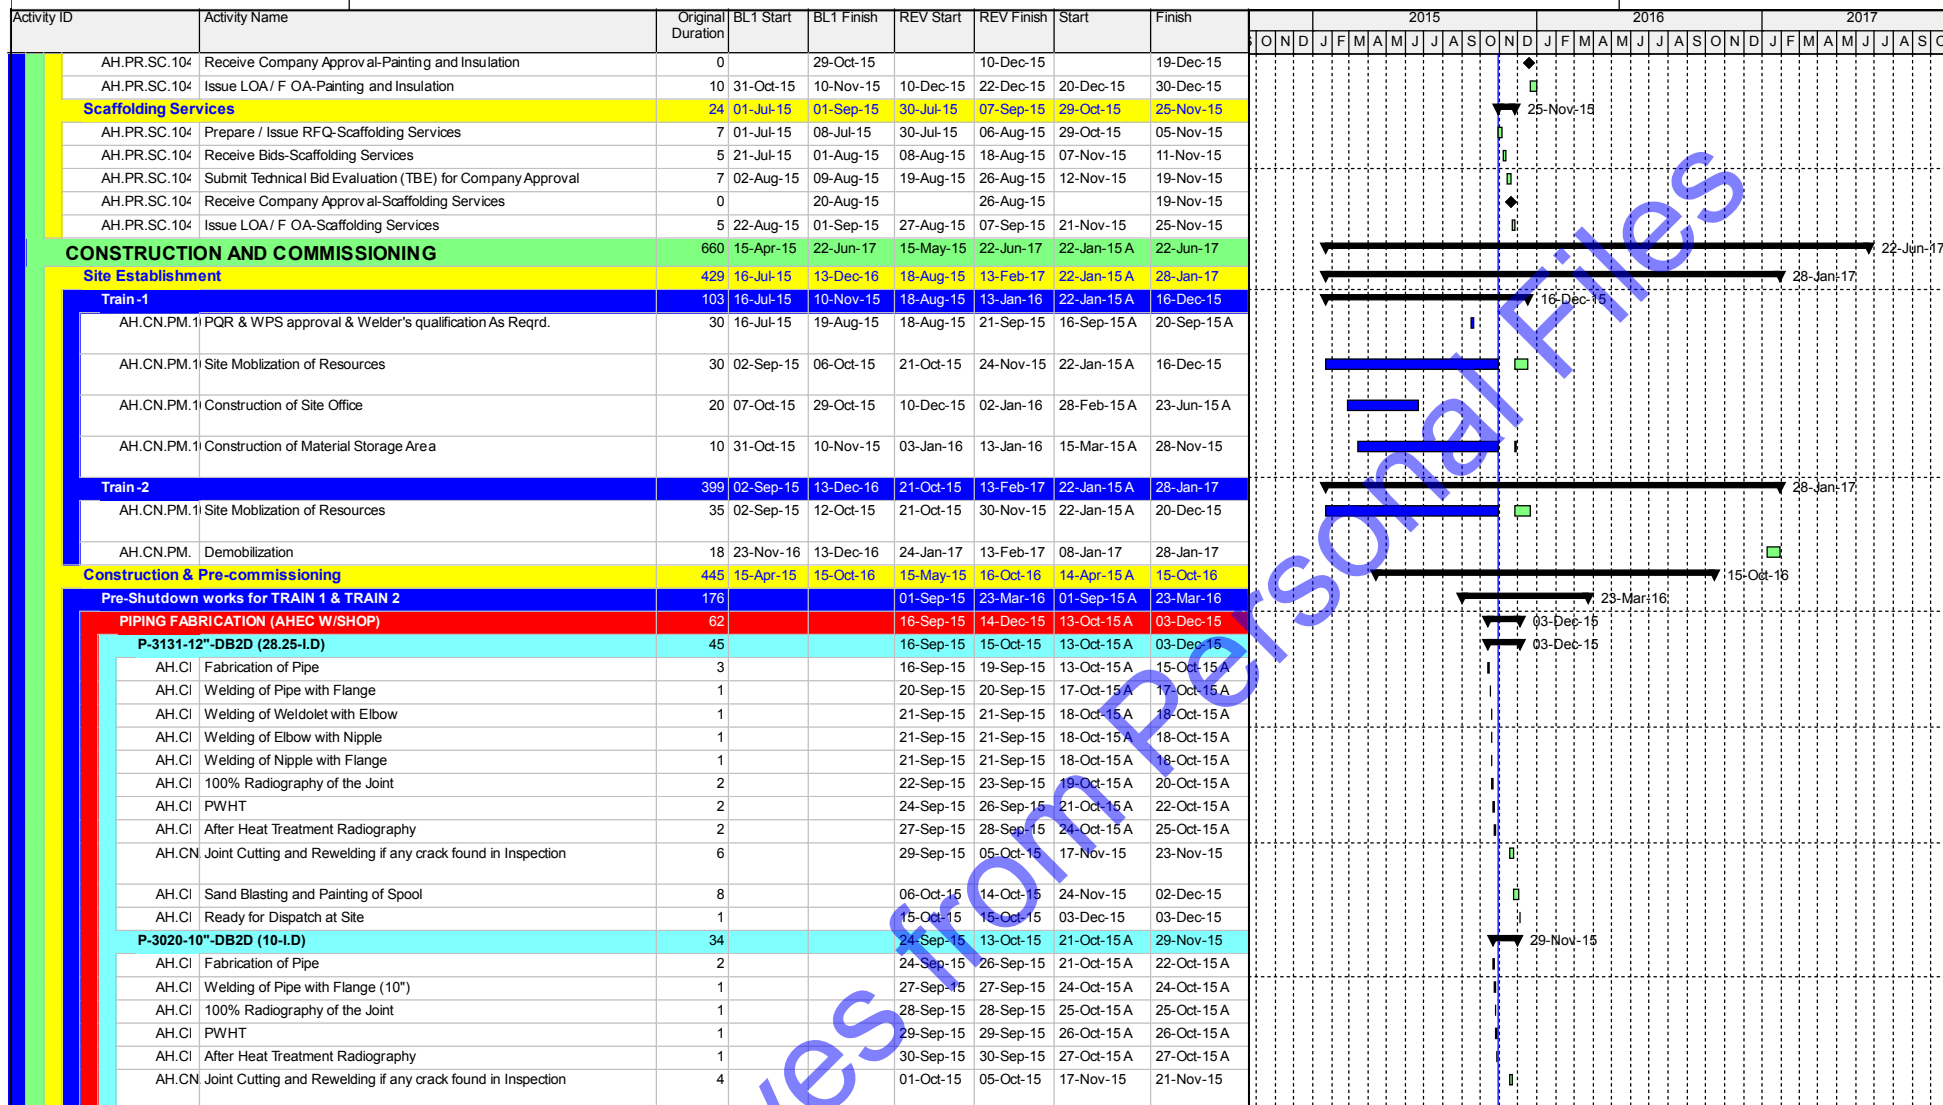

Actual Work Remaining Work Critic... Milest...	Page 10 of 22 Date Revision Checked Approved
29-Oct-15 Monthly Updated Schedule _ October, 2015	SZ RC

[illegible]

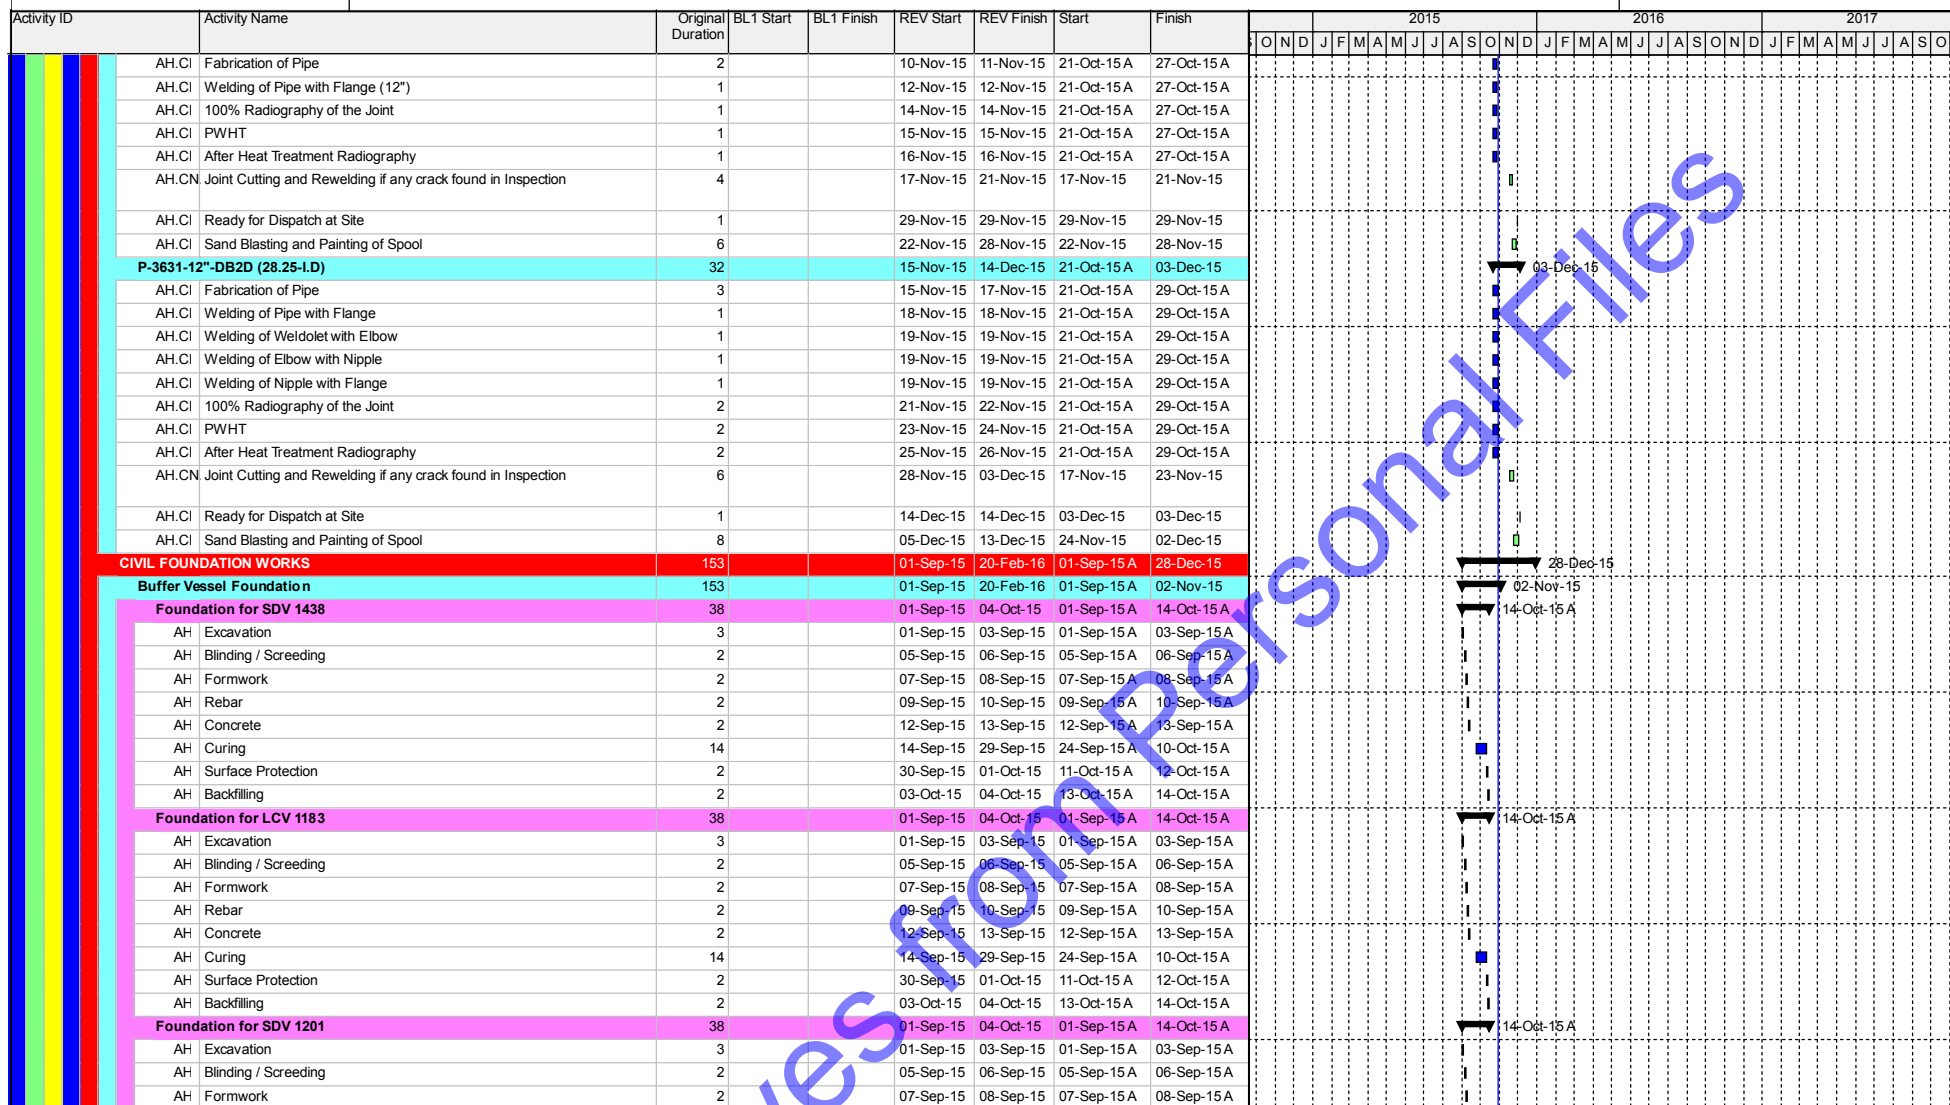

Actual Work Remaining Work Critic... Milest...	Page 13 of 22 Date 29-Oct-15 Revision Monthly Updated Schedule _ October, 2015 Checked SZ Approved RC
---	---

Activity	Duration (Days)	Start Date	End Date	Activity	Duration (Days)	Start Date	End Date
AH Rebar	2	16-Nov-15	17-Nov-15	01-Oct-15 A	21-Oct-15 A		
AH Concrete	2	18-Nov-15	19-Nov-15	01-Oct-15 A	21-Oct-15 A		
AH Curing	14	21-Nov-15	06-Dec-15	01-Oct-15 A	21-Oct-15 A		
AH Surface Protection	2	07-Dec-15	08-Dec-15	01-Oct-15 A	21-Oct-15 A		
AH Backfilling	2	09-Dec-15	10-Dec-15	01-Oct-15 A	21-Oct-15 A		
Foundation for SDV 1003	29	12-Dec-15	13-Jan-16	01-Oct-15 A	17-Oct-15 A		
AH Excavation	3	12-Dec-15	14-Dec-15	01-Oct-15 A	17-Oct-15 A		
AH Blinding / Screeding	2	15-Dec-15	16-Dec-15	01-Oct-15 A	17-Oct-15 A		
AH Formwork	2	17-Dec-15	19-Dec-15	01-Oct-15 A	17-Oct-15 A		
AH Rebar	2	20-Dec-15	21-Dec-15	01-Oct-15 A	17-Oct-15 A		
AH Concrete	2	22-Dec-15	23-Dec-15	01-Oct-15 A	17-Oct-15 A		
AH Curing	14	24-Dec-15	09-Jan-16	01-Oct-15 A	17-Oct-15 A		
AH Surface Protection	2	10-Jan-16	11-Jan-16	01-Oct-15 A	17-Oct-15 A		
AH Backfilling	2	12-Jan-16	13-Jan-16	01-Oct-15 A	17-Oct-15 A		
Foundation for SDV 1184	29	12-Dec-15	13-Jan-16	06-Oct-15 A	23-Oct-15 A		
AH Excavation	3	12-Dec-15	14-Dec-15	06-Oct-15 A	23-Oct-15 A		
AH Blinding / Screeding	2	15-Dec-15	16-Dec-15	06-Oct-15 A	23-Oct-15 A		
AH Formwork	2	17-Dec-15	19-Dec-15	06-Oct-15 A	23-Oct-15 A		
AH Rebar	2	20-Dec-15	21-Dec-15	06-Oct-15 A	23-Oct-15 A		
AH Concrete	2	22-Dec-15	23-Dec-15	06-Oct-15 A	23-Oct-15 A		
AH Curing	14	24-Dec-15	09-Jan-16	06-Oct-15 A	23-Oct-15 A		
AH Surface Protection	2	10-Jan-16	11-Jan-16	06-Oct-15 A	23-Oct-15 A		
AH Backfilling	2	12-Jan-16	13-Jan-16	06-Oct-15 A	23-Oct-15 A		
Foundation for SDV 2003	29	05-Oct-15	07-Nov-15	15-Oct-15 A	27-Oct-15 A		
AH Excavation	3	05-Oct-15	07-Oct-15	15-Oct-15 A	18-Oct-15 A		
AH Blinding / Screeding	2	08-Oct-15	10-Oct-15	19-Oct-15 A	20-Oct-15 A		
AH Formwork	2	11-Oct-15	12-Oct-15	19-Oct-15 A	22-Oct-15 A		
AH Rebar	2	13-Oct-15	14-Oct-15	19-Oct-15 A	25-Oct-15 A		
AH Concrete	2	15-Oct-15	17-Oct-15	19-Oct-15 A	27-Oct-15 A		
AH Curing	14	18-Oct-15	02-Nov-15	19-Oct-15 A	27-Oct-15 A		
AH Surface Protection	2	03-Nov-15	04-Nov-15	19-Oct-15 A	27-Oct-15 A		
AH Backfilling	2	05-Nov-15	07-Nov-15	19-Oct-15 A	27-Oct-15 A		
Foundation for SDV 2184	29	05-Oct-15	07-Nov-15	15-Oct-15 A	27-Oct-15 A		
AH Excavation	3	05-Oct-15	07-Oct-15	15-Oct-15 A	18-Oct-15 A		
AH Blinding / Screeding	2	08-Oct-15	10-Oct-15	19-Oct-15 A	20-Oct-15 A		
AH Formwork	2	11-Oct-15	12-Oct-15	19-Oct-15 A	22-Oct-15 A		
AH Rebar	2	13-Oct-15	14-Oct-15	19-Oct-15 A	25-Oct-15 A		
AH Concrete	2	15-Oct-15	17-Oct-15	19-Oct-15 A	27-Oct-15 A		
AH Curing	14	18-Oct-15	02-Nov-15	19-Oct-15 A	27-Oct-15 A		
AH Surface Protection	2	03-Nov-15	04-Nov-15	19-Oct-15 A	27-Oct-15 A		
AH Backfilling	2	05-Nov-15	07-Nov-15	19-Oct-15 A	27-Oct-15 A		
Foundation for SDV 2183	29	05-Oct-15	07-Nov-15	15-Oct-15 A	27-Oct-15 A		
AH Excavation	3	05-Oct-15	07-Oct-15	15-Oct-15 A	18-Oct-15 A		
AH Blinding / Screeding	2	08-Oct-15	10-Oct-15	19-Oct-15 A	20-Oct-15 A		

[illegible]



 Actual Work  Critic...
 Remaining Work   Milest...

Actual Work Remaining Work Critic... Milest...	Page 17 of 22 Date 29-Oct-15 Revision Monthly Updated Schedule _ October, 2015 Checked SZ Approved RC
---	---

Actual Work Remaining Work Critic... Milest...	Page 18 of 22	Date 29-Oct-15	Revision Monthly Updated Schedule _ October, 2015	Checked SZ	Approved RC
--	--------------------------	--------------------------------------	---	----------------------------------	-----------------------------------

Actual Work

Remaining Work

Critic...

Milest...

Page 19 of 22

Date

Revision

Checked

Approved

29-Oct-15	Monthly Updated Schedule _ October, 2015	SZ	RC
-----------	--	----	----

AH.CN	Instrumentation works fuctional test for newly installed Actuators for CAI valves	1	15-Apr-15	15-Apr-15	19-May-15	19-May-15	15-Apr-15 A	15-Apr-15 A
AH.CI	E& I works for newly Installaed Actuators	1	15-Apr-15	15-Apr-15	19-May-15	19-May-15	19-May-15 A	19-May-15 A
AH.CI	DCS modifictional works	1	15-Apr-15	15-Apr-15	23-Nov-15	23-Nov-15	22-Nov-15	22-Nov-15
AH.CI	Function test	1	15-Apr-15	15-Apr-15	23-Nov-15	23-Nov-15	22-Nov-15	22-Nov-15
AH.CI	Mechanical completion for 1 Day SD TRAIN 1	0		15-Apr-15		23-Nov-15		22-Nov-15
Replacement with 1 Day S/D Actuators (For CAI) QTY 05 Nos.-2			34	15-Oct-15	15-Oct-15	15-Oct-15	16-Oct-15	11-Oct-15 A
AH.CI	Removal of Existing Actuators	1	15-Oct-15	15-Oct-15	15-Oct-15	16-Oct-15	11-Oct-15 A	11-Oct-15 A
AH.CI	Installation of New Adtuators for CAI valves	1	15-Oct-15	15-Oct-15	15-Oct-15	16-Oct-15	11-Oct-15 A	11-Oct-15 A
AH.CN	Instrumentation works fuctional test for newly installed Actuators for CAI valves	1	15-Oct-15	15-Oct-15	15-Oct-15	16-Oct-15	11-Oct-15 A	11-Oct-15 A
AH.CI	E& I works for newly Installaed Actuators	1	15-Oct-15	15-Oct-15	15-Oct-15	16-Oct-15	11-Oct-15 A	11-Oct-15 A
AH.CI	DCS modifictional works	1	15-Oct-15	15-Oct-15	15-Oct-15	16-Oct-15	13-Nov-15	13-Nov-15
AH.CI	Function test	1	15-Oct-15	15-Oct-15	15-Oct-15	16-Oct-15	13-Nov-15	13-Nov-15
AH.CI	Mechanical completion for 1 Day SD TRAIN 1	0		15-Oct-15		16-Oct-15		13-Nov-15
Replacement with 1 Day S/D Actuators (For CAI) QTY 04 Nos.-3			1	15-Oct-16	15-Oct-16	15-Oct-16	16-Oct-16	15-Oct-16
AH.CI	Installation of New Adtuators for CAI valves	1	15-Oct-16	15-Oct-16	15-Oct-16	16-Oct-16	15-Oct-16	15-Oct-16
AH.CN	Instrumentation works fuctional test for newly installed Actuators for CAI valves	1	15-Oct-16	15-Oct-16	15-Oct-16	16-Oct-16	15-Oct-16	15-Oct-16
AH.CI	E& I works for newly Installaed Actuators	1	15-Oct-16	15-Oct-16	15-Oct-16	16-Oct-16	15-Oct-16	15-Oct-16
AH.CI	DCS modifictional works	1	15-Oct-16	15-Oct-16	15-Oct-16	16-Oct-16	15-Oct-16	15-Oct-16
AH.CI	Function test	1	15-Oct-16	15-Oct-16	15-Oct-16	16-Oct-16	15-Oct-16	15-Oct-16
AH.CI	Mechanical completion for 1 Day SD TRAIN 1	0		15-Oct-16		16-Oct-16		15-Oct-16
Post Shutdown works			50	13-Mar-16	09-May-16	13-Apr-16	09-Jun-16	13-Apr-16
AH.CN.T	Painting and touchups for Installed facilities	3	13-Mar-16	15-Mar-16	13-Apr-16	16-Apr-16	13-Apr-16	16-Apr-16
AH.CN.T	Removal of Scaffolding	3	16-Mar-16	19-Mar-16	17-Apr-16	19-Apr-16	17-Apr-16	19-Apr-16
AH.CN.T	Construction works for pavement	21	16-Mar-16	09-Apr-16	17-Apr-16	10-May-16	17-Apr-16	10-May-16
AH.CN.T	Civil construction works for Desmteled Fence	14	21-Mar-16	05-Apr-16	21-Apr-16	07-May-16	21-Apr-16	07-May-16
AH.CN.T	Installation of fence	7	09-Apr-16	16-Apr-16	10-May-16	17-May-16	10-May-16	17-May-16
AH.CN.T	Removal of Resedual from premises	4	17-Apr-16	20-Apr-16	18-May-16	22-May-16	18-May-16	22-May-16
AH.CN.T	Installation of Street lighting	14	21-Apr-16	07-May-16	23-May-16	07-Jun-16	23-May-16	07-Jun-16
AH.CN.T	Electrical works related to Street lighting	12	26-Apr-16	09-May-16	28-May-16	09-Jun-16	28-May-16	09-Jun-16
AH.CN.TR	Completion of Installation of road signs and road marking etc.	7	01-May-16	08-May-16	01-Jun-16	08-Jun-16	01-Jun-16	08-Jun-16
Train-2			340	15-May-15	16-May-16	15-May-15	14-Jun-16	15-May-15 A
Replacement with Major S/D Valves & Actuators (SDT)			11	28-Feb-16	09-Mar-16	28-Mar-16	07-Apr-16	28-Mar-16
AH.CN.T	GAS out	1	28-Feb-16	28-Feb-16	28-Mar-16	28-Mar-16	28-Mar-16	28-Mar-16
AH.CN.T	Demolition of existing valves	2	29-Feb-16	01-Mar-16	29-Mar-16	30-Mar-16	29-Mar-16	30-Mar-16
AH.CN.T	Installation of Piping spools	1	01-Mar-16	01-Mar-16	30-Mar-16	30-Mar-16	30-Mar-16	30-Mar-16
AH.CN.T	Installation of SDT valves	2	02-Mar-16	03-Mar-16	31-Mar-16	01-Apr-16	31-Mar-16	01-Apr-16
AH.CN.T	Instrumentation work related SDT valves	1	03-Mar-16	03-Mar-16	01-Apr-16	01-Apr-16	01-Apr-16	01-Apr-16
AH.CN.T	DCS modification works	1	04-Mar-16	04-Mar-16	02-Apr-16	02-Apr-16	02-Apr-16	02-Apr-16
AH.CN.T	modifications to the existing Instrument Ar Buffer vessel	1	05-Mar-16	05-Mar-16	03-Apr-16	03-Apr-16	03-Apr-16	03-Apr-16
AH.CN.T	Electrical cable laying and Connection	1	06-Mar-16	06-Mar-16	04-Apr-16	04-Apr-16	04-Apr-16	04-Apr-16
AH.CN.T	Loop test for instrumentation cable	1	07-Mar-16	07-Mar-16	05-Apr-16	05-Apr-16	05-Apr-16	05-Apr-16
AH.CN.T	Functional test for electrical connection	1	07-Mar-16	07-Mar-16	05-Apr-16	05-Apr-16	05-Apr-16	05-Apr-16

5621 - Buhasa Replacement of ESD Valves and Actuators_ Monthly Updated SCHEDULE (October, 2015)

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	REV Start	REV Finish	Start	Finish	201520162017																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
	AH.CN.TPainting and Touchups Etc.	1	08-Mar-16	08-Mar-16	06-Apr-16	06-Apr-16	06-Apr-16	06-Apr-16																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	

Actual Work
Remaining Work

Critic...
Milest...

Page 21 of 22

Date

29-Oct-15

Revision

Monthly Updated Schedule _ October, 2015

Checked

SZ

Approved

RC

5621 - Buhasa Replacement of ESD Valves and Actuators_ Monthly Updated SCHEDULE (October, 2015)

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	REV Start	REV Finish	Start	Finish	2015												2016												2017																	
									O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D			
Train-2		20	31-Oct-16	22-Nov-16	31-Oct-16	22-Nov-16	29-Oct-16	20-Nov-16																																										
	AH.CN.TR2	As Built Documentation for Train-2	20	31-Oct-16	22-Nov-16	31-Oct-16	22-Nov-16	29-Oct-16	20-Nov-16																																									
	AH.CN.TR2	Handing Over of train-2	0		22-Nov-16		22-Nov-16		20-Nov-16																																									
	AH.CN.TR2	PAC for train-2	0		22-Nov-16		22-Nov-16		20-Nov-16																																									
Project and Contract Completion		107	13-Dec-16	22-Jun-17	13-Feb-17	22-Jun-17	18-Feb-17	22-Jun-17																																										
AH.CM.PC.	Project Completion	0		13-Dec-16		13-Feb-17		18-Feb-17																																										
AH.CM.PC.	Contract Completion Date	0		22-Jun-17		22-Jun-17		22-Jun-17																																										

■ Actual Work
 ■ Critic...
 ■ Remaining Work
 ◆ Milest...

ATTACHMENT - 11

4 WEEK LOOK AHEAD SCHEDULE

Archives from Personal Files

5621_Replacement of ESD Valves and Actuators at BuHasa_04 Week Lookahead

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	BL2 Start	BL2 Finish	Start	Finish	2015	2016	2017	2018	2019			
5621_Revised Schedule_29 Oct 2015 Update			317	22-Dec-14	13-Feb-16	25-Jan-15	20-Feb-16	06-Nov-14 A	20-Mar-16	20-Mar-16: 5621 Revised Schedule 2						
PROJECT MILESTONE COMPLETION SCHEDULE			20	25-Jan-15	13-Feb-16	30-Jul-15	22-Nov-15	29-Oct-15	21-Nov-15	21-Nov-15: PROJECT MILESTONE COMPLETION						
Engineering			0	21-Mar-15	21-Mar-15	16-Aug-15	16-Aug-15	15-Nov-15	15-Nov-15	15-Nov-15: Engineering						
AH.EN.M1190	ISSUE E&I DWGS INCL. CABLE SCH, LAYOUTS, TRAY/SUPPORTS & II	0		21-Mar-15			16-Aug-15		15-Nov-15	21-Nov-15: ISSUE E&I DWGS INCL. CABLE SCH, LAYOUTS, TRAY/SUPPORTS & II						
Procurement & Delivery			20	25-Jan-15	07-Nov-15	18-Oct-15	22-Nov-15	29-Oct-15	21-Nov-15	21-Nov-15: Procurement & Delivery						
AH.EN.M1270	RECEIVE ALL E&I CABLES AT SITE	0		07-Nov-15			22-Nov-15		21-Nov-15	21-Nov-15: RECEIVE ALL E&I CABLES AT SITE						
AH.EN.M1280	SUBMIT G-SPIRS TO COMPANY AND PLACE ORDERS FOR ALL ITEM	0		25-Jan-15			18-Oct-15		29-Oct-15	29-Oct-15: SUBMIT G-SPIRS TO COMPANY AND PLACE ORDERS FOR ALL ITEM						
Construction / Commissioning Works			0	13-Feb-16	13-Feb-16	30-Jul-15	30-Jul-15	29-Oct-15	29-Oct-15	29-Oct-15: Construction / Commissioning Works						
AH.EN.M1310	COMPLETE FABRICATION AND INSTALLATION OF ALL STRUCTURAL	0		13-Feb-16			30-Jul-15		29-Oct-15	29-Oct-15: COMPLETE FABRICATION AND INSTALLATION OF ALL STRUCTURAL						
One Day Shutdowns			0	15-Nov-15	15-Nov-15	15-Nov-15	15-Nov-15	15-Nov-15	15-Nov-15	15-Nov-15: One Day Shutdowns						
AH.SD.M1040	ONE DAY SHUTDOWN FOR TRAIN - 2 No. 02	0		15-Nov-15			15-Nov-15		15-Nov-15	15-Nov-15: ONE DAY SHUTDOWN FOR TRAIN - 2 No. 02						
DETAILED ENGINEERING			138	22-Dec-14	12-Mar-15	25-Jan-15	04-Jul-15	06-Nov-14 A	15-Nov-15	15-Nov-15: DETAILED ENGINEERING						
Instrumentation			60	22-Dec-14	12-Mar-15	25-Jan-15	04-Apr-15	06-Nov-14 A	15-Nov-15	15-Nov-15: Instrumentation						
A1435	I/O List - DCS Final Issue	52		22-Dec-14			04-Apr-15		15-Nov-15	15-Nov-15: I/O List - DCS Final Issue						
A1440	Scope of Work for Existing DCS & ESD Modifications Final Issue	60		03-Jan-15			04-Apr-15		15-Nov-15	15-Nov-15: SCOPE OF WORK FOR EXISTING DCS & ESD MODIFICATIONS FINAL ISSUE						
A1565	Instrument Loop Diagrams - DCS Final Issue	40		28-Dec-14			29-Mar-15		09-Nov-15	09-Nov-15: INSTRUMENT LOOP DIAGRAMS - DCS FINAL ISSUE						
HSE			56	06-Jan-15	04-Mar-15	30-Apr-15	04-Jul-15	05-Apr-15 A	10-Nov-15	10-Nov-15: HSE						
A1680	HAZID Close-out Report Review and Final Issue	30		06-Jan-15			03-Jun-15		10-Nov-15	10-Nov-15: HAZID CLOSE-OUT REPORT REVIEW AND FINAL ISSUE						
A1690	HSE Action Tracking Register and Final Issue	20		10-Feb-15			04-Jul-15		05-Nov-15	05-Nov-15: HSE ACTION TRACKING REGISTER AND FINAL ISSUE						
PROCUREMENT			211	02-Feb-15	07-Nov-15	22-Dec-15	28-May-15	20-Mar-16		20-Mar-16: PROCUREMENT						
Bulk material			156	18-Mar-15	07-Nov-15	27-Jun-15	22-Nov-15	12-Jun-15 A	21-Nov-15	21-Nov-15: Bulk material						
Instrumentation Bulk Material			24	25-Aug-15	07-Nov-15	24-Oct-15	22-Nov-15	29-Oct-15	21-Nov-15	21-Nov-15: Instrumentation Bulk Material						
AH.PR.CI.10050	Shipping, Transportation and Receipt at Site_Bulk Instrumentation material	24		25-Aug-15			22-Nov-15		21-Nov-15	21-Nov-15: SHIPPING, TRANSPORTATION AND RECEIPT AT SITE_BULK INSTRUMENTATION MATERIAL						
Instrumentation Pressure Switches			29	22-Mar-15	08-Aug-15	22-Sep-15	20-Nov-15	28-Oct-15 A	20-Nov-15	20-Nov-15: Instrumentation Pressure Switches						
AH.PR.CI.10100	Complete Manufacturing and Final inspection_Pressure Switches	20		22-Mar-15			21-Oct-15		31-Oct-15	31-Oct-15: COMPLETE MANUFACTURING AND FINAL INSPECTION_PRESSURE SWITCHES						
AH.PR.CI.10110	Shipping, Transportation and Receipt at Site_Pressure Switches	20		05-Jul-15			20-Nov-15		20-Nov-15	20-Nov-15: SHIPPING, TRANSPORTATION AND RECEIPT AT SITE_PRESSURE SWITCHES						
Piping material			120	18-Mar-15	15-Jul-15	27-Jun-15	24-Oct-15	12-Jun-15 A	15-Nov-15	15-Nov-15: Piping material						
AH.PR.PI.10050	Shipping, Transportation and Receipt at Site_Line Pipes	120		18-Mar-15			24-Oct-15		15-Nov-15	15-Nov-15: SHIPPING, TRANSPORTATION AND RECEIPT AT SITE_LINE PIPES						
Long lead items			211	02-Feb-15	31-Jul-15	28-May-15	22-Dec-15	28-May-15 A	20-Mar-16	20-Mar-16: Long lead items						
SDT valves & Actuators			64				29-Aug-15	22-Dec-15	29-Sep-15 A	27-Dec-15	27-Dec-15: SDT VALVES & ACTUATORS					
AH.PR.CI.10172	Assembly of Complete ESD Valve and Actuator_SDT Valves with Actuator	40					29-Aug-15	05-Nov-15	29-Sep-15 A	03-Dec-15	03-Dec-15: ASSEMBLY OF COMPLETE ESD VALVE AND ACTUATOR_SDT VALVES WITH ACTUATOR					
AH.PR.CI.10173	Assembly of ESD Valve and Rotork Actuator_SDT Valves with Actuators	40					07-Nov-15	22-Dec-15	14-Oct-15 A	27-Dec-15	27-Dec-15: ASSEMBLY OF ESD VALVE AND ROTORK ACTUATOR_SDT VALVES WITH ACTUATORS					
Operating spares			180	02-Feb-15	31-Jul-15	28-May-15	23-Nov-15	28-May-15 A	20-Mar-16	20-Mar-16: OPERATING SPARES						
AH.PR.CI.10320	Complete Manufacturing and Final inspection_Operational Spares	180		02-Feb-15			23-Nov-15	28-May-15 A	20-Mar-16	20-Mar-16: COMPLETE MANUFACTURING AND FINAL INSPECTION_OPERATIONAL SPARES						
SUB-CONTRACTING SERVICES			31	01-Mar-15	10-Oct-15	30-Jul-15	21-Nov-15	29-Oct-15	03-Dec-15	03-Dec-15: SUB-CONTRACTING SERVICES						
Bolt torquing and tensioning			31	01-Mar-15	05-Apr-15	30-Jul-15	03-Sep-15	29-Oct-15	03-Dec-15	03-Dec-15: Bolt torquing and tensioning						
AH.PR.SC.10340	Prepare / Issue RFQ-Bolt torquing and tensioning	7		01-Mar-15			06-Aug-15		05-Nov-15	05-Nov-15: PREPARE / ISSUE RFQ-BOLT TORQUING AND TENSIONING						
AH.PR.SC.10350	Receive Bids-Bolt torquing and tensioning	14		21-Mar-15			03-Sep-15		03-Dec-15	03-Dec-15: RECEIVE BIDS-BOLT TORQUING AND TENSIONING						
Painting and insulation works			27	09-Sep-15	10-Oct-15	20-Oct-15	21-Nov-15	29-Oct-15	29-Nov-15	29-Nov-15: Painting and insulation works						

 Project Baseline Bar
  Remaining Work
  Baseline Milestone
  Actual Work
  Critical Remaining Work
  Milestone

Page 1 of 5

31-Oct-15

Date	Revision	Checked	Approved
29-Oct-15	Monthly Updated Schedule Oct' 15	SZ	RC

5621_Replacement of ESD Valves and Actuators at BuHasa_04 Week Lookahead

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	BL2 Start	BL2 Finish	Start	Finish	2015	2016	2017	2018	2019
AH.PR.SC.10390	Prepare / Issue RFQ-Painting and Insulation	7	09-Sep-15	16-Sep-15	20-Oct-15	28-Oct-15	29-Oct-15	05-Nov-15					
AH.PR.SC.10400	Receive Bids-Painting and Insulation	10	29-Sep-15	10-Oct-15	09-Nov-15	21-Nov-15	18-Nov-15	29-Nov-15					
Scaffolding Services		24	01-Jul-15	01-Sep-15	30-Jul-15	07-Sep-15	29-Oct-15	25-Nov-15					
AH.PR.SC.10440	Prepare / Issue RFQ-Scaffolding Services	7	01-Jul-15	08-Jul-15	30-Jul-15	06-Aug-15	29-Oct-15	05-Nov-15					
AH.PR.SC.10450	Receive Bids-Scaffolding Services	5	21-Jul-15	01-Aug-15	08-Aug-15	18-Aug-15	07-Nov-15	11-Nov-15					
AH.PR.SC.10460	Submit Technical Bid Evaluation (TBE) for Company Approval	7	02-Aug-15	09-Aug-15	19-Aug-15	26-Aug-15	12-Nov-15	19-Nov-15					
AH.PR.SC.10470	Receive Company Approval-Scaffolding Services	0		20-Aug-15		26-Aug-15		19-Nov-15					
AH.PR.SC.10480	Issue LOA / F OA-Scaffolding Services	5	22-Aug-15	01-Sep-15	27-Aug-15	07-Sep-15	21-Nov-15	25-Nov-15					
CONSTRUCTION AND COMMISSIONING		73	15-Apr-15	15-Nov-15	29-Sep-15	20-Feb-16	22-Jan-15 A	26-Dec-15					
Site Establishment		73	02-Sep-15	10-Nov-15	21-Oct-15	13-Jan-16	22-Jan-15 A	20-Dec-15					
Train-1		73	02-Sep-15	10-Nov-15	21-Oct-15	13-Jan-16	22-Jan-15 A	16-Dec-15					
AH.CN.PM.10010	Site Mobilization of Resources	30	02-Sep-15	06-Oct-15	21-Oct-15	24-Nov-15	22-Jan-15 A	16-Dec-15					
AH.CN.PM.10030	Construction of Material Storage Area	10	31-Oct-15	10-Nov-15	03-Jan-16	13-Jan-16	15-Mar-15 A	28-Nov-15					
Train-2		35	02-Sep-15	12-Oct-15	21-Oct-15	30-Nov-15	22-Jan-15 A	20-Dec-15					
AH.CN.PM.10040	Site Mobilization of Resources	35	02-Sep-15	12-Oct-15	21-Oct-15	30-Nov-15	22-Jan-15 A	20-Dec-15					
Construction & Pre-commissioning		50	15-Apr-15	15-Nov-15	29-Sep-15	20-Feb-16	29-Oct-15	26-Dec-15					
Pre-Shutdown works for TRAIN 1 & TRAIN 2		50			29-Sep-15	20-Feb-16	29-Oct-15	26-Dec-15					
PIPING FABRICATION (AHEC W/SHO P)		14			29-Sep-15	13-Dec-15	17-Nov-15	02-Dec-15					
P-3131-12"-DB2D (28.25-I.D)		14			29-Sep-15	14-Oct-15	17-Nov-15	02-Dec-15					
AH.CN.TR1.1360	Joint Cutting and Rewelding if any crack found in Inspection	6			29-Sep-15	05-Oct-15	17-Nov-15	23-Nov-15					
AH.CN.TR1.1365	Sand Blasting and Painting of Spool	8			06-Oct-15	14-Oct-15	24-Nov-15	02-Dec-15					
P-3020-10"-DB2D (10-I.D)		10			01-Oct-15	12-Oct-15	17-Nov-15	28-Nov-15					
AH.CN.TR1.1120	Joint Cutting and Rewelding if any crack found in Inspection	4			01-Oct-15	05-Oct-15	17-Nov-15	21-Nov-15					
AH.CN.TR1.1125	Sand Blasting and Painting of Spool	6			06-Oct-15	12-Oct-15	22-Nov-15	28-Nov-15					
P-3043-14"-DB2D (14-I.D)		10			06-Oct-15	17-Oct-15	17-Nov-15	28-Nov-15					
AH.CN.TR1.1190	Joint Cutting and Rewelding if any crack found in Inspection	4			06-Oct-15	10-Oct-15	17-Nov-15	21-Nov-15					
AH.CN.TR1.1195	Sand Blasting and Painting of Spool	6			11-Oct-15	17-Oct-15	22-Nov-15	28-Nov-15					
P-2103-14"-CA2D (14-I.D)		10			11-Oct-15	21-Oct-15	17-Nov-15	28-Nov-15					
AH.CN.TR1.1260	Joint Cutting and Rewelding if any crack found in Inspection	4			11-Oct-15	14-Oct-15	17-Nov-15	21-Nov-15					
AH.CN.TR1.1265	Sand Blasting and Painting of Spool	6			15-Oct-15	21-Oct-15	22-Nov-15	28-Nov-15					
P-3021-12"-DB2D (12-I.D)		10			15-Oct-15	26-Oct-15	17-Nov-15	28-Nov-15					
AH.CN.TR1.1050	Joint Cutting and Rewelding if any crack found in Inspection	4			15-Oct-15	19-Oct-15	17-Nov-15	21-Nov-15					
AH.CN.TR1.1055	Sand Blasting and Painting of Spool	6			20-Oct-15	26-Oct-15	22-Nov-15	28-Nov-15					
P-3216-12"-CC2D (12-I.D)		10			20-Oct-15	31-Oct-15	17-Nov-15	28-Nov-15					
AH.CN.TR1.1430	Joint Cutting and Rewelding if any crack found in Inspection	4			20-Oct-15	24-Oct-15	17-Nov-15	21-Nov-15					
AH.CN.TR1.1440	Sand Blasting and Painting of Spool	6			25-Oct-15	31-Oct-15	22-Nov-15	28-Nov-15					
P-2601-16"-CA2B (20-I.D)		10			25-Oct-15	04-Nov-15	17-Nov-15	28-Nov-15					
AH.CN.TR2.1050	Joint Cutting and Rewelding if any crack found in Inspection	4			25-Oct-15	28-Oct-15	17-Nov-15	21-Nov-15					
AH.CN.TR2.1070	Sand Blasting and Painting of Spool	6			29-Oct-15	04-Nov-15	22-Nov-15	28-Nov-15					
P-2603-14"-CA2D (18-I.D)		10			29-Oct-15	09-Nov-15	17-Nov-15	28-Nov-15					
AH.CN.TR2.1130	Joint Cutting and Rewelding if any crack found in Inspection	4			29-Oct-15	02-Nov-15	17-Nov-15	21-Nov-15					
AH.CN.TR2.1150	Sand Blasting and Painting of Spool	6			03-Nov-15	09-Nov-15	22-Nov-15	28-Nov-15					
P-3566-20"-DB2D (20-I.D)		10			03-Nov-15	14-Nov-15	17-Nov-15	28-Nov-15					
AH.CN.TR2.1210	Joint Cutting and Rewelding if any crack found in Inspection	4			03-Nov-15	07-Nov-15	17-Nov-15	21-Nov-15					

5621_Replacement of ESD Valves and Actuators at BuHasa_04 Week Lookahead

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	BL2 Start	BL2 Finish	Start	Finish	2015	2016	2017	2018	2019
AH.CN.TR2.1230	Sand Blasting and Painting of Spool	6			08-Nov-15	14-Nov-15	22-Nov-15	28-Nov-15					
P-3557-16"-CA2D (16-I.D)		10			08-Nov-15	18-Nov-15	17-Nov-15	28-Nov-15					
AH.CN.TR2.1290	Joint Cutting and Rewelding if any crack found in Inspection	4			08-Nov-15	11-Nov-15	17-Nov-15	21-Nov-15					
AH.CN.TR2.1310	Sand Blasting and Painting of Spool	6			12-Nov-15	18-Nov-15	22-Nov-15	28-Nov-15					
P-3520-10"-DB2D (10-I.D)		10			12-Nov-15	23-Nov-15	17-Nov-15	28-Nov-15					
AH.CN.TR2.1370	Joint Cutting and Rewelding if any crack found in Inspection	4			12-Nov-15	16-Nov-15	17-Nov-15	21-Nov-15					
AH.CN.TR2.1390	Sand Blasting and Painting of Spool	6			17-Nov-15	23-Nov-15	22-Nov-15	28-Nov-15					
P-3716-12"-CC2D (12-I.D)		10			17-Nov-15	28-Nov-15	17-Nov-15	28-Nov-15					
AH.CN.TR2.1450	Joint Cutting and Rewelding if any crack found in Inspection	4			17-Nov-15	21-Nov-15	17-Nov-15	21-Nov-15					
AH.CN.TR2.1470	Sand Blasting and Painting of Spool	6			22-Nov-15	28-Nov-15	22-Nov-15	28-Nov-15					
P-3631-12"-DB2D (28.25-I.D)		14			28-Nov-15	13-Dec-15	17-Nov-15	02-Dec-15					
AH.CN.TR2.1560	Joint Cutting and Rewelding if any crack found in Inspection	6			28-Nov-15	03-Dec-15	17-Nov-15	23-Nov-15					
AH.CN.TR2.1580	Sand Blasting and Painting of Spool	8			05-Dec-15	13-Dec-15	24-Nov-15	02-Dec-15					
CIVIL FOUNDATION WORKS		32			21-Oct-15	20-Feb-16	29-Oct-15	05-Dec-15					
Buffer Vessel Foundation		4			13-Jan-16	20-Feb-16	29-Oct-15	02-Nov-15					
Foundation for SDV 2470		4			13-Jan-16	17-Jan-16	29-Oct-15	02-Nov-15					
AH.CN.TR2.21	Surface Protection	2			13-Jan-16	14-Jan-16	29-Oct-15	31-Oct-15					
AH.CN.TR2.21	Backfilling	2			16-Jan-16	17-Jan-16	01-Nov-15	02-Nov-15					
Foundation for LCV 2183		4			16-Feb-16	20-Feb-16	29-Oct-15	02-Nov-15					
AH.CN.TR2.21	Surface Protection	2			16-Feb-16	17-Feb-16	29-Oct-15	31-Oct-15					
AH.CN.TR2.21	Backfilling	2			18-Feb-16	20-Feb-16	01-Nov-15	02-Nov-15					
Foundation for SDV 2201		4			16-Feb-16	20-Feb-16	29-Oct-15	02-Nov-15					
AH.CN.TR2.21	Surface Protection	2			16-Feb-16	17-Feb-16	29-Oct-15	31-Oct-15					
AH.CN.TR2.21	Backfilling	2			18-Feb-16	20-Feb-16	01-Nov-15	02-Nov-15					
Foundation for SDV 2046		4			16-Feb-16	20-Feb-16	29-Oct-15	02-Nov-15					
AH.CN.TR2.21	Surface Protection	2			16-Feb-16	17-Feb-16	29-Oct-15	31-Oct-15					
AH.CN.TR2.21	Backfilling	2			18-Feb-16	20-Feb-16	01-Nov-15	02-Nov-15					
Junction Box Foundation		32			21-Oct-15	26-Nov-15	29-Oct-15	05-Dec-15					
Foundation for 03-JD-1106-D		22			21-Oct-15	15-Nov-15	29-Oct-15	23-Nov-15					
AH.CN.TR1.21	Excavation	2			21-Oct-15	22-Oct-15	29-Oct-15	31-Oct-15					
AH.CN.TR1.21	Blinding / Screeding	1			24-Oct-15	24-Oct-15	01-Nov-15	01-Nov-15					
AH.CN.TR1.21	Formwork	1			25-Oct-15	25-Oct-15	02-Nov-15	02-Nov-15					
AH.CN.TR1.21	Rebar	1			26-Oct-15	26-Oct-15	03-Nov-15	03-Nov-15					
AH.CN.TR1.21	Concrete	1			27-Oct-15	27-Oct-15	04-Nov-15	04-Nov-15					
AH.CN.TR1.21	Curing	14			28-Oct-15	12-Nov-15	05-Nov-15	21-Nov-15					
AH.CN.TR1.21	Surface Protection	1			14-Nov-15	14-Nov-15	22-Nov-15	22-Nov-15					
AH.CN.TR1.21	Backfilling	1			15-Nov-15	15-Nov-15	23-Nov-15	23-Nov-15					
Foundation for 03-JD-1108-D		20			28-Oct-15	19-Nov-15	05-Nov-15	28-Nov-15					
AH.CN.TR1.21	Excavation	2			28-Oct-15	29-Oct-15	05-Nov-15	07-Nov-15					
AH.CN.TR1.21	Blinding / Screeding	1			31-Oct-15	31-Oct-15	08-Nov-15	08-Nov-15					
AH.CN.TR1.21	Formwork	1			01-Nov-15	01-Nov-15	09-Nov-15	09-Nov-15					
AH.CN.TR1.21	Rebar	1			02-Nov-15	02-Nov-15	10-Nov-15	10-Nov-15					
AH.CN.TR1.21	Concrete	1			03-Nov-15	03-Nov-15	11-Nov-15	11-Nov-15					
AH.CN.TR1.21	Curing	14			04-Nov-15	19-Nov-15	12-Nov-15	28-Nov-15					

5621_Replacement of ESD Valves and Actuators at BuHasa_04 Week Lookahead

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	BL2 Start	BL2 Finish	Start	Finish	2015	2016	2017	2018	2019
Foundation for 03-JD-1109-D/2103-D		20			04-Nov-15	26-Nov-15	12-Nov-15	05-Dec-15					
AH.CN.TR1.25	Excavation	2			04-Nov-15	05-Nov-15	12-Nov-15	14-Nov-15					
AH.CN.TR1.26	Blinding / Screeding	1			07-Nov-15	07-Nov-15	15-Nov-15	15-Nov-15					
AH.CN.TR1.27	Formwork	1			08-Nov-15	08-Nov-15	16-Nov-15	16-Nov-15					
AH.CN.TR1.28	Rebar	1			09-Nov-15	09-Nov-15	17-Nov-15	17-Nov-15					
AH.CN.TR1.30	Concrete	1			10-Nov-15	10-Nov-15	18-Nov-15	18-Nov-15					
AH.CN.TR1.31	Curing	14			11-Nov-15	26-Nov-15	19-Nov-15	05-Dec-15					
Foundation for 03-JD-1107-D/2102-D		6			11-Nov-15	17-Nov-15	19-Nov-15	25-Nov-15					
AH.CN.TR1.32	Excavation	2			11-Nov-15	12-Nov-15	19-Nov-15	21-Nov-15					
AH.CN.TR1.33	Blinding / Screeding	1			14-Nov-15	14-Nov-15	22-Nov-15	22-Nov-15					
AH.CN.TR1.34	Formwork	1			15-Nov-15	15-Nov-15	23-Nov-15	23-Nov-15					
AH.CN.TR1.35	Rebar	1			16-Nov-15	16-Nov-15	24-Nov-15	24-Nov-15					
AH.CN.TR1.36	Concrete	1			17-Nov-15	17-Nov-15	25-Nov-15	25-Nov-15					
INSTRUMENTATION WORKS		37			25-Oct-15	27-Dec-15	14-Nov-15	26-Dec-15					
Junction Box Installation		10			16-Nov-15	26-Nov-15	24-Nov-15	05-Dec-15					
AH.CN.TR1.3500	Installation of 03-JD-1106-D	10			16-Nov-15	26-Nov-15	24-Nov-15	05-Dec-15					
Primary Cable Laying		10			23-Nov-15	03-Dec-15	22-Nov-15	02-Dec-15					
AH.CN.TR1.3560	Removal of Interlocking Tiles	10			23-Nov-15	03-Dec-15	22-Nov-15	02-Dec-15					
Cable Tray Installation		30			23-Nov-15	27-Dec-15	22-Nov-15	26-Dec-15					
AH.CN.TR1.3750	Installation of 50mm Cable Tray (800MTRS)	30			23-Nov-15	27-Dec-15	22-Nov-15	26-Dec-15					
AH.CN.TR1.3760	Installation of 100mm Cable Tray (200MTRS)	20			23-Nov-15	15-Dec-15	22-Nov-15	14-Dec-15					
AH.CN.TR1.3770	Installation of 150mm Cable Tray (240MTRS)	20			23-Nov-15	15-Dec-15	22-Nov-15	14-Dec-15					
AH.CN.TR1.3780	Installation of 300mm Cable Tray (200MTRS)	15			23-Nov-15	09-Dec-15	22-Nov-15	08-Dec-15					
Pressure Switch Installation		12			21-Nov-15	03-Dec-15	21-Nov-15	03-Dec-15					
AH.CN.TR1.3700	Installation of Pressure Switch Stand for CAI Actuators (18)	12			21-Nov-15	03-Dec-15	21-Nov-15	03-Dec-15					
DCS System Modification Works		15			25-Oct-15	10-Nov-15	14-Nov-15	30-Nov-15					
AH.CN.TR1.3810	Installation of I/O Cards 04 Nos.	5			25-Oct-15	29-Oct-15	14-Nov-15	18-Nov-15					
AH.CN.TR1.3820	Installation of FTA Cards 04 Nos.	5			31-Oct-15	04-Nov-15	19-Nov-15	24-Nov-15					
AH.CN.TR1.3830	Installation of FTA Cables 04 Nos.	5			05-Nov-15	10-Nov-15	25-Nov-15	30-Nov-15					
Train-1		10	15-Apr-15	15-Oct-15	15-Oct-15	23-Nov-15	13-Nov-15	22-Nov-15					
Replacement with 1 Day S/D Actuators (For CAI) QTY 14 Nos.		10	15-Apr-15	15-Oct-15	15-Oct-15	23-Nov-15	13-Nov-15	22-Nov-15					
Replacement with 1 Day S/D Actuators (For CAI) QTY 05 Nos.-1		1	15-Apr-15	15-Apr-15	23-Nov-15	23-Nov-15	22-Nov-15	22-Nov-15					
AH.CN.TR1.10520	DCS modification works	1	15-Apr-15	15-Apr-15	23-Nov-15	23-Nov-15	22-Nov-15	22-Nov-15					
AH.CN.TR1.10530	Function test	1	15-Apr-15	15-Apr-15	23-Nov-15	23-Nov-15	22-Nov-15	22-Nov-15					
AH.CN.TR1.10650	Mechanical completion for 1 Day SD TRAIN 1	0		15-Apr-15		23-Nov-15		22-Nov-15					
Replacement with 1 Day S/D Actuators (For CAI) QTY 05 Nos.-2		1	15-Oct-15	15-Oct-15	15-Oct-15	16-Oct-15	13-Nov-15	13-Nov-15					
AH.CN.TR1.10850	DCS modification works	1	15-Oct-15	15-Oct-15	15-Oct-15	16-Oct-15	13-Nov-15	13-Nov-15					
AH.CN.TR1.10860	Function test	1	15-Oct-15	15-Oct-15	15-Oct-15	16-Oct-15	13-Nov-15	13-Nov-15					
AH.CN.TR1.10870	Mechanical completion for 1 Day SD TRAIN 1	0		15-Oct-15		16-Oct-15		13-Nov-15					
Train-2		8	15-May-15	15-Nov-15	15-Nov-15	23-Nov-15	15-Nov-15	22-Nov-15					
Replacement with 1 Day S/D Actuators (For CAI) QTY 14 Nos.		8	15-May-15	15-Nov-15	15-Nov-15	23-Nov-15	15-Nov-15	22-Nov-15					
Replacement with S/D Actuators (For CAI) QTY 05 Nos.-1		1	15-May-15	15-May-15	23-Nov-15	23-Nov-15	22-Nov-15	22-Nov-15					
AH.CN.TR2.10560	DCS modification works	1	15-May-15	15-May-15	23-Nov-15	23-Nov-15	22-Nov-15	22-Nov-15					
AH.CN.TR2.10570	Function test	1	15-May-15	15-May-15	23-Nov-15	23-Nov-15	22-Nov-15	22-Nov-15					

5621_Replacement of ESD Valves and Actuators at BuHasa_04 Week Lookahead

Activity ID	Activity Name	Original Duration	BL1 Start	BL1 Finish	BL2 Start	BL2 Finish	Start	Finish	2015	2016	2017	2018	2019
AH.CN.TR2.10710	Mechanical completion for 1 Day SD TRAIN 2	0		15-May-15		23-Nov-15		22-Nov-15					
	Replacement with S/D Actuators (For CAI) QTY 05 Nos.-2	1	15-Nov-15	15-Nov-15	15-Nov-15	16-Nov-15	15-Nov-15	15-Nov-15					
AH.CN.TR2.10580	Removal of Existing Actuators	1	15-Nov-15	15-Nov-15	15-Nov-15	16-Nov-15	15-Nov-15	15-Nov-15					
AH.CN.TR2.10590	Installation of New Actuators for CAI valves	1	15-Nov-15	15-Nov-15	15-Nov-15	16-Nov-15	15-Nov-15	15-Nov-15					
AH.CN.TR2.10600	Instrumentation works fuctional test for newly installed Actuators for CAI v:	1	15-Nov-15	15-Nov-15	15-Nov-15	16-Nov-15	15-Nov-15	15-Nov-15					
AH.CN.TR2.10610	E&I works for newly Installaed Actuators	1	15-Nov-15	15-Nov-15	15-Nov-15	16-Nov-15	15-Nov-15	15-Nov-15					
AH.CN.TR2.10620	DCS modifictional works	1	15-Nov-15	15-Nov-15	15-Nov-15	16-Nov-15	15-Nov-15	15-Nov-15					
AH.CN.TR2.10630	Function test	1	15-Nov-15	15-Nov-15	15-Nov-15	16-Nov-15	15-Nov-15	15-Nov-15					
AH.CN.TR2.10720	Mechanical completion for 1 Day SD TRAIN 2	0		15-Nov-15		16-Nov-15		15-Nov-15					

Archives from Personal File 109

ATTACHMENT - 12

**PROJECT DOCUMENT
DELIVERABLE REGISTER**

Archives from Personal Files

Page 1 of 6

UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE UAE <																									
---	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

Page 3 of 6

جاسكو Abu Dhabi Gas Industries Ltd. البحرين al Hassan BuHasa Replacement of Valves & Actuators for EPC Works GASCO PROJECT NO: 5621 Project Document Deliverables Register																																																Document Title:		Project Document Deliverables Register (PDDR)			
																											Document No:		5621-SCH-00-AA-0002																								
																											Rev:		1																								
																											Date:		30-Oct-15																								
						Trans.No During Submission					P	Submission to GASCO															Remark																										
											F	Issued for Comments/Review (CC; Rev-A1)			Issued for Approval (IFA; Rev-A2)			Issued for Approval (IFA; Rev-A3)			Issued for Approval (IFA; Rev-A4)			Issued for Approval (IFA; Rev-A5)									Issued for Implementation/ Construction (IFI/IFC; Rev-1)																				
Sr.No	Document No.	Document Title	Document Class	Target Date	Responsible	First Issue	Issue of Rev-A1	Issue Rev-A2	Issue Rev-A3	Rev-1	A	Submission	Feedback Date	Status	Submission	Feedback Date	Status	Submission	Feedback Date	Status	Submission	Feedback Date	Status	Submission	Feedback Date	Status																											
F.2.8	5621-ITP-00-NA-0001	Inspection and Test Plan for Hot Insulation Works	1	15/Jan/15							F																																										
											A																																										
F.2.9	5621-ITP-00-XA-V0001	Inspection and Test Plan for Blasting and Painting Work	1	21/Mar/15							P	21/Mar/15	4/Apr/15		11/Apr/15	21/Apr/15		28/Apr/15	8/May/15								18-May-15																										
											F																																										
											A																																										
F.3.0	5621-ITP-00-NA-0002	Inspection and Test Plan for Insulation Removal and Refixing of Existing Valves for Inspection	1	28/Mar/15							P	28/Mar/15	11/Apr/15		18/Apr/15	28/Apr/15		5/May/15	15/May/15								25-May-15																										
											F																																										
											A																																										
F.3.1	5621-ITP-00-LA-0005	Inspection and Testing Plan for Piping Fabrication and Erection at Site	1	18/Jan/15		T-0244	T-0244	T-0256		T-0283	P	18/Jan/15	1/Feb/15		8/Feb/15	18/Feb/15		25/Feb/15	7/Mar/15								17-Mar-15																										
											F																																										
											A	7/Apr/15	9/Apr/15	2	12/Apr/15	19/Apr/15	3	N-A	N-A	-							28-Apr-15																										
G. General Method Statements																																																					
G.1.1	5621-MS-00-AA-0001	Method Statement for Rigging Activities	1	15/Mar/15							P	15/Mar/15	29/Mar/15		5/Apr/15	15/Apr/15		22/Apr/15	2/May/15								12-May-15																										
											F																																										
											A																																										
G.1.2	5621-MS-00-AA-0002	Method Statement for Scaffolding	1	1/Jan/15							P	1/Jan/15	15/Jan/15		22/Jan/15	1/Feb/15		8/Feb/15	18/Feb/15								28-Feb-15																										
											F																																										
											A																																										
G.1.3	5621-PP-00-AA-0008	Material Handling and Storage Procedure	1	1/Jan/15		T-0227	T-0227			T-0380	P	1/Jan/15	15/Jan/15		22/Jan/15	1/Feb/15		8/Feb/15	18/Feb/15								28-Feb-15																										
											F																																										
											A	29/Mar/15	20/May/15	3													21-Jun-15																										
H. Instrumentation Engineering																																																					
H.1.1	5621-MS-00-JA-0001	Method Statement for Field Cabling Installation, Termination & Glanding	1	21/Dec/14		T-0195	T-0195	T-0205	T-0272	T-0291	P	21/Dec/14	4/Jan/15		11/Jan/15	21/Jan/15		28/Jan/15	7/Feb/15								17-Feb-15																										
											F																																										
											A	19/Mar/15	23/Mar/15	1	23/Mar/15	22/Apr/15	1	25/Apr/15	28/Apr/15	-							4-May-15																										
H.1.2	5621-MS-00-JA-0002	Method Statement for Field Instruments Installation	1	22/Dec/14		T-0221	T-0221			T-0271	P	22/Dec/14	5/Jan/15		12/Jan/15	22/Jan/15		29/Jan/15	8/Feb/15								18-Feb-15																										
											F																																										
											A	29/Mar/15	22/Apr/15	3	N-A	N-A		N-A	N-A	-							23-Apr-15																										
H.1.3	5621-MS-00-JA-0003	Method Statement for Instruments Testing and Calibration	1	23/Dec/14		T-0223	T-0223	T-0329		T-0357	P	23/Dec/14	6/Jan/15		13/Jan/15	23/Jan/15		30/Jan/15	9/Feb/15								19-Feb-15																										
											F																																										
											A	29/Mar/15	6/Apr/15	1	24/May/15	2/Jun/15	3										6-Jun-15																										
H.1.4	5621-MS-00-JA-0004	Method Statement for Instrumentation Tubing Installation and Testing	1	24/Dec/14		T-0219	T-0219			T-0241	P	24/Dec/14	7/Jan/15		14/Jan/15	24/Jan/15		31/Jan/15	10/Feb/15								20-Feb-15																										
											F																																										
											A	29/Mar/15	1/Apr/15	2	5/Apr/15	9/Apr/15	3	N-A	N-A	-							5-Apr-15																										
H.1.5	5621-ITP-00-JA-0001	Inspection and Test Plan for Field Cabling Installation, Termination & Glanding	1	21/Dec/14		T-0196	T-0196	T-0206		T-0312	P	21/Dec/14	4/Jan/15		11/Jan/15	21/Jan/15		28/Jan/15	7/Feb/15								17-Feb-15																										
											F																																										
											A	19/Mar/15	23/Mar/15	1	23/Mar/15	6/May/15	3	N-A	N-A	-							11-May-15																										
H.1.6	5621-ITP-00-JA-0002	Inspection and Test Plan for Field Instruments Installation	1	22/Dec/14		T-0222	T-0222			T-0374	P	22/Dec/14	5/Jan/15		12/Jan/15	22/Jan/15		29/Jan/15	8/Feb/15								18-Feb-15																										
											F																																										
											A	29/Mar/15	6/Apr/15	3													16-Jun-15																										
H.1.7	5621-ITP-00-JA-0003	Inspection and Test Plan for Instruments Testing and Calibration	1	23/Dec/14		T-0224	T-0224			T-0254	P	23/Dec/14	6/Jan/15		13/Jan/15	23/Jan/15		30/Jan/15	9/Feb/15								19-Feb-15																										
											F																																										
											A	29/Mar/15	6/Apr/15	3	N-A	N-A	-	N-A	N-A	-							12-Apr-15																										
H.1.8	5621-ITP-00-JA-0004	Inspection and Test Plan for Instrumentation Tubing Installation and Testing	1	24/Dec/14		T-0220	T-0220			T-0252	P	24/Dec/14	7/Jan/15		14/Jan/15	24/Jan/15		31/Jan/15	10/Feb/15								20-Feb-15																										
											F																																										
											A	29/Mar/15	6/Apr/15	3	N-A	N-A	-	N-A	N-A	-							12-Apr-15																										
H.1.9	5621-MS-00-JA-0005	Method Statement for Instrument Loop Checking	1	24/Dec/14		T-0225	T-0225	T-0333	T-0364 T-0433 (A4)		P	24/Dec/14	7/Jan/15		14/Jan/15	24/Jan/15		31/Jan/15	10/Feb/15								20-Feb-15																										
											F																																										
											A	29/Mar/15	20/May/15	1	26/May/15	2/Jun/15	1	8/Jun/15	5/Jul/15	2	25/Jul/15																																
H.2.0	5621-ITP-00-JA-0005	Inspection and Test Plan for Instrument Loop Checking	1	24/Dec/14		T-0226	T-0226	T-0253		T-0266	P	24/Dec/14	7/Jan/15		14/Jan/15	24/Jan/15		31/Jan/15	10/Feb/15								20-Feb-15																										
											F																																										
											A	29/Mar/15	6/Apr/15	1	12/Apr/15	16/Apr/15	3	N-A	N-A	-							20-Apr-15																										

UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE UAE Abu Dhabi Gas Industries Ltd. UAE																										
--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

جاسكو Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd. Abu Dhabi Gas Industries Ltd.																									
--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

Archives from Personal Files

ATTACHMENT - 13

CONSTRUCTION REGISTER

Archives from Personal Files



											Document Title:		Construction Register			
											Rev:		1			
											Date:		30-Oct-15			
Activity ID	Activity Name	WTG % L3	UoM	UNIT RATE MHS/UNIT QTY.	PLANNED QUANTITY	ACHEIVED QUANTITY	REVISED START	REVISED FINISH	ACTUAL START	ACTUAL FINISH	TOTAL MANHOURS	PLANNED ACTIVITY WTG %	PLANNED MHS	PLANNED PROGRESS %	ACHIEVED PROGRESS %	ACTUAL MHS
AH.CN.TR1.1010	Welding of Pipe with Flange (12")	0.10%	I.D		12.00	12.00	11-Oct-15	11-Oct-15			350.00	29.76%	350	0.10%	0.10%	350
AH.CN.TR1.1020	100% Radiography of the Joint	0.04%	I.D		12.00	12.00	12-Oct-15	12-Oct-15			150.00	12.76%	150	0.04%	0.04%	150
AH.CN.TR1.1030	PWHT	0.04%	I.D		12.00	12.00	13-Oct-15	13-Oct-15			150.00	12.76%	150	0.04%	0.04%	150
AH.CN.TR1.1040	After Heat Treatment Radiography	0.04%	I.D		12.00	12.00	14-Oct-15	14-Oct-15			150.00	12.76%	150	0.04%	0.04%	150
AH.CN.TR1.1050	Joint Cutting and Rewelding if any crack found in Inspection	0.00%	-				15-Oct-15	19-Oct-15				0.00%				
AH.CN.TR1.1055	Sand Blasting and Painting of Spool	0.03%	SqM				20-Oct-15	26-Oct-15			100.00	8.50%	100	0.03%		
AH.CN.TR1.1060	Ready for Dispatch at Site	0.00%	-				27-Oct-15	27-Oct-15								
P-3216-12"-CC2D (12-I.D)		0.33%					13-Oct-15	1-Nov-15			1176.00	5.74%	1176	0.33%	0.31%	1076
AH.CN.TR1.1380	Fabrication of Pipe	0.08%	I.D		12.00	12.00	13-Oct-15	14-Oct-15			276.00	23.47%	276	0.08%	0.08%	276
AH.CN.TR1.1390	Welding of Pipe with Flange (12")	0.10%	I.D		12.00	12.00	15-Oct-15	15-Oct-15			350.00	29.76%	350	0.10%	0.10%	350
AH.CN.TR1.1400	100% Radiography of the Joint	0.04%	I.D		12.00	12.00	17-Oct-15	17-Oct-15			150.00	12.76%	150	0.04%	0.04%	150
AH.CN.TR1.1410	PWHT	0.04%	I.D		12.00	12.00	18-Oct-15	18-Oct-15			150.00	12.76%	150	0.04%	0.04%	150
AH.CN.TR1.1420	After Heat Treatment Radiography	0.04%	I.D		12.00	12.00	19-Oct-15	19-Oct-15			150.00	12.76%	150	0.04%	0.04%	150
AH.CN.TR1.1430	Joint Cutting and Rewelding if any crack found in Inspection	0.00%	-				20-Oct-15	24-Oct-15				0.00%				
AH.CN.TR1.1440	Sand Blasting and Painting of Spool	0.03%	SqM				25-Oct-15	31-Oct-15			100.00	8.50%	100	0.03%		
AH.CN.TR1.1450	Ready for Dispatch at Site	0.00%	-				1-Nov-15	1-Nov-15				0.00%				
P-2601-16"-CA2B (20-I.D)		0.56%					18-Oct-15	5-Nov-15			1963.00	9.58%	1663	0.48%	0.47%	1563
AH.CN.TR2.1000	Fabrication of Pipe	0.13%	I.D		20.00	20.00	18-Oct-15	19-Oct-15			460.00	23.43%	460	0.13%	0.13%	460
AH.CN.TR2.1010	Welding of Pipe with Flange (12")	0.17%	I.D		20.00	20.00	20-Oct-15	20-Oct-15			603.00	30.72%	603	0.17%	0.17%	603
AH.CN.TR2.1020	100% Radiography of the Joint	0.06%	I.D		20.00	20.00	21-Oct-15	21-Oct-15			200.00	10.19%	200	0.06%	0.06%	200
AH.CN.TR2.1030	PWHT	0.06%	I.D		20.00	20.00	22-Oct-15	22-Oct-15			200.00	10.19%	100	0.03%	0.06%	100
AH.CN.TR2.1040	After Heat Treatment Radiography	0.06%	I.D		20.00	20.00	24-Oct-15	24-Oct-15			200.00	10.19%	200	0.06%	0.06%	200
AH.CN.TR2.1050	Joint Cutting and Rewelding if any crack found in Inspection	0.00%	-				25-Oct-15	28-Oct-15				0.00%				
AH.CN.TR2.1060	Ready for Dispatch at Site	0.00%	-				5-Nov-15	5-Nov-15				0.00%				
AH.CN.TR2.1070	Sand Blasting and Painting of Spool	0.09%	SqM				29-Oct-15	4-Nov-15			300.00	15.28%	100	0.03%		
P-2603-14"-CA2D (18-I.D)		0.50%					22-Oct-15	10-Nov-15			1766.00	8.61%	1466	0.42%	0.42%	1466
AH.CN.TR2.1080	Fabrication of Pipe	0.13%	I.D		18.00	18.00	22-Oct-15	24-Oct-15			466.00	26.39%	466	0.13%	0.13%	466
AH.CN.TR2.1090	Welding of Pipe with Flange (12")	0.16%	I.D		18.00	18.00	25-Oct-15	25-Oct-15			550.00	31.14%	550	0.16%	0.16%	550
AH.CN.TR2.1100	100% Radiography of the Joint	0.04%	I.D		18.00	18.00	26-Oct-15	26-Oct-15			150.00	8.49%	150	0.04%	0.04%	150
AH.CN.TR2.1110	PWHT	0.04%	I.D		18.00	18.00	27-Oct-15	27-Oct-15			150.00	8.49%	150	0.04%	0.04%	150
AH.CN.TR2.1120	After Heat Treatment Radiography	0.04%	I.D		18.00	18.00	28-Oct-15	28-Oct-15			150.00	8.49%	150	0.04%	0.04%	150
AH.CN.TR2.1130	Joint Cutting and Rewelding if any crack found in Inspection	0.00%	-				29-Oct-15	2-Nov-15				0.00%				
AH.CN.TR2.1140	Ready for Dispatch at Site	0.00%	-				10-Nov-15	10-Nov-15				0.00%				
AH.CN.TR2.1150	Sand Blasting and Painting of Spool	0.09%	SqM				3-Nov-15	9-Nov-15			300.00	16.99%				
P-3566-20"-DB2D (20-I.D)		0.56%					27-Oct-15	15-Nov-15			1963.00	9.58%	1463	0.42%	0.47%	1663
AH.CN.TR2.1160	Fabrication of Pipe	0.13%	I.D		20.00	20.00	27-Oct-15	28-Oct-15			460.00	23.43%	460	0.13%	0.13%	460
AH.CN.TR2.1170	Welding of Pipe with Flange (12")	0.17%	I.D		20.00	20.00	29-Oct-15	29-Oct-15			603.00	30.72%	603	0.17%	0.17%	603
AH.CN.TR2.1180	100% Radiography of the Joint	0.06%	I.D		20.00	20.00	31-Oct-15	31-Oct-15			200.00	10.19%	200	0.06%	0.06%	200
AH.CN.TR2.1190	PWHT	0.06%	I.D		20.00	20.00	1-Nov-15	1-Nov-15			200.00	10.19%	200	0.06%	0.06%	200
AH.CN.TR2.1200	After Heat Treatment Radiography	0.06%	I.D		20.00	20.00	2-Nov-15	2-Nov-15			200.00	10.19%			0.06%	200
AH.CN.TR2.1210	Joint Cutting and Rewelding if any crack found in Inspection	0.00%	-				3-Nov-15	7-Nov-15				0.00%				
AH.CN.TR2.1220	Ready for Dispatch at Site	0.00%	-				15-Nov-15	15-Nov-15				0.00%				
AH.CN.TR2.1230	Sand Blasting and Painting of Spool	0.09%	SqM				8-Nov-15	14-Nov-15			300.00	15.28%				
P-3557-16"-CA2D (16-I.D)		0.45%					1-Nov-15	19-Nov-15			1570.00	7.66%	0	0.00%	0.42%	1470
AH.CN.TR2.1240	Fabrication of Pipe	0.16%	I.D		16.00	16.00	1-Nov-15	2-Nov-15			550.00	35.03%			0.16%	550
AH.CN.TR2.1250	Welding of Pipe with Flange (12")	0.18%	I.D		16.00	16.00	3-Nov-15	3-Nov-15			620.00	39.49%			0.18%	620
AH.CN.TR2.1260	100% Radiography of the Joint	0.03%	I.D		16.00	16.00	4-Nov-15	4-Nov-15			100.00	6.37%			0.03%	100
AH.CN.TR2.1270	PWHT	0.03%	I.D		16.00	16.00	5-Nov-15	5-Nov-15			100.00	6.37%			0.03%	100
AH.CN.TR2.1280	After Heat Treatment Radiography	0.03%	I.D		16.00	16.00	7-Nov-15	7-Nov-15			100.00	6.37%			0.03%	100
AH.CN.TR2.1290	Joint Cutting and Rewelding if any crack found in Inspection	0.00%	-				8-Nov-15	11-Nov-15				0.00%				
AH.CN.TR2.1300	Ready for Dispatch at Site	0.00%	-				19-Nov-15	19-Nov-15				0.00%				
AH.CN.TR2.1310	Sand Blasting and Painting of Spool	0.03%	SqM				12-Nov-15	18-Nov-15			100.00	6.37%				
P-3520-10"-DB2D (10-I.D)		0.28%					5-Nov-15	24-Nov-15			981.00	4.79%	0	0.00%	0.25%	881
AH.CN.TR2.1320	Fabrication of Pipe	0.04%	I.D		10.00	10.00	5-Nov-15	7-Nov-15			150.00	15.29%			0.04%	150
AH.CN.TR2.1330	Welding of Pipe with Flange (12")	0.08%	I.D		10.00	10.00	8-Nov-15	8-Nov-15			281.00	28.64%			0.08%	281

											Document Title:		Construction Register			
											Rev:		1			
											Date:		30-Oct-15			
Activity ID	Activity Name	WTG % L3	UoM	UNIT RATE MHS/UNIT QTY.	PLANNED QUANTITY	ACHEIVED QUANTITY	REVISED START	REVISED FINISH	ACTUAL START	ACTUAL FINISH	TOTAL MANHOURS	PLANNED ACTIVITY WTG %	PLANNED MHS	PLANNED PROGRESS %	ACHIEVED PROGRESS %	ACTUAL MHS
AH.CN.TR2.1340	100% Radiography of the Joint	0.04%	I.D		10.00	10.00	9-Nov-15	9-Nov-15			150.00	15.29%			0.04%	150
AH.CN.TR2.1350	PWHT	0.04%	I.D		10.00	10.00	10-Nov-15	10-Nov-15			150.00	15.29%			0.04%	150
AH.CN.TR2.1360	After Heat Treatment Radiography	0.04%	I.D		10.00	10.00	11-Nov-15	11-Nov-15			150.00	15.29%			0.04%	150
AH.CN.TR2.1370	Joint Cutting and Rewelding if any crack found in Inspection	0.00%	-				12-Nov-15	16-Nov-15				0.00%				
AH.CN.TR2.1380	Ready for Dispatch at Site	0.00%	-				24-Nov-15	24-Nov-15				0.00%				
AH.CN.TR2.1390	Sand Blasting and Painting of Spool	0.03%	SqM				17-Nov-15	23-Nov-15			100.00	10.19%				
P-3716-12"-CC2D (12-I.D)		0.33%					10-Nov-15	29-Nov-15			1176.00	5.74%	0	0.00%	0.31%	1076
AH.CN.TR2.1400	Fabrication of Pipe	0.08%	I.D		12.00	12.00	10-Nov-15	11-Nov-15			276.00	23.47%			0.08%	276
AH.CN.TR2.1410	Welding of Pipe with Flange (12")	0.10%	I.D		12.00	12.00	12-Nov-15	12-Nov-15			350.00	29.76%			0.10%	350
AH.CN.TR2.1420	100% Radiography of the Joint	0.04%	I.D		12.00	12.00	14-Nov-15	14-Nov-15			150.00	12.76%			0.04%	150
AH.CN.TR2.1430	PWHT	0.04%	I.D		12.00	12.00	15-Nov-15	15-Nov-15			150.00	12.76%			0.04%	150
AH.CN.TR2.1440	After Heat Treatment Radiography	0.04%	I.D		12.00	12.00	16-Nov-15	16-Nov-15			150.00	12.76%			0.04%	150
AH.CN.TR2.1450	Joint Cutting and Rewelding if any crack found in Inspection	0.00%	-				17-Nov-15	21-Nov-15				0.00%				
AH.CN.TR2.1460	Ready for Dispatch at Site	0.00%	-				29-Nov-15	29-Nov-15				0.00%				
AH.CN.TR2.1470	Sand Blasting and Painting of Spool	0.03%	SqM				22-Nov-15	28-Nov-15			100.00	8.50%				
P-3631-12"-DB2D (28.25-I.D)		0.71%					15-Nov-15	14-Dec-15			2500.00	12.20%	0	0.00%	0.63%	2200
AH.CN.TR2.1480	Fabrication of Pipe	0.14%	I.D		28.25	28.25	15-Nov-15	17-Nov-15			500.00	20.00%			0.14%	500
AH.CN.TR2.1490	Welding of Pipe with Flange	0.14%	I.D		26	26	18-Nov-15	18-Nov-15			500.00	20.00%			0.14%	500
AH.CN.TR2.1500	Welding of Weldolet with Elbow	0.03%	I.D		0.75	0.75	19-Nov-15	19-Nov-15			100.00	4.00%			0.03%	100
AH.CN.TR2.1510	Welding of Elbow with Nipple	0.03%	I.D		0.75	0.75	19-Nov-15	19-Nov-15			100.00	4.00%			0.03%	100
AH.CN.TR2.1520	Welding of Nipple with Flange	0.03%	I.D		0.75	0.75	19-Nov-15	19-Nov-15			100.00	4.00%			0.03%	100
AH.CN.TR2.1530	100% Radiography of the Joint	0.09%	I.D		28.25	28.25	21-Nov-15	22-Nov-15			300.00	12.00%			0.09%	300
AH.CN.TR2.1540	PWHT	0.09%	I.D		28.25	28.25	23-Nov-15	24-Nov-15			300.00	12.00%			0.09%	300
AH.CN.TR2.1550	After Heat Treatment Radiography	0.09%	I.D		28.25	28.25	25-Nov-15	26-Nov-15			300.00	12.00%			0.09%	300
AH.CN.TR2.1560	Joint Cutting and Rewelding if any crack found in Inspection	0.00%	-				28-Nov-15	3-Dec-15				0.00%				
AH.CN.TR2.1570	Ready for Dispatch at Site	0.00%	-				14-Dec-15	14-Dec-15				0.00%				
AH.CN.TR2.1580	Sand Blasting and Painting of Spool	0.09%	SqM				5-Dec-15	13-Dec-15			300.00	12.00%				
CIVIL FOUNDATION WORKS		20.81%					1-Sep-15	20-Feb-16			73104.45	46.24%	18723.60	5.34%	15.19%	54024.60
Buffer Vessel Foundation		15.89%					1-Sep-15	20-Feb-16			55798.20	76.33%	18723.60	5.34%	15.19%	54024.60
Foundation for SDV 1438		0.64%					1-Sep-15	4-Oct-15			2243.40	4.02%	2243	0.63%	0.64%	2243
AH.CN.TR1.2000	Excavation	0.11%	CuM		3.61	3.61	15-Jul-15	20-Jul-15			400.00	17.83%	400	0.11%	0.11%	400
AH.CN.TR1.2010	Blinding / Screeding	0.04%	CuM		0.13	0.13	20-Jul-15	22-Jul-15			150.00	6.69%	150	0.04%	0.04%	150
AH.CN.TR1.2020	Formwork	0.04%	SqM		4.18	4.18	22-Jul-15	23-Jul-15			150.00	6.69%	150	0.04%	0.04%	150
AH.CN.TR1.2030	Rebar	0.26%	TON		0.11	0.11	23-Jul-15	25-Jul-15			900.00	40.12%	900	0.26%	0.26%	900
AH.CN.TR1.2040	Concrete	0.06%	CuM		1.15	1.15	25-Jul-15	26-Jul-15			200.00	8.92%	200	0.06%	0.06%	200
AH.CN.TR1.2050	Curing	0.00%	-				26-Jul-15	26-Jul-15			0.00	0.00%	0	0.00%		0
AH.CN.TR1.2060	Surface Protection	0.04%	SqM		5.02	5.02	27-Jul-15	27-Jul-15			143.40	6.39%	143	0.04%	0.04%	143
AH.CN.TR1.2070	Backfilling	0.09%	CuM		2.02	2.02	3-Oct-15	4-Oct-15			300.00	13.37%	300	0.09%	0.09%	300
Foundation for LCV 1183		0.64%					1-Sep-15	4-Oct-15			2243.40	4.02%	2243	0.64%	0.64%	2243
AH.CN.TR1.2080	Excavation	0.11%	CuM		3.61	3.61	15-Jul-15	16-Jul-15			400.00	17.83%	400	0.11%	0.11%	400.00
AH.CN.TR1.2090	Blinding / Screeding	0.04%	CuM		0.13	0.13	16-Jul-15	17-Jul-15			150.00	6.69%	150	0.04%	0.04%	150
AH.CN.TR1.2100	Formwork	0.04%	SqM		4.18	4.18	17-Jul-15	18-Jul-15			150.00	6.69%	150	0.04%	0.04%	150
AH.CN.TR1.2110	Rebar	0.26%	TON		0.11	0.11	19-Jul-15	20-Jul-15			900.00	40.12%	900	0.26%	0.26%	900
AH.CN.TR1.2120	Concrete	0.06%	CuM		1.15	1.15	20-Jul-15	24-Jul-15			200.00	8.92%	200	0.06%	0.06%	200
AH.CN.TR1.2130	Curing	0.00%	-				24-Jul-15	25-Jul-15			0.00	0.00%	0	0.00%		0
AH.CN.TR1.2140	Surface Protection	0.04%	SqM		5.02	5.02	25-Jul-15	26-Jul-15			143.40	6.39%	143	0.04%	0.04%	143
AH.CN.TR1.2150	Backfilling	0.09%	CuM		2.02	2.02	25-Jul-15	1-Aug-15			300.00	13.37%	300	0.09%	0.09%	300
Foundation for SDV 1201		0.64%					1-Sep-15	4-Oct-15			2243.40	4.02%	2243	0.64%	0.64%	2243
AH.CN.TR1.2160	Excavation	0.11%	CuM		3.61	3.61	1-Sep-15	3-Sep-15			400.00	17.83%	400	0.11%	0.11%	400.00
AH.CN.TR1.2170	Blinding / Screeding	0.04%	CuM		0.13	0.13	5-Sep-15	6-Sep-15			150.00	6.69%	150	0.04%	0.04%	150
AH.CN.TR1.2180	Formwork	0.04%	SqM		4.18	4.18	7-Sep-15	8-Sep-15			150.00	6.69%	150	0.04%	0.04%	150
AH.CN.TR1.2190	Rebar	0.26%	TON		0.11	0.11	9-Sep-15	10-Sep-15			900.00	40.12%	900	0.26%	0.26%	900
AH.CN.TR1.2200	Concrete	0.06%	CuM		1.15	1.15	12-Sep-15	13-Sep-15			200.00	8.92%	200	0.06%	0.06%	200
AH.CN.TR1.2210	Curing	0.00%	-				14-Sep-15	29-Sep-15			0.00	0.00%	0	0.00%		0
AH.CN.TR1.2220	Surface Protection	0.04%	SqM		5.02	5.02	30-Sep-15	1-Oct-15			143.40	6.39%	143	0.04%	0.04%	143

											Document Title:		Construction Register			
											Rev:		1			
											Date:		30-Oct-15			
Activity ID	Activity Name	WTG % L3	UoM	UNIT RATE MHS/UNIT QTY.	PLANNED QUANTITY	ACHEIVED QUANTITY	REVISED START	REVISED FINISH	ACTUAL START	ACTUAL FINISH	TOTAL MANHOURS	PLANNED ACTIVITY WTG %	PLANNED MHS	PLANNED PROGRESS %	ACHIEVED PROGRESS %	ACTUAL MHS
AH.CN.TR1.2230	Backfilling	0.09%	CuM		2.02	2.02	3-Oct-15	4-Oct-15			300.00	13.37%	300	0.09%	0.09%	300
Foundation for SDV 1046		0.64%					1-Sep-15	4-Oct-15			2243.40	4.02%	2243	0.64%	0.53%	2243
AH.CN.TR1.2240	Excavation	0.11%	CuM		5.00	3.61	1-Sep-15	3-Sep-15			400.00	17.83%	400	0.11%	0.08%	400
AH.CN.TR1.2250	Blinding / Screeding	0.04%	CuM		0.21	0.13	5-Sep-15	6-Sep-15			150.00	6.69%	150	0.04%	0.03%	150
AH.CN.TR1.2260	Formwork	0.04%	SqM		5.32	4.18	7-Sep-15	8-Sep-15			150.00	6.69%	150	0.04%	0.03%	150
AH.CN.TR1.2270	Rebar	0.26%	TON		0.11	0.11	9-Sep-15	10-Sep-15			900.00	40.12%	900	0.26%	0.26%	900
AH.CN.TR1.2280	Concrete	0.06%	CuM		1.86	1.15	12-Sep-15	13-Sep-15			200.00	8.92%	200	0.06%	0.04%	200
AH.CN.TR1.2290	Curing	0.00%	-				14-Sep-15	29-Sep-15			0.00	0.00%	0	0.00%		0
AH.CN.TR1.2300	Surface Protection	0.04%	SqM		6.38	5.02	30-Sep-15	1-Oct-15			143.40	6.39%	143	0.04%	0.03%	143
AH.CN.TR1.2310	Backfilling	0.09%	CuM		2.80	2.02	3-Oct-15	4-Oct-15			300.00	13.37%	300	0.09%	0.06%	300
Foundation for SDV 1107 B		0.64%					5-Oct-15	7-Nov-15			2243.40	4.02%	1650	0.49%	0.64%	2243
AH.CN.TR1.2320	Excavation	0.11%	CuM		3.61	3.61	5-Oct-15	7-Oct-15			400.00	17.83%	400	0.11%	0.11%	400
AH.CN.TR1.2330	Blinding / Screeding	0.04%	CuM		0.13	0.13	8-Oct-15	10-Oct-15			150.00	6.69%	150	0.04%	0.04%	150
AH.CN.TR1.2340	Formwork	0.04%	SqM		4.18	4.18	11-Oct-15	12-Oct-15			150.00	6.69%	150	0.04%	0.04%	150
AH.CN.TR1.2350	Rebar	0.26%	TON		0.11	0.11	13-Oct-15	14-Oct-15			900.00	40.12%	750	0.23%	0.26%	900
AH.CN.TR1.2360	Concrete	0.06%	CuM		1.15	1.15	15-Oct-15	17-Oct-15			200.00	8.92%	200	0.06%	0.06%	200
AH.CN.TR1.2370	Curing	0.00%	-				18-Oct-15	2-Nov-15			0.00	0.00%				0
AH.CN.TR1.2380	Surface Protection	0.04%	SqM		5.02	5.02	3-Nov-15	4-Nov-15			143.40	6.39%			0.04%	143
AH.CN.TR1.2390	Backfilling	0.09%	CuM		2.02	2.02	5-Nov-15	7-Nov-15			300.00	13.37%			0.09%	300
Foundation for SDV 1083		0.64%					5-Oct-15	7-Nov-15			2243.40	4.02%	1800	0.52%	0.53%	2243
AH.CN.TR1.2400	Excavation	0.11%	CuM		5.00	3.61	5-Oct-15	7-Oct-15			400.00	17.83%	400	0.11%	0.08%	400
AH.CN.TR1.2410	Blinding / Screeding	0.04%	CuM		0.21	0.13	8-Oct-15	10-Oct-15			150.00	6.69%	150	0.04%	0.03%	150
AH.CN.TR1.2420	Formwork	0.04%	SqM		5.32	4.18	11-Oct-15	12-Oct-15			150.00	6.69%	150	0.04%	0.03%	150
AH.CN.TR1.2430	Rebar	0.26%	TON		0.11	0.11	13-Oct-15	14-Oct-15			900.00	40.12%	900	0.26%	0.26%	900
AH.CN.TR1.2440	Concrete	0.06%	CuM		1.86	1.15	15-Oct-15	17-Oct-15			200.00	8.92%	200	0.06%	0.04%	200
AH.CN.TR1.2450	Curing	0.00%	-				18-Oct-15	2-Nov-15			0.00	0.00%				0
AH.CN.TR1.2460	Surface Protection	0.04%	SqM		6.38	5.02	3-Nov-15	4-Nov-15			143.40	6.39%			0.03%	143
AH.CN.TR1.2470	Backfilling	0.09%	CuM		2.80	2.02	5-Nov-15	7-Nov-15			300.00	13.37%			0.06%	300
Foundation for SDV 1451		0.64%					8-Nov-15	10-Dec-15			2243.40	4.02%	0	0.00%	0.64%	2243
AH.CN.TR1.2480	Excavation	0.11%	CuM		3.61	3.61	8-Nov-15	10-Nov-15			400.00	17.83%			0.11%	400
AH.CN.TR1.2490	Blinding / Screeding	0.04%	CuM		0.13	0.13	11-Nov-15	12-Nov-15			150.00	6.69%			0.04%	150
AH.CN.TR1.2500	Formwork	0.04%	SqM		4.18	4.18	14-Nov-15	15-Nov-15			150.00	6.69%			0.04%	150
AH.CN.TR1.2510	Rebar	0.26%	TON		0.11	0.11	16-Nov-15	17-Nov-15			900.00	40.12%			0.26%	900
AH.CN.TR1.2520	Concrete	0.06%	CuM		1.15	1.15	18-Nov-15	19-Nov-15			200.00	8.92%			0.06%	200
AH.CN.TR1.2530	Curing	0.00%	-				21-Nov-15	6-Dec-15			0.00	0.00%				0
AH.CN.TR1.2540	Surface Protection	0.04%	SqM		5.02	5.02	7-Dec-15	8-Dec-15			143.40	6.39%			0.04%	143
AH.CN.TR1.2550	Backfilling	0.09%	CuM		2.02	2.02	9-Dec-15	10-Dec-15			300.00	13.37%			0.09%	300
Foundation for SDV 1041		0.64%					8-Nov-15	10-Dec-15			2243.40	4.02%	0	0.00%	0.64%	2243
AH.CN.TR1.2560	Excavation	0.11%	CuM		5.00	5.00	8-Nov-15	10-Nov-15			400.00	17.83%			0.11%	400
AH.CN.TR1.2570	Blinding / Screeding	0.04%	CuM		0.21	0.21	11-Nov-15	12-Nov-15			150.00	6.69%			0.04%	150
AH.CN.TR1.2580	Formwork	0.04%	SqM		5.32	5.32	14-Nov-15	15-Nov-15			150.00	6.69%			0.04%	150
AH.CN.TR1.2590	Rebar	0.26%	TON		0.11	0.11	16-Nov-15	17-Nov-15			900.00	40.12%			0.26%	900
AH.CN.TR1.2600	Concrete	0.06%	CuM		1.86	1.86	18-Nov-15	19-Nov-15			200.00	8.92%			0.06%	200
AH.CN.TR1.2610	Curing	0.00%	-				21-Nov-15	6-Dec-15			0.00	0.00%				0
AH.CN.TR1.2620	Surface Protection	0.04%	SqM		6.38	6.38	7-Dec-15	8-Dec-15			143.40	6.39%			0.04%	143
AH.CN.TR1.2630	Backfilling	0.09%	CuM		2.80	2.80	9-Dec-15	10-Dec-15			300.00	13.37%			0.09%	300
Foundation for SDV 1003		0.64%					12-Dec-15	13-Jan-16			2243.40	4.02%	0	0.00%	0.64%	2243
AH.CN.TR1.2640	Excavation	0.11%	CuM		5.00	5.00	12-Dec-15	14-Dec-15			400.00	17.83%			0.11%	400
AH.CN.TR1.2650	Blinding / Screeding	0.04%	CuM		0.21	0.21	15-Dec-15	16-Dec-15			150.00	6.69%			0.04%	150
AH.CN.TR1.2660	Formwork	0.04%	SqM		5.32	5.32	17-Dec-15	19-Dec-15			150.00	6.69%			0.04%	150
AH.CN.TR1.2670	Rebar	0.26%	TON		0.11	0.11	20-Dec-15	21-Dec-15			900.00	40.12%			0.26%	900
AH.CN.TR1.2680	Concrete	0.06%	CuM		1.86	1.86	22-Dec-15	23-Dec-15			200.00	8.92%			0.06%	200
AH.CN.TR1.2690	Curing	0.00%	-				24-Dec-15	9-Jan-16			0.00	0.00%				0
AH.CN.TR1.2700	Surface Protection	0.04%	SqM		6.38	6.38	10-Jan-16	11-Jan-16			143.40	6.39%			0.04%	143
AH.CN.TR1.2710	Backfilling	0.09%	CuM		2.80	2.80	12-Jan-16	13-Jan-16			300.00	13.37%			0.09%	300

											Document Title:		Construction Register			
											Rev:		1			
											Date:		30-Oct-15			
Activity ID	Activity Name	WTG % L3	UoM	UNIT RATE MHS/UNIT QTY.	PLANNED QUANTITY	ACHEIVED QUANTITY	REVISED START	REVISED FINISH	ACTUAL START	ACTUAL FINISH	TOTAL MANHOURS	PLANNED ACTIVITY WTG %	PLANNED MHS	PLANNED PROGRESS %	ACHIEVED PROGRESS %	ACTUAL MHS
Foundation for SDV 1184		0.72%					12-Dec-15	13-Jan-16			2543.40	4.56%	0	0.00%	0.72%	2543
AH.CN.TR1.2720	Excavation	0.17%	CuM		3.61	3.61	12-Dec-15	14-Dec-15			600.00	23.59%			0.17%	600
AH.CN.TR1.2730	Blinding / Screeding	0.04%	CuM		0.13	0.13	15-Dec-15	16-Dec-15			150.00	5.90%			0.04%	150
AH.CN.TR1.2740	Formwork	0.04%	SqM		4.18	4.18	17-Dec-15	19-Dec-15			150.00	5.90%			0.04%	150
AH.CN.TR1.2750	Rebar	0.28%	TON		0.11	0.11	20-Dec-15	21-Dec-15			1000.00	39.32%			0.28%	1000
AH.CN.TR1.2760	Concrete	0.06%	CuM		1.15	1.15	22-Dec-15	23-Dec-15			200.00	7.86%			0.06%	200
AH.CN.TR1.2770	Curing	0.00%	-				24-Dec-15	9-Jan-16			0.00	0.00%				0
AH.CN.TR1.2780	Surface Protection	0.04%	SqM		5.02	5.02	10-Jan-16	11-Jan-16			143.40	5.64%			0.04%	143
AH.CN.TR1.2790	Backfilling	0.09%	CuM		2.02	2.02	12-Jan-16	13-Jan-16			300.00	11.80%			0.09%	300
Foundation for SDV 2003		0.72%					5-Oct-15	7-Nov-15			2543.40	4.56%	2100	0.59%	0.72%	2543
AH.CN.TR2.2720	Excavation	0.17%	CuM		5.00	5.00	5-Oct-15	7-Oct-15			600.00	23.59%	600	0.17%	0.17%	600
AH.CN.TR2.2730	Blinding / Screeding	0.04%	CuM		0.21	0.21	8-Oct-15	10-Oct-15			150.00	5.90%	150	0.04%	0.04%	150
AH.CN.TR2.2740	Formwork	0.04%	SqM		5.32	5.32	11-Oct-15	12-Oct-15			150.00	5.90%	150	0.04%	0.04%	150
AH.CN.TR2.2750	Rebar	0.28%	TON		0.11	0.11	13-Oct-15	14-Oct-15			1000.00	39.32%	1000	0.28%	0.28%	1000
AH.CN.TR2.2760	Concrete	0.06%	CuM		1.86	1.86	15-Oct-15	17-Oct-15			200.00	7.86%	200	0.06%	0.06%	200
AH.CN.TR2.2770	Curing	0.00%	-				18-Oct-15	2-Nov-15			0.00	0.00%				
AH.CN.TR2.2780	Surface Protection	0.04%	SqM		6.38	6.38	3-Nov-15	4-Nov-15			143.40	5.64%			0.04%	143
AH.CN.TR2.2790	Backfilling	0.09%	CuM		2.80	2.80	5-Nov-15	7-Nov-15			300.00	11.80%			0.09%	300
Foundation for SDV 2184		0.72%					5-Oct-15	7-Nov-15			2543.40	4.56%	2100	0.60%	0.72%	2543
AH.CN.TR2.2640	Excavation	0.17%	CuM		3.61	3.61	5-Oct-15	7-Oct-15			600.00	23.59%	600	0.17%	0.17%	600
AH.CN.TR2.2650	Blinding / Screeding	0.04%	CuM		0.13	0.13	8-Oct-15	10-Oct-15			150.00	5.90%	150	0.04%	0.04%	150
AH.CN.TR2.2660	Formwork	0.04%	SqM		4.18	4.18	11-Oct-15	12-Oct-15			150.00	5.90%	150	0.04%	0.04%	150
AH.CN.TR2.2670	Rebar	0.28%	TON		0.11	0.11	13-Oct-15	14-Oct-15			1000.00	39.32%	1000	0.28%	0.28%	1000
AH.CN.TR2.2680	Concrete	0.06%	CuM		1.15	1.15	15-Oct-15	17-Oct-15			200.00	7.86%	200	0.06%	0.06%	200
AH.CN.TR2.2690	Curing	0.00%	-				18-Oct-15	2-Nov-15			0.00	0.00%				
AH.CN.TR2.2700	Surface Protection	0.04%	SqM		5.02	5.02	3-Nov-15	4-Nov-15			143.40	5.64%			0.04%	143
AH.CN.TR2.2710	Backfilling	0.09%	CuM		2.02	2.02	5-Nov-15	7-Nov-15			300.00	11.80%			0.09%	300
Foundation for SDV 2183		0.72%					5-Oct-15	7-Nov-15			2543.40	4.56%	2100	0.60%	0.72%	2543
AH.CN.TR2.2800	Excavation	0.17%	CuM		3.61	3.61	5-Oct-15	7-Oct-15			600.00	23.59%	600	0.17%	0.17%	600
AH.CN.TR2.2810	Blinding / Screeding	0.04%	CuM		0.13	0.13	8-Oct-15	10-Oct-15			150.00	5.90%	150	0.04%	0.04%	150
AH.CN.TR2.2820	Formwork	0.04%	SqM		4.18	4.18	11-Oct-15	12-Oct-15			150.00	5.90%	150	0.04%	0.04%	150
AH.CN.TR2.2830	Rebar	0.28%	TON		0.11	0.11	13-Oct-15	14-Oct-15			1000.00	39.32%	1000	0.28%	0.28%	1000
AH.CN.TR2.2840	Concrete	0.06%	CuM		1.15	1.15	15-Oct-15	17-Oct-15			200.00	7.86%	200	0.06%	0.06%	200
AH.CN.TR2.2850	Curing	0.00%	-				18-Oct-15	2-Nov-15			0.00	0.00%				
AH.CN.TR2.2860	Surface Protection	0.04%	SqM		5.02	5.02	3-Nov-15	4-Nov-15			143.40	5.64%			0.04%	143
AH.CN.TR2.2870	Backfilling	0.09%	CuM		2.02	2.02	5-Nov-15	7-Nov-15			300.00	11.80%			0.09%	300
Foundation for SDV 2041		0.72%					8-Nov-15	7-Dec-15			2543.40	4.56%			0.72%	2543
AH.CN.TR2.2960	Excavation	0.17%	CuM		5.00	5.00	8-Nov-15	10-Nov-15			600.00	23.59%			0.17%	600
AH.CN.TR2.2970	Blinding / Screeding	0.04%	CuM		0.21	0.21	8-Nov-15	9-Nov-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2980	Formwork	0.04%	SqM		5.32	5.32	10-Nov-15	11-Nov-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2990	Rebar	0.28%	TON		0.11	0.11	12-Nov-15	14-Nov-15			1000.00	39.32%			0.28%	1000
AH.CN.TR2.3000	Concrete	0.06%	CuM		1.86	1.86	15-Nov-15	16-Nov-15			200.00	7.86%			0.06%	200
AH.CN.TR2.3010	Curing	0.00%	-				17-Nov-15	2-Dec-15			0.00	0.00%				
AH.CN.TR2.3020	Surface Protection	0.04%	SqM		6.38	6.38	3-Dec-15	5-Dec-15			143.40	5.64%			0.04%	143
AH.CN.TR2.3030	Backfilling	0.09%	CuM		2.80	2.80	6-Dec-15	7-Dec-15			300.00	11.80%			0.09%	300
Foundation for SDV 2439		0.72%					8-Nov-15	10-Dec-15			2543.40	4.56%			0.72%	2543
AH.CN.TR2.2880	Excavation	0.17%	CuM		3.61	3.61	8-Nov-15	10-Nov-15			600.00	23.59%			0.17%	600
AH.CN.TR2.2890	Blinding / Screeding	0.04%	CuM		0.13	0.13	11-Nov-15	12-Nov-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2900	Formwork	0.04%	SqM		4.18	4.18	14-Nov-15	15-Nov-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2910	Rebar	0.28%	TON		0.11	0.11	16-Nov-15	17-Nov-15			1000.00	39.32%			0.28%	1000
AH.CN.TR2.2920	Concrete	0.06%	CuM		1.15	1.15	18-Nov-15	19-Nov-15			200.00	7.86%			0.06%	200
AH.CN.TR2.2930	Curing	0.00%	-				21-Nov-15	6-Dec-15			0.00	0.00%				
AH.CN.TR2.2940	Surface Protection	0.04%	SqM		5.02	5.02	7-Dec-15	8-Dec-15			143.40	5.64%			0.04%	143
AH.CN.TR2.2950	Backfilling	0.09%	CuM		2.02	2.02	9-Dec-15	10-Dec-15			300.00	11.80%			0.09%	300
Foundation for SDV 2451		0.72%					11-Nov-15	14-Dec-15			2543.40	4.56%			0.72%	2543

											Document Title:		Construction Register			
											Rev:		1			
											Date:		30-Oct-15			
Activity ID	Activity Name	WTG % L3	UoM	UNIT RATE MHS/UNIT QTY.	PLANNED QUANTITY	ACHEIVED QUANTITY	REVISED START	REVISED FINISH	ACTUAL START	ACTUAL FINISH	TOTAL MANHOURS	PLANNED ACTIVITY WTG %	PLANNED MHS	PLANNED PROGRESS %	ACHIEVED PROGRESS %	ACTUAL MHS
AH.CN.TR2.2320	Excavation	0.17%	CuM		3.61	3.61	11-Nov-15	14-Nov-15			600.00	23.59%			0.17%	600
AH.CN.TR2.2330	Blinding / Screeding	0.04%	CuM		0.13	0.13	15-Nov-15	16-Nov-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2340	Formwork	0.04%	SqM		4.18	4.18	17-Nov-15	18-Nov-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2350	Rebar	0.28%	TON		0.11	0.11	19-Nov-15	21-Nov-15			1000.00	39.32%			0.28%	1000
AH.CN.TR2.2360	Concrete	0.06%	CuM		1.15	1.15	22-Nov-15	23-Nov-15			200.00	7.86%			0.06%	200
AH.CN.TR2.2370	Curing	0.00%	-				24-Nov-15	9-Dec-15			0.00	0.00%				
AH.CN.TR2.2380	Surface Protection	0.04%	SqM		5.02	5.02	10-Dec-15	12-Dec-15			143.40	5.64%			0.04%	143
AH.CN.TR2.2390	Backfilling	0.09%	CuM		2.02	2.02	13-Dec-15	14-Dec-15			300.00	11.80%			0.09%	300
Foundation for SDV 2107 B		0.72%					15-Dec-15	17-Jan-16			2543.40	4.56%			0.72%	2543
AH.CN.TR2.2160	Excavation	0.17%	CuM		3.61	3.61	15-Dec-15	17-Dec-15			600.00	23.59%			0.17%	600
AH.CN.TR2.2170	Blinding / Screeding	0.04%	CuM		0.13	0.13	19-Dec-15	20-Dec-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2180	Formwork	0.04%	SqM		4.18	4.18	21-Dec-15	22-Dec-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2190	Rebar	0.28%	TON		0.11	0.11	23-Dec-15	23-Dec-15			1000.00	39.32%			0.28%	1000
AH.CN.TR2.2200	Concrete	0.06%	CuM		1.15	1.15	26-Dec-15	27-Dec-15			200.00	7.86%			0.06%	200
AH.CN.TR2.2210	Curing	0.00%	-				28-Dec-15	12-Jan-16			0.00	0.00%				
AH.CN.TR2.2220	Surface Protection	0.04%	SqM		5.02	5.02	13-Jan-16	14-Jan-16			143.40	5.64%			0.04%	143
AH.CN.TR2.2230	Backfilling	0.09%	CuM		2.02	2.02	16-Jan-16	17-Jan-16			300.00	11.80%			0.09%	300
Foundation for SDV 2438		0.72%					15-Dec-15	17-Jan-16			2543.40	4.56%			0.72%	2543
AH.CN.TR2.2480	Excavation	0.17%	CuM		3.61	3.61	15-Dec-15	17-Dec-15			600.00	23.59%			0.17%	600
AH.CN.TR2.2490	Blinding / Screeding	0.04%	CuM		0.13	0.13	19-Dec-15	20-Dec-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2500	Formwork	0.04%	SqM		4.18	4.18	21-Dec-15	22-Dec-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2510	Rebar	0.28%	TON		0.11	0.11	23-Dec-15	24-Dec-15			1000.00	39.32%			0.28%	1000
AH.CN.TR2.2520	Concrete	0.06%	CuM		1.15	1.15	26-Dec-15	27-Dec-15			200.00	7.86%			0.06%	200
AH.CN.TR2.2530	Curing	0.00%	-				28-Dec-15	12-Jan-16			0.00	0.00%				
AH.CN.TR2.2540	Surface Protection	0.04%	SqM		5.02	5.02	13-Jan-16	14-Jan-16			143.40	5.64%			0.04%	143
AH.CN.TR2.2550	Backfilling	0.09%	CuM		2.02	2.02	16-Jan-16	17-Jan-16			300.00	11.80%			0.09%	300
Foundation for SDV 2470		0.72%					15-Dec-15	17-Jan-16			2543.40	4.56%			0.60%	2100
AH.CN.TR2.2560	Excavation	0.17%	CuM		3.61	3.61	15-Dec-15	17-Dec-15			600.00	23.59%			0.17%	600
AH.CN.TR2.2570	Blinding / Screeding	0.04%	CuM		0.13	0.13	19-Dec-15	20-Dec-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2580	Formwork	0.04%	SqM		4.18	4.18	21-Dec-15	22-Dec-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2590	Rebar	0.28%	TON		0.11	0.11	23-Dec-15	24-Dec-15			1000.00	39.32%			0.28%	1000
AH.CN.TR2.2600	Concrete	0.06%	CuM		1.15	1.15	26-Dec-15	27-Dec-15			200.00	7.86%			0.06%	200
AH.CN.TR2.2610	Curing	0.00%	-				28-Dec-15	12-Jan-16			0.00	0.00%				
AH.CN.TR2.2620	Surface Protection	0.04%	SqM		5.02		13-Jan-16	14-Jan-16			143.40	5.64%			0.00%	
AH.CN.TR2.2630	Backfilling	0.09%	CuM		2.02		16-Jan-16	17-Jan-16			300.00	11.80%			0.00%	
Foundation for SDV 2083		0.72%					15-Dec-15	17-Jan-16			2543.40	4.56%			0.72%	2543
AH.CN.TR2.2400	Excavation	0.17%	CuM		5.00	5.00	15-Dec-15	17-Dec-15			600.00	23.59%			0.17%	600
AH.CN.TR2.2410	Blinding / Screeding	0.04%	CuM		0.21	0.21	19-Dec-15	20-Dec-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2420	Formwork	0.04%	SqM		5.32	5.32	21-Dec-15	22-Dec-15			150.00	5.90%			0.04%	150
AH.CN.TR2.2430	Rebar	0.28%	TON		0.11	0.11	23-Dec-15	24-Dec-15			1000.00	39.32%			0.28%	1000
AH.CN.TR2.2440	Concrete	0.06%	CuM		1.86	1.86	26-Dec-15	27-Dec-15			200.00	7.86%			0.06%	200
AH.CN.TR2.2450	Curing	0.00%	-				28-Dec-15	12-Jan-16			0.00	0.00%				
AH.CN.TR2.2460	Surface Protection	0.04%	SqM		6.38	6.38	13-Jan-16	14-Jan-16			143.40	5.64%			0.04%	143
AH.CN.TR2.2470	Backfilling	0.09%	CuM		2.80	2.80	16-Jan-16	17-Jan-16			300.00	11.80%			0.09%	300
Foundation for LCV 2183		0.72%					18-Jan-16	20-Feb-16			2543.40	4.56%			0.60%	2100
AH.CN.TR2.2000	Excavation	0.17%	CuM		3.61	3.61	18-Jan-16	20-Jan-16			600.00	23.59%			0.17%	600
AH.CN.TR2.2010	Blinding / Screeding	0.04%	CuM		0.13	0.13	21-Jan-16	23-Jan-16			150.00	5.90%			0.04%	150
AH.CN.TR2.2020	Formwork	0.04%	SqM		4.18	4.18	24-Jan-16	25-Jan-16			150.00	5.90%			0.04%	150
AH.CN.TR2.2030	Rebar	0.28%	TON		0.11	0.11	26-Jan-16	27-Jan-16			1000.00	39.32%			0.28%	1000
AH.CN.TR2.2040	Concrete	0.06%	CuM		1.15	1.15	28-Jan-16	30-Jan-16			200.00	7.86%			0.06%	200
AH.CN.TR2.2050	Curing	0.00%	-				31-Jan-16	15-Feb-16			0.00	0.00%				
AH.CN.TR2.2060	Surface Protection	0.04%	SqM		5.02		16-Feb-16	17-Feb-16			143.40	5.64%			0.00%	
AH.CN.TR2.2070	Backfilling	0.09%	CuM		2.02		18-Feb-16	20-Feb-16			300.00	11.80%			0.00%	
Foundation for SDV 2201		0.72%					18-Jan-16	20-Feb-16			2543.40	4.56%			0.60%	2100
AH.CN.TR2.2080	Excavation	0.17%	CuM		3.61	3.61	18-Jan-16	20-Jan-16			600.00	23.59%			0.17%	600

											Document Title:		Construction Register			
											Rev:		1			
											Date:		30-Oct-15			
Activity ID	Activity Name	WTG % L3	UoM	UNIT RATE MHS/UNIT QTY.	PLANNED QUANTITY	ACHEIVED QUANTITY	REVISED START	REVISED FINISH	ACTUAL START	ACTUAL FINISH	TOTAL MANHOURS	PLANNED ACTIVITY WTG %	PLANNED MHS	PLANNED PROGRESS %	ACHIEVED PROGRESS %	ACTUAL MHS
AH.CN.TR2.2090	Blinding / Screeding	0.04%	CuM		0.13	0.13	21-Jan-16	23-Jan-16			150.00	5.90%			0.04%	150
AH.CN.TR2.2100	Formwork	0.04%	SqM		4.18	4.18	24-Jan-16	25-Jan-16			150.00	5.90%			0.04%	150
AH.CN.TR2.2110	Rebar	0.28%	TON		0.11	0.11	26-Jan-16	27-Jan-16			1000.00	39.32%			0.28%	1000
AH.CN.TR2.2120	Concrete	0.06%	CuM		1.15	1.15	28-Jan-16	30-Jan-16			200.00	7.86%			0.06%	200
AH.CN.TR2.2130	Curing	0.00%	-				31-Jan-16	15-Feb-16			0.00	0.00%				
AH.CN.TR2.2140	Surface Protection	0.04%	SqM		5.02		16-Feb-16	17-Feb-16			143.40	5.64%			0.00%	
AH.CN.TR2.2150	Backfilling	0.09%	CuM		2.02		18-Feb-16	20-Feb-16			300.00	11.80%			0.00%	
Foundation for SDV 2046		0.72%					18-Jan-16	20-Feb-16			2543.40	4.56%			0.60%	2100
AH.CN.TR2.2240	Excavation	0.17%	CuM		5.00	5.00	18-Jan-16	20-Jan-16			600.00	23.59%			0.17%	600
AH.CN.TR2.2250	Blinding / Screeding	0.04%	CuM		0.21	0.21	21-Jan-16	23-Jan-16			150.00	5.90%			0.04%	150
AH.CN.TR2.2260	Formwork	0.04%	SqM		5.32	5.32	24-Jan-16	25-Jan-16			150.00	5.90%			0.04%	150
AH.CN.TR2.2270	Rebar	0.28%	TON		0.11	0.11	26-Jan-16	27-Jan-16			1000.00	39.32%			0.28%	1000
AH.CN.TR2.2280	Concrete	0.06%	CuM		1.86	1.86	28-Jan-16	30-Jan-16			200.00	7.86%			0.06%	200
AH.CN.TR2.2290	Curing	0.00%	-				31-Jan-16	15-Feb-16			0.00	0.00%				
AH.CN.TR2.2300	Surface Protection	0.04%	SqM		6.38		16-Feb-16	17-Feb-16			143.40	5.64%			0.00%	
AH.CN.TR2.2310	Backfilling	0.09%	CuM		2.80		18-Feb-16	20-Feb-16			300.00	11.80%			0.00%	
Junction Box Foundation		4.93%					21-Oct-15	20-Dec-15			17306.25	31.02%				
Foundation for 03-JD-1106-D		0.69%					21-Oct-15	15-Nov-15			2437.50	14.08%			0.00%	
AH.CN.TR1.2800	Excavation	0.17%	CuM		0.73		21-Oct-15	22-Oct-15			600.00	24.62%			0.00%	
AH.CN.TR1.2810	Blinding / Screeding	0.04%	CuM		0.01		24-Oct-15	24-Oct-15			150.00	6.15%			0.00%	
AH.CN.TR1.2820	Formwork	0.04%	SqM		0.72		25-Oct-15	25-Oct-15			150.00	6.15%			0.00%	
AH.CN.TR1.2830	Rebar	0.28%	TON		0.04		26-Oct-15	26-Oct-15			1000.00	41.03%			0.00%	
AH.CN.TR1.2840	Concrete	0.06%	CuM		0.05		27-Oct-15	27-Oct-15			200.00	8.21%			0.00%	
AH.CN.TR1.2850	Curing	0.00%	-				28-Oct-15	12-Nov-15			0.00	0.00%				
AH.CN.TR1.2860	Surface Protection	0.04%	SqM		0.86		14-Nov-15	14-Nov-15			137.50	5.64%			0.00%	
AH.CN.TR1.2870	Backfilling	0.06%	CuM		0.57		15-Nov-15	15-Nov-15			200.00	8.21%			0.00%	
Foundation for 03-JD-1108-D		0.69%					28-Oct-15	22-Nov-15			2437.50	14.08%			0.00%	
AH.CN.TR1.2880	Excavation	0.17%	CuM		0.73		28-Oct-15	29-Oct-15			600.00	24.62%			0.00%	
AH.CN.TR1.2890	Blinding / Screeding	0.04%	CuM		0.01		31-Oct-15	31-Oct-15			150.00	6.15%			0.00%	
AH.CN.TR1.2900	Formwork	0.04%	SqM		0.72		1-Nov-15	1-Nov-15			150.00	6.15%			0.00%	
AH.CN.TR1.2910	Rebar	0.28%	TON		0.04		2-Nov-15	2-Nov-15			1000.00	41.03%			0.00%	
AH.CN.TR1.2920	Concrete	0.06%	CuM		0.05		3-Nov-15	3-Nov-15			200.00	8.21%			0.00%	
AH.CN.TR1.2930	Curing	0.00%	-				4-Nov-15	19-Nov-15			0.00	0.00%				
AH.CN.TR1.2940	Surface Protection	0.04%	SqM		0.86		21-Nov-15	21-Nov-15			137.50	5.64%			0.00%	
AH.CN.TR1.2950	Backfilling	0.06%	CuM		0.57		22-Nov-15	22-Nov-15			200.00	8.21%			0.00%	
Foundation for 03-JD-1109-D/2103-D		1.39%					4-Nov-15	29-Nov-15			4875.00	28.17%			0.00%	
AH.CN.TR1.2960	Excavation	0.34%	CuM		1.46		4-Nov-15	5-Nov-15			1200.00	24.62%			0.00%	
AH.CN.TR1.2970	Blinding / Screeding	0.09%	CuM		0.02		7-Nov-15	7-Nov-15			300.00	6.15%			0.00%	
AH.CN.TR1.2980	Formwork	0.09%	SqM		1.44		8-Nov-15	8-Nov-15			300.00	6.15%			0.00%	
AH.CN.TR1.2990	Rebar	0.57%	TON		0.08		9-Nov-15	9-Nov-15			2000.00	41.03%			0.00%	
AH.CN.TR1.3000	Concrete	0.11%	CuM		0.11		10-Nov-15	10-Nov-15			400.00	8.21%			0.00%	
AH.CN.TR1.3010	Curing	0.00%	-				11-Nov-15	26-Nov-15			0.00	0.00%				
AH.CN.TR1.3020	Surface Protection	0.08%	SqM		1.73		28-Nov-15	28-Nov-15			275.00	5.64%			0.00%	
AH.CN.TR1.3030	Backfilling	0.11%	CuM		1.13		29-Nov-15	29-Nov-15			400.00	8.21%			0.00%	
Foundation for 03-JD-1107-D/2102-D		1.39%					11-Nov-15	6-Dec-15			4875.00	28.17%			0.00%	
AH.CN.TR1.3040	Excavation	0.34%	CuM		1.46		11-Nov-15	12-Nov-15			1200.00	24.62%			0.00%	
AH.CN.TR1.3050	Blinding / Screeding	0.09%	CuM		0.02		14-Nov-15	14-Nov-15			300.00	6.15%			0.00%	
AH.CN.TR1.3060	Formwork	0.09%	SqM		1.44		15-Nov-15	15-Nov-15			300.00	6.15%			0.00%	
AH.CN.TR1.3070	Rebar	0.57%	TON		0.08		16-Nov-15	16-Nov-15			2000.00	41.03%			0.00%	
AH.CN.TR1.3080	Concrete	0.11%	CuM		0.11		17-Nov-15	17-Nov-15			400.00	8.21%			0.00%	
AH.CN.TR1.3090	Curing	0.00%	-				18-Nov-15	3-Dec-15			0.00	0.00%				
AH.CN.TR1.3100	Surface Protection	0.08%	SqM		1.73		5-Dec-15	5-Dec-15			275.00	5.64%			0.00%	
AH.CN.TR1.3110	Backfilling	0.11%	CuM		1.13		6-Dec-15	6-Dec-15			400.00	8.21%			0.00%	
Foundation for 03-JD-2101-D		0.69%					18-Nov-15	13-Dec-15			2437.50	14.08%			0.00%	
AH.CN.TR1.3120	Excavation	0.17%	CuM		0.73		18-Nov-15	19-Nov-15			600.00	24.62%			0.00%	

											Document Title:		Construction Register			
											Rev:		1			
											Date:		30-Oct-15			
Activity ID	Activity Name	WTG % L3	UoM	UNIT RATE MHS/UNIT QTY.	PLANNED QUANTITY	ACHEIVED QUANTITY	REVISED START	REVISED FINISH	ACTUAL START	ACTUAL FINISH	TOTAL MANHOURS	PLANNED ACTIVITY WTG %	PLANNED MHS	PLANNED PROGRESS %	ACHIEVED PROGRESS %	ACTUAL MHS
AH.CN.TR1.3130	Blinding / Screeding	0.04%	CuM		0.01		21-Nov-15	21-Nov-15			150.00	6.15%			0.00%	
AH.CN.TR1.3140	Formwork	0.04%	SqM		0.72		22-Nov-15	22-Nov-15			150.00	6.15%			0.00%	
AH.CN.TR1.3150	Rebar	0.28%	TON		0.04		23-Nov-15	23-Nov-15			1000.00	41.03%			0.00%	
AH.CN.TR1.3160	Concrete	0.06%	CuM		0.05		24-Nov-15	24-Nov-15			200.00	8.21%			0.00%	
AH.CN.TR1.3170	Curing	0.00%	-				25-Nov-15	10-Dec-15			0.00	0.00%				
AH.CN.TR1.3180	Surface Protection	0.04%	SqM		0.86		12-Dec-15	12-Dec-15			137.50	5.64%			0.00%	
AH.CN.TR1.3190	Backfilling	0.06%	CuM		0.57		13-Dec-15	13-Dec-15			200.00	8.21%			0.00%	
Foundation for 03-JD-2104-D		0.07%					25-Nov-15	20-Dec-15			243.75	1.41%			0.00%	
AH.CN.TR1.3200	Excavation	0.02%	CuM		0.73		25-Nov-15	26-Nov-15			60.00	24.62%			0.00%	
AH.CN.TR1.3210	Blinding / Screeding	0.00%	CuM		0.01		28-Nov-15	28-Nov-15			15.00	6.15%			0.00%	
AH.CN.TR1.3220	Formwork	0.00%	SqM		0.72		29-Nov-15	29-Nov-15			15.00	6.15%			0.00%	
AH.CN.TR1.3230	Rebar	0.03%	TON		0.04		30-Nov-15	30-Nov-15			100.00	41.03%			0.00%	
AH.CN.TR1.3240	Concrete	0.01%	CuM		0.05		1-Dec-15	1-Dec-15			20.00	8.21%			0.00%	
AH.CN.TR1.3250	Curing	0.00%	-				2-Dec-15	17-Dec-15			0.00	0.00%				
AH.CN.TR1.3260	Surface Protection	0.00%	SqM		0.86		19-Dec-15	19-Dec-15			13.75	5.64%			0.00%	
AH.CN.TR1.3270	Backfilling	0.01%	CuM		0.57		20-Dec-15	20-Dec-15			20.00	8.21%			0.00%	
INSTRUMENTATION WORKS		9.82%					25-Oct-15	23-Mar-16			34500.00	21.82%				
Junction Box Installation		0.98%					16-Nov-15	31-Dec-15			3450.00	10.00%				
AH.CN.TR1.3500	Installation of 03-JD-1106-D	0.11%	Nos.		1		16-Nov-15	26-Nov-15			375.00	10.87%				
AH.CN.TR1.3510	Instalaltion of 03-JD-1108-D	0.11%	Nos.		1		23-Nov-15	3-Dec-15			375.00	10.87%				
AH.CN.TR1.3520	Instalaltion of 03-JD-1109-D/2103-D	0.28%	Nos.		2		30-Nov-15	16-Dec-15			1000.00	28.99%				
AH.CN.TR1.3530	Installation of 03-JD-1107-D/2102-D	0.28%	Nos.		2		7-Dec-15	23-Dec-15			1000.00	28.99%				
AH.CN.TR1.3540	Instalaltion of 03-JD-2101-D	0.10%	Nos.		1		14-Dec-15	24-Dec-15			350.00	10.14%				
AH.CN.TR1.3550	Instalaltion of 03-JD-2104-D	0.10%	Nos.		1		21-Dec-15	31-Dec-15			350.00	10.14%				
Primary Cable Laying		3.93%					23-Nov-15	8-Mar-16			13800.00	40.00%				
AH.CN.TR1.3560	Removal of Interlocking Tiles	0.21%	Nos.				23-Nov-15	3-Dec-15			750.00	5.43%				
AH.CN.TR1.3570	Removal of Existing Cable Trench Tiles	0.21%	Nos.				5-Dec-15	15-Dec-15			750.00	5.43%				
AH.CN.TR1.3580	Multi Core Cable Laying from 03-JD-1106-D to SS2 (55MTRS)	0.14%	MTRS		55		16-Dec-15	21-Dec-15			500.00	3.62%				
AH.CN.TR1.3590	Multi Core Cable Laying from 03-JD-1108-D to SS2 (140MTRS)	0.21%	MTRS		140		16-Dec-15	28-Dec-15			750.00	5.43%				
AH.CN.TR1.3600	Multi Core Cable Laying from 03-JD-1109-D to SS2 (212MTRS)	0.38%	MTRS		212		16-Dec-15	5-Jan-16			1350.00	9.78%				
AH.CN.TR1.3610	Multi Core Cable Laying from 03-JD-1107-D to SS2 (360MTRS)	0.57%	MTRS		360		16-Dec-15	13-Jan-16			2000.00	14.49%				
AH.CN.TR1.3620	Multi Core Cable Laying from 03-JD-2101-D to SS3 (80MTRS)	0.14%	MTRS		80		16-Dec-15	23-Dec-15			500.00	3.62%				
AH.CN.TR1.3630	Multi Core Cable Laying from 03-JD-2102-D to SS3 (360MTRS)	0.57%	MTRS		360		16-Dec-15	13-Jan-16			2000.00	14.49%				
AH.CN.TR1.3640	Multi Core Cable Laying from 03-JD-2103-D to SS3 (215MTRS)	0.38%	MTRS		215		16-Dec-15	5-Jan-16			1350.00	9.78%				
AH.CN.TR1.3650	Multi Core Cable Laying from 03-JD-2104-D to SS3 (160MTRS)	0.28%	MTRS		160		16-Dec-15	29-Dec-15			1000.00	7.25%				
AH.CN.TR1.3655	Cable Glanding and Terminations (157 Nos.)	0.23%	Nos.				30-Dec-15	21-Jan-16			800.00	5.80%				
AH.CN.TR1.3660	Cable Laying Inspection	0.00%	-				23-Jan-16	2-Feb-16				0.00%				
AH.CN.TR1.3670	Cable Laying Cold Loop Checking	0.16%	Nos.				3-Feb-16	14-Feb-16			550.00	3.99%				
AH.CN.TR1.3680	Reinstatement of Existing Cable Trench Tiles	0.21%	Nos.				15-Feb-16	25-Feb-16			750.00	5.43%				
AH.CN.TR1.3690	Reinstatement of Interlocking Tiles	0.21%	Nos.				27-Feb-16	8-Mar-16			750.00	5.43%				
Cable Tray Installation		1.47%					23-Nov-15	27-Dec-15			5175.00	15.00%				
AH.CN.TR1.3750	Installation of 50mm Cable Tray (800MTRS)	0.62%	MTRS		800		23-Nov-15	27-Dec-15			2175.00	42.03%				
AH.CN.TR1.3760	Installation of 100mm Cable Tray (200MTRS)	0.27%	MTRS		200		23-Nov-15	15-Dec-15			950.00	18.36%				
AH.CN.TR1.3770	Instalaltion of 150mm Cable Tray (240MTRS)	0.31%	MTRS		240		23-Nov-15	15-Dec-15			1100.00	21.26%				
AH.CN.TR1.3780	Installation of 300mm Cable Tray (200MTRS)	0.27%	MTRS		200		23-Nov-15	9-Dec-15			950.00	18.36%				
Pressure Switch Installation		0.98%					21-Nov-15	29-Feb-16			3450.00	10.00%				
AH.CN.TR1.3700	Instalaltion of Pressure Switch Stand for CAI Actuators (18)	0.19%	Nos.		18		21-Nov-15	3-Dec-15			650.00	18.84%				
AH.CN.TR1.3710	Instalaltion of Pressure Switch Stand for Existing Actuators (14)	0.19%	Nos.		14		5-Dec-15	15-Dec-15			650.00	18.84%				
AH.CN.TR1.3720	Installation of Pressure Switch for CAI Actuators (18)	0.10%	Nos.		18		16-Dec-15	7-Jan-16			350.00	10.14%				
AH.CN.TR1.3730	Installation of Pressure Switch for Existing Actuators (14)	0.10%	Nos.		14		9-Jan-16	25-Jan-16			350.00	10.14%				
AH.CN.TR1.3740	Secondary Cable Laying from PS to JB	0.41%	MTRS		500		26-Jan-16	29-Feb-16			1450.00	42.03%				
Tubing Installation		1.47%					26-Jan-16	23-Mar-16			5175.00	15.00%				
AH.CN.TR1.3790	Tubing Installation for ESD Valves and Actuators	0.90%	MTRS		50		26-Jan-16	29-Feb-16			3175.00	61.35%				
AH.CN.TR1.3800	Tubing Installation from PS to Buffer Vessel	0.57%	MTRS		50		1-Mar-16	23-Mar-16			2000.00	38.65%				
DCS System Modification Works		0.98%					25-Oct-15	4-Feb-16			3450.00	10.00%				

											Document Title:		Construction Register			
											Rev:		1			
											Date:		30-Oct-15			
Activity ID	Activity Name	WTG % L3	UoM	UNIT RATE MHS/UNIT QTY.	PLANNED QUANTITY	ACHEIVED QUANTITY	REVISED START	REVISED FINISH	ACTUAL START	ACTUAL FINISH	TOTAL MANHOURS	PLANNED ACTIVITY WTG %	PLANNED MHS	PLANNED PROGRESS %	ACHIEVED PROGRESS %	ACTUAL MHS
AH.CN.TR1.3810	Installation of I/O Cards 04 Nos.	0.41%	Nos.		4		25-Oct-15	29-Oct-15			1450.00	42.03%				
AH.CN.TR1.3820	Installation of FTA Cards 04 Nos.	0.14%	Nos.		4		31-Oct-15	4-Nov-15			500.00	14.49%				
AH.CN.TR1.3830	Installation of FTA Cables 04 Nos.	0.14%	Nos.		4		5-Nov-15	10-Nov-15			500.00	14.49%				
AH.CN.TR1.3840	Installation of Terminal Blocks	0.14%	Nos.				11-Nov-15	16-Nov-15			500.00	14.49%				
AH.CN.TR1.3850	Cold Loop Check	0.14%	Nos.				3-Feb-16	4-Feb-16			500.00	14.49%				
SCAFFOLDING WORKS		8.54%					1-Oct-15	23-Mar-16			30000.00	18.97%	0	0.00%		
Scaffolding Works		8.54%					1-Oct-15	23-Mar-16			30000.00	100.00%	0	0.00%		
AH.CN.TR1.3860	Scaffolding Works for Cable Tray Installation	4.27%	CuM				1-Oct-15	24-Oct-15			15000.00	50.00%				
AH.CN.TR1.3870	Scaffolding Works for Cable Laying	2.14%	CuM				13-Oct-15	4-Nov-15			7500.00	25.00%				
AH.CN.TR1.3880	Scaffolding works for 23 ESD Valves Replacement	2.14%	CuM				1-Mar-16	23-Mar-16			7500.00	25.00%				
Train-1		22.49%					14-Apr-15	16-Oct-16			79000.00	24.99%	15225.00	4.33%	3.34%	11725.00
Replacement with Major S/D Valves & Actuators (SDT)		9.40%					1-Apr-16	12-Apr-16			33000.00	41.77%				
AH.CN.TR1.10390	GAS out						1-Apr-16	1-Apr-16								
AH.CN.TR1.10400	Demolition of existing valves	1.99%	Nos.		10		2-Apr-16	3-Apr-16			7000	21.21%				
AH.CN.TR1.10410	Installation of Piping spools	0.85%	Nos.		8		3-Apr-16	4-Apr-16			3000	9.09%				
AH.CN.TR1.10420	Installation of SDT valves	2.42%	Nos.		10		4-Apr-16	5-Apr-16			8500	25.76%				
AH.CN.TR1.10430	Instrumentation work related SDT valves	0.71%	Nos.		10		5-Apr-16	6-Apr-16			2500	7.58%				
AH.CN.TR1.10440	DCS modification works	0.43%	Nos.		1		5-Apr-16	6-Apr-16			1500	4.55%				
AH.CN.TR1.10450	modifications to the existing Instrument Air Buffer vessel	1.42%	Nos.		10		7-Apr-16	7-Apr-16			5000	15.15%				
AH.CN.TR1.10460	Electrical cable laying and Connection	0.43%	MTRS		100		7-Apr-16	7-Apr-16			1500	4.55%				
AH.CN.TR1.10540	Loop test for instrumentation cable	0.57%	Nos.		20		8-Apr-16	9-Apr-16			2000	6.06%				
AH.CN.TR1.10550	Painting and Touchups Etc.	0.28%	SqM		2		9-Apr-16	10-Apr-16			1000	3.03%				
AH.CN.TR1.10560	Functional test for electrical connection	0.28%	Nos.		20		11-Apr-16	11-Apr-16			1000	3.03%				
AH.CN.TR1.10570	GAS In						12-Apr-16	12-Apr-16								
Replacement with 1 Day S/D Actuators (For CAI) QTY 14 Nos.		10.25%					12-Apr-15	16-Oct-16			36000.00	45.57%	15225	4.33%	3.34%	11725
Replacement with 1 Day S/D Actuators (For CAI) QTY 05 Nos.-1		3.42%					14-Apr-15	15-Apr-15			12000.00	33.33%	3225	0.92%	0.92%	3225
AH.CN.TR1.10480	Removal of Existing Actuators	0.71%	Nos.		5	5	14-Apr-15	14-Apr-15			2500	20.83%	725	22.48%	22.48%	725
AH.CN.TR1.10490	Installation of New Actuators for CAI valves	1.28%	Nos.		5	5	14-Apr-15	15-Apr-15			4500	37.50%	925	28.68%	28.68%	925
AH.CN.TR1.10500	Instrumentation works fuctional test for newly installed Actuators for CAI valves	0.43%	Nos.		5	5	15-Apr-15	15-Apr-15			1500	12.50%	350	10.85%	10.85%	350
AH.CN.TR1.10510	E& I works for newly Installaed Actuators	0.43%	MTRS		20		15-Apr-15	15-Apr-15			1500	12.50%	600	18.60%	18.60%	600
AH.CN.TR1.10520	DCS modifictional works	0.28%	Nos.		1		15-Apr-15	15-Apr-15			1000	8.33%	300	9.30%	9.30%	300
AH.CN.TR1.10530	Function test	0.28%	Nos.		5		15-Apr-15	15-Apr-15			1000	8.33%	325	10.08%	10.08%	325
AH.CN.TR1.10650	Mechanical completion for 1 Day SD TRAIN 1							15-Apr-15								
Replacement with 1 Day S/D Actuators (For CAI) QTY 05 Nos.-2		3.42%					15-Oct-15	15-Oct-15			12000.00	33.33%	12000	3.42%	2.42%	8500
AH.CN.TR1.10810	Removal of Existing Actuators	0.71%	Nos.		5	5	15-Oct-15	15-Oct-15			2500	20.83%	2500	0.71%	0.71%	2500
AH.CN.TR1.10820	Installation of New Actuators for CAI valves	1.28%	Nos.		5	5	15-Oct-15	15-Oct-15			4500	37.50%	4500	1.28%	1.28%	4500
AH.CN.TR1.10830	Instrumentation works fuctional test for newly installed Actuators for CAI valves	0.43%	Nos.		5	5	15-Oct-15	15-Oct-15			1500	12.50%	1500	0.43%	0.43%	1500
AH.CN.TR1.10840	E& I works for newly Installaed Actuators	0.43%	MTRS		20		15-Oct-15	15-Oct-15			1500	12.50%	1500	0.43%	0.00%	
AH.CN.TR1.10850	DCS modifictional works	0.28%	Nos.		1		15-Oct-15	15-Oct-15			1000	8.33%	1000	0.28%	0.00%	
AH.CN.TR1.10860	Function test	0.28%	Nos.		5		15-Oct-15	15-Oct-15			1000	8.33%	1000	0.28%	0.00%	
AH.CN.TR1.10870	Mechanical completion for 1 Day SD TRAIN 1							15-Oct-15								
Replacement with 1 Day S/D Actuators (For CAI) QTY 04 Nos.-3		3.42%					15-Oct-16	16-Oct-16			12000.00	33.33%				
AH.CN.TR1.10880	Removal of Existing Actuators	0.71%	Nos.		3		15-Oct-16	15-Oct-16			2500	20.83%				
AH.CN.TR1.10890	Installation of New Actuators for CAI valves	1.28%	Nos.		3		15-Oct-16	15-Oct-16			4500	37.50%				
AH.CN.TR1.10900	Instrumentation works fuctional test for newly installed Actuators for CAI valves	0.43%	Nos.		3		15-Oct-16	15-Oct-16			1500	12.50%				
AH.CN.TR1.10910	E& I works for newly Installaed Actuators	0.43%	MTRS		15		15-Oct-16	15-Oct-16			1500	12.50%				
AH.CN.TR1.10920	DCS modifictional works	0.28%	Nos.		1		15-Oct-16	15-Oct-16			1000	8.33%				
AH.CN.TR1.10930	Function test	0.28%	Nos.		3		15-Oct-16	15-Oct-16			1000	8.33%				
AH.CN.TR1.10940	Mechanical completion for 1 Day SD TRAIN 1							15-Oct-16								
Post Shutdown works		2.85%					13-Apr-16	9-Jun-16			10000	12.66%				
AH.CN.TR1.10200	Painting and touchups for Installed facilities						13-Apr-16	16-Apr-16			1000	10.00%				
AH.CN.TR1.10210	Removal of Scaffolding						17-Apr-16	19-Apr-16			1000	10.00%				
AH.CN.TR1.10220	Construction works for pavement						17-Apr-16	10-May-16			1000	10.00%				
AH.CN.TR1.10230	Civil construction works for Desmenteled Fence						21-Apr-16	7-May-16			1000	10.00%				
AH.CN.TR1.10240	Installation of fence						10-May-16	17-May-16			1000	10.00%				

BuHasa Replacement of Valves & Actuators for EPC Works

GASCO PROJECT NO: 5621

REVISED BASELINE Construction Register

											Document Title:		Construction Register			
											Rev:		1			
											Date:		30-Oct-15			
Activity ID	Activity Name	WTG % L3	UoM	UNIT RATE MHS/UNIT QTY.	PLANNED QUANTITY	ACHEIVED QUANTITY	REVISED START	REVISED FINISH	ACTUAL START	ACTUAL FINISH	TOTAL MANHOURS	PLANNED ACTIVITY WTG %	PLANNED MHS	PLANNED PROGRESS %	ACHIEVED PROGRESS %	ACTUAL MHS
AH.CN.TR1.10250	Removal of Resedual from premises						18-May-16	22-May-16			1000	10.00%				
AH.CN.TR1.10260	Installation of Street lighting						23-May-16	7-Jun-16			1000	10.00%				
AH.CN.TR1.10270	Electrical works related to Street lighting						28-May-16	9-Jun-16			1500	15.00%				
AH.CN.TR1.10360	Completion of Installation of road signs and road marking etc.						1-Jun-16	8-Jun-16			1500	15.00%				
Train-2		22.49%					15-May-15	14-Jun-16			79000.00	24.99%	3225	0.92%	3.34%	11725
Replacement with Major S/D Valves & Actuators (SDT)		9.40%					28-Mar-16	7-Apr-16			33000	41.77%				
AH.CN.TR2.10390	GAS out						28-Mar-16	28-Mar-16								
AH.CN.TR2.10400	Demolition of existing valves	1.99%	Nos.		13		29-Mar-16	30-Mar-16			7000	21.21%				
AH.CN.TR2.10410	Installation of Piping spools	0.85%	Nos.		8		30-Mar-16	30-Mar-16			3000	9.09%				
AH.CN.TR2.10420	Installation of SDT valves	2.42%	Nos.		13		31-Mar-16	1-Apr-16			8500	25.76%				
AH.CN.TR2.10430	Instrumentation work related SDT valves	0.71%	Nos.		13		1-Apr-16	1-Apr-16			2500	7.58%				
AH.CN.TR2.10440	DCS modification works	0.43%	Nos.		1		2-Apr-16	2-Apr-16			1500	4.55%				
AH.CN.TR2.10450	modifications to the existing Instrument Air Buffer vessel	1.42%	Nos.		13		3-Apr-16	3-Apr-16			5000	15.15%				
AH.CN.TR2.10460	Electrical cable laying and Connection	0.43%	MTRS		100		4-Apr-16	4-Apr-16			1500	4.55%				
AH.CN.TR2.10470	Loop test for instrumentation cable	0.57%	Nos.		26		5-Apr-16	5-Apr-16			2000	6.06%				
AH.CN.TR2.10480	Functional test for electrical connection	0.28%	Nos.		26		5-Apr-16	5-Apr-16			1000	3.03%				
AH.CN.TR2.10500	Painting and Touchups Etc.	0.28%	SqM		2		6-Apr-16	6-Apr-16			1000	3.03%				
AH.CN.TR2.10510	GAS In						7-Apr-16	7-Apr-16								
Replacement with 1 Day S/D Actuators (For CAI) QTY 14 Nos.		10.25%					12-May-15	16-May-16			36000.00	45.57%	3225	0.92%	3.34%	11725
Replacement with S/D Actuators (For CAI) QTY 05 Nos.-1		3.42%					15-May-15	23-Nov-15			12000.00	33.33%	3225	0.92%	0.92%	3225
AH.CN.TR2.10520	Removal of Existing Actuators	0.71%	Nos.		5		15-May-15	15-May-15			2500	20.83%	725	22.48%	22.48%	725
AH.CN.TR2.10530	Installation of New Actuators for CAI valves	1.28%	Nos.		5		15-May-15	15-May-15			4500	37.50%	925	28.68%	28.68%	925
AH.CN.TR2.10540	Instrumentation works fuctional test for newly installed Actuators for CAI valves	0.43%	Nos.		5		15-May-15	15-May-15			1500	12.50%	350	10.85%	10.85%	350
AH.CN.TR2.10550	E& I works for newly Installaed Actuators	0.43%	MTRS		20		15-May-15	15-May-15			1500	12.50%	600	18.60%	18.60%	600
AH.CN.TR2.10560	DCS modifictional works	0.28%	Nos.		1		15-May-15	15-May-15			1000	8.33%	300	9.30%	9.30%	300
AH.CN.TR2.10570	Function test	0.28%	Nos.		5		15-May-15	15-May-15			1000	8.33%	325	10.08%	10.08%	325
AH.CN.TR2.10710	Mechanical completion for 1 Day SD TRAIN 2							15-May-15								
Replacement with S/D Actuators (For CAI) QTY 05 Nos.-2		3.42%					15-Nov-15	16-Nov-15			12000.00	33.33%	0	0.00%	2.42%	8500
AH.CN.TR2.10580	Removal of Existing Actuators	0.71%	Nos.		5	5	15-Nov-15	16-Nov-15			2500	20.83%			0.71%	2500
AH.CN.TR2.10590	Installation of New Actuators for CAI valves	1.28%	Nos.		5	5	15-Nov-15	16-Nov-15			4500	37.50%			1.28%	4500
AH.CN.TR2.10600	Instrumentation works fuctional test for newly installed Actuators for CAI valves	0.43%	Nos.		5	5	15-Nov-15	16-Nov-15			1500	12.50%			0.43%	1500
AH.CN.TR2.10610	E& I works for newly Installaed Actuators	0.43%	MTRS		20		15-Nov-15	16-Nov-15			1500	12.50%			0.00%	
AH.CN.TR2.10620	DCS modifictional works	0.28%	Nos.		1		15-Nov-15	16-Nov-15			1000	8.33%			0.00%	
AH.CN.TR2.10630	Function test	0.28%	Nos.		5		15-Nov-15	16-Nov-15			1000	8.33%			0.00%	
AH.CN.TR2.10720	Mechanical completion for 1 Day SD TRAIN 2							16-Nov-15								
Replacement with S/D Actuators (For CAI) QTY 04 Nos.-3		3.42%					15-May-16	16-May-16			12000.00	33.33%				
AH.CN.TR2.10820	Removal of Existing Actuators	0.71%	Nos.		3		15-May-16	16-May-16			2500	20.83%				
AH.CN.TR2.10830	Instrumentation works fuctional test for newly installed Actuators for CAI valves	1.28%	Nos.		3		15-May-16	16-May-16			4500	37.50%				
AH.CN.TR2.10840	E& I works for newly Installaed Actuators	0.43%	Nos.		3		15-May-16	16-May-16			1500	12.50%				
AH.CN.TR2.10850	DCS modifictional works	0.43%	MTRS		15		15-May-16	16-May-16			1500	12.50%				
AH.CN.TR2.10860	Function test	0.28%	Nos.		1		15-May-16	16-May-16			1000	8.33%				
AH.CN.TR2.10870	Mechanical completion for 1 Day SD TRAIN 2	0.28%	Nos.		3			16-May-16			1000	8.33%				
AH.CN.TR2.10880	Installation of New Actuators for CAI valves						15-May-16	16-May-16								
Post Shutdown works		2.85%					9-Apr-16	14-Jun-16			10000	12.66%				
AH.CN.TR2.10200	Painting and touchups for Installed facilities						9-Apr-16	11-Apr-16			1000	10.00%				
AH.CN.TR2.10210	Removal of Scaffolding						12-Apr-16	14-Apr-16			1000	10.00%				
AH.CN.TR2.10220	Construction works for pavement						16-Apr-16	12-May-16			1000	10.00%				
AH.CN.TR2.10230	Civil construction works for Desmenteled Fence						20-Apr-16	5-May-16			1000	10.00%				
AH.CN.TR2.10240	Installation of fence						7-May-16	14-May-16			1000	10.00%				
AH.CN.TR2.10250	Removal of Resedual from premises						15-May-16	18-May-16			1000	10.00%				
AH.CN.TR2.10260	Installation of Street lighting						19-May-16	4-Jun-16			1000	10.00%				
AH.CN.TR2.10270	Electrical works related to Street lighting						24-May-16	6-Jun-16			1500	15.00%				
AH.CN.TR2.10360	Completion of Installation of road signs and road marking etc.						7-Jun-16	14-Jun-16			1500	15.00%				
Commissioning & As-built Drawings							31-Oct-16	22-Jun-17			35110	10.00%				
Train-1		5.00%					31-Oct-16	22-Nov-16			17555	50.00%				


		BuHasa Replacement of Valves & Actuators for EPC Works GASCO PROJECT NO: 5621 REVISED BASELINE Construction Register																
												Document Title:		Construction Register				
												Rev:		1				
												Date:		30-Oct-15				
Activity ID	Activity Name	WTG % L3	UoM	UNIT RATE MHS/UNIT QTY.	PLANNED QUANTITY	ACHEIVED QUANTITY	REVISED START	REVISED FINISH	ACTUAL START	ACTUAL FINISH	TOTAL MANHOURS	PLANNED ACTIVITY WTG %	PLANNED MHS	PLANNED PROGRESS %	ACHIEVED PROGRESS %	ACTUAL MHS		
AH.CN.TR1.PM.10000	As Built Documentation for Train-1						31-Oct-16	22-Nov-16										
AH.CN.TR1.PM.10010	Handing Over of train-1							22-Nov-16										
AH.CN.TR1.PM.10020	PAC for train-1							22-Nov-16										
Train-2		5.00%					31-Oct-16	22-Nov-16			17555	50.00%						
AH.CN.TR2.PM.10000	As Built Documentation for Train-2						31-Oct-16	22-Nov-16										
AH.CN.TR2.PM.10010	Handing Over of train-2							22-Nov-16										
AH.CN.TR2.PM.10020	PAC for train-2							22-Nov-16										
Project and Contract Completion							13-Dec-16	22-Jun-17										
AH.CM.PC.10000	Project Completion							13-Dec-16										
AH.CM.PC.10010	Contract Completion Date							22-Jun-17										

Archives from Personal Files

ATTACHMENT - 14

CONSTRUCTION S CURVE

Archives from Personal Files

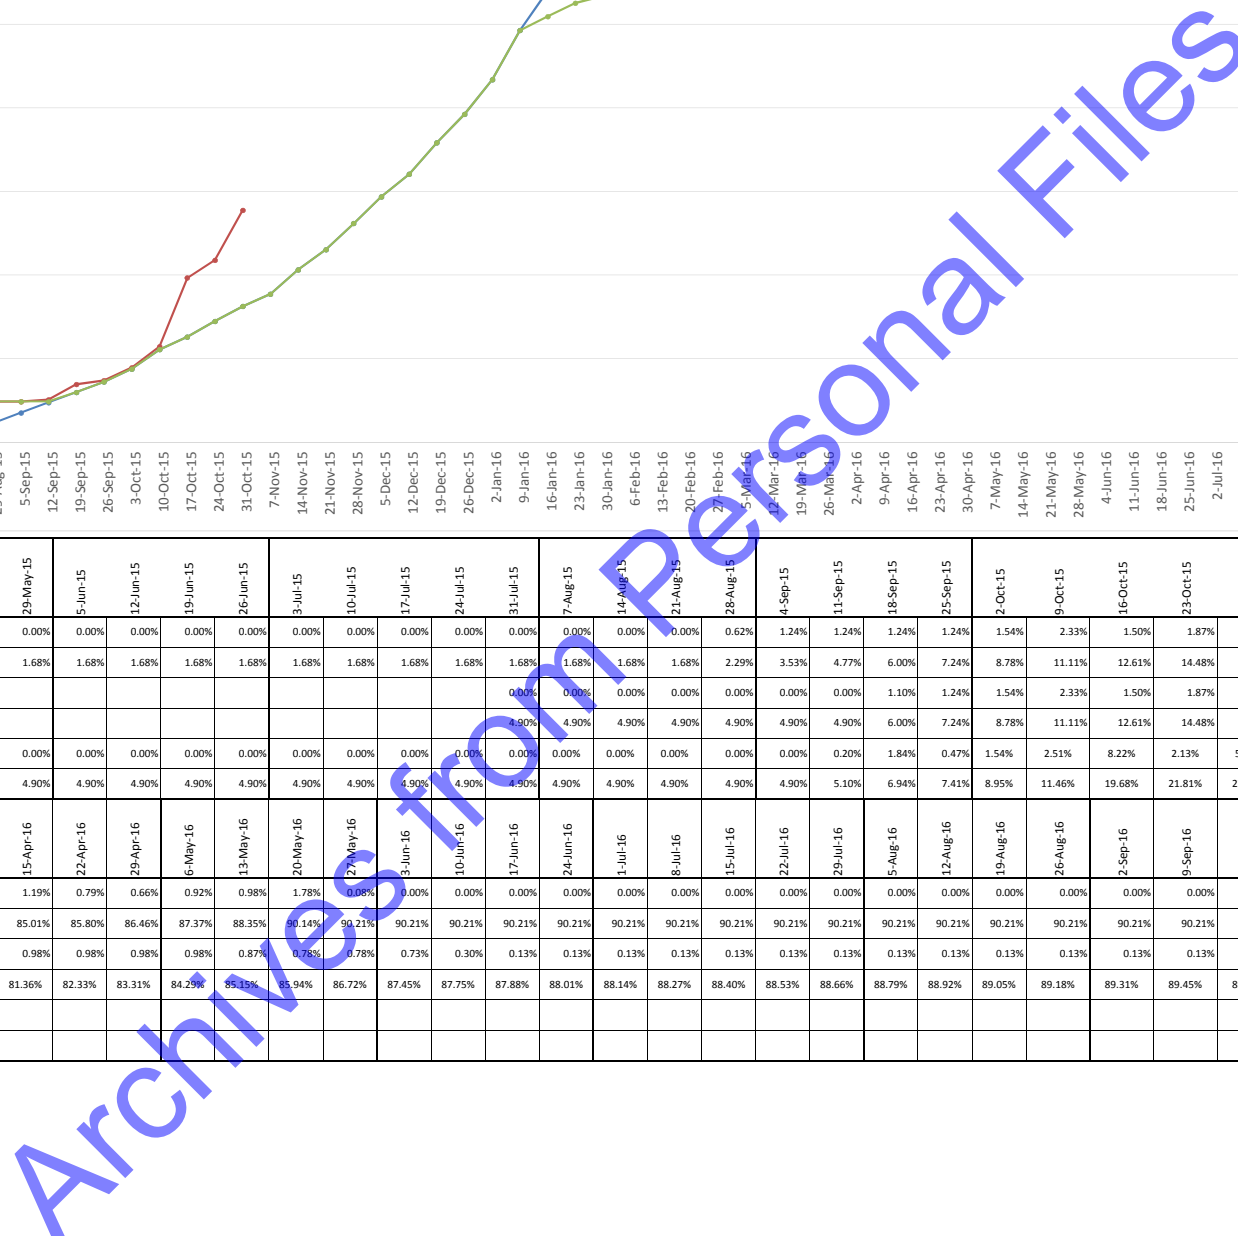

	28-Feb-15	6-Mar-15	13-Mar-15	20-Mar-15	27-Mar-15	3-Apr-15	10-Apr-15	17-Apr-15	24-Apr-15	1-May-15	8-May-15	15-May-15	22-May-15	29-May-15	5-Jun-15	12-Jun-15	19-Jun-15	26-Jun-15	3-Jul-15	10-Jul-15	17-Jul-15	24-Jul-15	31-Jul-15	7-Aug-15	14-Aug-15	21-Aug-15	28-Aug-15	4-Sep-15	11-Sep-15	18-Sep-15	25-Sep-15	2-Oct-15	9-Oct-15	16-Oct-15	23-Oct-15	30-Oct-15	6-Nov-15	13-Nov-15	20-Nov-15	27-Nov-15	4-Dec-15	11-Dec-15	18-Dec-15	25-Dec-15	1-Jan-16	8-Jan-16		
PLAN FOR THE WEEK	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.84%	0.00%	0.00%	0.00%	0.84%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.62%	1.24%	1.24%	1.24%	1.24%	1.54%	2.33%	1.50%	1.87%	1.79%	1.49%	2.89%	2.41%	3.13%	3.19%	2.71%	3.78%	3.38%	4.15%	5.8		
PLAN CUMM	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.84%	0.84%	0.84%	0.84%	1.68%	1.68%	1.68%	1.68%	1.68%	1.68%	1.68%	1.68%	1.68%	1.68%	1.68%	1.68%	1.68%	1.68%	1.68%	1.68%	2.29%	3.53%	4.77%	6.00%	7.24%	8.78%	11.11%	12.61%	14.48%	16.27%	17.76%	20.65%	23.06%	26.19%	29.38%	32.09%	35.87%	39.25%	43.40%	49.2		
REVISED PLAN FOR THE WEEK																																																
REVISED CUMM																																																
ACTUAL FOR THE WEEK	0.00%	0.00%	1.07%	0.00%	0.00%	0.00%	2.15%	0.84%	0.00%	0.00%	0.00%	0.84%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.20%	1.84%	0.47%	1.54%	2.51%	8.22%	2.13%	5.96%													
ACTUAL CUMM	0.00%	0.00%	1.07%	1.07%	1.07%	1.07%	3.22%	4.06%	4.06%	4.06%	4.06%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	4.90%	5.10%	6.94%	7.41%	8.95%	11.46%	19.68%	21.81%	27.77%												
	15-Jan-16	22-Jan-16	29-Jan-16	5-Feb-16	12-Feb-16	19-Feb-16	26-Feb-16	4-Mar-16	11-Mar-16	18-Mar-16	25-Mar-16	1-Apr-16	8-Apr-16	15-Apr-16	22-Apr-16	29-Apr-16	6-May-16	13-May-16	20-May-16	27-May-16	3-Jun-16	10-Jun-16	17-Jun-16	24-Jun-16	1-Jul-16	8-Jul-16	15-Jul-16	22-Jul-16	29-Jul-16	5-Aug-16	12-Aug-16	19-Aug-16	26-Aug-16	2-Sep-16	9-Sep-16	16-Sep-16	23-Sep-16	30-Sep-16	7-Oct-16	14-Oct-16	21-Oct-16	28-Oct-16	4-Nov-16	11-Nov-16	18-Nov-16	25-Nov-16		
PLAN FOR THE WEEK	0.00%	4.72%	4.65%	7.76%	5.68%	2.27%	0.98%	0.20%	2.49%	2.50%	1.05%	0.94%	1.28%	1.19%	0.79%	0.66%	0.92%	0.98%	1.78%	0.68%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.84%	0.00%	0.00%	2.24%	2.69%	1.3				
PLAN CUMM	49.27%	54.00%	58.65%	66.41%	72.09%	74.36%	75.35%	75.55%	78.04%	80.54%	81.59%	82.53%	83.81%	85.01%	85.80%	86.46%	87.37%	88.35%	91.14%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	90.21%	91.05%	91.05%	93.29%	95.97%	98.66%	100.00%	0.0				
REVISED PLAN FOR THE WEEK	1.68%	1.59%	0.85%	0.70%	0.96%	0.85%	0.94%	1.27%	1.13%	0.94%	4.08%	11.94%	4.10%	0.98%	0.98%	0.98%	0.98%	0.87%	0.78%	0.78%	0.73%	0.30%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	0.13%	1.85%	3.18%	3.18%	1.82%	0.00%	0.00%	0.00%	0.0
REVISED CUMM	50.96%	52.55%	53.40%	54.10%	55.06%	55.91%	56.85%	58.12%	59.31%	60.25%	64.33%	76.28%	80.38%	81.36%	82.33%	83.31%	84.29%	85.13%	85.94%	86.72%	87.45%	87.75%	87.88%	88.01%	88.14%	88.27%	88.40%	88.53%	88.66%	88.79%	88.92%	89.05%	89.18%	89.31%	89.45%	89.58%	89.71%	89.84%	89.97%	91.82%	95.00%	98.18%	100.00%	100.00%	100.00%	100.00%	100.00%	0.0
ACTUAL FOR THE WEEK																																																
ACTUAL CUMM																																																

ATTACHMENT - 15

MILESTONES SUMMARY

Archives from Personal Files

Progress Review / Verification Sheet
Milestone Progress Detail

PROJECT TITLE : BUHASA - REPLACEMENT OF VALVES AND ACTUATORS FOR EPC WORKS

MONTH : Oct' 15

PROJECT No : 5621

PROGRESS AS ON : 29-Oct-15

MILESTONE NO.	MILESTONE TITLE	DOCUMENT NO.	DETAIL DESCRIPTION / REMARKS	MILESTONE WEIGHT %	MILESTONE DATES			MILESTONE WEIGHT ACHIEVED	
					BASELINE PLAN	REVISED PLAN	ACTUAL	REPORTING PERIOD	CUMMULATIVE
A	ENGINEERING								
A.01	COMPLETE SITE SURVEY AND SUBMIT FINAL REPORT	5621-RT-00-AA-V101	The Document was approved from Company in the Letter No. PX7/M2/5621/15/082 - with CODE - 2 (Approved with Comments)	0.25	21-Oct-14		26-Feb-15		0.25
A.02	ISSUE DESIGN BASIS MEMORANDUM FOR ALL DISCIPLINES, AFTER COMPANY REVIEW, FINAL ISSUE	5621-SP-00-AA-V101	The Document was approved from Company in the Letter No. PX7/M2/5621/15/046 - with CODE - 3 (Approved)	0.50	5-Apr-15		15-Feb-15		0.50
A.03	ISSUE PLOT PLAN, PFDs & P&IDs FOR HAZOP REVIEW	5621-00-LD-V102 5621-51-BD-V102/V111 5621-52-BD-V102/V111	HAZID SESSION CONDUCTED ON 18TH FEB, 2015	0.25	24-Mar-15		18-Feb-15		0.25
A.04	COMPLETE HAZOP / SIL REVIEW AND ISSUE FINAL REPORT TO COMPANY	5621-RT-00-AA-V103	The Document was approved from Company in the Letter No. PX7/M2/5621/15/152 - with CODE - 3 (Approved)	0.50	26-Mar-15		20-Apr-15		0.50
A.05	ISSUE TIE-IN AND SHUTDOWN PHILOSOPHY FOR COMPANY APPROVAL	5621-SCH-AA-V102	The Document was approved from Company in the Letter No. PX7/M2/5621/15/054 - with CODE - 3 (Approved)	0.25	15-Jan-15		15-Feb-15		0.25
A.06	ISSUE STRESS ANALYSIS REPORT (FINAL)	5621-RT-00-AA-V102	The Document was approved from Company in the Letter No. PX7/M2/5621/15/120 - with CODE - 3 (Approved)	0.25	9-Apr-15		28-Mar-15		0.25
A.07	ISSUE GA's ISOMETRICS AND PIPE SUPPORT DRAWINGS FOR PIPING MODIFICATIONS, TIE-IN WORKS (IFC), ALSO EXISTING PLANT DWGS	5621-00-LD-V101	ALL THE GENERAL ARRANGEMENTS, PIPING MODIFICATION (DEMOLITION) DRAWINGS AND TIE-IN DRAWINGS ARE ISSUED.	0.75	31-Mar-15		25-Jun-15		0.75

Progress Review / Verification Sheet
Milestone Progress Detail

PROJECT TITLE : BUHASA - REPLACEMENT OF VALVES AND ACTUATORS FOR EPC WORKS

MONTH : Oct' 15

PROJECT No : 5621

PROGRESS AS ON : 29-Oct-15

MILESTONE NO.	MILESTONE TITLE	DOCUMENT NO.	DETAIL DESCRIPTION / REMARKS	MILESTONE WEIGHT %	MILESTONE DATES			MILESTONE WEIGHT ACHIEVED	
					BASELINE PLAN	REVISED PLAN	ACTUAL	REPORTING PERIOD	CUMMULATIVE
A.08	ISSUE ALL CIVIL / RCC DRAWINGS INCL. PAVING DETAILS AND CABLE TRENCHES (IFC), ALSO UPDATING EXISTING PLANT DWGS	5621-RT-00-AA-V106	Adequacy Study of Existing Structures and their foundations and Modifications as Necessary for Additional Loading. Issued on 16 June 2015 Approved by Company on 23 June 2015	0.75	28-Mar-15		16-Jun-15		0.75
A.09	ISSUE STRUCTURAL STEEL FABRICATION AND INSTALLATION DETAILS FOR ALL FACILITIES (IFC)	5621-RT-00-AA-V106	Adequacy Study of Existing Structures and their foundations and Modifications as Necessary for Additional Loading. Issued on 16 June 2015 Approved by Company on 23 June 2015	0.50	11-Mar-15		23-Jun-15		0.50
A.10	ISSUE E&I DWGS INCL. CABLE SCH, LAYOUTS, TRAY/SUPPORTS & IPS/DCS MODIFICATIONS, I&C INDEX FOR CONST (IFC), UPDATE			0.50	21-Mar-15	16-Aug-15			
A.11	ISSUE ALL HSE DELIVERABLES INCLUDING UPDATING HSE PLAN AND HSE PHILOSOPHY (IFC) AND COMP. SIMOPS & HAZID REVIEWS	5621-PP-00-YA-0001 5621-PP-00-AA-V102	The Document was approved from Company in the Letter No. PX7/M2/5621/15/028 - with CODE - 3 (Approved) The Document was approved from Company in the Letter No. PX7/M2/5621/15/054 - with CODE - 3 (Approved)	0.25	4-Mar-15		4-Mar-15		0.25
A.12	COMPLETE CONSTRUCTABILITY REVIEW AND SUBMIT FINAL REPORT AFTER INCORPORATING COMPANY COMMENTS		Constructability Review Conducted on 23 June 2015	0.25	25-Mar-15		23-Jun-15		0.25
B	PROCUREMENT & DELIVERY								
B.01	ISSUE P.O FOR ALL SDT VALVS / ACTUATORS - 23 SETS	PURPOSE/4007	The Commencement date of the delivery Schedule as per P.O is FEB 25, 2015 - The Submission of Unpriced Copy of P.O was done via 5621/E025/AHEC/GC/T-00181. Dated: 10th Mar, 2015	2.00	18-Jan-15		25-Feb-15		2.00
B.02	ISSUE P.O FOR 28 NOS. OF ACTUATORS AFOR CAI VALVES	PURREQ/8629	The Commencement date of the delivery Schedule as per P.O is NOV 24, 2014 - The Submission of Unpriced Copy of P.O was done via 5621/E025/AHEC/GC/T-00073. Dated: 30th Dec, 2014	2.00	2-Dec-14		15-Dec-14		2.00

Progress Review / Verification Sheet
Milestone Progress Detail

PROJECT TITLE : BUHASA - REPLACEMENT OF VALVES AND ACTUATORS FOR EPC WORKS

PROJECT No : 5621

MONTH : Oct' 15

PROGRESS AS ON : 29-Oct-15

MILESTONE NO.	MILESTONE TITLE	DOCUMENT NO.	DETAIL DESCRIPTION / REMARKS	MILESTONE WEIGHT %	MILESTONE DATES			MILESTONE WEIGHT ACHIEVED	
					BASELINE PLAN	REVISED PLAN	ACTUAL	REPORTING PERIOD	CUMMULATIVE
B.03	ISSUE P.O FOR E&I CABLES			1.00	27-Apr-15		27-Jul-15		1.00
B.04	RECEIVE ALL SDT VALVES / ACTUATORS SET AT SITE			16.00	12-Oct-15	3-Feb-16			
B.05	RECEIVE ALL ACTUATORS FOR CAI VALVES		ALL ACTUATORS DELIVERED IN BUHASA PLANT	8.00	14-Apr-15	26-Sep-15	24-Sep-15		8.00
B.06	REVEIVE ALL E&I CABLES AT SITE			4.00	7-Nov-15	22-Nov-15			
B.07	SUBMIT G-SPIRS TO COMPANY AND PLACE ORDERS FOR ALL ITEMS AFTER OBTAINING COMAPNY APPROVAL			2.00	25-Jan-15	18-Oct-15			
B.08	RECEIVE INSURANCE / COMMISSIONING AND OPERATING SPARES FOR EQUIPMENTS & PACKAGES AT SITE & HANDOVER TO COMPANY			3.00	4-Sep-15	24-Jan-16			
B.09	COMPLETE TESTING OF VALVES AFTER SHIPPING			2.00	17-Nov-15	29-Feb-16			
C	CONSTRUCTION / COMMISSIONING WORKS								
C.01	COMPLETE CIVIL WORKS FOR ALL SLOPE PROTECTION, CABLE TRENCHES & DUCTS AND FOUNDATIONS		FOUNDATIONS FOR ALL BUFFER VESSELS COMPLETED FOR BOTH TRAINS 1 & 2	3.00	6-Apr-16	7-May-16	27-Oct-15	1.00	1.00

Progress Review / Verification Sheet
Milestone Progress Detail

PROJECT TITLE : BUHASA - REPLACEMENT OF VALVES AND ACTUATORS FOR EPC WORKS

MONTH : Oct' 15

PROJECT No : 5621

PROGRESS AS ON : 29-Oct-15

MILESTONE NO.	MILESTONE TITLE	DOCUMENT NO.	DETAIL DESCRIPTION / REMARKS	MILESTONE WEIGHT %	MILESTONE DATES			MILESTONE WEIGHT ACHIEVED	
					BASELINE PLAN	REVISED PLAN	ACTUAL	REPORTING PERIOD	CUMMULATIVE
C.02	COMPLETE FABRICATION AND INSTALLATION OF ALL STRUCTURAL STEEL WORKS			3.00	13-Feb-16	30-Jul-15			
C.03	COMPLETE ROADS, PAVING, STREET LIGHTNING, ROAD SIGNAGE AND FENCING AS REQUIRED			3.00	30-Jun-16	1-Aug-16			
C.04	COMPLETE RE-HABILITATION OF ANY TEMP. OR PERMANENT E&I FACILITIES IF DISTUBRED			2.00	12-Oct-16	8-Jun-16			
C.05	COMPLETE REROUTING OF EXISTING UNDERGROUND CABLES & PIPING			2.00	29-Feb-16	8-Jun-16			
C.06	COMPLETE INSTALLATION OF 28 NOS. OF NEW CAI ACTUATORS DULY HOOKED UP TO THE EXISTING IPS/DCS CONTROL SYSTEM		21 OUT OF 28 ACTUATORS INSTALLED IN 03 ONE DAY S/Ds	11.00	15-Oct-16	16-Oct-16	15-Oct-15	5.50	5.50
C.07	COMPLETE INSTALLATION OF 23 DOUBLE ACTING VALVES AND ACTUATORS DULY HOOKED UP TO THE EXISTING IPS/DCS CONTROL SYSTEM			16.00	12-Mar-16	12-Apr-16			
C.08	COMPLETE INSTALLATION OF ALL FIELD INSTRUMENTS, CABLING AND PIPING WORKS			4.00	12-Mar-16	12-Apr-16			
C.09	COMPLETE ALL DCS MODIFICATION WORKS			4.00	5-Apr-16	7-May-16			

Progress Review / Verification Sheet
Milestone Progress Detail

PROJECT TITLE : BUHASA - REPLACEMENT OF VALVES AND ACTUATORS FOR EPC WORKS

MONTH : Oct' 15

PROJECT No : 5621

PROGRESS AS ON : 29-Oct-15

MILESTONE NO.	MILESTONE TITLE	DOCUMENT NO.	DETAIL DESCRIPTION / REMARKS	MILESTONE WEIGHT %	MILESTONE DATES			MILESTONE WEIGHT ACHIEVED	
					BASELINE PLAN	REVISED PLAN	ACTUAL	REPORTING PERIOD	CUMMULATIVE
C.10	ACHIEVE MECHANICAL COMPLETION FOR TRAIN - 1			0.50	18-Oct-16	17-Dec-16			
C.11	ACHIEVE MECHANICAL COMPLETION FOR TRAIN - 2			0.50	15-Oct-16	16-Oct-16			
C.12	COMPLETE DEMOLITION OF ALL OBSOLETE VALVES AND ACTUATORS AND ANY OTHER REDUNTANT MATERIAL / EQUIPMENT			2.00	15-Oct-16	16-Oct-16			
C.13	COMPLETE ALL COMMISSIONING, TEST RUN AND ACHIEVE PAC			2.00	13-Dec-16	13-Feb-17			
C.14	SUBMIT FINAL DOSSIER / AS BUILT DOCUMENTATIONS / COMMISSIONING AND OPERATING SPARES			1.00	22-Nov-16	23-Jan-17			
C.15	CONTRACT COMPLETION OF THE PROJECT			1.00	22-Jun-17	22-Jun-17			
			TOTAL	100%				6.50%	24.00%
Note-1:	All Milestones (B.01 to B.03) related to "Issue of Purchase Orders" shall be considered as achieved only after issue of a valid Purchase Order and final updated Purchase Requisition (PR) to Vendor, with a copy to Company. Issue of Letter of Award (LOA) or Letter of Intent (LOI) will not be considered as achievement of this Milestone.								

Requested By : Project Manager (CONTRACTOR)	Sign		Certified By : Sr. Project Manager (COMPANY)				
	Name						
	Date						

ATTACHMENT - 16

**VENDOR DOCUMENT
DELIVERABLE REGISTER**

Archives from Personal Files



BuHasa Replacement of SDT Valves & Actuators for EPC Works



VENDOR DOCUMENT DELIVERABLE REGISTER

S/N	VENDOR NAME	VENDOR CODE	WTG%	Document No.										5621-SCH-00-AA-0011																			
1	MSA VALVES	V4	1.0%	Revision No.										A3																			
2	CAI ACTUATORS	V2	0.5%	Date:										30-Oct-15																			
3	HONEYWELL	V3	0.5%																														
														DATE:										30-Oct-15									
S/N	PROJECT DOCUMENT NUMBER		Document Title	DWG/DO C	MHS WTG	MHS	P	SUBMISSION SCHEDULE																PLAN	ACTUAL								
							F	A1		A2		A3		IFA / A4		R1		FINAL ISSUE															
							A	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	90.04%	40.69%												
PROGRESS %								5%		8%		10%		15%		20%		35%		50%		60%		70%		80%		95%		100%			
OVERALL VENDOR PROGRESS %																												1.80%		0.81%			
CAI ACTUATORS (0.5%)						100%		3215																				98%					
																														73%			
1	ACTUATOR BRACKET DRAWINGS		5621-00-GA-V2TY01 - V2TY06	DWG	3.11%	100	P	15-Jan-15	29-Jan-15	3-Feb-15	10-Feb-15	20-Aug-15	27-Aug-15	1-Sep-15	8-Sep-15	13-Sep-15	20-Sep-15	25-Sep-15	2-Oct-15	3.11%													
																														3.11%			
2	ACTUATOR SIZING CACLUATIONS		5621-NC-00-DA-V201	DOC	3.11%	100	P	15-Dec-14	29-Dec-14	3-Jan-15	10-Jan-15	20-Aug-15	27-Aug-15	1-Sep-15	8-Sep-15	13-Sep-15	20-Sep-15	25-Sep-15	2-Oct-15	3.11%													
																														3.11%			
3	FAT PROCEDURE		5621-TP-00-LA-V201	DOC	2.49%	80	P	1-Feb-15	1-Apr-15	20-Feb-15	27-Feb-15	7-Aug-15	14-Aug-15	19-Aug-15	26-Aug-15	3-Aug-15	7-Sep-15	12-Sep-15	19-Sep-15	2.49%													
																														2.49%			
4	FAT REPORTS (April)		5621-RT-00-AA-V210	DOC	2.49%	80	P	1-Apr-15	15-Apr-15	22-Aug-15	29-Aug-15	5-Sep-15	12-Sep-15	17-Sep-15	24-Sep-15	24-Sep-15	6-Oct-15	11-Oct-15	18-Oct-15	2.49%													
																														2.49%			
5	MANUFACTURING DATA RECORD (April)		5621-GEN-00-AA-V210	DOC	2.18%	70	P	1-Apr-15	15-Apr-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15	2-Nov-15	9-Nov-15	1.74%													
																														2.18%			
6	FAT REPORTS (July)		5621-GEN-00-AA-V211	DOC	2.02%	65	P	15-Jul-15	29-Jul-15	3-Aug-15	10-Aug-15	15-Aug-15	22-Aug-15	27-Aug-15	3-Sep-15	8-Sep-15	15-Sep-15	20-Sep-15	27-Sep-15	2.02%													
																														2.02%			
7	MANUFACTURING DATA RECORD (July)		5621-GEN-00-AA-V211	DOC	1.87%	60	P	15-Jul-15	29-Jul-15	3-Aug-15	10-Aug-15	15-Aug-15	22-Aug-15	27-Aug-15	3-Sep-15	8-Sep-15	15-Sep-15	20-Sep-15	27-Sep-15	1.87%													
																														1.87%			
8	ACTUATOR INSTALLATION PROCEDURE		5621-PP-00-AA-V205	DOC	0.62%	20	P	15-Jul-15	29-Jul-15	3-Aug-15	10-Aug-15	15-Aug-15	22-Aug-15	27-Aug-15	3-Sep-15	8-Sep-15	15-Sep-15	20-Sep-15	27-Sep-15	0.62%													
																														0.62%			
9	INSTALLATION, OPERATION AND MAINTENANCE MANUAL		5621-PP-00-AA-V206	DOC	3.11%	100	P	15-Sep-15	29-Sep-15	4-Oct-15	11-Oct-15	16-Oct-15	23-Oct-15	28-Oct-15	4-Nov-15	9-Nov-15	16-Nov-15	21-Nov-15	28-Nov-15	1.56%													
																														0.00%			
10	CERTIFICATES FOR LIMIT SWITCHES USED		5621-SP-00-JA-V201	DOC	1.24%	40	P	15-Jul-15	29-Jul-15	3-Aug-15	10-Aug-15	15-Aug-15	22-Aug-15	27-Aug-15	3-Sep-15	8-Sep-15	15-Sep-15	20-Sep-15	27-Sep-15	1.24%													
																														0.00%			
11	LIST OF ALL SPARES PER ACTUATOR (Ind. 1 Year Maintenance & 2 Years Operation)		5621-GEN-00-AA-V204	DOC	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15	1.87%													
																														0.00%			
12	LIST OF TOOLS PER ACTUATOR		5621-SCH-00-AA-V202	DOC	1.24%	40	P	20-Jul-15	3-Aug-15	8-Aug-15	15-Aug-15	20-Aug-15	27-Aug-15	1-Sep-15	8-Sep-15	13-Sep-15	20-Sep-15	25-Sep-15	2-Oct-15	1.24%													
																														0.00%			
13	G-SPR PACKAGE		5621-GEN-00-AA-V206	DOC	0.62%	20	P	15-Sep-15	29-Sep-15	4-Oct-15	11-Oct-15	16-Oct-15	23-Oct-15	28-Oct-15	4-Nov-15	9-Nov-15	16-Nov-15	21-Nov-15	28-Nov-15	0.31%													
																														0.00%			
14	MANUFACTURING DATA RECORD (July)		5621-GEN-00-AA-V211	DOC	1.24%	40	P	20-Jul-15	3-Aug-15	8-Aug-15	15-Aug-15	20-Aug-15	27-Aug-15	1-Sep-15	8-Sep-15	13-Sep-15	20-Sep-15	25-Sep-15	2-Oct-15	1.24%													
																														0.00%			
15	ACTUATOR DATASHEETS		5621-DS-00-AA-V102-11668	DOC	1.87%	60	P	30-Dec-14	14-Dec-14	19-Dec-14	26-Dec-14	31-Dec-14	7-Jan-15	12-Jan-15	19-Jan-15	15-Jun-15	22-Jun-15	27-Jun-15	4-Jul-15	1.87%													
																														1.87%			
16	DETAIL DRAWING WITH NOMENCLATURE		5621-00-GB-V2D0/11668	DWG	1.24%	40	P	30-Dec-14	13-Jan-15	18-Jan-15	25-Jan-15	30-Jan-15	6-Feb-15	11-Feb-15	18-Feb-15	15-Jun-15	22-Jun-15	27-Jun-15	4-Jul-15	1.24%													
																														1.24%			
17	SCHEMATICS DIAGRAMS		5621-00-GB-V2SC/11668	DWG	1.24%	40	P	29-Jan-15	12-Feb-15	17-Feb-15	24-Feb-15	1-Mar-15	8-Mar-15	13-Mar-15	20-Mar-15	15-Jun-15	22-Jun-15	27-Jun-15	4-Jul-15	1.24%													
																														1.24%			
18	GENERAL ARRANGEMENT DIAGRAMS		5621-00-GB-V2D0/11668	DWG	1.87%	60	P	17-Jan-15	31-Jan-15	5-Feb-15	12-Feb-15	17-Feb-15	24-Feb-15	1-Mar-15	8-Mar-15	15-Jun-15	22-Jun-15	27-Jun-15	4-Jul-15	1.87%													
																														1.87%			
19	3 DIMENSIONAL DIAGRAMS		5621-00-GB-V2D0/11668	DWG	1.87%	60	P	17-Jan-15	31-Jan-15	5-Feb-15	12-Feb-15	17-Feb-15	24-Feb-15	1-Mar-15	8-Mar-15	15-Jun-15	22-Jun-15	27-Jun-15	4-Jul-15	1.87%													
																														1.87%			
20	ACTUATOR DATASHEETS		5621-DS-00-AA-V102-2250	DOC	1.87%	60	P	30-Nov-14	14-Dec-14	19-Dec-14	26-Dec-14	31-Dec-14	7-Jan-15	12-Jan-15	19-Jan-15	24-Jan-15	31-Jan-15	5-Feb-15	12-Feb-15	1.87%													
																														1.87%			
																														1.24%			



BuHasa Replacement of SDT Valves & Actuators for EPC Works



VENDOR DOCUMENT DELIVERABLE REGISTER

S/N	VENDOR NAME	VENDOR CODE	WTG%	Document No.		5621-SCH-00-AA-0011														
1	MSA VALVES	V4	1.0%	Revision No.		A3														
2	CAI ACTUATORS	V2	0.5%	Date:		30-Oct-15														
3	HONEYWELL	V3	0.5%	DATE:		30-Oct-15														
S/N	PROJECT DOCUMENT NUMBER	Document Title	DWG/DO C	MHS WTG	MHS	P F A	SUBMISSION SCHEDULE												PLAN	ACTUAL
							A1		A2		A3		IFA / A4		R1		FINAL ISSUE		90.04%	40.69%
PROGRESS %							SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT		
21	DETAIL DRAWING WITH NOMENCLATURE	5621-00-GB-V2D0/2250		1.24%		F														
22	SCHEMATICS DIAGRAMS	5621-00-GB-V25C/2250	DWG	1.24%	40	A	17-Jan-15	3-Feb-15	5-Feb-15	4-Mar-15	10-Mar-15									1.24%
				1.24%		P	29-Jan-15	12-Feb-15	17-Feb-15	24-Feb-15	1-Mar-15	8-Mar-15	13-Mar-15	20-Mar-15	25-Mar-15	1-Apr-15	6-Apr-15	10-Jul-15		
23	GENERAL ARRANGEMENT DIAGRAMS	5621-00-GB-V2D0/2250	DWG	1.24%	60	F														1.24%
				1.87%		A	17-Jan-15	3-Feb-15	28-Feb-15	10-Mar-15	21-Apr-15							10-Jul-15		
24	3 DIMENSIONAL DIAGRAMS	5621-00-GB-V23D/2250	DWG	1.87%	60	F														1.87%
				1.87%		A	17-Jan-15	3-Feb-15										10-Jul-15		
25	ACTUATOR DATASHEETS	5621-05-00-AA-V102-2166C	DOC	1.87%	60	F														1.87%
				1.87%		A	17-Jan-15	3-Feb-15										10-Jul-15		
26	DETAIL DRAWING WITH NOMENCLATURE	5621-00-GB-V2D0/2166C	DWG	1.24%	40	P	30-Oct-14	17-Nov-14	15-Jan-15	27-Jan-15	26-Feb-15									1.24%
				1.24%		A	30-Dec-14	13-Jan-15	18-Jan-15	25-Jan-15	30-Jan-15	6-Feb-15	11-Feb-15	18-Feb-15	24-Feb-15	2-Mar-15	7-Mar-15	14-Mar-15		
27	SCHEMATICS DIAGRAMS	5621-00-GB-V25C/2166C	DWG	1.24%	40	P	17-Jan-15	3-Feb-15	15-Feb-15	4-Mar-15	10-Mar-15									1.24%
				1.24%		A	29-Jan-15	12-Feb-15	17-Feb-15	24-Feb-15	1-Mar-15	8-Mar-15	13-Mar-15	20-Mar-15	25-Mar-15	1-Apr-15	6-Apr-15	13-Apr-15		
28	GENERAL ARRANGEMENT DIAGRAMS	5621-00-GB-V2D0/2166C	DWG	1.24%		F														1.24%
				1.87%		A	17-Jan-15	3-Feb-15	28-Feb-15	10-Mar-15	21-Apr-15							10-Jul-15		
29	3 DIMENSIONAL DIAGRAMS	5621-00-GB-V23D/2166C	DWG	1.87%	60	P	17-Jan-15	31-Jan-15	5-Feb-15	12-Feb-15	17-Feb-15	24-Feb-15	1-Mar-15	8-Mar-15	13-Mar-15	20-Mar-15	25-Mar-15	1-Apr-15		1.87%
				1.87%		F												10-Jul-15		
30	ACTUATOR DATASHEETS	5621-05-00-AA-V102-2047	DOC	1.87%	60	A	17-Jan-15	3-Feb-15												1.87%
				1.87%		P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		
31	DETAIL DRAWING WITH NOMENCLATURE	5621-00-GB-V2D0/2047	DWG	1.24%	40	F														1.87%
				1.24%		A	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		
32	SCHEMATICS DIAGRAMS	5621-00-GB-V25C/2047	DWG	1.24%	40	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		1.24%
				1.24%		A												14-Jul-15		
33	GENERAL ARRANGEMENT DIAGRAMS	5621-00-GB-V2D0/2047	DWG	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		0.00%
				1.87%		F												14-Jul-15		
34	3 DIMENSIONAL DIAGRAMS	5621-00-GB-V23D/2047	DWG	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		1.87%
				1.87%		F												14-Jul-15		
35	ACTUATOR DATASHEETS	5621-05-00-AA-V102-1165C	DOC	1.87%	60	A														1.87%
				1.87%		P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		
36	DETAIL DRAWING WITH NOMENCLATURE	5621-00-GB-V2D0/1165C	DWG	1.24%	40	F														1.87%
				1.24%		A	14-Jul-15											14-Jul-15		
37	SCHEMATICS DIAGRAMS	5621-00-GB-V25C/1165C	DWG	1.24%	40	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		1.24%
				1.24%		F												14-Jul-15		
38	GENERAL ARRANGEMENT DIAGRAMS	5621-00-GB-V2D0/1165C	DWG	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		0.00%
				1.87%		A	14-Jul-15											14-Jul-15		
39	3 DIMENSIONAL DIAGRAMS	5621-00-GB-V23D/1165C	DWG	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		1.87%
				1.87%		F												14-Jul-15		
40	ACTUATOR DATASHEETS	5621-05-00-AA-V102-2165D	DOC	1.87%	60	A														1.87%
				1.87%		P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		
41	DETAIL DRAWING WITH NOMENCLATURE	5621-00-GB-V2D0/2165D	DWG	1.24%	40	F														1.87%
				1.24%		A	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		
42	SCHEMATICS DIAGRAMS	5621-00-GB-V25C/2165D	DWG	1.24%	40	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		1.24%
				1.24%		F												14-Jul-15		
			DWG	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15		0.00%



BuHasa Replacement of SDT Valves & Actuators for EPC Works



VENDOR DOCUMENT DELIVERABLE REGISTER

S/N	VENDOR NAME	VENDOR CODE	WTG%	Document No. 5621-SCH-00-AA-0011																
1	MSA VALVES	V4	1.0%	Revision No. A3																
2	CAI ACTUATORS	V2	0.5%	Date: 30-Oct-15																
3	HONEYWELL	V3	0.5%	DATE: 30-Oct-15																
S/N	PROJECT DOCUMENT NUMBER	Document Title	DWG/DO C	MHS WTG	MHS	P	SUBMISSION SCHEDULE												PLAN	ACTUAL
S/N	PROJECT DOCUMENT NUMBER	Document Title	DWG/DO C	MHS WTG	MHS	P	A1		A2		A3		IFA / A4		R1		FINAL ISSUE		90.04%	40.69%
							SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT		
PROGRESS %							5%	8%	10%	15%	20%	35%	50%	60%	70%	80%	95%	100%		
43	GENERAL ARRANGEMENT DIAGRAMS	5621-00-GB-V2DD/2165D		1.87%		F														
44	3 DIMENSIONAL DIAGRAMS	5621-00-GB-V23D/2165D	DWG	1.87%	60	P	14-Jul-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	14-Jul-15	1.87%	1.87%
					F															
45	ACTUATOR DATASHEETS	5621-05-00-AA-V102-1469	DOC	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	14-Jul-15	1.87%	1.87%
					F															
46	DETAIL DRAWING WITH NOMENCLATURE	5621-00-GB-V2DD/1469	DWG	1.24%	40	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	14-Jul-15	1.24%	1.24%
					F															
47	SCHEMATICS DIAGRAMS	5621-00-GB-V25C/1469	DWG	1.24%	40	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	14-Jul-15	1.24%	1.24%
					F															
48	GENERAL ARRANGEMENT DIAGRAMS	5621-00-GB-V2DD/1469	DWG	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15	1.87%	1.87%
					F															
49	3 DIMENSIONAL DIAGRAMS	5621-00-GB-V23D/1469	DWG	1.87%	60	P	14-Jul-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	14-Jul-15	1.87%	1.87%
					F															
50	ACTUATOR DATASHEETS	5621-05-00-AA-V102-2455	DOC	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	14-Jul-15	1.87%	1.87%
					F															
51	DETAIL DRAWING WITH NOMENCLATURE	5621-00-GB-V2DD/2455	DWG	1.24%	40	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	14-Jul-15	1.24%	1.24%
					F															
52	SCHEMATICS DIAGRAMS	5621-00-GB-V25C/2455	DWG	1.24%	40	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	14-Jul-15	1.24%	1.24%
					F															
53	GENERAL ARRANGEMENT DIAGRAMS	5621-00-GB-V2DD/2455	DWG	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15	1.87%	1.87%
					F															
54	3 DIMENSIONAL DIAGRAMS	5621-00-GB-V23D/2455	DWG	1.87%	60	P	14-Jul-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	14-Jul-15	1.87%	1.87%
					F															
55	ACTUATOR DATASHEETS	5621-05-00-AA-V102-0299	DOC	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15	1.87%	1.87%
					F															
56	DETAIL DRAWING WITH NOMENCLATURE	5621-00-GB-V2DD/0299	DWG	1.24%	40	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15	1.24%	1.24%
					F															
57	SCHEMATICS DIAGRAMS	5621-00-GB-V25C/0299	DWG	1.24%	40	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15	1.24%	1.24%
					F															
58	GENERAL ARRANGEMENT DIAGRAMS	5621-00-GB-V2DD/0299	DWG	1.87%	60	P	15-Aug-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	28-Oct-15	1.87%	1.87%
					F															
59	3 DIMENSIONAL DIAGRAMS	5621-00-GB-V23D/0299	DWG	1.87%	60	P	14-Jul-15	29-Aug-15	3-Sep-15	10-Sep-15	15-Sep-15	22-Sep-15	27-Sep-15	4-Oct-15	9-Oct-15	16-Oct-15	21-Oct-15	14-Jul-15	1.87%	1.87%
					F															
MSA VALVES & ROTORK (1%)				100%	6430	P												90%	0.00%	
60	GENERAL ARRANGEMENT DRAWINGS - MSA Valves	5621-00-MB-V401	2-DWG	7.78%	500	P	4-May-15	18-May-15	1-Jul-15	8-Jul-15					8-Jul-15	15-Jul-15	20-Jul-15	27-Jul-15	7.78%	42%
			2-DWG		F															
61	GENERAL ARRANGEMENT DRAWINGS - BUFFER VESSELS + CALCULATIONS	5621-00-MB-V403	2-DWG	7.78%	300	P	6-Apr-15	5-May-15	1-Jul-15			1-Jul-15			8-Jul-15	15-Jul-15	20-Jul-15	27-Jul-15	4.67%	3.89%
			2-DWG	4.67%	F	10-Apr-15	24-Apr-15	11-Jul-15	18-Jul-15											
62	GENERAL ASSEMBLY DRAWING - VALVE AND ACTUATOR	5621-00-MB-V404	2-DWG	7.78%	500	P	6-Apr-15	5-May-15	16-Jul-15			1-Jul-15			8-Jul-15	15-Jul-15	20-Jul-15	27-Jul-15	7.78%	2.33%
			2-DWG	7.78%	F	4-May-15	18-May-15	1-Jul-15	8-Jul-15											
63	ACTUATOR GENERAL ARRANGEMENT DRAWINGS - Re- Oreinted	5621-00-MB-V405	2-DWG	6.22%	400	P	23-May-15	15-Apr-15				1-Jul-15		1-Jul-15	8-Jul-15	15-Jul-15	20-Jul-15	27-Jul-15	6.22%	3.89%
			2-DWG	6.22%	F	10-Apr-15	24-Apr-15	1-Jul-15	8-Jul-15											
			2-DWG	6.22%	400	P	4-May-15	18-May-15	1-Jul-15	8-Jul-15				8-Jul-15	15-Jul-15	20-Jul-15	27-Jul-15	6.22%	0.00%	



BuHasa Replacement of SDT Valves & Actuators for EPC Works



VENDOR DOCUMENT DELIVERABLE REGISTER

S/N	VENDOR NAME	VENDOR CODE	WTG%	Document No.		Revision No.		Date:		5621-SCH-00-AA-0011		A3		30-Oct-15		DATE:		30-Oct-15				
S/N	PROJECT DOCUMENT NUMBER	Document Title	DWG/DO C	MHS WTG	MHS	P	F	A	SUBMISSION SCHEDULE										PLAN	ACTUAL		
									A1		A2		A3		IFA / A4		R1		FINAL ISSUE		90.04%	40.69%
									SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	90.04%	40.69%
PROGRESS %									5%	8%	10%	15%	20%	35%	50%	60%	70%	80%	95%	100%		
64	GENERAL ASSEMBLY DRAWING - VALVE WITH ACTUATOR AND FIRE PROOFING BOX	5621-00-MB-V406	2-DWG			F																
			2-DWG	6.22%		A		28-Jun-15	15-Jul-15					1-Jul-15								3.11%
			2-DWG	4.67%	300	P		5-Apr-15	19-Apr-15	1-Jul-15	8-Jul-15					10-May-15	17-May-15	22-May-15	29-May-15		4.67%	
65	VALVE AND ACTUATOR SCHEMATIC DRAWINGS	5621-00-JB-V401	2-DWG			F																
			2-DWG	4.67%		A																3.27%
			2-DWG	1.56%	100	P		8-Jul-15	15-Jul-15	22-Jul-15	29-Jul-15			1-Jul-15	2-Aug-15	4-Aug-15	12-Aug-15	17-Aug-15	24-Aug-15		1.56%	
66	VALVE AND ACTUATOR PIOLTING SCHEME	5621-00-JB-V402	2-DWG			F																
			2-DWG	1.56%		A																0.00%
			2-DWG	1.56%	100	P		8-Jul-15	15-Jul-15	22-Jul-15	29-Jul-15					5-Aug-15	12-Aug-15	17-Aug-15	24-Aug-15		1.56%	
67	VALVE & ACTUATOR CONTROL BOX DRAWINGS	5621-00-JA-V401	2-DWG			F																
			2-DWG	1.56%		A																0.00%
			2-DWG	1.56%	100	P		8-Jul-15	15-Jul-15	22-Jul-15	29-Jul-15					5-Aug-15	12-Aug-15	17-Aug-15	24-Aug-15		1.56%	
68	HOOK UP/ INSTALLATION DRAWINGS	5621-00-JB-V403	2-DWG			F																
			2-DWG	1.56%		A																0.00%
			2-DWG	1.56%	100	P		8-Jul-15	15-Jul-15	22-Jul-15	29-Jul-15					5-Aug-15	12-Aug-15	17-Aug-15	24-Aug-15		1.56%	
69	MSA VALVES + ACTUATOR DATA SHEET	5621-DS-00-AA-V401	2-DWG	10.11%	650	P		25-Mar-15	8-Apr-15	15-Apr-15	22-Apr-15					1-Jul-15	4-Jul-15	9-Aug-15			10.11%	8.09%
			2-DWG	10.11%		A		24-Jun-15	29-Jun-15	20-Jul-15												
			2-DWG	2.49%	160	P		30-Mar-15	13-Apr-15	20-Apr-15	27-Apr-15					4-May-15	11-May-15	16-May-15	23-May-15		2.49%	
70	PAINTING PROCEDURE FOR VALVES & ACTUATORS	5621-PP-00-AA-V401	2-DWG			F																
			2-DWG	2.49%		A		4-Jul-15														0.12%
71	VENDOR PROJECT QUALITY PLAN - ROTORK & MSA	5621-PP-00-AA-V402	2-DWG	0.93%	60	P		8-Jul-15	15-Jul-15	22-Jul-15	29-Jul-15					5-Aug-15	12-Aug-15	17-Aug-15	24-Aug-15		0.93%	0.93%
			2-DWG	0.93%		A														15-May-15	24-Aug-15	0.93%
72	DETAILS OF INHOUSE TEST FACILITY- ROTORK & MSA	5621-GEN-00-AA-V402	2-DWG	0.93%	60	P		8-Jul-15	15-Jul-15	22-Jul-15	29-Jul-15					5-Aug-15	12-Aug-15	17-Aug-15	24-Aug-15		0.93%	0.93%
			2-DWG	0.93%		F														15-May-15		0.93%
			2-DWG	1.09%	70	P		22-Oct-15	5-Nov-15	12-Nov-15	19-Nov-15					26-Nov-15	3-Dec-15	8-Dec-15	15-Dec-15		0.05%	
73	ALL CERTIFICATES AND TEST REPORTS - LOG/DOSSEIR	5621-RT-00-AA-V404	2-DWG			F																
			2-DWG	1.09%		A																0.00%
			2-DWG	3.11%	200	P		8-Jul-15	15-Jul-15	22-Jul-15	29-Jul-15					5-Aug-15	12-Aug-15	17-Aug-15	24-Aug-15		3.11%	
74	MONTHLY PROGRESS REPORTS (INCL. SUB ORDER STATUS)	5621-RT-00-AA-V402	2-DWG			F																
			2-DWG	3.11%		A														30-Jul-15		3.11%
75	WEEKLY PROGRESS REPORTS	5621-RT-00-AA-V401	2-DWG	2.33%	150	P		27-Mar-15	10-Apr-15	17-Apr-15	24-Apr-15					1-May-15	8-May-15	13-May-15	20-May-15		2.33%	
			2-DWG	2.33%		F		4-Jun-15												4-Jun-15		2.33%
76	DETAILED MANUFACTURING & DELIVERY SCHEDULE INCLUDING SUB VENDOR ACTIVITY	5621-SCH-00-AA-V401	2-DWG	3.11%	200	P		8-Jul-15	15-Jul-15	22-Jul-15	29-Jul-15					29-Jul-15	29-Jul-15	6-Jan-00	13-Jan-00		3.11%	
			2-DWG	3.11%		F																
			2-DWG	3.11%		A		4-Jun-15												4-Jun-15		3.11%
77	COPIES OF PO SUB VENDORS(UN PRICED)	5621-PO-00-AA-V401	2-DWG	2.33%	150	P		22-Mar-15	5-Apr-15	12-Apr-15	19-Apr-15					26-Apr-15	3-May-15	8-May-15	15-May-15		2.33%	
			2-DWG	2.33%		F																
			2-DWG	2.33%		A		4-Jun-15												4-Jun-15		2.33%
78	INSPECTION & TEST PLAN -VALVES (AS PER DGS-1511-046)	5621-ITP-00-AA-V401	2-DWG	2.33%	150	P		11-Mar-15	25-Mar-15	1-Apr-15	8-Apr-15					15-Apr-15	22-Apr-15	27-Apr-15	4-May-15		2.33%	
			2-DWG	2.33%		F																
			2-DWG	2.33%		A		24-Mar-15	6-Apr-15													0.19%
79	INSPECTION & TEST PLAN -ACTUATORS (AS PER DGS-1511-046)	5621-ITP-00-AA-V402	2-DWG	2.33%	150	P		8-Jul-15	15-Jul-15	22-Jul-15	29-Jul-15					5-Aug-15	12-Aug-15	17-Aug-15	24-Aug-15		2.33%	
			2-DWG	2.33%		F																
			2-DWG	2.33%		A		14-Jul-15														0.12%
80	MANUFACTURING PROCEDURE SPECIFICATION	5621-SP-00-JB-V401	2-DWG	1.09%	70	P		30-Apr-15	14-May-15	21-May-15	28-May-15					4-Jun-15	11-Jun-15	16-Jun-15	23-Jun-15		1.09%	
			2-DWG	1.09%		F																
			2-DWG	1.09%		A		1-Jun-15												12-Jul-15		1.09%
81	ACTUATOR SIZING FINAL CALCULATIONS WITH MAST & TORQUE VALUES - AS BUILT	5621-NC-00-AA-V402	2-DWG	1.56%	100	P		10-Apr-15	24-Apr-15	1-May-15	8-May-15					15-May-15	22-May-15	27-May-15	3-Jun-15		1.56%	
			2-DWG	1.56%		F																
			2-DWG	1.40%	90	P		15-Mar-15	29-Mar-15	5-Apr-15	12-Apr-15			1-Jul-15		19-Apr-15	26-Apr-15	1-May-15	8-May-15		1.40%	0.78%
82	NDE PROCEDURE'S	5621-PP-00-AA-V403	2-DWG			F																
			2-DWG	1.40%		A		1-Apr-15	19-Apr-15	5-Jul-15												0.14%
			2-DWG	1.09%	70	P		30-Mar-15	13-Apr-15	20-Apr-15	27-Apr-15					4-May-15	11-May-15	16-May-15	23-May-15		1.09%	
83	PRESSURE TEST PROCEDURE - MSA VALVES	5621-PP-00-AA-V404	2-DWG			F																
			2-DWG	1.09%		A		28-Apr-15	10-May-15	6-Jul-15												0.11%
			2-DWG	2.33%	150	P		8-Jul-15	15-Jul-15	22-Jul-15	29-Jul-15					5-Aug-15	12-Aug-15	17-Aug-15	24-Aug-15		2.33%	
84	VALVE AND ACTUATOR INSTALLATION PROCEDURE	5621-PP-00-AA-V405	2-DWG			F																
			2-DWG	2.33%		A																0.00%
			2-DWG	1.24%	80	P		22-Oct-15	5-Nov-15	12-Nov-15	19-Nov-15					26-Nov-15	3-Dec-15	8-Dec-15	15-Dec-15		0.06%	
85	INSTALLATION , OPERATION & MAINTENANCE MANUAL	5621-PP-00-AA-V406	2-DWG			F																
			2-DWG	1.24%		A		28-Apr-15	6-May-15													0.06%
			2-DWG	0.93%	60	P		30-Mar-15	13-Apr-15	20-Apr-15	27-Apr-15					4-May-15	11-May-15	16-May-15	23-May-15		0.93%	

VENDOR DOCUMENT DELIVERABLE REGISTER

S/N	VENDOR NAME	VENDOR CODE		WTG%	Document No. 5621-SCH-00-AA-0011																			
1	MSA VALVES	V4		1.0%	Revision No. A3																			
2	CAI ACTUATORS	V2		0.5%	Date: 30-Oct-15																			
3	HONEYWELL	V3		0.5%	DATE: 30-Oct-15																			
S/N	PROJECT DOCUMENT NUMBER	Document Title	DWG/DO C	MHS WTG	MHS	P F A	SUBMISSION SCHEDULE																PLAN	ACTUAL
							A1		A2		A3		IFA / A4		R1		FINAL ISSUE							
							SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT						
PROGRESS %							5%	8%	10%	15%	20%	35%	50%	60%	70%	80%	95%	100%	90.04%	40.69%				
86	PACKING, SHIPPING, PRESERVATION, HANDLING & STORAGE PROCEDURE	5621-PP-00-AA-V408	2-DWG			F																		
					A	1-Apr-15	12-May-15																	
					P	26-Apr-15	10-May-15	17-May-15	24-May-15															
87	FACTORY ACCEPTANCE & TEST PROCEDURE	5621-PP-00-AA-V409	2-DWG		100	P																		
						F																		
						A	1-Apr-15	13-May-15	7-Jun-15	22-Jun-15														
88	WPS & PQR	5621-PP-00-AA-V410	2-DWG		70	P																		
						F																		
						A	8-Jun-15	5-Jul-15																
89	Vendor PMI Procedure	5621-PP-00-AA-V411	2-DWG		80	P																		
						F																		
						A	4-Jun-15	4-Jun-15	6-Jul-15															
90	ISO 9001 CERTIFICATE / QUALITY MANUAL / CERTIFICATES - ROTORK, MSA	5621-GEN-00-AA-V401	2-DWG		100	P																		
						F																		
						A	1-Apr-15	19-Apr-15	23-Apr-15															
91	PRE-COMMISSIONING/ COMMISSIONING/START UP SPARES AND CONSUMABLES DURING CONSTRUCTION	5621-GEN-00-AA-V403	2-DWG		70	P																		
						F																		
						A	22-Oct-15	5-Nov-15	12-Nov-15	19-Nov-15														
92	1 YEAR MAINTENANCE AND OPERATION SPARES IN SPIR FORM	5621-GEN-00-AA-V404	2-DWG		70	P																		
						F																		
						A																		
93	2 YEARS OPERATING SPARE LIST(PRICED) IN THE FORM FOR RECOMMENDED TWO YEARS OPERATING SPARE PART PRICED LIST	5621-GEN-00-AA-V405	2-DWG		80	P																		
						F																		
						A																		
94	SUBMISSION OF G-SPIR PACKAGE	5621-GEN-00-AA-V406	2-DWG		80	P																		
						F																		
						A																		
95	LIST OF SPECIAL TOOLS & TACKLES	5621-SCH-00-AA-V402	2-DWG		90	P																		
						F																		
						A																		
96	SHIPPING SCHEDULE AND PACKING LIST	5621-SCH-00-AA-V403	2-DWG		90	P																		
						F																		
						A																		
97	MANUFACTURING RECORD BOOK (MRB) INDEX	5621-SCH-00-AA-V404	2-DWG		60	P																		
						F																		
						A	8-Jul-15	15-Jul-15	22-Jul-15	29-Jul-15														
98	MANUFACTURER DATA BOOK	5621-SCH-00-AA-V405	2-DWG		100	P																		
						F																		
						A																		
99	TAG PLATES SCHEDULE (INCL. PRESSURE SWITCHES, LIMIT SWITCHES, PSVs, SOVs)	5621-SCH-00-AA-V406	2-DWG		60	P																		
						F																		
						A	15-Jul-15	29-Jul-15	5-Aug-15	12-Aug-15														
100	TAG DIMENSIONAL DRAWINGS	5621-00-JA-V402	2-DWG		60	P																		
						F																		
						A	20-Jun-15																	
HONEYWELL (0.5%)				100%	3215	P																		
101	MODBUS IP ADDRESS	5621-SP-00-JA-V301				F																		
						A																		
						P	25-Jul-15	2-Aug-15	7-Aug-15	12-Aug-15														
102	ETHERNET / CAT-6 CABLE SCHEDULE	5621-SCH-00-JA-V301				F																		
						A																		
						P	22-Jul-15	1-Aug-15	6-Aug-15	11-Aug-15														
103	SYSTEM ARCHITECTURE	5621-SP-00-JA-V302				F																		
						A																		
						P	15-Jun-15	25-Jun-15	30-Jun-15	5-Jul-15														
104	BILL OF MATERIALS	5621-MTO-00-JA-V301				F																		
						A	2-Jul-15																	
						P	30-Jun-15	10-Jul-15	15-Jul-15	20-Jul-15														
105	HARDWARE / SOFTWARE SPECIFICATIONS	5621-SP-00-JA-V303				F																		
						A																		
						P	15-Jul-15	25-Jul-15	30-Jul-15	4-Aug-15														
106	EXISTING CABINET LAYOUT MODIFICATION	5621-00-JB-V301				F																		
						A																		
						P	30-Jun-15	10-Jul-15	15-Jul-15	20-Jul-15														



BuHasa Replacement of SDT Valves & Actuators for EPC Works



VENDOR DOCUMENT DELIVERABLE REGISTER

S/N	VENDOR NAME	VENDOR CODE		WTG%	Document No. 5621-SCH-00-AA-0011										Revision No. A3		Date: 30-Oct-15		DATE: 30-Oct-15					
1	MSA VALVES	V4		1.0%																				
2	CAI ACTUATORS	V2		0.5%																				
3	HONEYWELL	V3		0.5%																				
S/N	PROJECT DOCUMENT NUMBER	Document Title	DWG/DO C	MHS WTG	MHS	P	SUBMISSION SCHEDULE																PLAN	ACTUAL
							A1		A2		A3		IFA / A4		R1		FINAL ISSUE							
							SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT				
PROGRESS %							5%	8%	10%	15%	20%	35%	50%	60%	70%	80%	95%	100%	90.04%	40.69%				
107	SYSTEM INTERCONNECTION CABLE SCHEDULE	5621-SCH-00-JB-V305		9.33%		F																		
				4.48%	144	P	7-Aug-15	17-Aug-15	22-Aug-15	27-Aug-15						1-Sep-15	6-Sep-15	11-Sep-15	18-Sep-15	4.48%				
108	GA DRAWING FOR SS3-DCS-01	5621-00-JB-V302-SS3/1		4.48%		F																		
				4.48%	144	P	7-Aug-15	17-Aug-15	22-Aug-15	27-Aug-15						1-Sep-15	6-Sep-15	11-Sep-15	18-Sep-15	4.48%				
109	GA DRAWING FOR SS3-DMC-02	5621-00-JB-V302-SS3/2		4.48%		F																		
				4.48%	144	P	7-Aug-15	17-Aug-15	22-Aug-15	27-Aug-15						1-Sep-15	6-Sep-15	11-Sep-15	18-Sep-15	4.48%				
110	GA DRAWING FOR SS3-DMC-01	5621-00-JB-V302-SS3/3		4.48%		F																		
				4.48%	144	P	7-Aug-15	17-Aug-15	22-Aug-15	27-Aug-15						1-Sep-15	6-Sep-15	11-Sep-15	18-Sep-15	4.48%				
111	GA DRAWING FOR SS2-DCS-01	5621-00-JB-V302-SS2/1		4.48%		F																		
				4.48%	144	P	7-Aug-15	17-Aug-15	22-Aug-15	27-Aug-15						1-Sep-15	6-Sep-15	11-Sep-15	18-Sep-15	4.48%				
112	GA DRAWING FOR SS2-DMC-02	5621-00-JB-V302-SS2/2		4.48%		F																		
				4.48%	144	P	7-Aug-15	17-Aug-15	22-Aug-15	27-Aug-15						1-Sep-15	6-Sep-15	11-Sep-15	18-Sep-15	4.48%				
113	GA DRAWING FOR SS2-DMC-01	5621-00-JB-V302-SS2/3		4.48%		F																		
				4.48%	144	P	7-Aug-15	17-Aug-15	22-Aug-15	27-Aug-15						1-Sep-15	6-Sep-15	11-Sep-15	18-Sep-15	4.48%				
114	GA DRAWING FOR SS4-DMC-02	5621-00-JB-V302-SS4/1		4.48%		F																		
				4.48%	144	P	7-Aug-15	17-Aug-15	22-Aug-15	27-Aug-15						1-Sep-15	6-Sep-15	11-Sep-15	18-Sep-15	4.48%				
115	GA DRAWING FOR SS5-DMC-01	5621-00-JB-V302-SS5/1		4.48%		F																		
				4.48%	144	P	7-Aug-15	17-Aug-15	22-Aug-15	27-Aug-15						1-Sep-15	6-Sep-15	11-Sep-15	18-Sep-15	4.48%				
116	GA DRAWING FOR AR2-IPS-01	5621-00-JB-V302-AR2/1		4.48%		F																		
				4.48%	144	P	7-Aug-15	17-Aug-15	22-Aug-15	27-Aug-15						1-Sep-15	6-Sep-15	11-Sep-15	18-Sep-15	4.48%				
117	GA DRAWING FOR AR2-IMC-01	5621-00-JB-V302-AR2/2		4.48%		F																		
				1.56%	50	P	7-Aug-15	17-Aug-15	22-Aug-15	27-Aug-15						1-Sep-15	6-Sep-15	11-Sep-15	18-Sep-15	1.56%				
118	LOGIC SCREEN SHOTS BEFORE & AFTER MODIFICATIONS	5621-00-JA-V303		1.56%		F																		
				2.33%	75	P	20-Mar-16	30-Mar-16	4-Apr-16	9-Apr-16						14-Apr-16	19-Apr-16	24-Apr-16	1-May-16	0.00%				
119	UPDATING THE HPM, IPS-2 SYSTEM / MARSHALLING CABINET LAYOUT	5621-00-JA-V304		2.33%		F																		
				0.78%	25	P	20-Mar-16	30-Mar-16	4-Apr-16	9-Apr-16						14-Apr-16	19-Apr-16	24-Apr-16	1-May-16	0.00%				
120	UPDATING THE PANEL GA DRAWINGS AND PREPARATION OF NEW DRAWINGS - REDLINE MARK UP	5621-00-JA-V305		0.78%		F																		
				0.78%	25	P	20-Mar-16	30-Mar-16	4-Apr-16	9-Apr-16						14-Apr-16	19-Apr-16	24-Apr-16	1-May-16	0.00%				
121	UPDATING THE EXISTING WIRING DRAWINGS AND PREPARATION OF NEW DRAWINGS - REDLINE MARK UP	5621-00-JA-V306		0.78%		F																		
				0.78%	25	P	20-Mar-16	30-Mar-16	4-Apr-16	9-Apr-16						14-Apr-16	19-Apr-16	24-Apr-16	1-May-16	0.00%				
122	UPDATING THE EXISTING DISTRIBUTION DRAWINGS AND PREPARATION OF NEW DRAWINGS - REDLINE MARK UP	5621-00-JA-V307		0.78%		F																		
				0.78%	25	P	20-Mar-16	30-Mar-16	4-Apr-16	9-Apr-16						14-Apr-16	19-Apr-16	24-Apr-16	1-May-16	0.00%				
123	UPDATING HPM FTA CABLE SCHEDULE - RED LINE MARK UP	5621-00-JA-V308		0.78%		F																		
				0.78%	25	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15						14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	0.78%				
124	UPDATING IPS-2 FTA CABLE SCHEDULE - RED LINE MARK UP	5621-00-JA-V309		0.78%		F																		
				0.78%	25	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15						14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	0.78%				
125	UPDATING OF GRAPHICS	5621-00-JA-V310		0.78%		F																		
				0.78%	25	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15						14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	0.78%				
126	UPDATING OF GROUP DISPLAYS	5621-00-JA-V311		0.78%		F																		
				0.78%	25	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15						14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	0.78%				
127	UPDATING OF LOOP DISPLAYS	5621-00-JA-V312		0.78%		F																		
				0.78%	25	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15						14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	0.78%				
128	UPDATING OF TREND DISPLAYS	5621-00-JA-V313		0.78%		F																		
				0.78%	25	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15						14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	0.78%				

S/N		VENDOR NAME	VENDOR CODE			WTG%	Document No. 5621-SCH-00-AA-0011														
1		MSA VALVES	V4			1.0%	Revision No. A3														
2		CAI ACTUATORS	V2			0.5%	Date: 30-Oct-15														
3		HONEYWELL	V3			0.5%	DATE: 30-Oct-15														
S/N	PROJECT DOCUMENT NUMBER		Document Title	DWG/DO C	MHS WTG	MHS	P F A	SUBMISSION SCHEDULE												PLAN	ACTUAL
								A1		A2		A3		IFA / A4		R1		FINAL ISSUE			
								SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT	SUBMISSION	RCV. COMT		
PROGRESS %								5%	8%	10%	15%	20%	35%	50%	60%	70%	80%	95%	100%		
129	UPDATING OF ALARM DISPLAYS		5621-00-JA-V314				F														
					0.78%		A														
					0.62%	20	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15					14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	0.62%	0.00%
130	UPDATING OF LOGS / REPORTS		5621-00-JA-V315				F														
					0.62%		A														
					0.62%	20	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15					14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	0.62%	0.00%
131	METHOD STATEMENT AND RIST ASSESMENTS FOR EXISTING DCS AND IPS SYSTEM MODIFICATION		5621-MS-00-JA-V301				F														
					0.62%		A														
					0.62%	20	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15					14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	0.62%	0.00%
132	QUALITY CONTROL MANUAL		5621-PP-00-JA-V301				F														
					0.62%		A														
					0.62%	20	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15					14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	0.62%	0.00%
133	QUALITY CONTROL PLAN		5621-PP-00-JA-V302				F														
					0.62%		A														
					0.62%		P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15					14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	0.00%	0.00%
134	WEEKLY PROGRESS REPORT		5621-RT-00-JA-V302				F														
					0.00%		A														
					2.33%	75	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15					14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	2.33%	0.00%
135	SCHEDULE		5621-SCH-00-JB-V303				F														
					2.33%		A														
					2.33%	75	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15					14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	2.33%	0.00%
136	SPARE PARTS LIST (COMMISSIONING SPARES)		5621-SCH-00-JA-V304				F														
					2.33%		A														
					2.33%	75	P	20-Aug-15	30-Aug-15	4-Sep-15	9-Sep-15					14-Sep-15	19-Sep-15	24-Sep-15	1-Oct-15	2.33%	0.00%
