



**ABU DHABI GAS INDUSTRIES LTD.
(GASCO)**

**PROJECT TITLE:
EPC for ESD Valves and Actuators Replacement at BuHasa in
TRAIN 1 & TRAIN 2**

**REPORT NO:
WPR-007**

**DOCUMENT TITLE:
WEEKLY PROGRESS REPORT-007
(13-Dec-14 to 19-Dec-14)**

**DOCUMENT NO:
5621-RT-00-AA-0001**

			Saad Zaman	Rishi Chadda		
			(Prepared By)	(Checked By)	GASCO	GASCO
			AHEC	AHEC	APPROVED	

INDEX

Sr.No	Description	Page no
1	Weekly Narrative Report	3
2	HSE Statistics	4
3	Overall Progress Summary	5
5	Major Activities Delayed (More than 2 weeks)	6
6	Critical Documents Awaiting Company Review (More Than 2 Weeks)	7
7	EDDR - S Curve - ATTACHMENT 1	
8	PSR - S Curve - ATTACHMENT 2	
9	Overall - S Curve - ATTACHMENT 3	
10	EDDR SUMMARY - ATTACHMENT 4	
11	PSR SUMMARY - ATTACHMENT 5	
12	Weekly Construction Quantity Based Progress Report(Civil)	WILL BE SUBMITTED AFTER BOQ PREPARATION
13	Weekly Construction Quantity Based Progress Report(Mech)	WILL BE SUBMITTED AFTER BOQ PREPARATION
14	Weekly Construction Quantity Based Progress Report(E & I)	WILL BE SUBMITTED AFTER BOQ PREPARATION
15	Summary Status of Milestones	UNDER PREPARATION

AttachmentS

Sr.No	Description	Page no
1		
2		



EPC for ESD Valves and Actuators Replacement at BuHasa in TRAIN 1 & TRAIN 2
Project No: 5621



WEEKLY NARRATIVE REPORT

Weekly Progress Report No.: WPR-007

Cut-Off Date: 19-Dec-14

PROGRESS SUMMARY:	% Progress (as of 19-Dec-14)
Cumulative Baseline Planned Progress Percentage (%)	2.89%
Cumulative Recovery Planned Progress Percentage (%)	N-A
Cumulative Actual Progress Percentage (%)	3.29%
Cumulative Variance (%) [Actual Progress - Recovery Plan Progress]	N-A
Cumulative Variance (%) [Actual Progress - Baseline Plan Progress]	0.40%

Major Activities Performed During This Period	Major Activities Planned for Next Week
HOME OFFICE ENGINEERING & PROJECT MANAGEMENT	
1. Comments Received and Compiled on Planning Package Rev A4 2. Submission of Piping Material Specifications Rev 1 3. Submission of Project Specification Addendum - Structural (DGS-1882-001 Rev. 1) 5. Submission of P&ID Index and P&IDs Rev A1 6. Submission of Waste Management Plan Rev 1 7. Submission and Comments receiving on Emergency Response Plan Rev A2 8. Submission of Project Co-ordination Procedure Rev A3 9. Preparation of Method Statement for Work Packs in Progress 10. TBT for Valves & Actuators is under progress	1. Submission & finalization of Planning Package Rev A4 2. Submission of Emergency Response Plan A3 3. Submission of HSE Plan Rev A2 4. Submission of Datasheets for Valves & Actuators Rev A3 5. Submission of Method Statement for Work Packs 6. Final Datasheets for Valve & Actuators
PROCUREMENT	
1. CAI Datasheets - Comments being Incorporated 2. Vendor Technical Clarifications is in Progress 3. Technical offers and Dwgs received and submitted for TBE 4. PO released to CAI Actuators 5. Insulation & Scaffolding Subcontractor finalization	1. CAI Actuators Revised Datasheets 2. Kickoff meeting with Honey Well 3. Revised Valve Datasheets to be received & sharing with Vendor 4. Insulation Removal Vendor Finalization
CONSTRUCTION	
1. PTW Training for HSE Engineer has been done 2. HIRA Training for HSE Engineer is in Progress 3. Discussions and Site Visits with Insulation removal Team 4. Submission of Following Civil Drawings Rev A2 - i General Notes - Civil Works - ii General Notes Structural Works - iii Raods and Paving Details - iv Typical Details - Ladder and Handrails - v Standard Details - Concrete Protection 5. Piping Engineer - Interviewed and Approved	1. HIRA Training Completion for HSE Engineer 2. Temperory Sitting Arrangments for AHEC Site Team 3. HSE Inductions for De-Insulation Crew 4. Commence De-Insulation of 9 Valves Preparations and Surveys

Remark/Area of Concerns:			
Sr.No	Description	Action By	Remark
1	DATASHEETS FOR SDT VALVE AND ACTUATORS	TEBODIN	



EPC for ESD Valves and Actuators Replacement at BuHasa in TRAIN 1 & TRAIN 2
Project No: 5621



HSE Statistics

Date 19-Dec-14

Sr. No	Safety Statistics	Up to Last Week	In This Period	Cumulative
1	Man-Hours Worked Without LTI (Home Office)	3100	330	3430
2	Total No Of Days Worked Without LTI	0	0	0
3	Man-Hours Worked Without LTI, Site	0	0	0
4	LTI	0	0	0
5	Restricted Work Cases (RWC)	0	0	0
6	Medical Treatment Cases (MTC)	0	0	0
7	Total HSE Supervisors (Nos.)	0	0	0
8	Ratio of HSE Supervisor Vs Employees	0	0	0
9	Total Manpower Mobilized, Home Office	6	0	6
10	Total Man-Hours Worked	3100	330	3430



EPC for ESD Valves and Actuators Replacement at BuHasa in TRAIN 1 & TRAIN 2

GASCO PROJECT NO: 5621

Progress Statistics

Overall Project Progress summary (Level- 2)



Progress for Week Ending : 19-Dec-14

SI No.	Activity Description	Weight Factors		Cumulative Progress (%)			Progress during Reporting			Completion Date		
		Level-1	Level-2	Base Plan	Recovery Plan	Actual	Base Plan	Recovery Plan	Actual	Early Plan	Forecast	Actual
1. Detailed Engineering												
a)	General	1.19%	23.88%	76.10%		47.71%	6.09%		0.00%	08-Apr-15	-	-
b)	Process	0.22%	4.49%	64.00%		59.32%	16.93%		0.00%	15-Apr-15	-	-
c)	Mechanical / Piping	1.26%	25.19%	41.96%		28.15%	7.61%		0.00%	01-Apr-15	-	-
d)	Instrumentation	1.26%	25.19%	30.57%		24.40%	10.54%		0.00%	08-Apr-15	-	-
e)	HSE	0.24%	4.71%	7.67%		7.67%	4.18%		0.00%	08-Apr-15	-	-
f)	Civil / Structure	0.83%	16.54%	13.05%		32.12%	8.20%		0.00%	15-Apr-15	-	-
Sub-Total (Detail Engineering)		5.00%	100.00%	41.83%		32.97%	4.22%		0.00%	15-Apr-15		
2. Procurement												
a)	Long Lead Items	19.20%	48.00%	3.00%		7.07%	1.00%		0.57%	04-Sep-15	-	-
b)	Bulk Materials	16.00%	40.00%	0.50%		0.00%	0.50%		0.00%	11-Sep-15	-	-
c)	Operating Spares	4.80%	12.00%	3.00%		6.00%	1.00%		0.00%	04-Sep-15	-	-
Sub-Total (Procurement)		40.00%	100.00%	2.00%		4.11%	0.80%		0.27%	11-Sep-15		
3. Construction & Commissioning												
a)	Construction & Pre-commissioning	50.08%	90.00%	0.00%		0.00%	0.00%		0.00%	18-Dec-16	-	-
b)	Commissioning & As-Built Drawings	4.92%	10.00%	0.00%		0.00%	0.00%		0.00%	08-Feb-17	-	-
Sub-Total (Construction & Commissioning)		55.00%	100.00%	0.00%		0.00%	0.00%		0.00%	08-Feb-17		
Overall Progress %		100.00%		2.89%		3.29%	0.53%		0.11%			

Note : 1. Above details shall be consistent with the agreed WBS, Progress Measurement and Progress Reporting Systems.

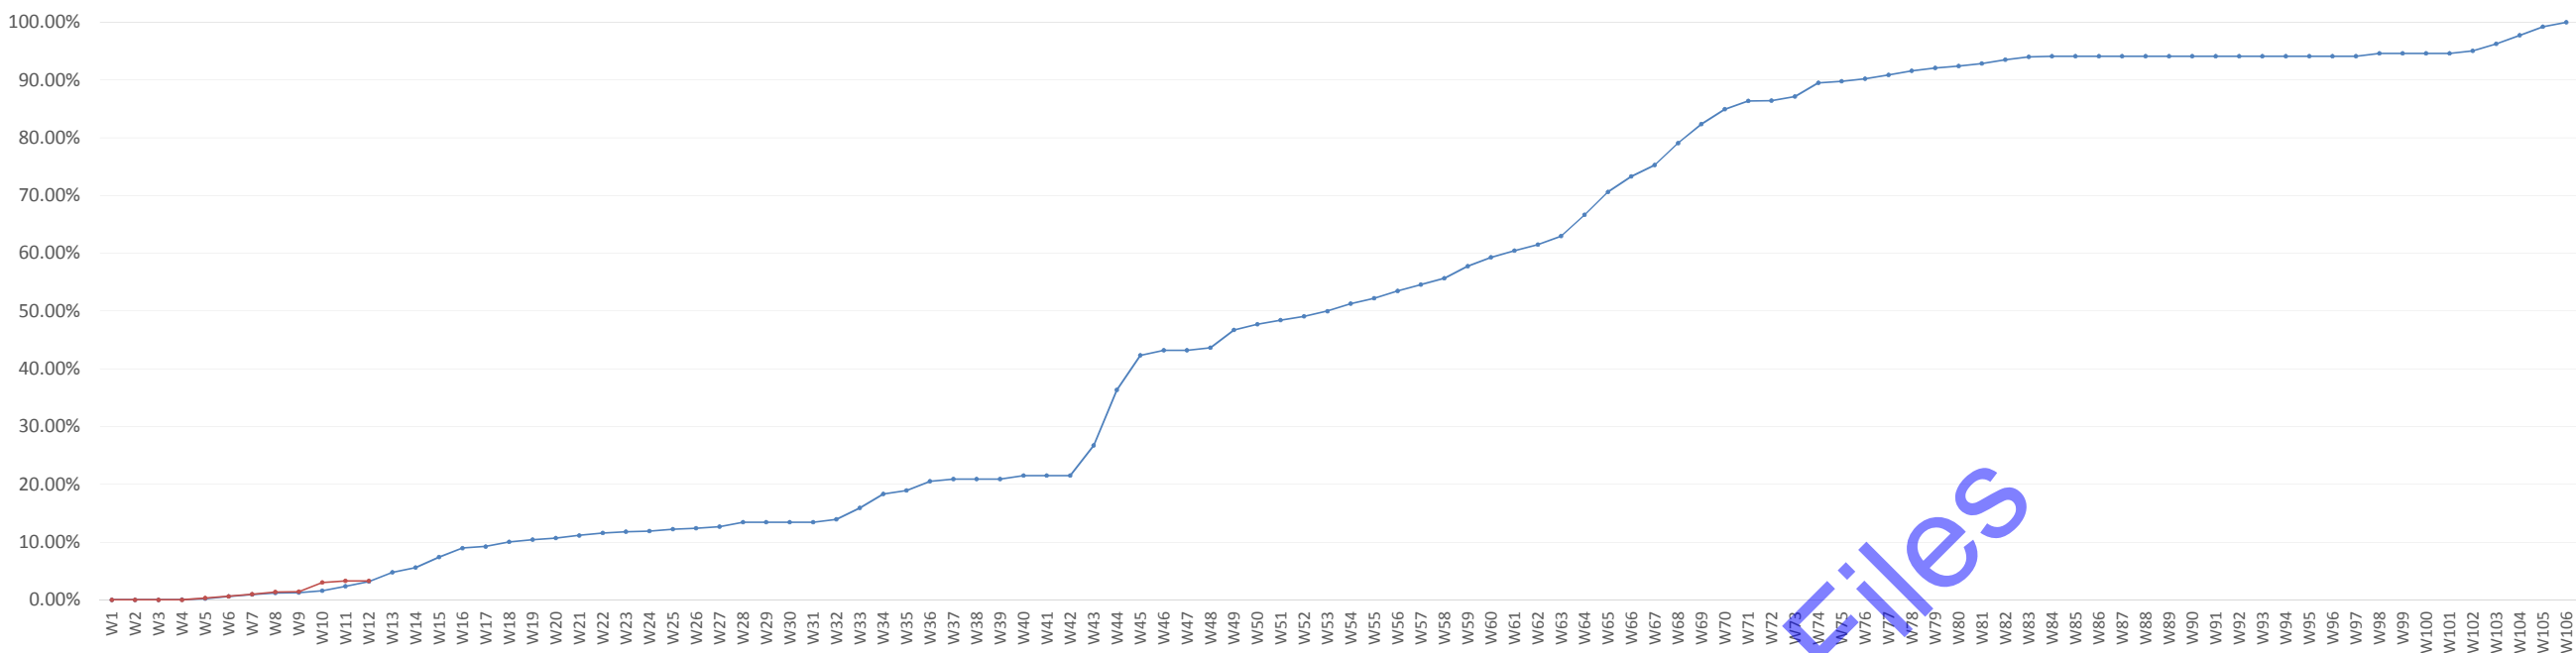
A large grid of graph paper, consisting of a 20x20 square grid of cells. A diagonal watermark in blue text, reading "Archives from Personal Files", is overlaid across the grid from the bottom-left to the top-right.

Progress for Week Ending : 19-Dec-14

[illegible]

[illegible]

[illegible]

[illegible]



EPC Work for Replacement of Valves & Actuators
GASCO PROJECT NO: 5621
Engineering Document Deliverables Register
(SUMMARY)



CUT OFF: 19-Dec-14

Sr. #	Description	Total (Class1, Class2 & Class3)	Drafting Completed			Submitted by AHEC ICR (Class1 & Class2)			COMPANY Review / Approval (Class1 & Class2)			Issued for Construction (Class1, Class2 & Class3)		
			Plan	Forecast	Actual	Plan	Forecast	Actual	Plan	Forecast	Actual	Plan	Forecast	Actual
1	GENERAL	4	4	-	4	4	-	2	2	-	0	0	-	0
2	PROCESS	54	54	-	53	28	-	13	0	-	13	0	-	13
3	MECHANICAL / PIPING	6	3	-	4	3	-	1	1	-	1	0	-	1
4	INSTRUMENTATION	26	11	-	10	9	-	6	0	-	1	0	-	1
5	HSE	6	1	-	1	0	-	0	0	-	0	0	-	0
6	CIVIL & STRUCTURE	18	2	-	7	1	-	6	0	-	1	0	-	1
TOTAL		114	75	0	79	45	0	28	3	0	16	0	0	16

Archives from Personal Files

