

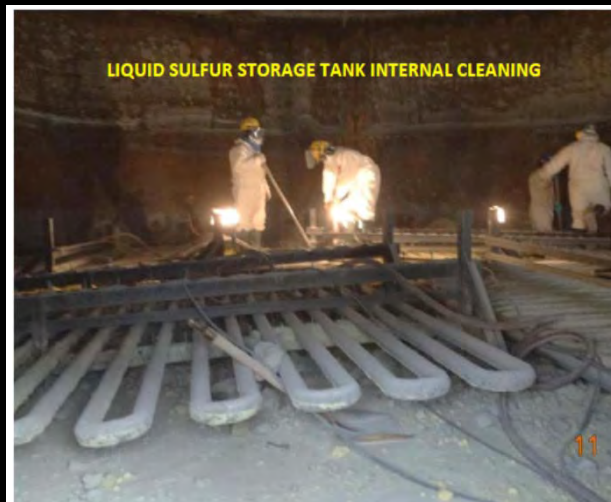


TURN AROUND QCHEM JAN/FEB/MAR 2017



CLIENT: QATAR CHEMICAL COMPANY [QCHEM]

PROJECT: 8505



DESCON PROGRESS MONITORING REPORT



Thursday, February 16, 2017

SAFETY MESSAGE

*Safety rules are
your best tools*

Barricade is the means of warning
the personnel to know about hazards
and to prevent entry
in the particular area



DAILY TURN AROUND PROGRESS REPORT

TURNAROUND WORKS

QCHEM-TA-2017



INDEX

- > HSE STATISTICS
- > OVERALL PROGRESS CURVE
- > MAJOR HIGHLIGHTS / CONCERNS
- > ETHYLENE PROGRESS CURVE
- > SRU PROGRESS CURVE
- > POLYETHYLENE PROGRESS CURVE
- > HEXENET PROGRESS CURVE
- > UTILITY PROGRESS CURVE
- > LOGISTICS PROGRESS CURVE
- > TWR PROGRESS CURVE
- > EQUIPEMT TYPE WISE PROGRESS
- > JOB TYPE WISE PROGRESS
- > MANPOWER AND EQUIPMENT STATUS
- > LT&T STATUS
- > EQUIPMENT&VALVES STATUS



CUT OFF TIME: 06:00 am

REPORT DATE :

15-Feb-17

SHUTDOWN DAY: 17

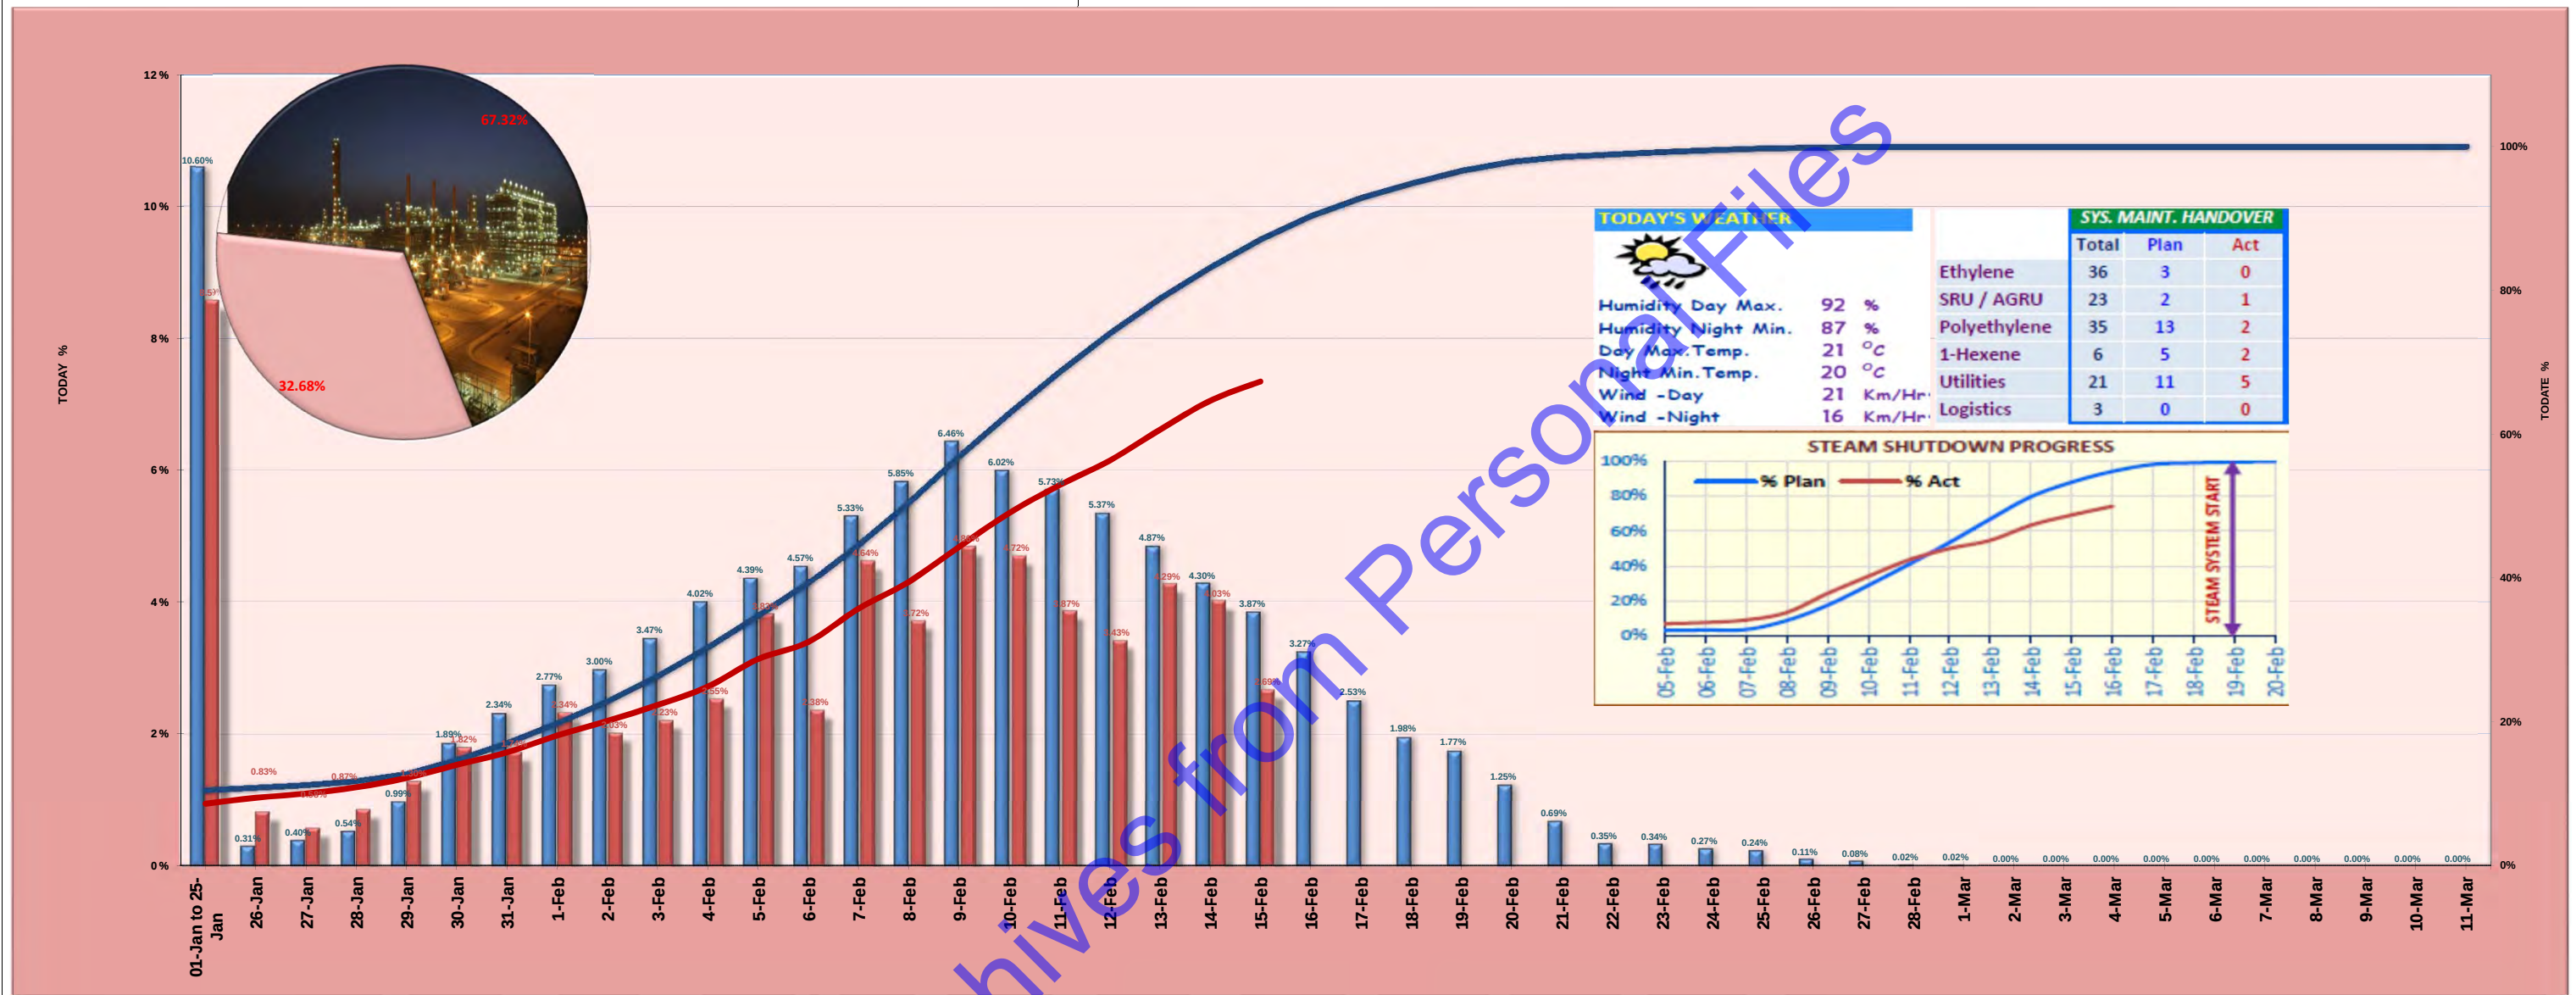
REPORT SUBMISSION :

16-Feb-17

HSE STATISTICS	TODAY	TODATE		TODAY	TODATE
Near Misses: (Reported)	-	3	No. of confine space entries	17	187
No. of First Aid Cases:	-	1	Man-hours Without LTI:	27,744	516,876
No. of LTI's:	-	-	No of Tools Box Talks:	137	1,759

OVERALL PROGRESS

Overall	Planned	Actual	Variance	Overall	Planned	Actual	Variance	
Today	3.87%	2.69%	↓ -1.18%	Todate	87.09%	67.32%	↓ -19.77%	

[illegible]

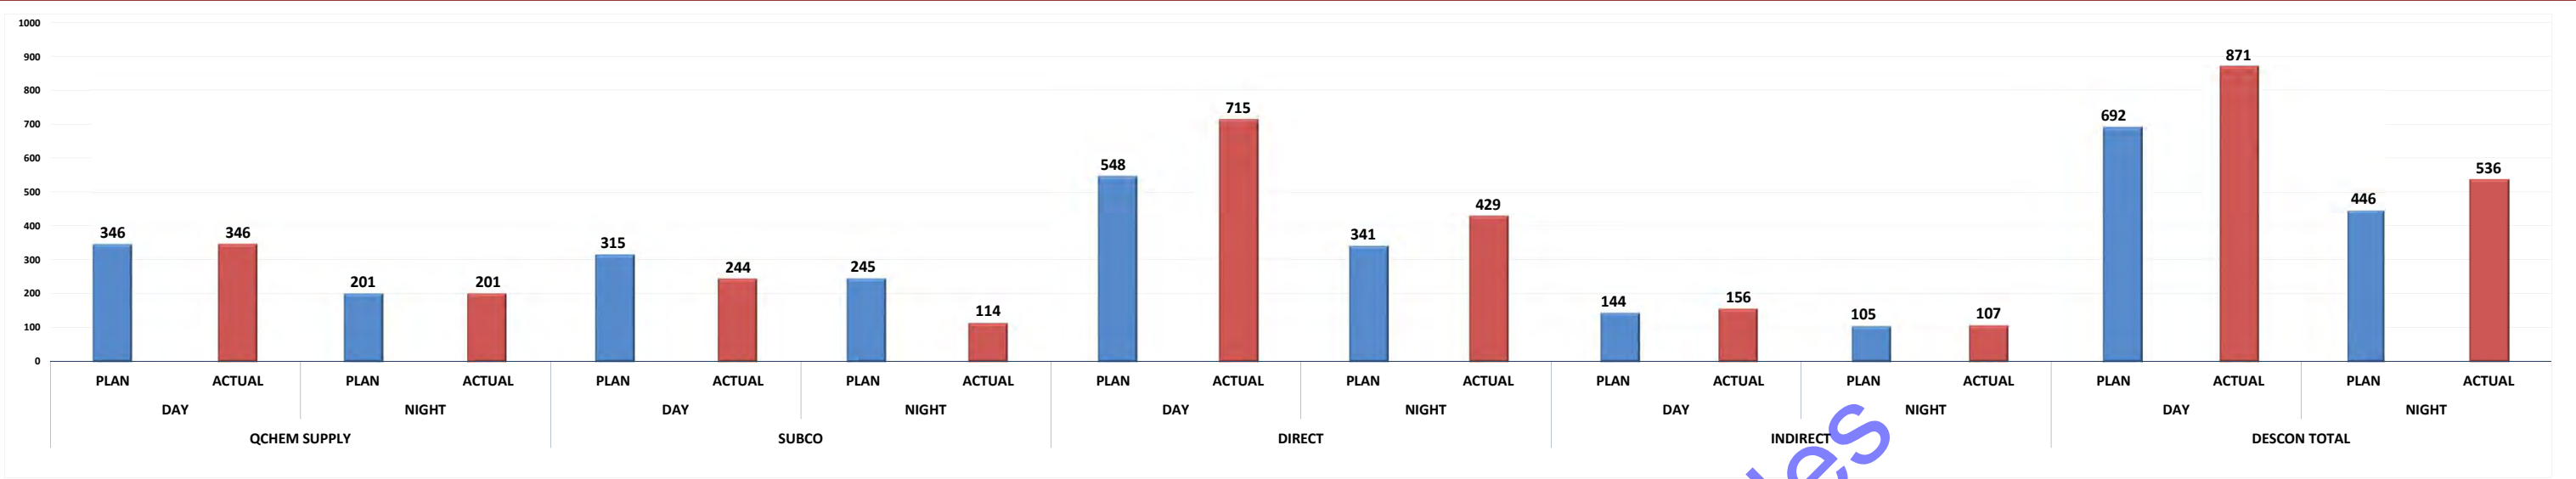


QATAR CHEMICAL COMPANY [QCHEM]
TURN AROUND QATAR CHEMICALS JAN / FEB / MAR 2017
PROGRESS REPORT



Wednesday, February 15, 2017

MAN POWER STATUS



MAJOR HIGHLIGHTS:-

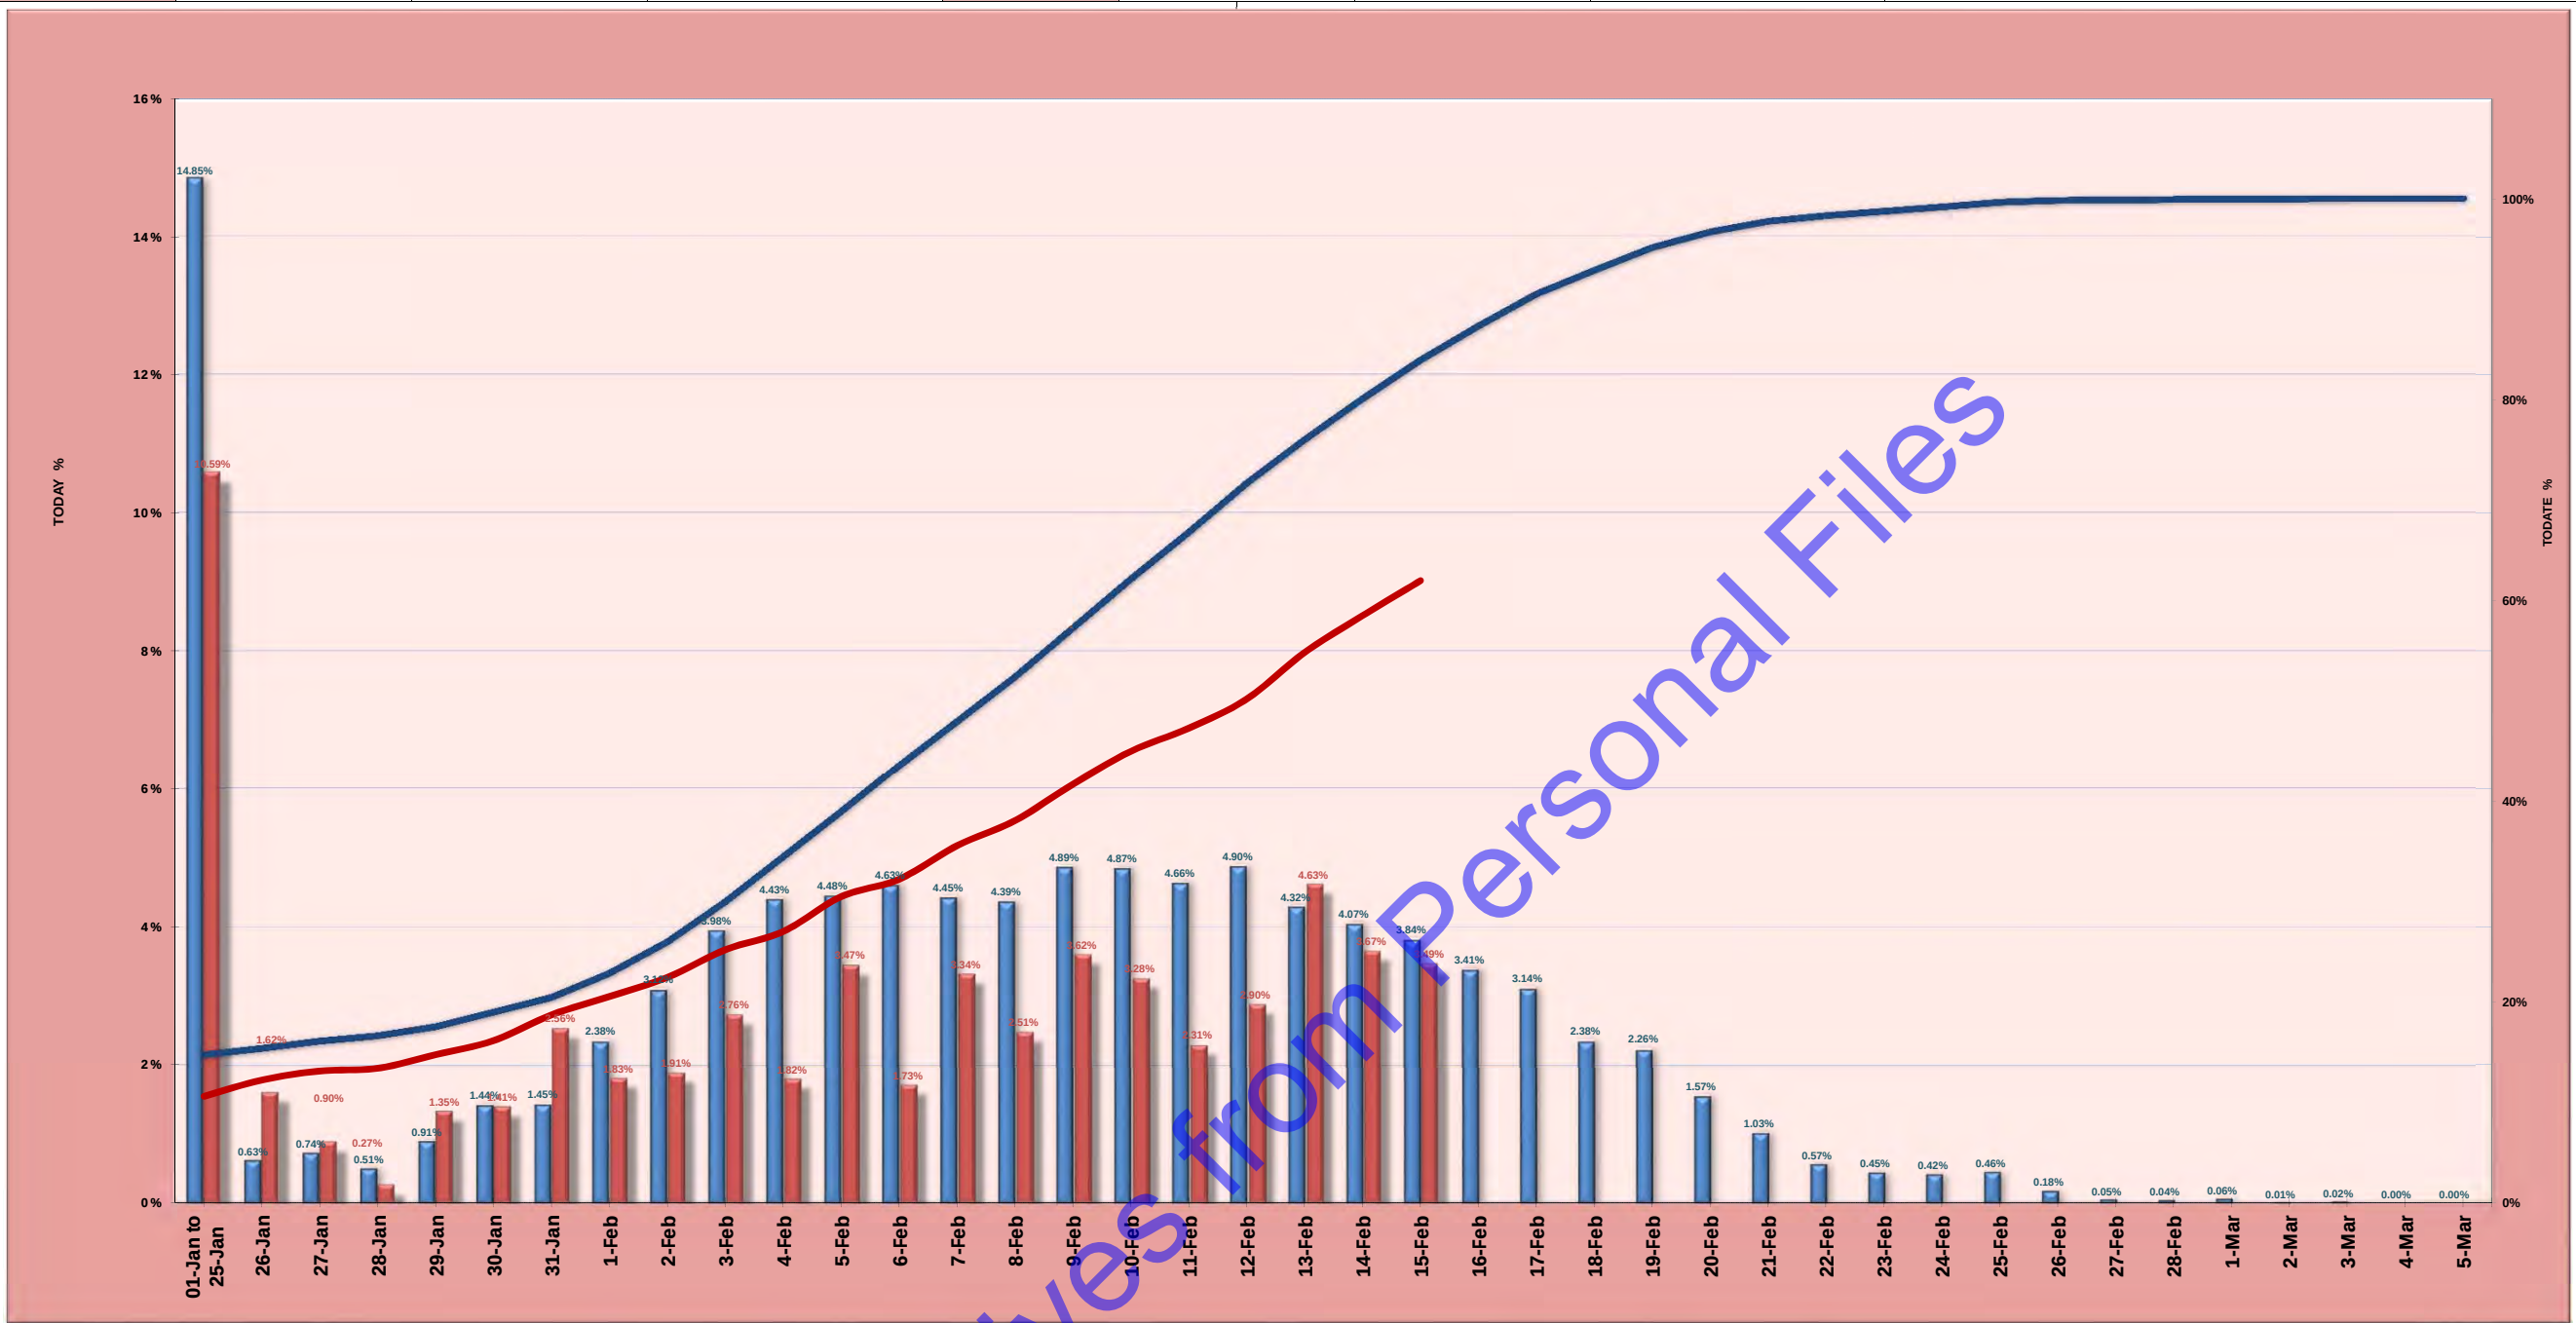
1	ETHYLENE: New Cold box Instillation of Spools & Structure in progress
2	Critical Path: Caustic tower trays installation in progress, 37/50 installed.
3	UTILITY: De-aerator nozzle welding in progress & Sea water intake coating and civil works in progress
4	UTILITY: Spent caustic storage tank chemical cleaning in progress & Steam SD job- De-aerator nozzle welding in progress
5	PE: Gaskets & Bolts Replacement job in progress
6	SRU: SRU incinerator 200 internal refractory repair in progress & CO2 absorber internal trays installation completed
7	SRU:Refractory Repair & Belzona work in incenerator & acid gas separator is in progress.
8	172 Control Valves & 410 Mechanical Valves removed. 569 Valves shifted to workshop. 305 Valves re-installed.
9	Steam Shutdown Jobs: 30 out of 34 cut&weld jobs are completed. 01 under repair, 0993 in progress. 03 out of 05 TWR Jobs completed, TWR-1299 HT in progress, TWR-1341 additional modification work in progress.

CONCERNS:-

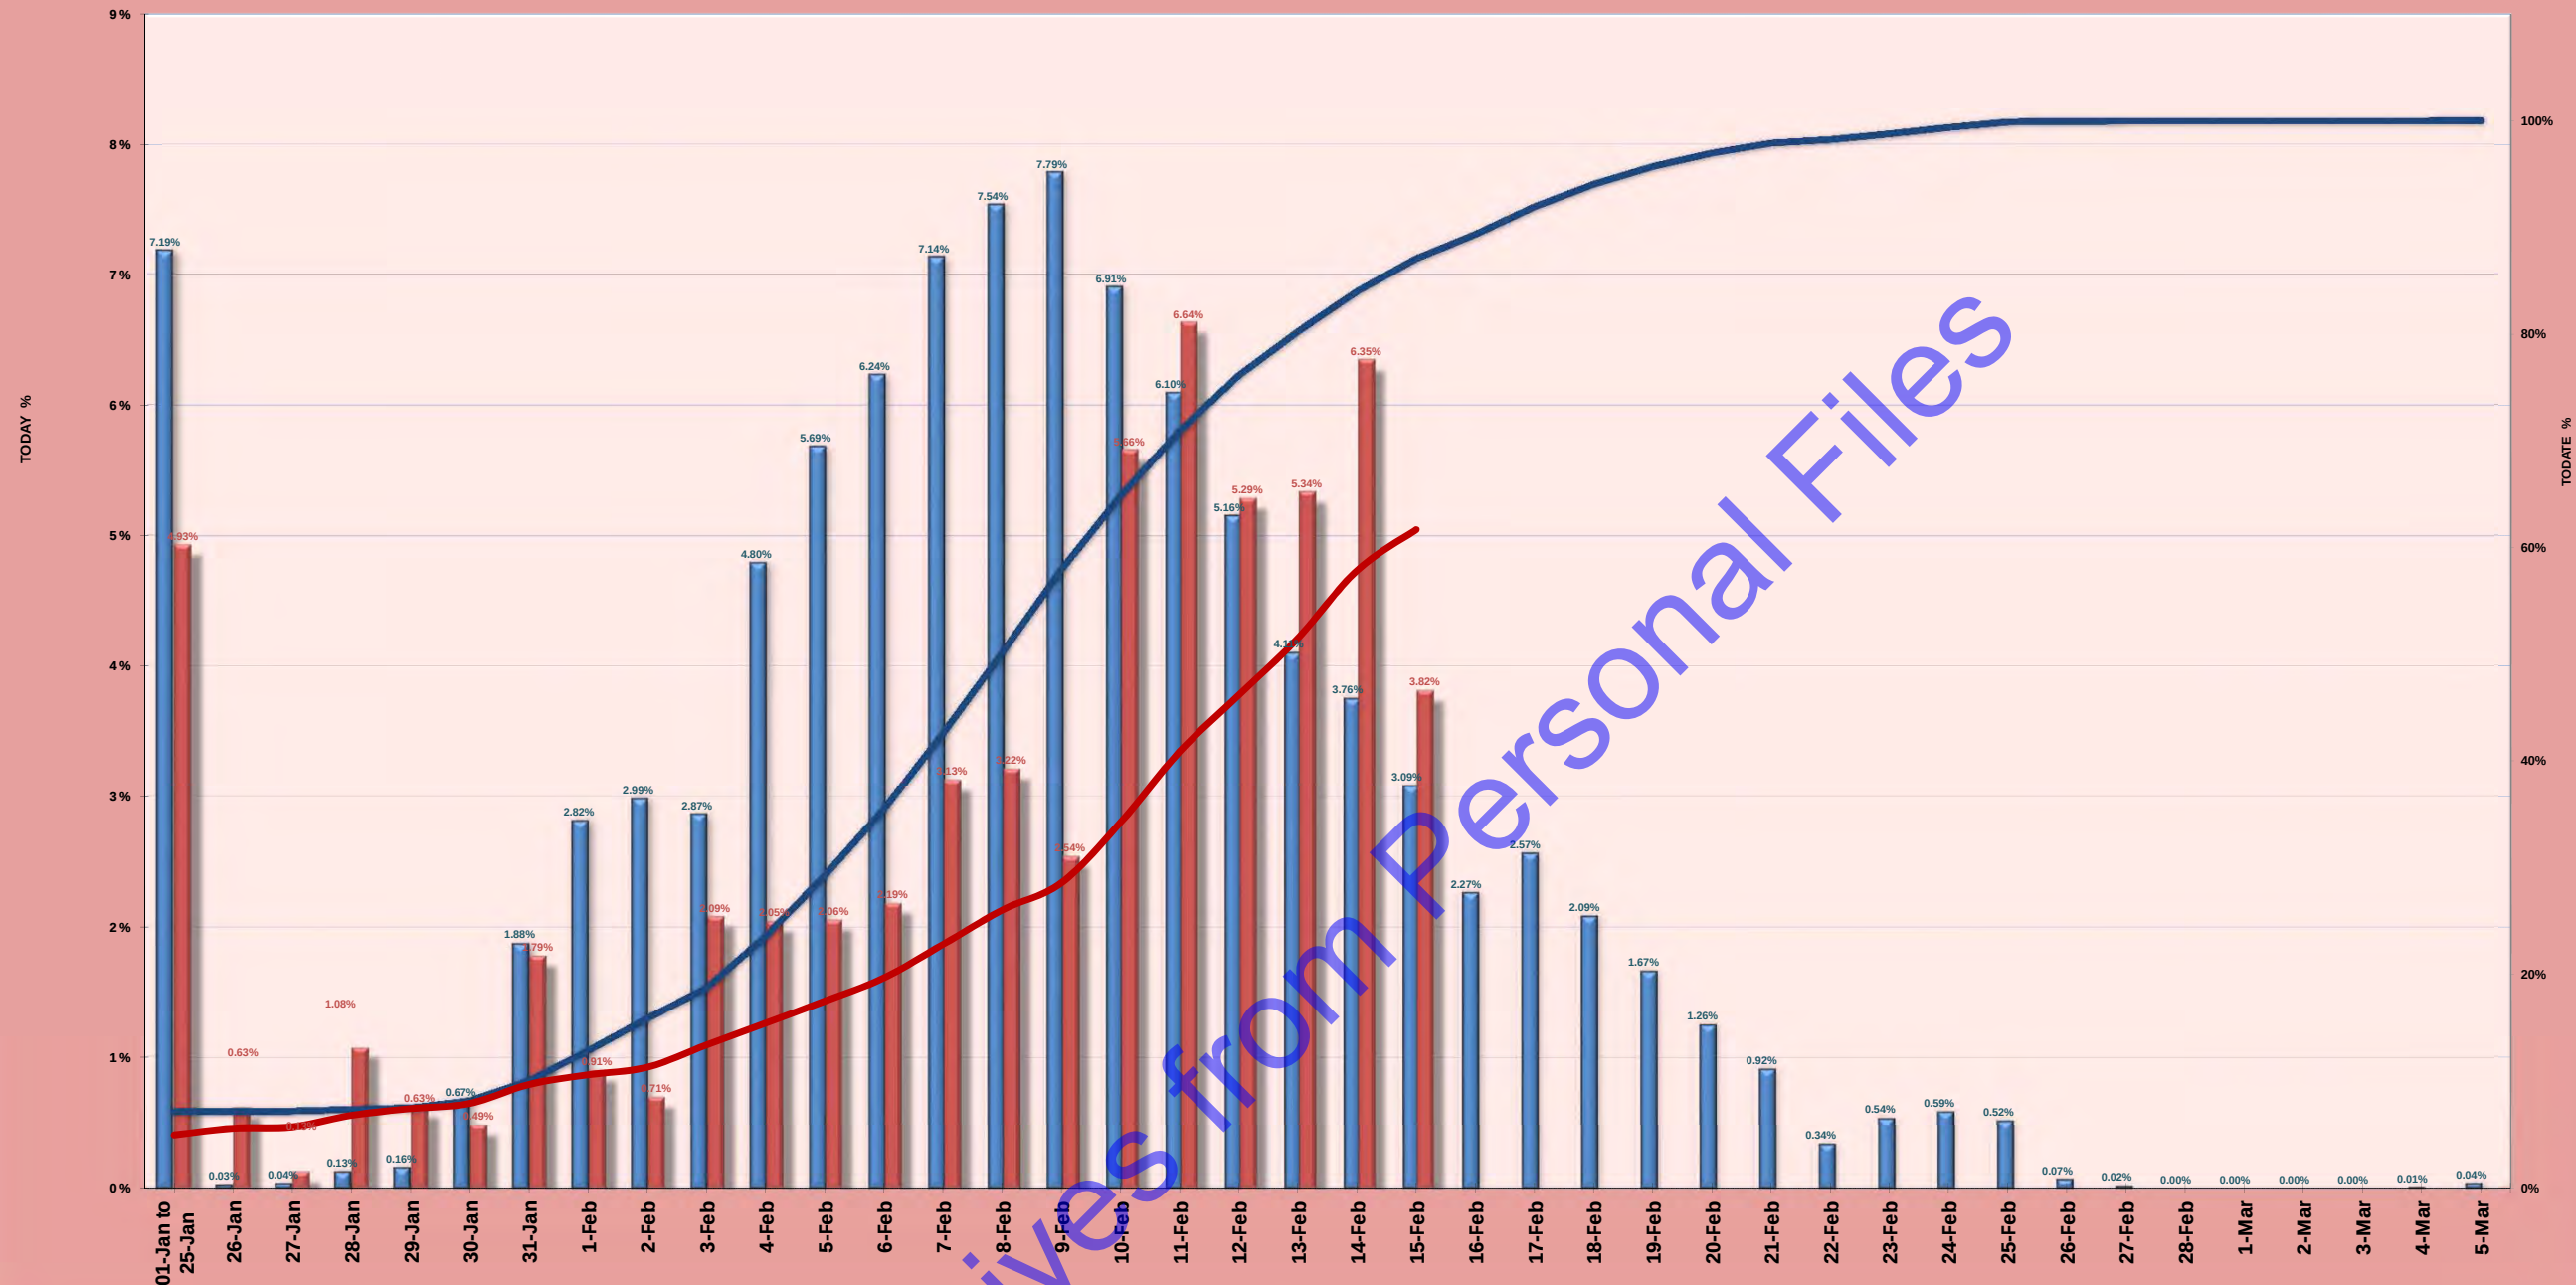
1	SYSTEMS: Polyethylene Flare LT&T not done in Utility.
2	85 Control valves & 132 Mech Valves are in workshop for overhauling.
3	3.23% of total progress delay is due to other contractors activities.
4	552 LT&T Done against plan of 575.
5	Chemical Cleaning is ongoing in spent cstc tank, skimmer replacement to be followed after that.
6	INECO work is ongoing in 07 Equipment of SRU before final inspection & box up.
7	Job stopped in night shift of 14th for 03 Hrs due to Rain & 01 Hr due to emergency & Job stopped for 06 Hrs in Last Night shift due to rain & 04 Emergencies

ETHYLENE PROGRESS CURVE:-

Overall	Planned	Actual	Variance	Overall	Planned	Actual	Variance	
Today	3.84%	3.49%	↓ -0.35%	Todate	83.94%	61.99%	↓ -21.95%	

[illegible]

Overall	Planned	Actual	Variance	Overall	Planned	Actual	Variance	
Today	3.09%	3.82%	↑ 0.73%	Today	87.09%	61.67%	↓ -25.42%	

[illegible]

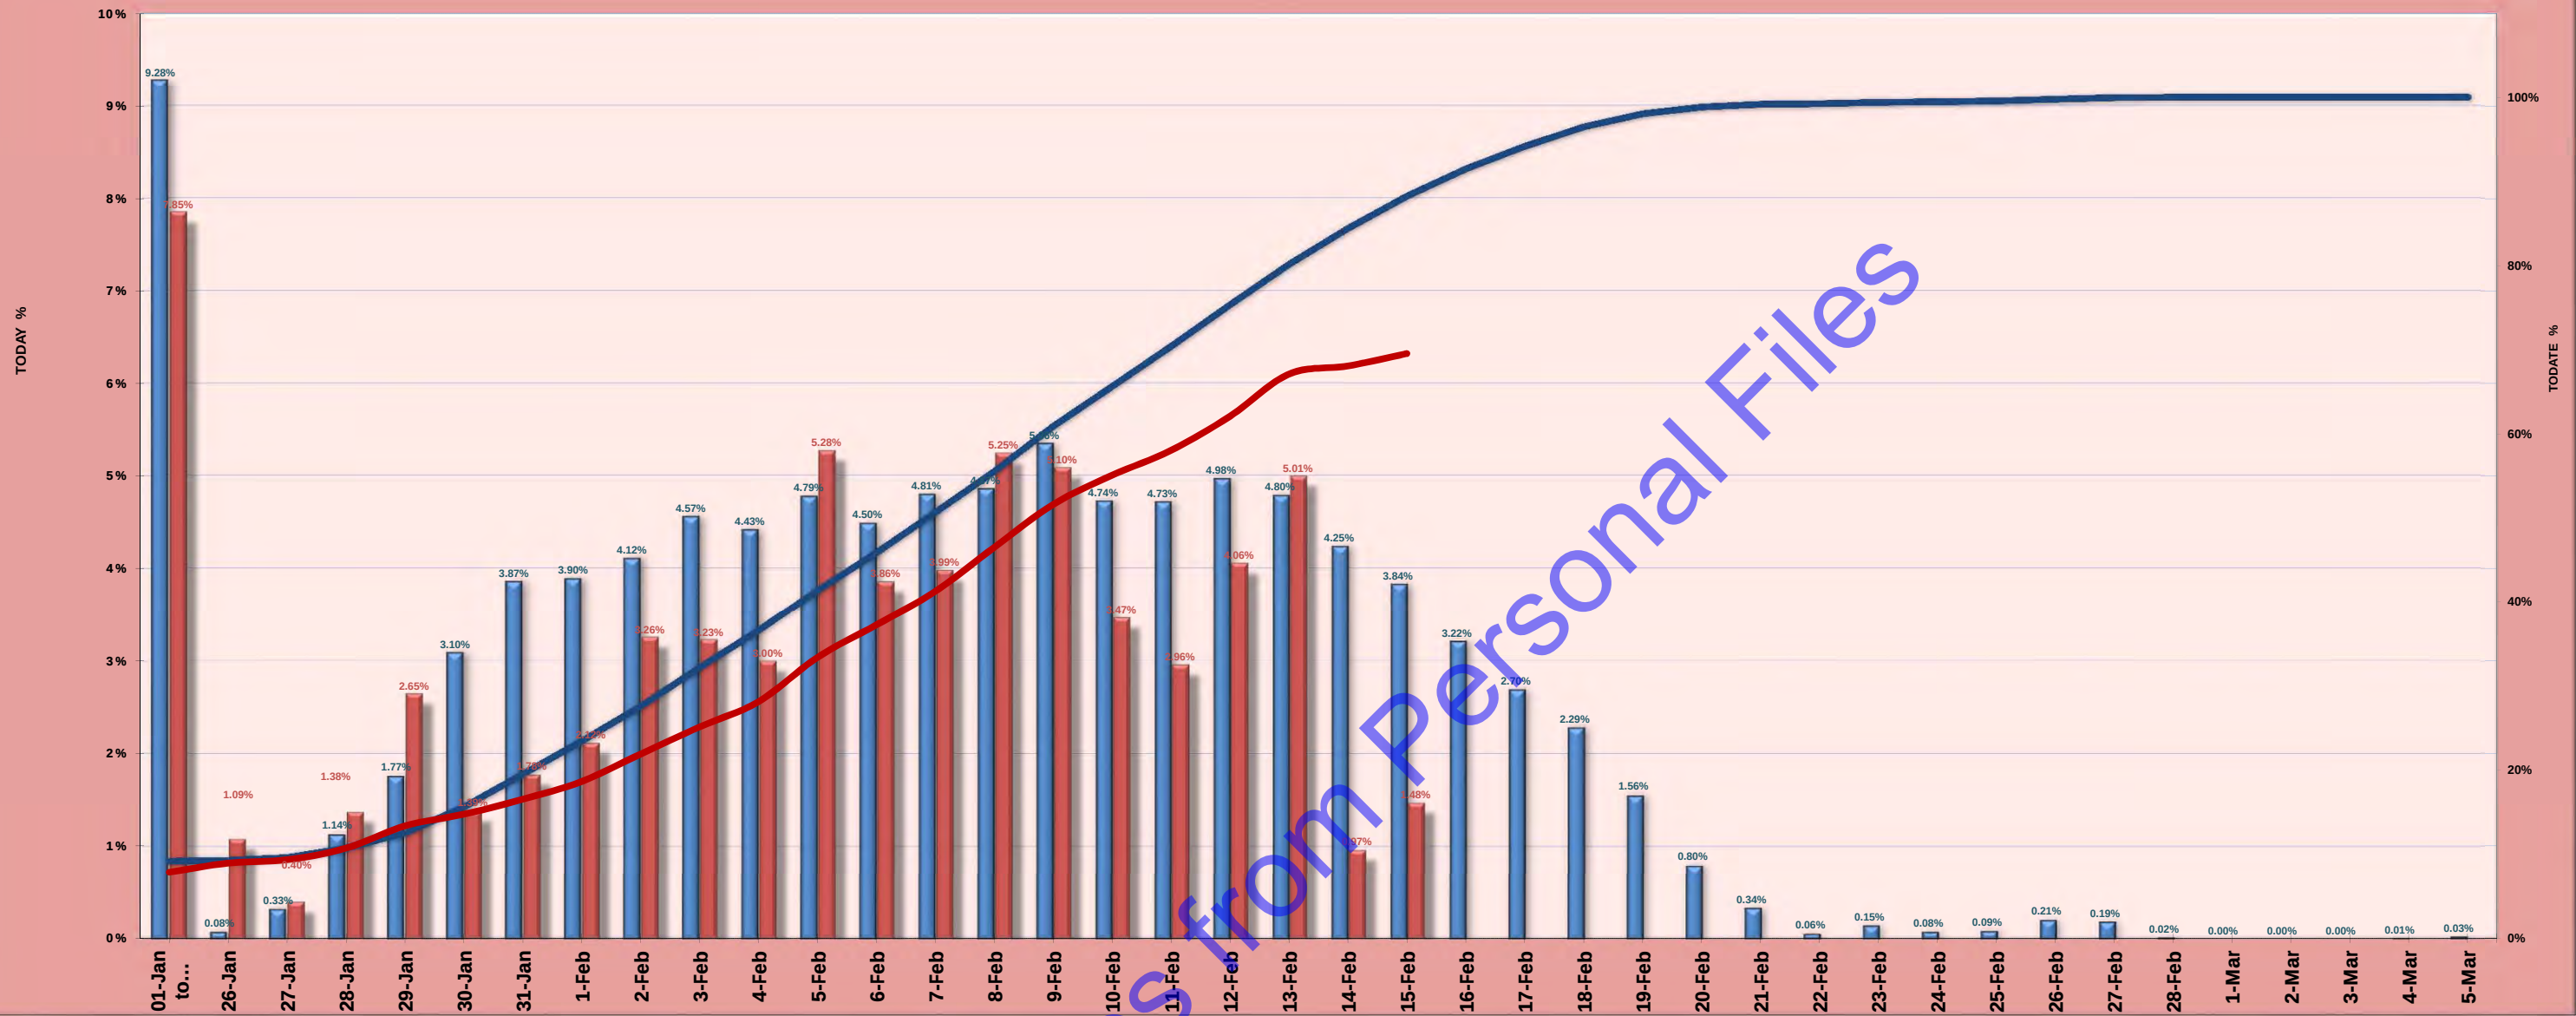


UNIT-POLYETHYLENE



POLYETHYLENE PROGRESS CURVE:-

Overall	Planned	Actual	Variance	Overall	Planned	Actual	Variance	
Today	3.84%	1.48%	↓ -2.36%	Todate	88.26%	69.56%	↓ -18.70%	

[illegible]

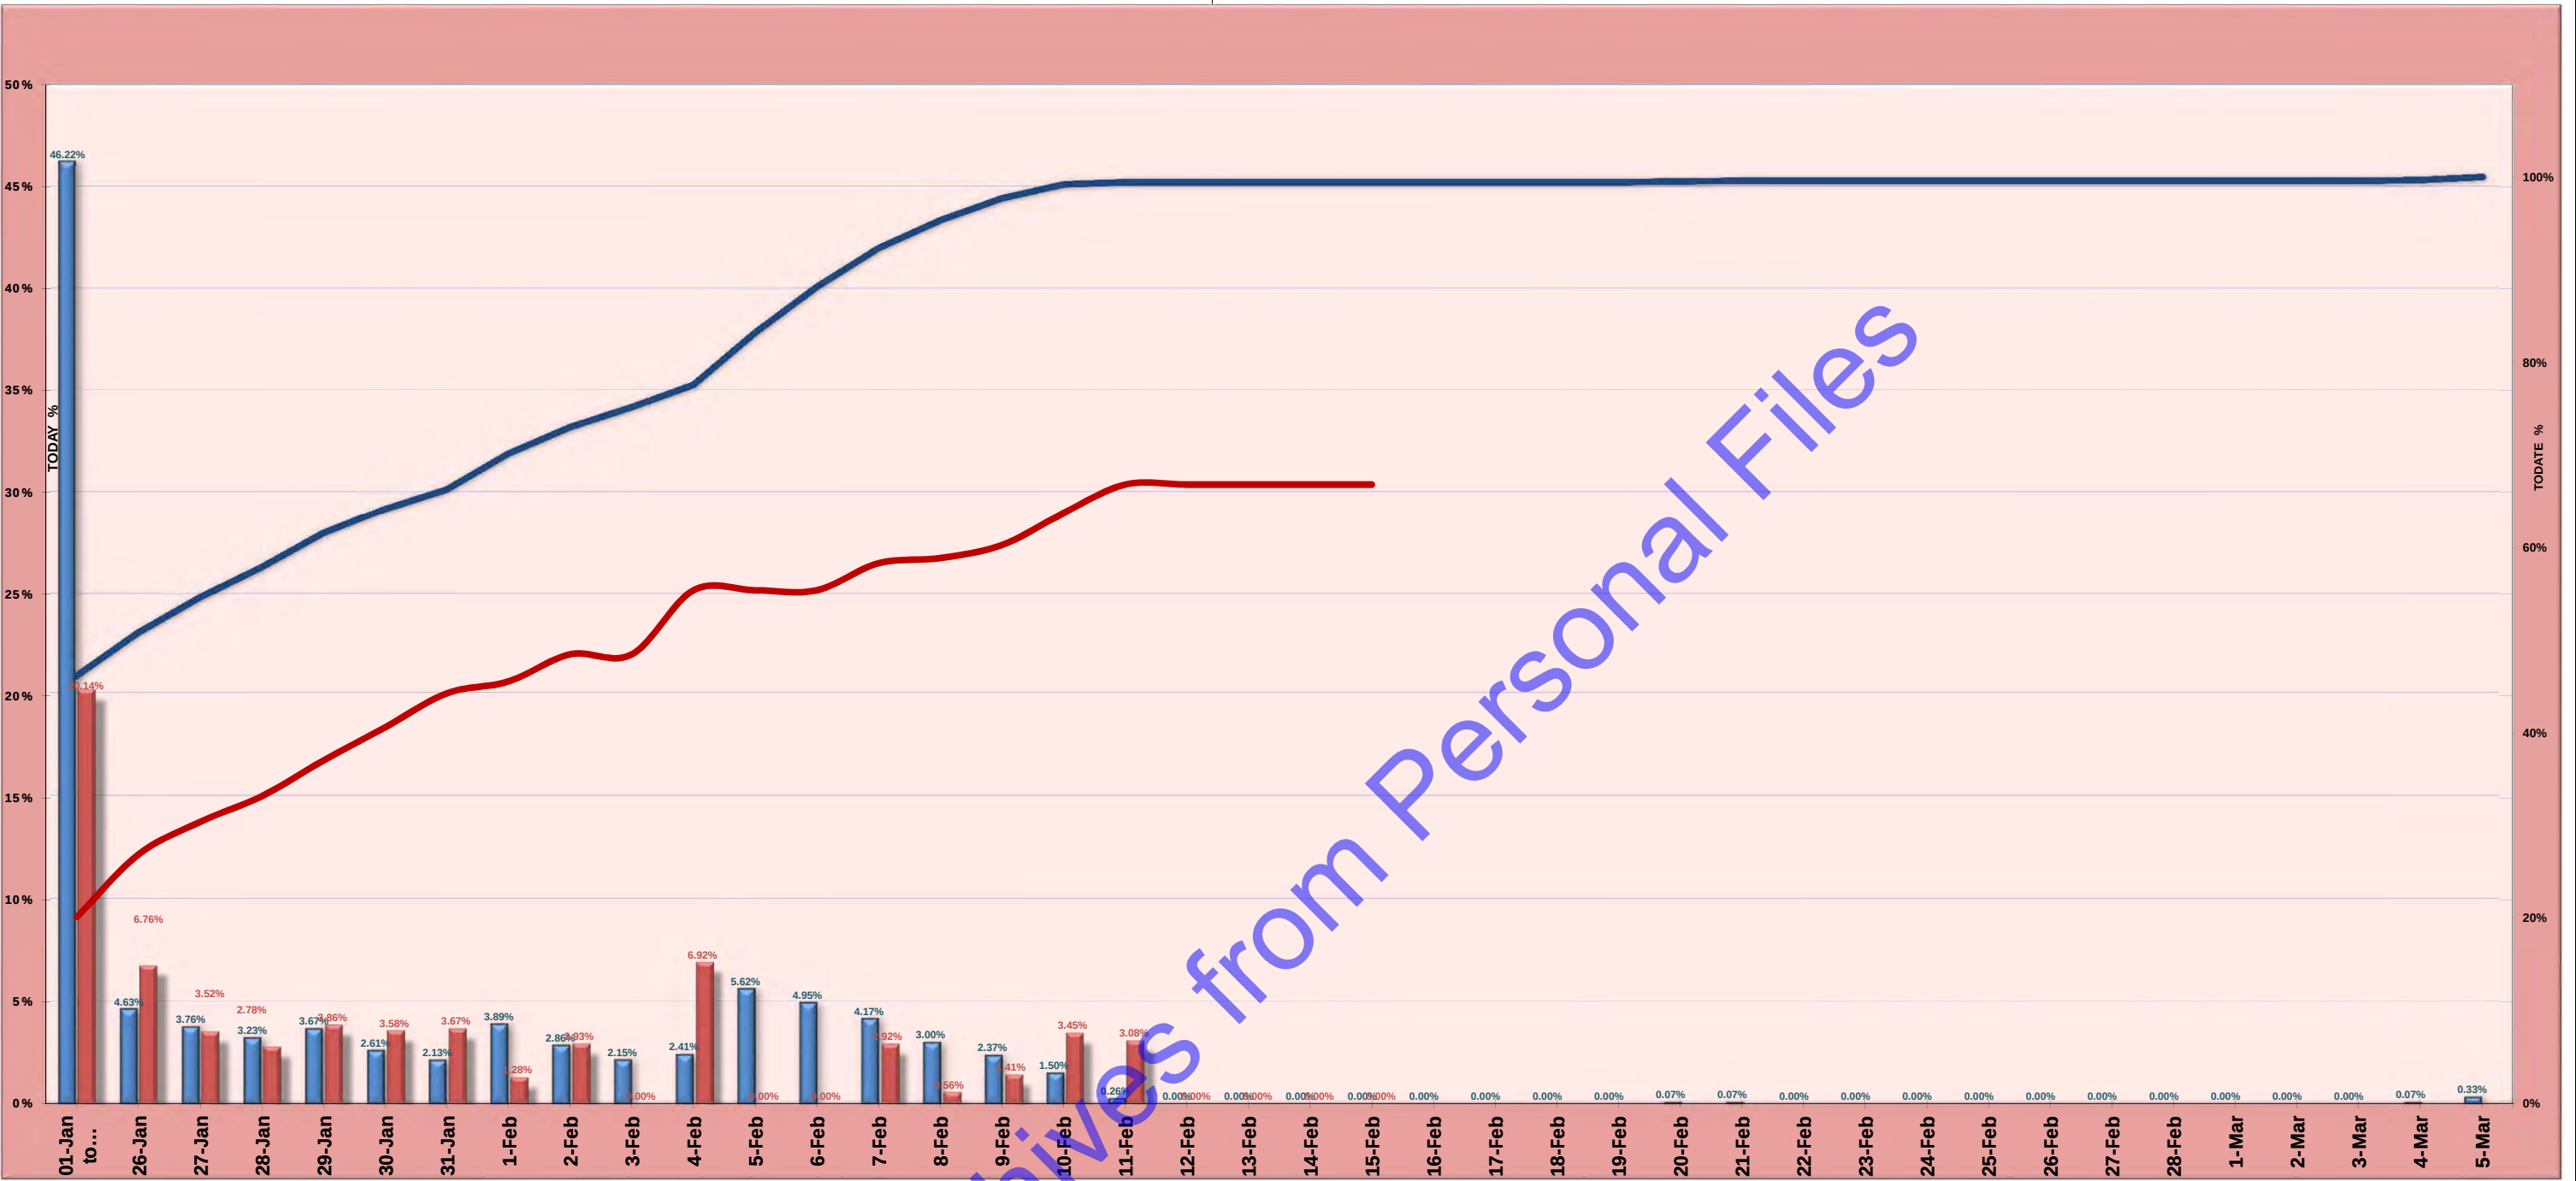


UNIT-HEXENE



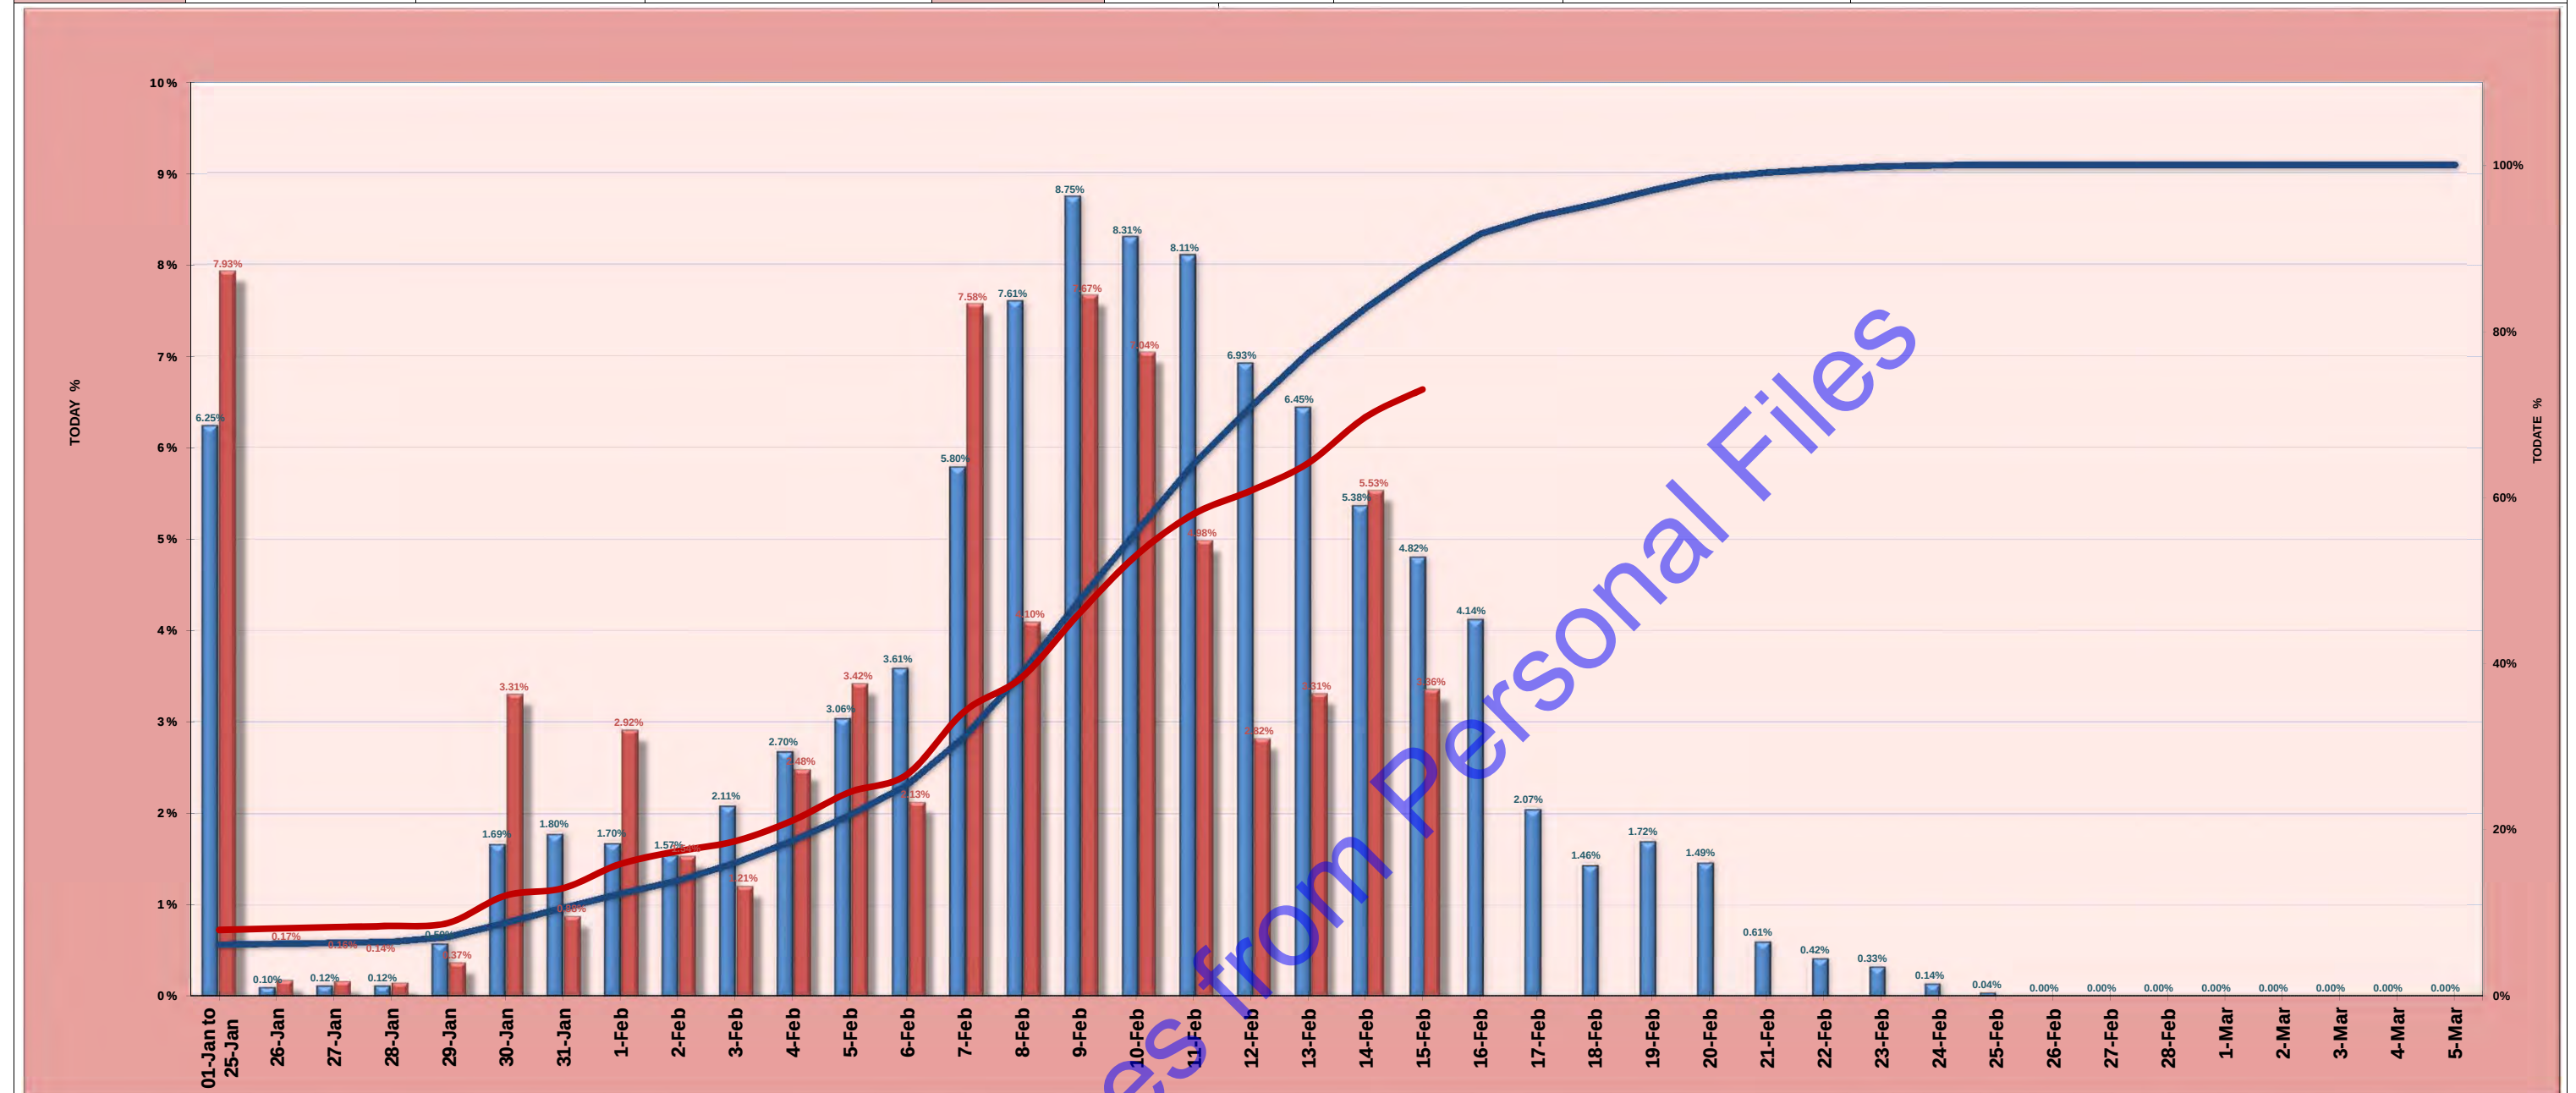
HEXENE PROGRESS CURVE:-

Overall	Planned	Actual	Variance	Overall	Planned	Actual	Variance
Today	0.00%	0.00%	➡ 0.00%	TODATE	99.44%	66.83%	⬇ -32.61%

[illegible]

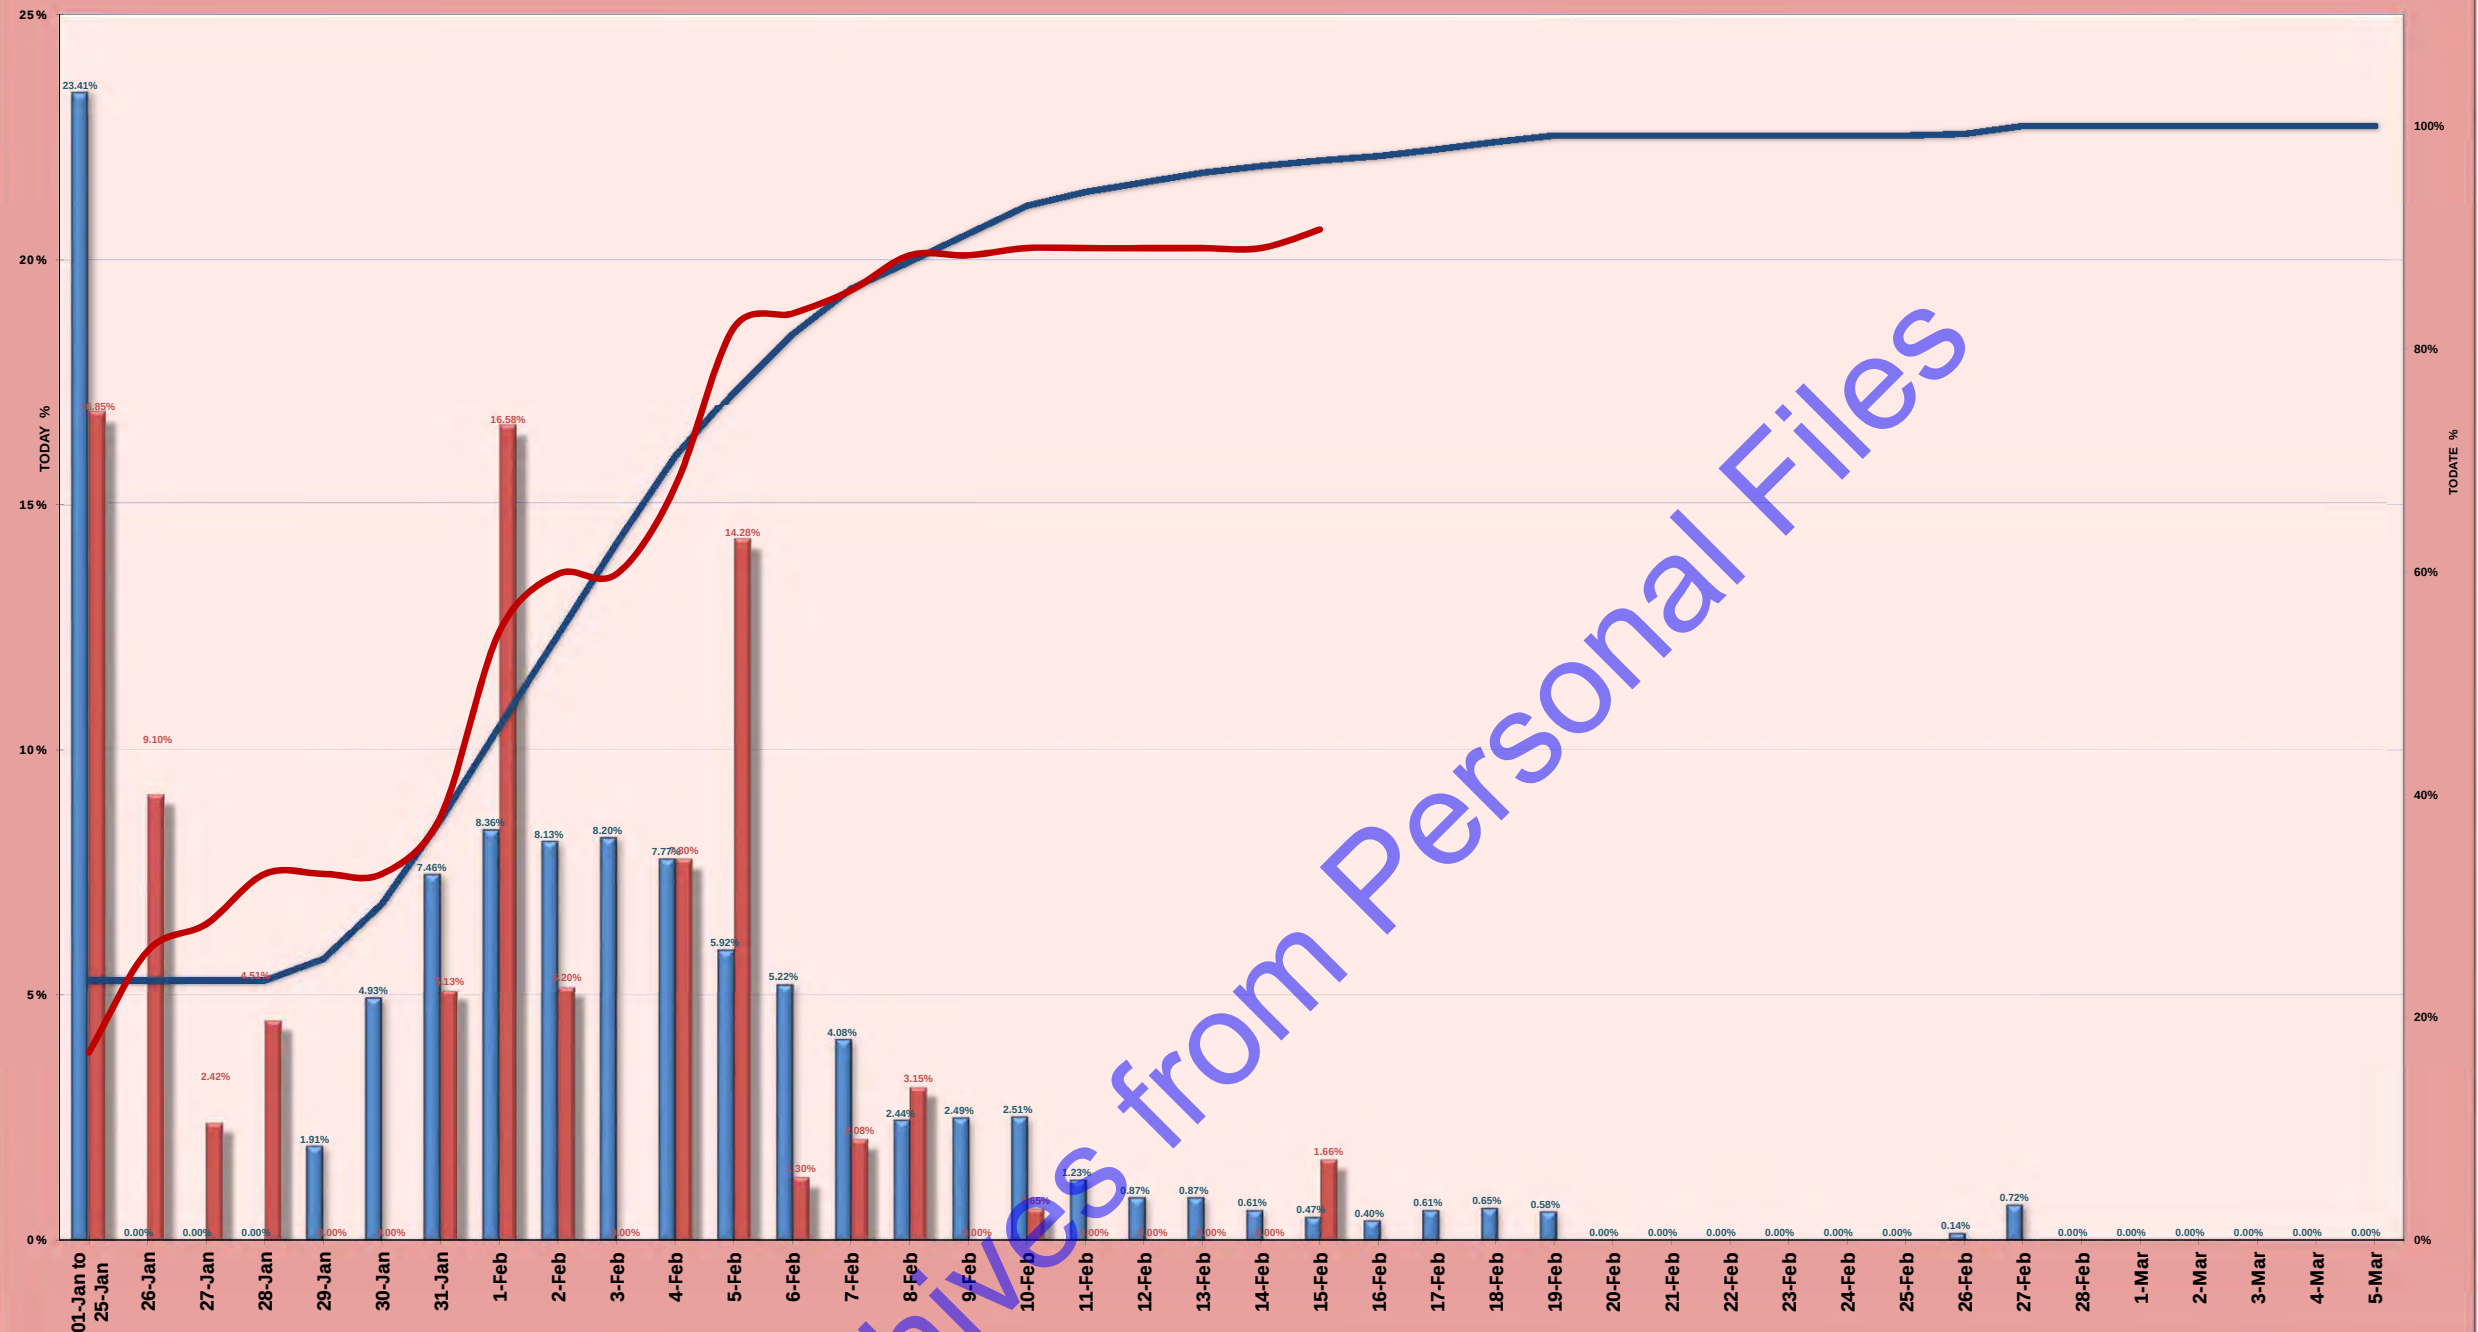
UTILITY PROGRESS CURVE:-

Overall	Planned	Actual	Variance	Overall	Planned	Actual	Variance	
Today	4.82%	3.36%	↓ -1.46%	Todate	87.57%	73.04%	↓ -14.53%	

[illegible]

LOGISTICS PROGRESS CURVE:-

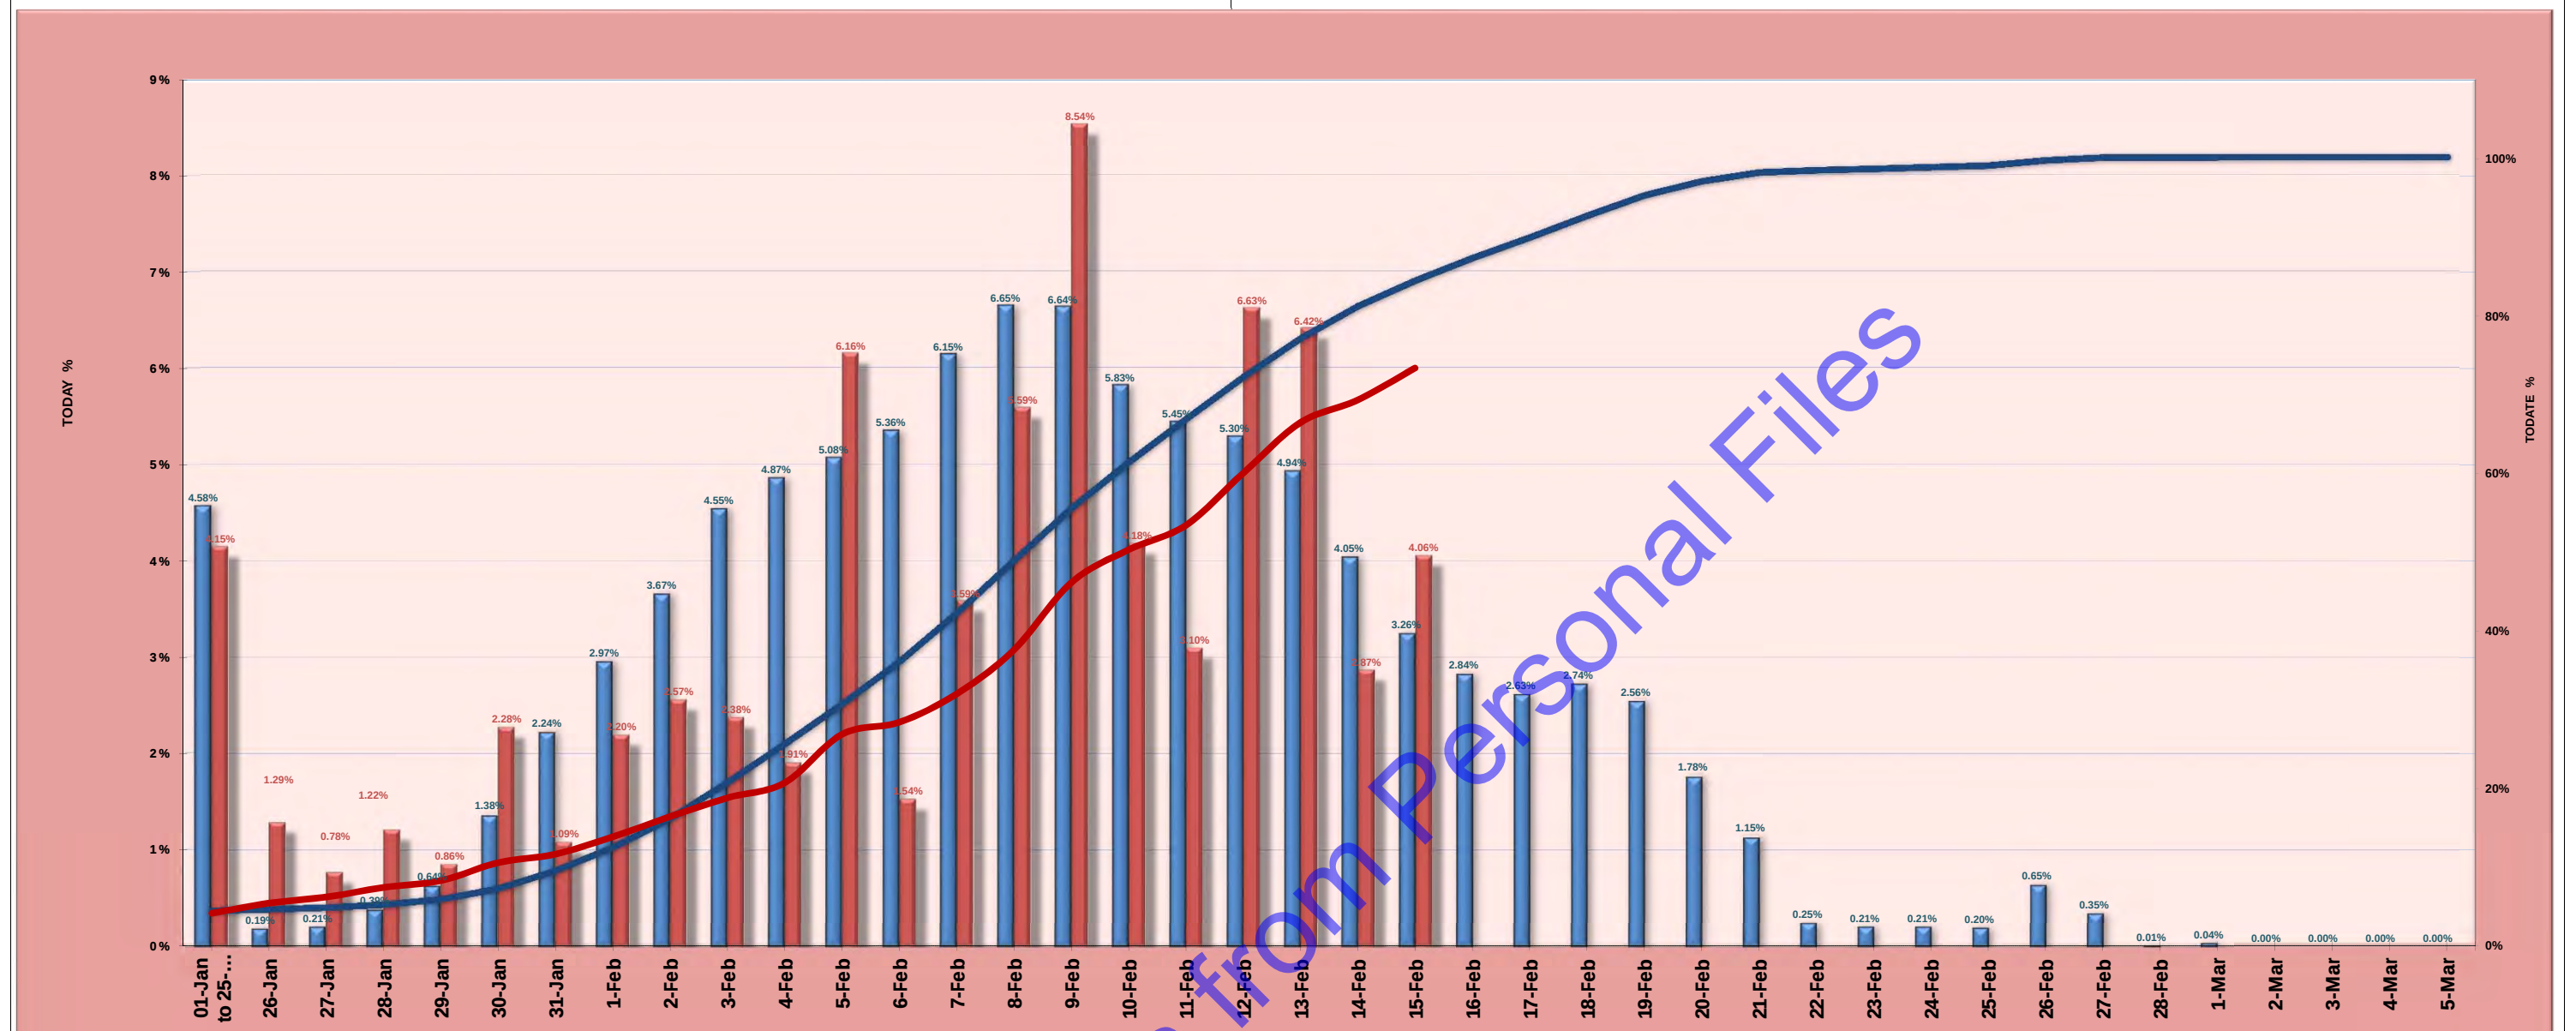
Overall	Planned	Actual	Variance	Overall	Planned	Actual	Variance		
Today	0.47%	1.66%	↑ 1.19%	Today	96.89%	90.72%	↓ -6.17%		

[illegible]

[illegible]

CONTROL VALVES PROGRESS CURVE:-

Overall	Planned	Actual	Variance	Overall	Planned	Actual	Variance	
Today	3.26%	4.06%	↑ 0.80%	Todate	84.40%	73.40%	↓ -11.00%	

[illegible]

MECHANICAL VALVES PROGRESS CURVE:-

Overall	Planned	Actual	Variance	Overall	Planned	Actual	Variance	
Today	3.95%	5.58%	1.63%	ToDate	92.71%	91.36%	-1.35%	

[illegible]

EQUIPMENT PROGRESS CURVE:-

Overall	Planned	Actual	Variance	Overall	Planned	Actual	Variance	
Today	4.04%	2.75%	↓ -1.29%	Todate	83.74%	71.05%	↓ -12.69%	

[illegible]

The chart displays the progress of file processing. The left Y-axis, labeled 'TODAY %', ranges from 0% to 18% in 2% increments. The right Y-axis, labeled 'TODATE %', ranges from 0% to 100% in 20% increments. The X-axis shows dates from 01-Jan to 05-Mar. Blue bars represent the percentage of files processed today, and a red line represents the cumulative percentage processed to date. A large blue watermark 'Files from Personal Files' is overlaid diagonally across the chart.

Date	Today % (Blue Bar)	To Date % (Red Line)
01-Jan to 25-Jan	16.57%	16.19%
26-Jan	0.27%	1.69%
27-Jan	0.48%	0.37%
28-Jan	0.62%	0.16%
29-Jan	1.40%	0.05%
30-Jan	2.12%	0.07%
31-Jan	2.45%	2.32%
1-Feb	3.22%	2.83%
2-Feb	3.25%	0.51%
3-Feb	3.24%	2.96%
4-Feb	3.68%	2.95%
5-Feb	3.80%	1.99%
6-Feb	3.51%	0.51%
7-Feb	3.93%	2.20%
8-Feb	5.09%	2.35%
9-Feb	5.68%	2.69%
10-Feb	4.87%	4.19%
11-Feb	5.22%	3.81%
12-Feb	5.60%	3.00%
13-Feb	4.51%	5.04%
14-Feb	4.35%	4.07%
15-Feb	4.10%	4.69%
16-Feb	3.88%	
17-Feb	2.95%	
18-Feb	1.62%	
19-Feb	1.29%	
20-Feb	0.92%	
21-Feb	0.39%	
22-Feb	0.22%	
23-Feb	0.35%	
24-Feb	0.28%	
25-Feb	0.11%	
26-Feb	0.00%	
27-Feb	0.04%	
28-Feb	0.00%	
1-Mar	0.00%	
2-Mar	0.00%	
3-Mar	0.00%	
4-Mar	0.00%	
5-Mar	0.00%	

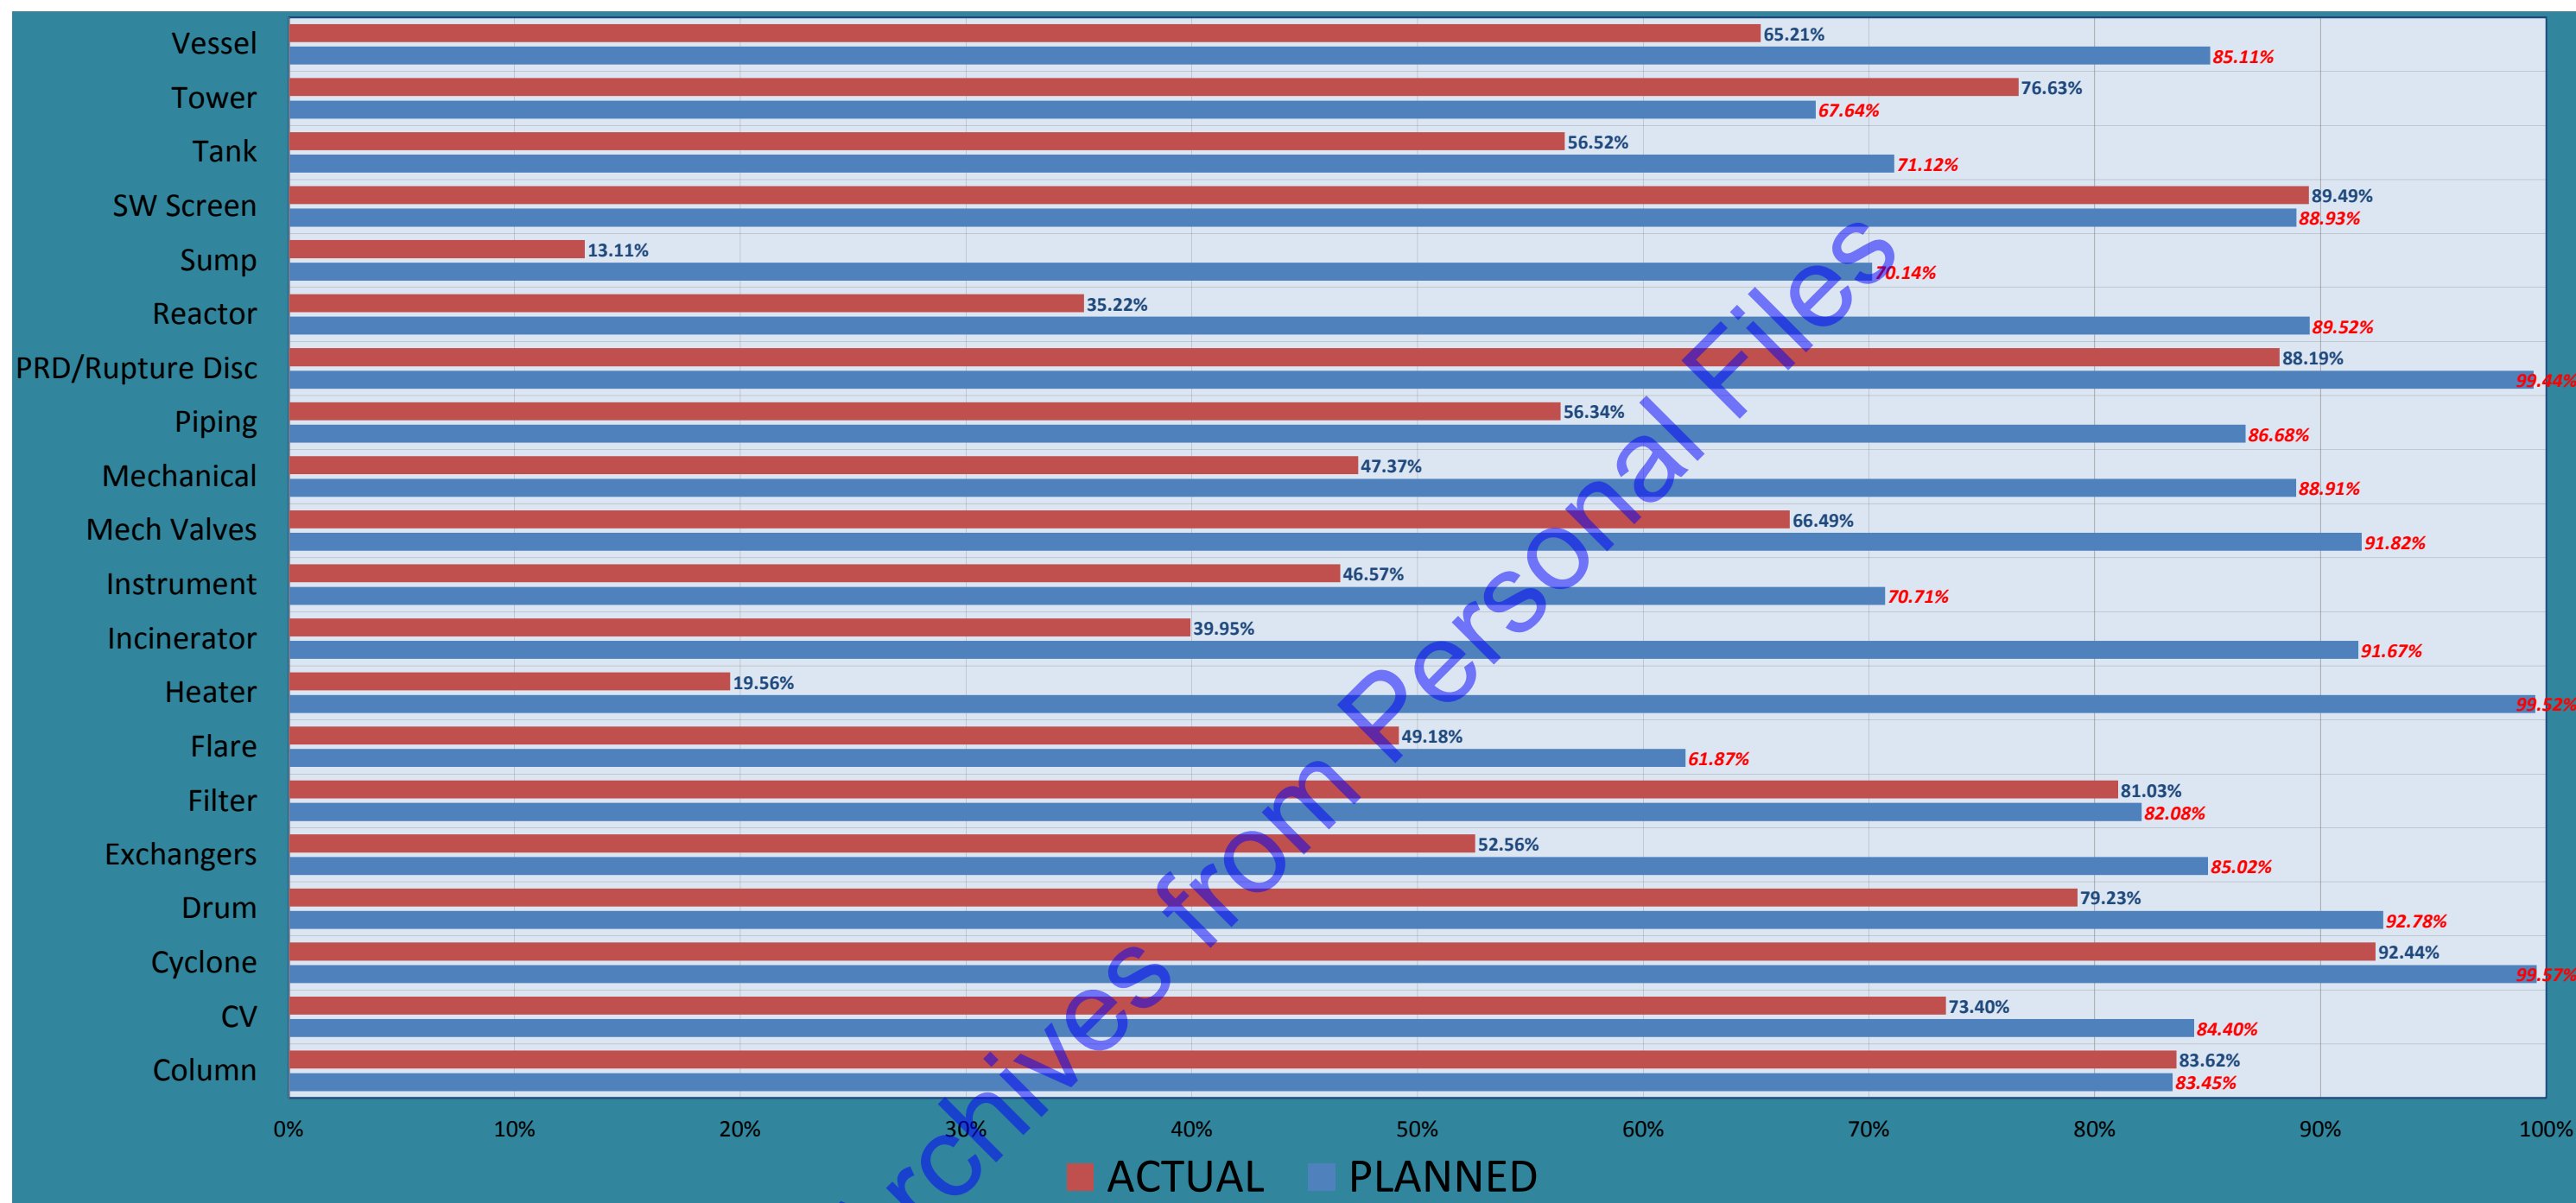
[illegible]



TURN AROUND QATAR CHEMICALS [QCHEM] JAN/ FEB / MAR 2017



EQUIPMENT TYPE WISE PROGRESS





TA JOB TAG WISE PROGRESS



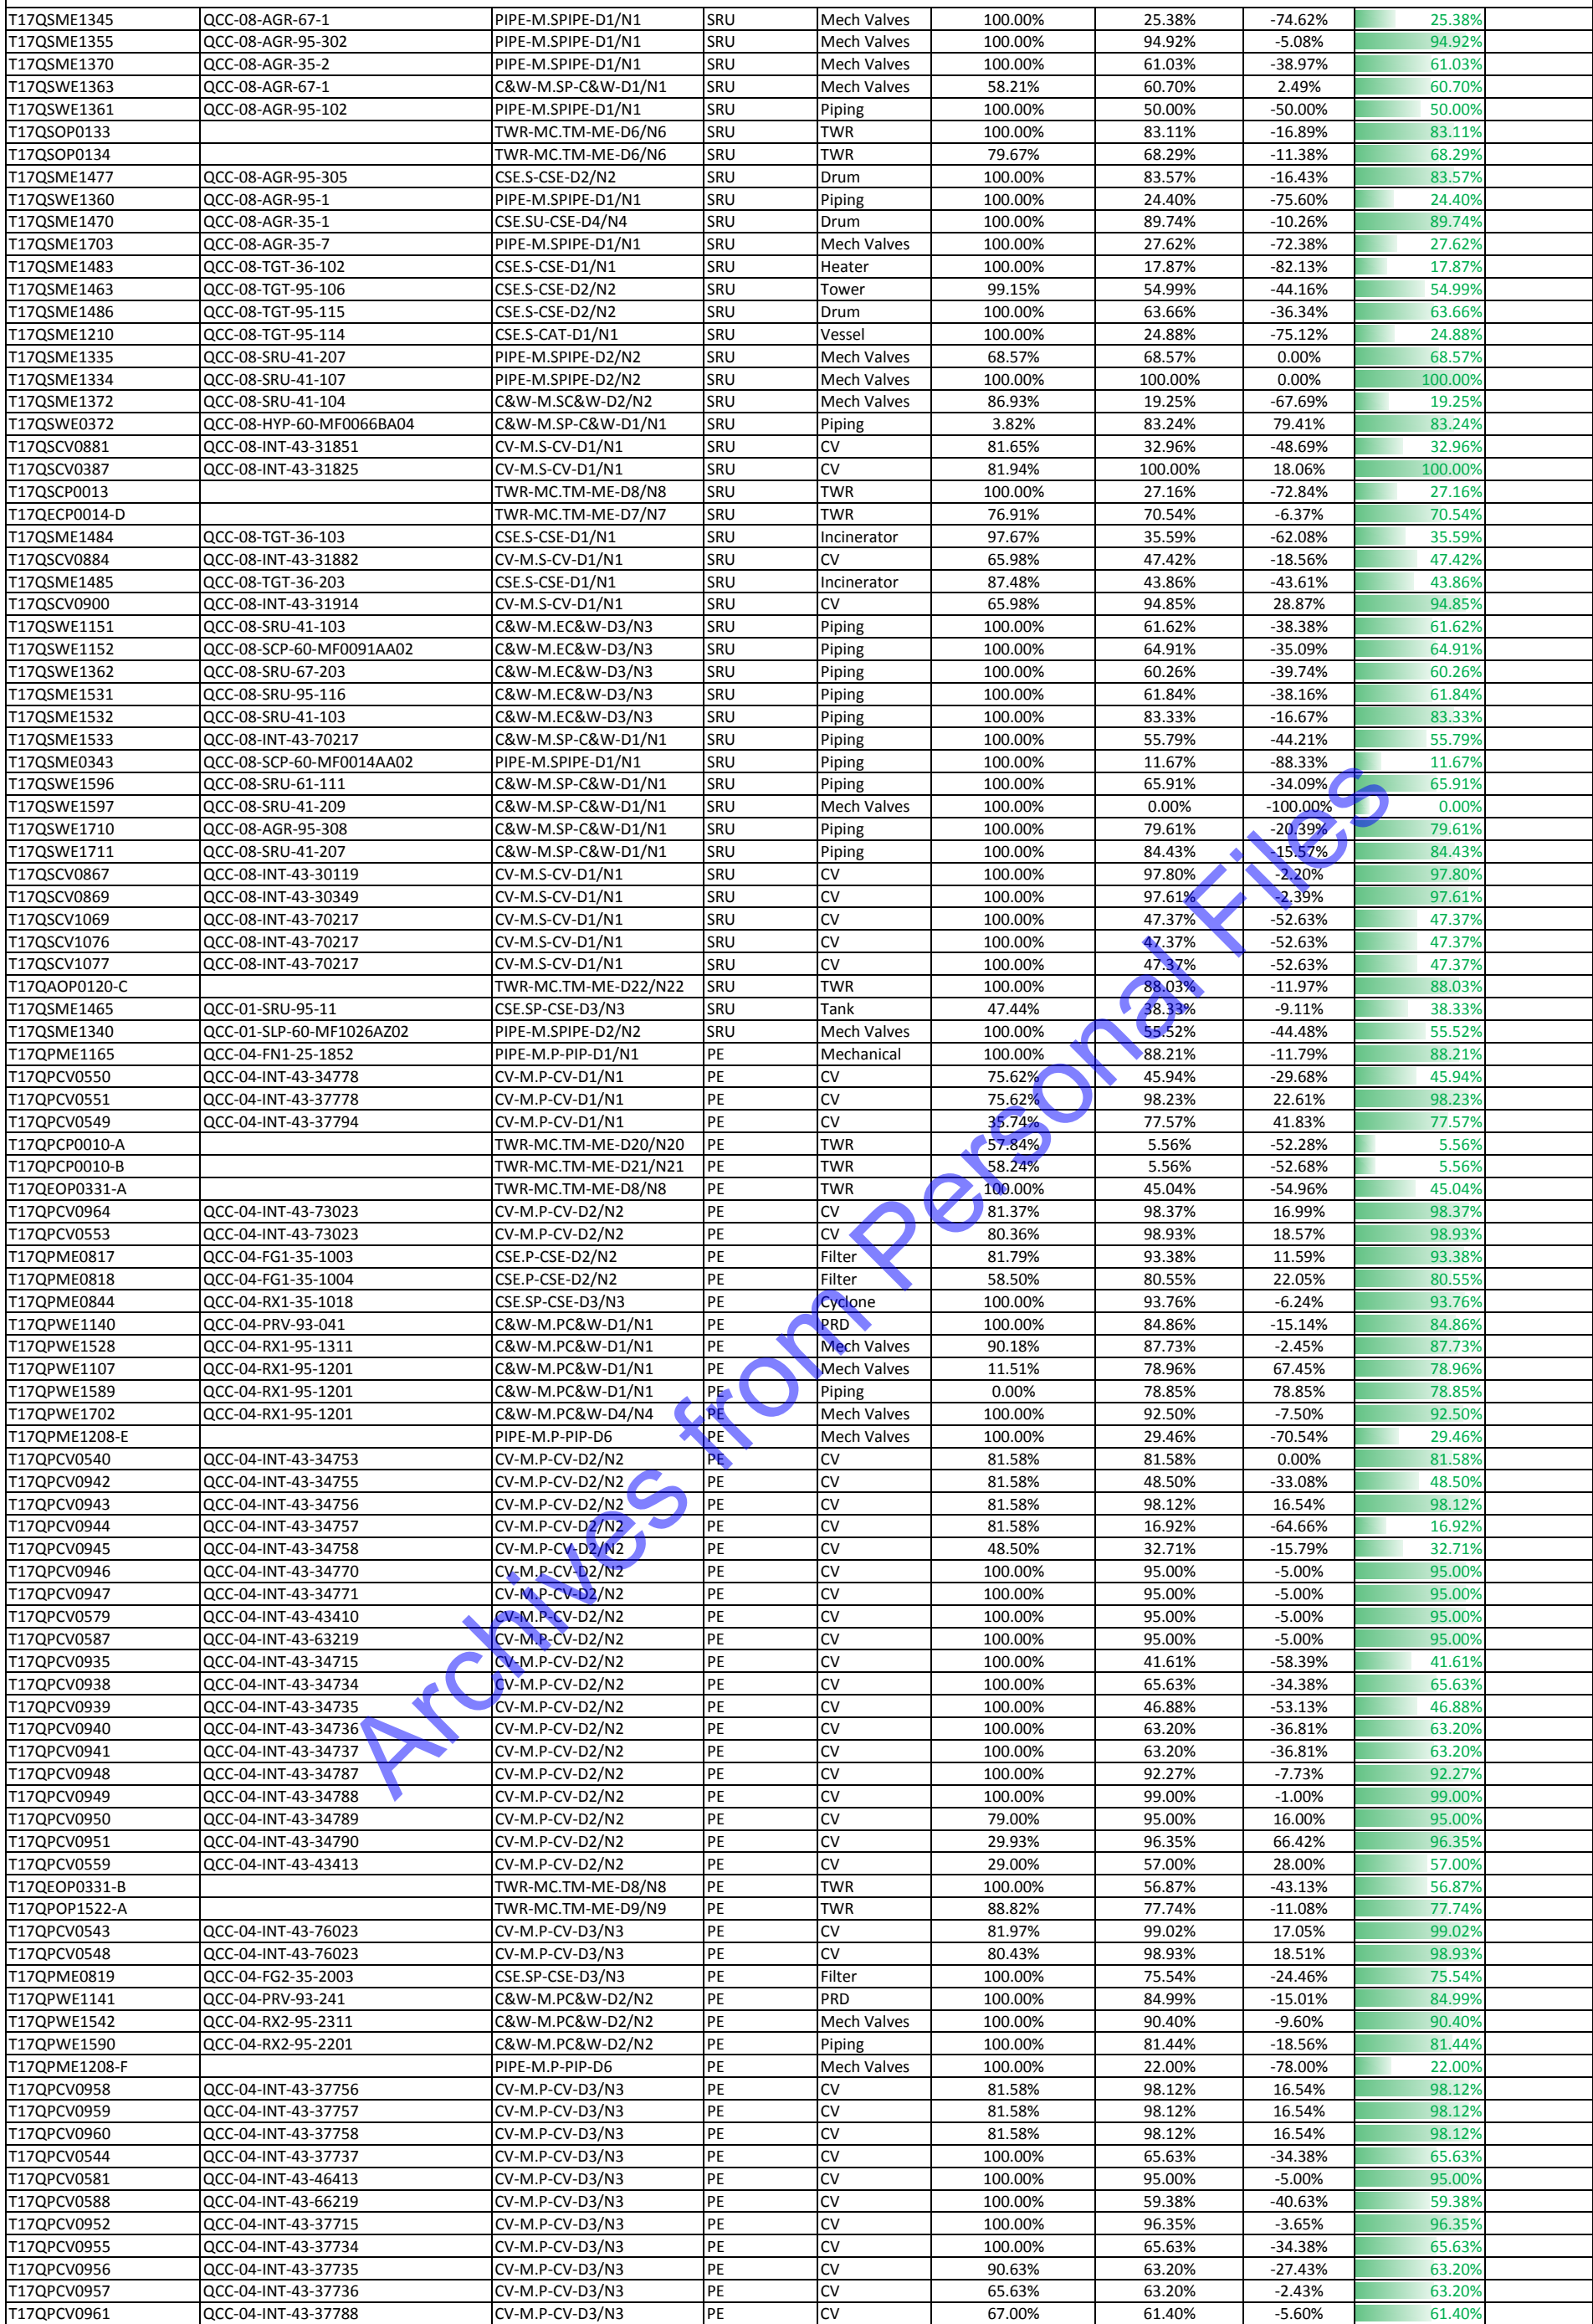
TA15 JOB ID	EQPT TAG	Work Group	Unit	Equip Type	PLANNED TILL DATE	ACTUAL TILL DATE	VARIANCE %	% COMPLETION	REMARKS
T17QEWE1715	QCC-02-XSP-60-MF1039FE31	C&W-M.EC&W-D1/N1	ETH	Piping	43.08%	0.00%	-43.08%	0.00%	
T17QEOP1229-A		TWR-MC.TM-ME-D1/N1	ETH	TWR	100.00%	90.06%	-9.94%	90.06%	
T17QEME1448	QCC-02-FR2-95-302	CSE.E-CSE-D1/N1	ETH	Drum	100.00%	100.00%	0.00%	100.00%	
T17QEME1314	QCC-02-PRC-60-MF1004AA01	PIPE-M.EPIPE-D2/N2	ETH	Mech Valves	100.00%	43.26%	-56.74%	43.26%	
T17QECV0764	QCC-02-INT-43-30077	CV-M.ECV-D1/N1	ETH	CV	100.00%	36.95%	-63.05%	36.95%	
T17QECV0753	QCC-02-INT-43-60231	CV-M.ECV-D1/N1	ETH	CV	100.00%	100.00%	0.00%	100.00%	
T17QECV0752	QCC-02-INT-43-60226	CV-M.ECV-D1/N1	ETH	CV	100.00%	100.00%	0.00%	100.00%	
T17QEOP1229-B		TWR-MC.TM-ME-D1/N1	ETH	TWR	100.00%	84.20%	-15.80%	84.20%	
T17QEME1449	QCC-02-FR3-95-303	CSE.E-CSE-D4/N4	ETH	Drum	100.00%	100.00%	0.00%	100.00%	
T17QEME1382	QCC-02-PRC-60-MF1083AA01	PIPE-M.EPIPE-D2/N2	ETH	Piping	100.00%	72.52%	-27.48%	72.52%	
T17QECV0765	QCC-02-INT-43-30107	CV-M.ECV-D1/N1	ETH	CV	100.00%	100.00%	0.00%	100.00%	
T17QEOP1229-C		TWR-MC.TM-ME-D1/N1	ETH	TWR	100.00%	92.38%	-7.62%	92.38%	
T17QEME1390	QCC-02-PRC-60-MF1084AA01	PIPE-M.EPIPE-D2/N2	ETH	Piping	0.00%	10.56%	10.56%	10.56%	
T17QEOP1229-D		TWR-MC.TM-ME-D1/N1	ETH	TWR	59.48%	77.83%	18.35%	77.83%	
T17QEME1454	QCC-02-FR5-95-305	CSE.E-CSE-D4/N4	ETH	Drum	100.00%	100.00%	0.00%	100.00%	
T17QEME1384	QCC-02-PRC-60-MF1007AA01	PIPE-M.EPIPE-D2/N2	ETH	Piping	100.00%	68.98%	-31.02%	68.98%	
T17QECV0767	QCC-02-INT-43-30167	CV-M.ECV-D1/N1	ETH	CV	100.00%	100.00%	0.00%	100.00%	
T17QECV0754	QCC-02-INT-43-60321	CV-M.ECV-D1/N1	ETH	CV	100.00%	100.00%	0.00%	100.00%	
T17QEOP1229-E		TWR-MC.TM-ME-D1/N1	ETH	TWR	100.00%	91.96%	-8.04%	91.96%	
T17QEWE1260	QCC-02-FR1-36-101	C&W-M.EC&W-D1/N1	ETH	Mech Valves	100.00%	66.89%	-33.11%	66.89%	
T17QEWE1261	QCC-02-FR2-36-102	C&W-M.EC&W-D1/N1	ETH	Mech Valves	100.00%	78.41%	-21.59%	78.41%	
T17QEWE1280	QCC-02-FR3-36-103	C&W-M.EC&W-D1/N1	ETH	Mech Valves	100.00%	69.32%	-30.68%	69.32%	
T17QEWE1262	QCC-02-FR4-36-104	C&W-M.EC&W-D1/N1	ETH	Mech Valves	100.00%	48.86%	-51.14%	48.86%	
T17QEWE1279	QCC-02-FR5-36-105	C&W-M.EC&W-D1/N1	ETH	Mech Valves	100.00%	1.43%	-98.57%	1.43%	
T17QEWE1267	QCC-02-FR4-36-104	C&W-M.EC&W-D1/N1	ETH	Mech Valves	100.00%	83.33%	-16.67%	83.33%	
T17QEWE0305	QCC-02-FR5-36-105	C&W-M.EC&W-D1/N1	ETH	Mech Valves	100.00%	94.53%	-5.47%	94.53%	
T17QEME1431	QCC-02-AUX-95-357	CSE.E-CSE-D1/N1	ETH	Drum	72.30%	87.77%	15.47%	87.77%	
T17QEME1436	QCC-02-CGC-95-314	CSE.E-CSE-D2/N2	ETH	Drum	80.29%	90.63%	10.34%	90.63%	
T17QEME1419	QCC-02-CGC-95-312	CSE.E-CSE-D2/N2	ETH	Drum	78.99%	88.65%	9.66%	88.65%	
T17QEME1489	QCC-02-CGC-95-316	CSE.E-CSE-D2/N2	ETH	Drum	79.95%	90.46%	10.51%	90.46%	
T17QEME1293	QCC-02-PRC-95-18	PIPE-M.EPIPE-D2/N2	ETH	Piping	100.00%	87.14%	-12.86%	87.14%	
T17QEME1292	QCC-02-CGC-16-101	PIPE-M.EPIPE-D2/N2	ETH	Mech Valves	100.00%	0.00%	-100.00%	0.00%	
T17QEME1287	QCC-02-CGC-16-101	PIPE-M.EPIPE-D2/N2	ETH	Piping	49.49%	0.00%	-49.49%	0.00%	
T17QEME1403	QCC-02-PRC-60-MF1101AA03	PIPE-M.EPIPE-D2/N2	ETH	Piping	57.34%	30.56%	-26.79%	30.56%	
T17QEWE1270	QCC-02-CGC-16-101	C&W-M.EC&W-D2/N2	ETH	Piping	70.60%	69.87%	-0.73%	69.87%	
T17QEWE1274	QCC-02-CGC-67-22A	C&W-M.EC&W-D2/N2	ETH	Piping	100.00%	76.47%	-23.53%	76.47%	
T17QEME1288	QCC-02-CGC-16-101	PIPE-M.EPIPE-D4/N4	ETH	Mechanical	67.07%	46.30%	-20.76%	46.30%	
T17QECV0755	QCC-02-INT-43-60488	CV-M.ECV-D1/N1	ETH	CV	81.65%	17.23%	-64.42%	17.23%	
T17QECV0702	QCC-02-INT-43-30875	CV-M.ECV-D1/N1	ETH	CV	81.65%	98.13%	16.48%	98.13%	
T17QECV0744	QCC-02-INT-43-40850	CV-M.ECV-D1/N1	ETH	CV	81.94%	23.08%	-58.85%	23.08%	
T17QECV0745	QCC-02-INT-43-40904	CV-M.ECV-D1/N1	ETH	CV	79.80%	18.72%	-61.08%	18.72%	
T17QECV0726	QCC-02-INT-43-67525	CV-M.ECV-D1/N1	ETH	CV	65.98%	40.21%	-25.77%	40.21%	
T17QEOP0128		TWR-MC.TM-CV-D1	ETH	TWR	100.00%	100.00%	0.00%	100.00%	
T17QEOP0130		TWR-MC.TM-ME-D12/N12	ETH	TWR	100.00%	57.14%	-42.86%	57.14%	
T17QEME1291	QCC-02-PRC-16-103	PIPE-M.EPIPE-D1/N1	ETH	Piping	92.47%	0.00%	-92.47%	0.00%	
T17QEWE1307	QCC-02-PRC-84-103	C&W-M.EC&W-D3/N3	ETH	Piping	100.00%	53.83%	-46.17%	53.83%	
T17QEWE1309	QCC-02-PRC-95-212	PIPE-M.EU-PIPE-D3/N3	ETH	Piping	100.00%	25.22%	-74.78%	25.22%	
T17QEME1290	QCC-02-PRC-16-103	PIPE-M.EPIPE-D4/N4	ETH	Mechanical	100.00%	49.44%	-50.56%	49.44%	
T17QEME1457	QCC-02-PRC-95-329	CSE.E-CSE-D2/N2	ETH	Drum	100.00%	81.21%	-18.79%	81.21%	
T17QEME1409	QCC-02-PRC-95-330	CSE.E-CSE-D2/N2	ETH	Drum	100.00%	89.35%	-10.65%	89.35%	
T17QEME1410	QCC-02-PRC-95-331	CSE.E-CSE-D2/N2	ETH	Drum	100.00%	90.31%	-9.69%	90.31%	
T17QEME1318	QCC-02-PRV-93-279	PIPE-M.EU-PIPE-D3/N3	ETH	Mech Valves	100.00%	48.65%	-51.35%	48.65%	
T17QECV0748	QCC-02-INT-43-41745	CV-M.ECV-D1/N1	ETH	CV	100.00%	100.00%	0.00%	100.00%	
T17QECV0749	QCC-02-INT-43-41752	CV-M.ECV-D1/N1	ETH	CV	100.00%	81.94%	-18.06%	81.94%	
T17QECV0750	QCC-02-INT-43-41775	CV-M.ECV-D1/N1	ETH	CV	100.00%	81.94%	-18.06%	81.94%	
T17QERO1220	QCC-02-ETC-16-102	PIPE-M.EPIPE-D2/N2	ETH	Piping	100.00%	26.55%	-73.45%	26.55%	
T17QEWE1306	QCC-02-ETC-84-102	C&W-M.EC&W-D3/N3	ETH	Piping	100.00%	56.20%	-43.80%	56.20%	
T17QEME1289	QCC-02-ETC-16-102	PIPE-M.EPIPE-D4/N4	ETH	Mechanical	100.00%	21.09%	-78.91%	21.09%	
T17QECV0747	QCC-02-INT-43-41600	CV-M.ECV-D1/N1	ETH	CV	81.94%	100.00%	18.06%	100.00%	
T17QECV0746	QCC-02-INT-43-41596	CV-M.ECV-D1/N1	ETH	CV	73.38%	100.00%	26.62%	100.00%	
T17QECV0727	QCC-02-INT-43-67725	CV-M.ECV-D1/N1	ETH	CV	65.98%	100.00%	34.02%	100.00%	
T17QECV0728	QCC-02-INT-43-67731	CV-M.ECV-D1/N1	ETH	CV	65.98%	64.95%	-1.03%	64.95%	
T17QEME1424	QCC-02-QWS-95-202	CSE.E-CSE-D1/N1	ETH	Tower	100.00%	72.41%	-27.59%	72.41%	
T17QEME1424-A		CSE.E-CSE-D1/N1	ETH	Drum	100.00%	67.39%	-32.61%	67.39%	
T17QEME1425	QCC-02-QWS-95-309	CSE.E-CSE-D1/N1	ETH	Drum	95.31%	67.36%	-27.95%	67.36%	
T17QEME1548	QCC-02-QWS-67-5A	PIPE-M.EPIPE-D1/N1	ETH	Mech Valves	100.00%	73.53%	-26.47%	73.53%	
T17QECV0689	QCC-02-INT-43-30793	CV-M.ECV-D1/N1	ETH	CV	68.69%	39.39%	-29.29%	39.39%	
T17QECV0014-A		TWR-MC.TM-ME-D3/N3	ETH	TWR	70.21%	67.27%	-2.94%	67.27%	
T17QEME1423	QCC-02-CAU-95-203	CSE.E-CSE-D3/N3	ETH	Tower	54.59%	76.66%	22.07%	76.66%	
T17QEME1423-A		CSE.E-CSE-D3/N3	ETH	Drum	100.00%	71.50%	-28.50%	71.50%	
T17QEME1434	QCC-02-CAU-95-315	CSE.E-CSE-D4/N4	ETH	Drum	100.00%	79.39%	-20.61%	79.39%	
T17QEME1435	QCC-02-CAU-95-317	CSE.E-CSE-D4/N4	ETH	Drum	100.00%	73.91%	-26.09%	73.91%	
T17QEME1373	QCC-02-DRY-95-313	CSE.E-CSE-D4/N4	ETH	Drum	100.00%	49.70%	-50.30%	49.70%	
T17QEOP1566		TWR-MC.TM-ME-D4/N4	ETH	TWR	91.17%	2.33%	-88.85%	2.33%	
T17QEME1717	QCC-02-EFD-41-64	MC-EXE-D1/N1	ETH	Exchangers	100.00%	50.60%	-49.40%	50.60%	
T17QEWE1299	QCC-02-C2S-67-10A	C&W-M.EC&W-D3/N3	ETH	Mech Valves	100.00%	1.69%	-98.31%	1.69%	
T17QEWE1264	QCC-02-CHP-60-MF1220AA01	C&W-M.EC&W-D3/N3	ETH	Piping	64.24%	0.00%	-64.24%	0.00%	
T17QECV0014-B		TWR-MC.TM-ME-D4/N4	ETH	TWR	100.00%	18.71%	-81.29%	18.71%	
T17QEME1420	QCC-02-DRY-95-318	CSE.E-CSE-D2/N2	ETH	Drum	75.55%	37.85%	-37.70%	37.85%	
T17QEWE1282	QCC-02-DRY-41-20	C&W-M.EC&W-D3/N3	ETH	Exchangers	0.00%	0.00%	0.00%	0.00%	
T17QEME1297	QCC-02-DRY-95-318	PIPE-M.EPIPE-D2/N2	ETH	Mech Valves	100.00%	47.62%	-52.38%	47.62%	
T17QECV1747	QCC-02-INT-43-31115	CV-M.ECV-D2/N2	ETH	CV	100.00%	17.23%	-82.77%	17.23%	
T17QECV1748	QCC-02-INT-43-31116	CV-M.ECV-D2/N2	ETH	CV	100.00%	17.08%	-82.92%	17.08%	
T17QEWE1265	QCC-02-PSA-95-332	C&W-M.EC&W-D1/N1	ETH	Piping	100.00%	73.35%	-26.65%	73.35%	
T17QEME1219	QCC-02-DC2-95-204	CSE.E-CSE-D1/N1	ETH	Column	54.73%	82.93%	28.20%	82.93%	
T17QEWE1294	QCC-02-DC2-41-12A	C&W-M.EC&W-D1/N1	ETH	Mech Valves	100.00%	0.00%	-100.00%	0.00%	
T17QEWE1263	QCC-02-PRC-60-MF1132BJ01	C&W-M.EC&W-D1/N1	ETH	Piping	100.00%	0.00%	-100.00%	0.00%	
T17QEOP0121		TWR-MC.TM-ME-D2/N2	ETH	TWR	70.07%	0.00%	-70.07%	0.00%	
T17QEME1218	QCC-02-DC3-95-207	CSE.E-CSE-D4/N4	ETH	Column	100.00%	59.81%	-40.19%	59.81%	
T17QEME1407	QCC-02-EXP-95-323	CSE.E-CSE-D2/N2	ETH	Drum	79.06%	68.79%	-10.27%	68.79%	
T17QEME1408	QCC-02-EXP-95-324	CSE.E-CSE-D2/N2	ETH	Drum	70.84%	78.23%	7.39%	78.23%	
T17QEME1317	QCC-02-EXP-16-105	PIPE-M.EU-PIPE-D3/N3	ETH	Piping	85.56%	0.00%	-85.56%	0.00%	
T17QECV0389	QCC-02-EXP-16-104	CV-M.ECV-D2/N2	ETH	CV	100.00%	24.63%	-75.37%	24.63%	
T17QECV0756	QCC-02-INT-43-61476	CV-M.ECV-D2/N2	ETH	CV	100.00%	75.91%	-24.09%	75.91%	
T17QECV0757	QCC-02-INT-43-61506	CV-M.ECV-D2/N2	ETH	CV	100.00%	76.09%	-23.91%	76.09%	
T17QECV0705	QCC-02-EXP-16-105	CV-M.ECV-D2/N2	ETH	CV	100.00%	70.51%	-29.49%	70.51%	
T17QECV0708	QCC-02-EXP-16-104	CV-M.ECV-D2/N2	ETH	CV	100.00%	91.03%	-8.97%	91.03%	
T17QEOP0122		TWR-MC.TM-ME-D5/N5	ETH	TWR	100.00%	63.83%	-36.17%	63.83%	
T17QEME1406	QCC-02-EXP-95-322	CSE.E-CSE-D2/N2	ETH	Drum	63.48%	92.16%	28.68%	92.16%	
T17QEWE1606	QCC-02-DC2-95-208	PIPE-M.EPIPE-D1/N1	ETH	Mech Valves	0.00%	67.22%	67.22%	67.22%	
T17QECV0690	QCC-02-INT-43-31208	CV-M.ECV-D2/N2	ETH	CV	81.65%	81.65%	0.00%	81.65%	



TA JOB TAG WISE PROGRESS



T17QECV0775	QCC-02-INT-43-31205	CV-M.ECV-D2/N2	ETH	CV	81.65%	81.65%	0.00%	81.65%
T17QECV0777	QCC-02-INT-43-31213	CV-M.ECV-D2/N2	ETH	CV	81.65%	81.65%	0.00%	81.65%
T17QECV0779	QCC-02-INT-43-31215	CV-M.ECV-D2/N2	ETH	CV	68.68%	82.26%	13.58%	82.26%
T17QECV0772	QCC-02-INT-43-31164	CV-M.ECV-D2/N2	ETH	CV	100.00%	47.71%	-52.29%	47.71%
T17QECV0774	QCC-02-INT-43-31166	CV-M.ECV-D2/N2	ETH	CV	99.35%	96.73%	-2.61%	96.73%
T17QECV0776	QCC-02-INT-43-31209	CV-M.ECV-D2/N2	ETH	CV	73.20%	96.73%	23.53%	96.73%
T17QECV0860	QCC-02-INT-43-31281	CV-M.ECV-D2/N2	ETH	CV	73.20%	96.73%	23.53%	96.73%
T17QECV0862	QCC-02-INT-43-31283	CV-M.ECV-D2/N2	ETH	CV	62.04%	47.45%	-14.60%	47.45%
T17QECV0770	QCC-02-INT-43-31162	CV-M.ECV-D2/N2	ETH	CV	30.21%	38.54%	8.33%	38.54%
T17QECV0771	QCC-02-INT-43-31163	CV-M.ECV-D2/N2	ETH	CV	30.21%	46.88%	16.67%	46.88%
T17QECV0778	QCC-02-INT-43-31214	CV-M.ECV-D2/N2	ETH	CV	30.85%	67.02%	36.17%	67.02%
T17QECV0864	QCC-02-INT-43-31343	CV-M.ECV-D2/N2	ETH	CV	30.21%	46.88%	16.67%	46.88%
T17QECV0014-C		TWR-MC.TM-ME-D2/N2	ETH	TWR	92.18%	10.50%	-81.68%	10.50%
T17QEME1283	QCC-02-FUR-95-201A	PIPE-M.EU-PIPE-D3/N3	ETH	Mech Valves	100.00%	0.00%	-100.00%	0.00%
T17QEME1284	QCC-02-FUR-67-1A	C&W-M.EC&W-D1/N1	ETH	Piping	74.74%	0.00%	-74.74%	0.00%
T17QECV0700	QCC-02-INT-43-50639	CV-M.ECV-D1/N1	ETH	CV	71.05%	47.37%	-23.68%	47.37%
T17QEOP0125		TWR-MC.TM-ME-D12/N12	ETH	TWR	92.47%	16.75%	-75.72%	16.75%
T17QEOP1493		TWR-MC.TM-ME-D12/N12	ETH	TWR	0.00%	0.00%	0.00%	0.00%
T17QEWE1252	QCC-01-ETP-67-1	C&W-M.EC&W-D4/N4	ETH	Piping	100.00%	0.00%	-100.00%	0.00%
T17QEWE1546	QCC-02-PRC-60-MF1223AJ01	C&W-M.EC&W-D2/N2	ETH	Piping	100.00%	0.00%	-100.00%	0.00%
T17QEWE1275	QCC-01-ETP-61-200	C&W-M.EC&W-D4/N4	ETH	Piping	100.00%	100.00%	0.00%	100.00%
T17QECV0763	QCC-01-INT-43-30025	CV-M.ECV-D2/N2	ETH	CV	100.00%	37.62%	-62.38%	37.62%
T17QEOP1529-A		TWR-MC.TM-ME-D14/N14	ETH	TWR	25.81%	22.82%	-2.99%	22.82%
T17QEOP1529-B		TWR-MC.TM-ME-D16/N16	ETH	TWR	100.00%	96.92%	-3.08%	96.92%
T17QEOP1529-C		TWR-MC.TM-ME-D17/N17	ETH	TWR	100.00%	25.59%	-74.41%	25.59%
T17QEME1418	QCC-02-CBX-95-7	CSE.E-CBX-D1/N1	ETH	Exchangers	94.62%	62.68%	-31.94%	62.68%
T17QECV0769	QCC-02-INT-43-30819	CV-M.ECV-D2/N2	ETH	CV	100.00%	48.46%	-51.54%	48.46%
T17QECV0863	QCC-02-INT-43-31338	CV-M.ECV-D2/N2	ETH	CV	100.00%	49.37%	-50.63%	49.37%
T17QECV0701	QCC-02-INT-43-41330	CV-M.ECV-D2/N2	ETH	CV	100.00%	97.78%	-2.22%	97.78%
T17QEME1295	QCC-02-ETP-41-40	PIPE-M.EPIPE-D1/N1	ETH	Piping	72.78%	29.84%	-42.94%	29.84%
T17QEOP0340		TWR-MC.TM-ME-D5/N5	ETH	TWR	100.00%	69.68%	-30.32%	69.68%
T17QEME1429	QCC-02-PSA-95-501	CSE.E-CSE-D1/N1	ETH	Vessel	100.00%	82.67%	-17.33%	82.67%
T17QEME1458	QCC-02-PSA-95-342	CSE.E-CSE-D1/N1	ETH	Vessel	100.00%	77.72%	-22.28%	77.72%
T17QEME1312	QCC-02-PRV-93-265	PIPE-M.EPIPE-D1/N1	ETH	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QEME1323	QCC-01-PRC-60-P4071	PIPE-M.EPIPE-D1/N1	ETH	Piping	100.00%	0.00%	-100.00%	0.00%
T17QEME1325	QCC-02-ETP-67-11	PIPE-M.EPIPE-D1/N1	ETH	Piping	100.00%	0.00%	-100.00%	0.00%
T17QEWE1316	QCC-02-ETP-41-40	C&W-M.EC&W-D3/N3	ETH	Mech Valves	22.54%	0.00%	-22.54%	0.00%
T17QEWE1266	QCC-02-INT-43-63125	C&W-M.EC&W-D4/N4	ETH	Piping	100.00%	84.33%	15.67%	84.33%
T17QEWE1271	QCC-02-DRY-41-20	C&W-M.EC&W-D4/N4	ETH	Mech Valves	100.00%	93.69%	-6.31%	93.69%
T17QEWE1253	QCC-02-ETP-41-39	C&W-M.EC&W-D3/N3	ETH	Mech Valves	100.00%	77.05%	-22.95%	77.05%
T17QEWE1310	QCC-02-SCP-60-MF2027AA02	C&W-M.EC&W-D4/N4	ETH	Piping	65.45%	86.55%	21.09%	86.55%
T17QEWE1599	QCC-02-STM-61-1	C&W-M.EC&W-D3/N3	ETH	Piping	100.00%	55.56%	-44.44%	55.56%
T17QEWE1598	QCC-02-STM-61-1A	C&W-M.EC&W-D3/N3	ETH	Piping	100.00%	88.89%	-11.11%	88.89%
T17QEWE1607	QCC-02-FUR-67-1	C&W-M.EC&W-D3/N3	ETH	Mech Valves	100.00%	90.24%	-9.76%	90.24%
T17QECV0723	QCC-02-INT-43-63263	CV-M.ECV-D1/N1	ETH	CV	100.00%	100.00%	0.00%	100.00%
T17QECV0722	QCC-02-INT-43-63262	CV-M.ECV-D1/N1	ETH	CV	81.94%	100.00%	18.06%	100.00%
T17QECV0724	QCC-02-INT-43-63124	CV-M.ECV-D1/N1	ETH	CV	100.00%	73.38%	-26.62%	73.38%
T17QECV0720	QCC-02-INT-43-73065	CV-M.ECV-D1/N1	ETH	CV	100.00%	65.98%	-34.02%	65.98%
T17QECV0721	QCC-02-INT-43-73066	CV-M.ECV-D1/N1	ETH	CV	100.00%	100.00%	0.00%	100.00%
T17QEOP0127		TWR-MC.TM-ME-D1/N1	ETH	TWR	100.00%	70.52%	-29.48%	70.52%
T17QEME0308	QCC-02-CGC-61-457	PIPE-M.EPIPE-D1/N1	ETH	Mech Valves	100.00%	54.79%	-45.21%	54.79%
T17QECV0150		TWR-MC.TM-ME-D25/N25	ETH	TWR	44.28%	67.98%	23.70%	67.98%
T17QSME1479	QCC-08-SRU-36-101	CSE.S-CSE-D1/N1	SRU	Reactor	90.45%	32.13%	-58.32%	32.13%
T17QSME1640	QCC-08-SRU-95-113	CSE.S-CSE-D1/N1	SRU	Vessel	60.29%	73.87%	13.58%	73.87%
T17QSME1348	QCC-08-SRU-95-105	PIPE-M.SPIPE-D2/N2	SRU	Mech Valves	100.00%	37.74%	-62.26%	37.74%
T17QSME1349	QCC-08-SRU-05-101A	PIPE-M.SPIPE-D2/N2	SRU	Mech Valves	100.00%	90.00%	-10.00%	90.00%
T17QSME1350	QCC-08-SRU-05-101	PIPE-M.SPIPE-D2/N2	SRU	Mech Valves	100.00%	90.00%	-10.00%	90.00%
T17QSME1356	QCC-08-SRU-36-101	PIPE-M.SPIPE-D2/N2	SRU	Mech Valves	100.00%	91.67%	-8.33%	91.67%
T17QSW1154	QCC-08-NUP-60-MF0086AA32	C&W-M.SC&W-D2/N2	SRU	Piping	100.00%	81.84%	-18.16%	81.84%
T17QSCV0870	QCC-08-INT-43-30433	CV-M.S-CV-D1/N1	SRU	CV	100.00%	97.80%	-2.20%	97.80%
T17QSCV0871	QCC-08-INT-43-31802	CV-M.S-CV-D1/N1	SRU	CV	100.00%	81.78%	-18.22%	81.78%
T17QSCV0876	QCC-08-INT-43-31815	CV-M.S-CV-D1/N1	SRU	CV	100.00%	97.30%	-2.70%	97.30%
T17QSME1480	QCC-08-SRU-36-201	CSE.S-CSE-D1/N1	SRU	Reactor	90.76%	37.20%	-53.55%	37.20%
T17QSME1641	QCC-08-SRU-95-213	CSE.S-CSE-D1/N1	SRU	Vessel	60.29%	59.05%	-1.23%	59.05%
T17QSME1351	QCC-08-SRU-05-201	PIPE-M.SPIPE-D2/N2	SRU	Mech Valves	100.00%	72.67%	-27.33%	72.67%
T17QSME1352	QCC-08-SRU-05-201A	PIPE-M.SPIPE-D2/N2	SRU	Mech Valves	100.00%	72.67%	-27.33%	72.67%
T17QSME1357	QCC-08-SRU-36-201	PIPE-M.SPIPE-D2/N2	SRU	Mech Valves	100.00%	65.00%	-35.00%	65.00%
T17QSW1155	QCC-08-NUP-60-MF0077AA32	C&W-M.SC&W-D2/N2	SRU	Piping	100.00%	81.42%	-18.58%	81.42%
T17QSCV0896	QCC-08-INT-43-31903	CV-M.S-CV-D1/N1	SRU	CV	85.46%	97.80%	12.33%	97.80%
T17QSCV0911	QCC-08-INT-43-31892	CV-M.S-CV-D1/N1	SRU	CV	80.89%	81.78%	0.89%	81.78%
T17QSCV0898	QCC-08-INT-43-31911	CV-M.S-CV-D1/N1	SRU	CV	100.00%	34.48%	-65.52%	34.48%
T17QSCV0899	QCC-08-INT-43-31912	CV-M.S-CV-D1/N1	SRU	CV	100.00%	37.17%	-62.83%	37.17%
T17QSME1338	QCC-08-SRU-36-101	PIPE-M.SPIPE-D3/N3	SRU	Piping	100.00%	54.38%	-45.62%	54.38%
T17QSIN0678	QCC-01-INT-43-71618	FLARE.S-FLR-IN D/N	SRU	Instrument	66.51%	0.23%	-66.29%	0.23%
T17QSME1426	QCC-08-AGR-95-101	CSE.S-CSE-D2/N2	SRU	Tower	48.07%	88.19%	40.13%	88.19%
T17QSME1475	QCC-08-AGR-95-103	CSE.S-CSE-D2/N2	SRU	Tower	79.31%	73.00%	-6.30%	73.00%
T17QSME1346	QCC-08-AGR-95-101	PIPE-M.SPIPE-D1/N1	SRU	Mech Valves	100.00%	75.13%	-24.87%	75.13%
T17QSME1341	QCC-08-AGR-95-103	PIPE-M.SPIPE-D1/N1	SRU	Mech Valves	100.00%	25.38%	-74.62%	25.38%
T17QSME1226	QCC-08-PRV-93-002A	PIPE-M.SPIPE-D1/N1	SRU	Mech Valves	100.00%	35.47%	-64.53%	35.47%
T17QSME1353	QCC-08-AGR-95-301	PIPE-M.SPIPE-D1/N1	SRU	Mech Valves	100.00%	94.34%	-5.66%	94.34%
T17QSME1358	QCC-08-AGR-95-301	PIPE-M.SPIPE-D1/N1	SRU	Mech Valves	100.00%	94.34%	-5.66%	94.34%
T17QSME1354	QCC-08-AGR-95-301	PIPE-M.SPIPE-D1/N1	SRU	Mech Valves	100.00%	94.34%	-5.66%	94.34%
T17QSME1365	QCC-08-AGR-95-101	PIPE-M.SPIPE-D1/N1	SRU	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QSW1146	QCC-08-AGR-95-103	PIPE-M.SPIPE-D1/N1	SRU	Piping	100.00%	84.44%	-15.56%	84.44%
T17QSW1153	QCC-08-INT-43-40221	C&W-M.SP-C&W-D1/N1	SRU	Piping	100.00%	79.46%	-20.54%	79.46%
T17QSW1728	QCC-08-LGP-60-MF0003AA11	C&W-M.SC&W-D2/N2	SRU	Piping	100.00%	0.00%	-100.00%	0.00%
T17QSCV0760	QCC-08-INT-43-50222	CV-M.S-CV-D1/N1	SRU	CV	81.94%	97.80%	15.86%	97.80%
T17QSCV0865	QCC-08-INT-43-30024	CV-M.S-CV-D1/N1	SRU	CV	81.94%	32.60%	-49.34%	32.60%
T17QSCV0866	QCC-08-INT-43-30045	CV-M.S-CV-D1/N1	SRU	CV	81.94%	97.80%	15.86%	97.80%
T17QSOP0324		TWR-MC.TM-IE-D1/N1	SRU	TWR	100.00%	68.86%	-31.14%	68.86%
T17QSME1405	QCC-08-AGR-35-6	CSE.SU-CSE-D4/N4	SRU	Filter	100.00%	68.94%	-31.06%	68.94%
T17QSME1347	QCC-08-AGR-35-6	PIPE-M.SPIPE-D2/N2	SRU	Mech Valves	100.00%	50.25%	-49.75%	50.25%
T17QSME1366	QCC-08-PRV-93-033B	PIPE-M.SPIPE-D2/N2	SRU	Mech Valves	100.00%	94.34%	-5.66%	94.34%
T17QSCV0868	QCC-08-INT-43-30250	CV-M.S-CV-D1/N1	SRU	CV	100.00%	81.94%	-18.06%	81.94%
T17QSCV0910	QCC-08-INT-43-33195	CV-M.S-CV-D1/N1	SRU	CV	100.00%	59.79%	-40.21%	59.79%
T17QSME1478	QCC-08-AGR-95-307	CSE.SU-CSE-D4/N4	SRU	Drum	100.00%	72.27%	-27.73%	72.27%
T17QSME1368	QCC-08-AGR-67-5A	PIPE-M.SPIPE-D3/N3	SRU	Mech Valves	100.00%	71.49%	-28.51%	71.49%
T17QSME1342	QCC-08-AGR-67-5	PIPE-M.SPIPE-D3/N3	SRU	Mech Valves	100.00%	25.38%	-74.62%	25.38%
T17QSME1364	QCC-08-AGR-41-4	PIPE-M.SPIPE-D1/N1	SRU	Mech Valves	100.00%	25.50%	-74.50%	25.50%
T17QEME1385	QCC-08-AGP-60-MF0015AA02	PIPE-M.SPIPE-D2/N2	SRU	Piping	48.48%	12.80%	-35.67%	12.80%
T17QSME1427	QCC-08-AGR-95-102	CSE.SU-CSE-D4/N4	SRU	Drum	100.00%	85.05%	-14.95%	85.05%
T17QSME1476	QCC-08-AGR-95-302	CSE.SU-CSE-D4/N4	SRU	Drum	100.00%	90.12%	-9.88%	90.12%
T17QSME1367	QCC-08-AGR-67-1	PIPE-M.SPIPE-D1/N1	SRU	Mech Valves	100.00%	61.97%	-38.03%	61.97%





TA JOB TAG WISE PROGRESS



T17QPCV0962	QCC-04-INT-43-37789	CV-M.P-CV-D3/N3	PE	CV	67.00%	61.40%	-5.60%	61.40%
T17QPCV0963	QCC-04-INT-43-37790	CV-M.P-CV-D3/N3	PE	CV	75.91%	96.35%	20.44%	96.35%
T17QPCV0560	QCC-04-INT-43-46410	CV-M.P-CV-D3/N3	PE	CV	67.00%	95.00%	28.00%	95.00%
T17QEOP0331-C		TWR-MC.TM-ME-D8/N8	PE	TWR	69.47%	56.87%	-12.60%	56.87%
T17QPOP1522-B		TWR-MC.TM-ME-D9/N9	PE	TWR	89.16%	79.04%	-10.12%	79.04%
T17QPM1166	QCC-04-PUR-35-23A	PIPE-M.P-PIP-D1/N1	PE	Mech Valves	100.00%	0.00%	-100.00%	0.00%
T17QPM1182	QCC-04-PUR-35-23	PIPE-M.P-PIP-D1/N1	PE	Mech Valves	100.00%	0.00%	-100.00%	0.00%
T17QPCV0928	QCC-04-INT-43-31717	CV-M.P-CV-D3/N3	PE	CV	81.94%	48.46%	-33.48%	48.46%
T17QPCV0916	QCC-04-INT-43-31705	CV-M.P-CV-D2/N2	PE	CV	100.00%	64.58%	-35.42%	64.58%
T17QPCV0917	QCC-04-INT-43-31706	CV-M.P-CV-D2/N2	PE	CV	100.00%	38.54%	-61.46%	38.54%
T17QPCV0920	QCC-04-INT-43-31709	CV-M.P-CV-D2/N2	PE	CV	100.00%	38.54%	-61.46%	38.54%
T17QPCV0921	QCC-04-INT-43-31710	CV-M.P-CV-D2/N2	PE	CV	100.00%	64.58%	-35.42%	64.58%
T17QPCV0924	QCC-04-INT-43-31713	CV-M.P-CV-D2/N2	PE	CV	100.00%	66.00%	-34.00%	66.00%
T17QPCV0925	QCC-04-INT-43-31714	CV-M.P-CV-D2/N2	PE	CV	100.00%	95.00%	-5.00%	95.00%
T17QPCV0918	QCC-04-INT-43-31707	CV-M.P-CV-D3/N3	PE	CV	100.00%	8.33%	-91.67%	8.33%
T17QPCV0919	QCC-04-INT-43-31708	CV-M.P-CV-D3/N3	PE	CV	100.00%	94.79%	-5.21%	94.79%
T17QPCV0922	QCC-04-INT-43-31711	CV-M.P-CV-D3/N3	PE	CV	100.00%	94.79%	-5.21%	94.79%
T17QPCV0923	QCC-04-INT-43-31712	CV-M.P-CV-D3/N3	PE	CV	100.00%	43.54%	-56.46%	43.54%
T17QPCV0926	QCC-04-INT-43-31715	CV-M.P-CV-D3/N3	PE	CV	100.00%	64.58%	-35.42%	64.58%
T17QPCV0927	QCC-04-INT-43-31716	CV-M.P-CV-D3/N3	PE	CV	100.00%	63.54%	-36.46%	63.54%
T17QEOP0331-D		TWR-MC.TM-ME-D11/N11	PE	TWR	100.00%	0.00%	-100.00%	0.00%
T17QPCP0012		TWR-MC.TM-IE-D2/N2	PE	TWR	100.00%	96.26%	-3.74%	96.26%
T17QPWE1142	QCC-04-CF1-95-1306	C&W-M.PU-C&W-D3/N3	PE	Mech Valves	100.00%	91.13%	-8.87%	91.13%
T17QPWE1144	QCC-04-CF1-95-1306	C&W-M.PU-C&W-D3/N3	PE	Mech Valves	100.00%	90.21%	-9.79%	90.21%
T17QPWE1143	QCC-04-CF2-95-2306	C&W-M.PU-C&W-D3/N3	PE	Mech Valves	84.18%	85.41%	1.23%	85.41%
T17QPWE1145	QCC-04-CF2-95-2306	C&W-M.PU-C&W-D3/N3	PE	Mech Valves	100.00%	90.46%	-9.54%	90.46%
T17QPM1176	QCC-04-INT-43-37775	PIPE-M.P-PIP-D1/N1	PE	Piping	100.00%	98.73%	-1.27%	98.73%
T17QPWE1593	QCC-04-FG1-95-1317	C&W-M.PC&W-D1/N1	PE	Piping	100.00%	59.32%	-40.68%	59.32%
T17QPWE1594	QCC-04-FT1-05-1102	C&W-M.PC&W-D1/N1	PE	Piping	100.00%	56.82%	-43.18%	56.82%
T17QPCV0570	QCC-04-INT-43-34776	CV-M.P-CV-D1/N1	PE	CV	81.94%	97.80%	15.86%	97.80%
T17QPCV0571	QCC-04-INT-43-34777	CV-M.P-CV-D1/N1	PE	CV	81.94%	97.80%	15.86%	97.80%
T17QPCV0572	QCC-04-INT-43-37776	CV-M.P-CV-D1/N1	PE	CV	81.94%	81.94%	0.00%	81.94%
T17QPCV0573	QCC-04-INT-43-37777	CV-M.P-CV-D1/N1	PE	CV	81.94%	97.80%	15.86%	97.80%
T17QEOP0331-E		TWR-MC.TM-ME-D11/N11	PE	TWR	100.00%	73.21%	-26.79%	73.21%
T17QPM10420	QCC-04-FST-95-204	PIPE-M.P-PIP-D2/N2	PE	Mech Valves	100.00%	82.54%	-17.46%	82.54%
T17QPM1208-A		PIPE-M.P-PIP-D6	PE	Mech Valves	100.00%	62.40%	-37.60%	62.40%
T17QPM10824	QCC-04-FST-95-366	CSE.P-CSE-D2/N2	PE	Tank	100.00%	100.00%	0.00%	100.00%
T17QPWE1170	QCC-04-FST-95-366	PIPE-M.P-PIP-D1/N1	PE	Piping	100.00%	100.00%	0.00%	100.00%
T17QPM1186	QCC-04-FST-67-4B	PIPE-M.PU-PIP-D3/N3	PE	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QPCV0931	QCC-04-INT-43-31738	CV-M.P-CV-D1/N1	PE	CV	100.00%	100.00%	0.00%	100.00%
T17QPM1203	QCC-04-FST-95-207	C&W-M.PC&W-D4/N4	PE	Mech Valves	100.00%	61.71%	-38.29%	61.71%
T17QPM1137	QCC-04-PRC-60-MF0309DA01	C&W-M.PC&W-D4/N4	PE	Piping	100.00%	26.29%	-73.71%	26.29%
T17QPM1209-C		PIPE-M.PU-PIP-D3/N3	PE	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QPM10420-D		PIPE-M.P-PIP-D2/N2	PE	Mech Valves	100.00%	83.00%	-17.00%	83.00%
T17QPM1208-B		PIPE-M.P-PIP-D6	PE	Mech Valves	100.00%	60.31%	-39.69%	60.31%
T17QPM10825	QCC-04-FST-95-367	CSE.P-CSE-D2/N2	PE	Tank	100.00%	91.76%	-8.24%	91.76%
T17QPCV0932	QCC-04-INT-43-31739	CV-M.P-CV-D1/N1	PE	CV	100.00%	100.00%	0.00%	100.00%
T17QPM1205	QCC-04-FST-95-206	PIPE-M.PU-PIP-D3/N3	PE	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QPM1209-B		PIPE-M.PU-PIP-D3/N3	PE	Mech Valves	100.00%	68.70%	-31.30%	68.70%
T17QPM10420-C		PIPE-M.P-PIP-D2/N2	PE	Mech Valves	100.00%	90.41%	-9.59%	90.41%
T17QPM1208-C		PIPE-M.P-PIP-D6	PE	Mech Valves	100.00%	80.43%	-19.57%	80.43%
T17QPM10823	QCC-04-FST-95-365	CSE.P-CSE-D2/N2	PE	Tank	100.00%	85.34%	-14.66%	85.34%
T17QPM1603	QCC-04-FST-67-3	PIPE-M.P-PIP-D6	PE	Mech Valves	100.00%	89.62%	-10.38%	89.62%
T17QPCV0930	QCC-04-INT-43-31737	CV-M.P-CV-D1/N1	PE	CV	100.00%	94.85%	-5.15%	94.85%
T17QPM10420-B		PIPE-M.P-PIP-D2/N2	PE	Mech Valves	90.62%	71.86%	-18.76%	71.86%
T17QPM1208-D		PIPE-M.P-PIP-D6	PE	Mech Valves	100.00%	42.69%	-57.31%	42.69%
T17QECP0014-E		TWR-MC.TM-ME-D13/N13	PE	TWR	100.00%	53.21%	-46.79%	53.21%
T17QPCV0934	QCC-04-INT-43-31766	CV-M.P-CV-D1/N1	PE	CV	100.00%	39.18%	-60.82%	39.18%
T17QPM1183	QCC-04-FST-95-204	PIPE-M.P-PIP-D4/N4	PE	Piping	96.78%	24.23%	-72.54%	24.23%
T17QPM1201	QCC-04-FST-95-204A	PIPE-M.PU-PIP-D3/N3	PE	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QPM1202	QCC-04-FST-95-204	PIPE-M.PU-PIP-D3/N3	PE	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QPM1206	QCC-04-FST-95-204	PIPE-M.PU-PIP-D3/N3	PE	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QPM1209-A		PIPE-M.PU-PIP-D3/N3	PE	Mech Valves	100.00%	50.00%	-50.00%	50.00%
T17QPM10420-A		PIPE-M.P-PIP-D2/N2	PE	Mech Valves	87.43%	35.73%	-51.71%	35.73%
T17QPM1208	QCC-04-FST-95-204	PIPE-M.P-PIP-D6	PE	Mech Valves	62.86%	61.07%	-1.79%	61.07%
T17QPWE1610	QCC-04-FST-95-204	C&W-M.PC&W-D4/N4	PE	Piping	100.00%	66.82%	-33.18%	66.82%
T17QECP0014-F		TWR-MC.TM-ME-D11/N11	PE	TWR	100.00%	47.98%	-52.02%	47.98%
T17QPM10843	QCC-04-BUT-95-211	CSE.P-CSE-D1/N1	PE	Column	58.28%	99.21%	40.93%	99.21%
T17QPM1187	QCC-04-BUT-67-14	PIPE-M.P-PIP-D1/N1	PE	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QPWE1129	QCC-04-PRC-60-MF0324BA04	C&W-M.PC&W-D2/N2	PE	Piping	100.00%	79.07%	-20.93%	79.07%
T17QPM10815	QCC-04-PUR-95-362	C&W-M.PC&W-D2/N2	PE	Vessel	45.37%	52.12%	6.76%	52.12%
T17QPM10832	QCC-04-PUR-95-209	CSE.P-CSE-D1/N1	PE	Column	100.00%	88.77%	-11.23%	88.77%
T17QPM1535	QCC-04-PUR-95-363	PIPE-M.P-PIP-D1/N1	PE	Drum	100.00%	11.94%	-88.06%	11.94%
T17QPM1184	QCC-04-PUR-67-2A	PIPE-M.P-PIP-D1/N1	PE	Mech Valves	100.00%	95.65%	-4.35%	95.65%
T17QPM1604	QCC-04-PUR-41-13	PIPE-M.P-PIP-D1/N1	PE	Mech Valves	100.00%	95.59%	-4.41%	95.59%
T17QPCV0929	QCC-04-INT-43-31736	CV-M.P-CV-D1/N1	PE	CV	100.00%	32.60%	-67.40%	32.60%
T17QPCV0555	QCC-04-INT-43-40451	CV-M.P-CV-D1/N1	PE	CV	100.00%	95.05%	-4.95%	95.05%
T17QPCV0576	QCC-04-INT-43-40448	CV-M.P-CV-D1/N1	PE	CV	100.00%	95.05%	-4.95%	95.05%
T17QPCV0585	QCC-04-INT-43-60272	CV-M.P-CV-D1/N1	PE	CV	100.00%	88.66%	-11.34%	88.66%
T17QPCV0604	QCC-04-INT-43-40450	CV-M.P-CV-D1/N1	PE	CV	100.00%	96.75%	-3.25%	96.75%
T17QPCV0605	QCC-04-INT-43-40452	CV-M.P-CV-D1/N1	PE	CV	100.00%	96.38%	-3.62%	96.38%
T17QPCV0914	QCC-04-INT-43-30875	CV-M.P-CV-D1/N1	PE	CV	100.00%	99.28%	-0.72%	99.28%
T17QPCV0915	QCC-04-INT-43-30876	CV-M.P-CV-D1/N1	PE	CV	94.85%	63.92%	-30.93%	63.92%
T17QPCV0933	QCC-04-INT-43-31765	CV-M.P-CV-D1/N1	PE	CV	100.00%	94.85%	-5.15%	94.85%
T17QPM10831	QCC-04-PUR-95-208	CSE.P-CSE-D1/N1	PE	Column	100.00%	96.02%	-3.98%	96.02%
T17QPM10833	QCC-04-PUR-95-361	CSE.P-CSE-D2/N2	PE	Vessel	100.00%	100.00%	0.00%	100.00%
T17QPM1171	QCC-04-PUR-67-1A	PIPE-M.P-PIP-D4/N4	PE	Mech Valves	100.00%	9.09%	-90.91%	9.09%
T17QPM1179	QCC-04-PUR-16-109	PIPE-M.P-PIP-D4/N4	PE	Mech Valves	100.00%	93.75%	-6.25%	93.75%
T17QPM1181	QCC-04-PUR-67-1	PIPE-M.P-PIP-D4/N4	PE	Mech Valves	100.00%	6.25%	-93.75%	6.25%
T17QPM1207	QCC-04-PUR-41-9	PIPE-M.P-PIP-D4/N4	PE	Mech Valves	83.52%	16.48%	-67.03%	16.48%
T17QPM1571	QCC-04-PUR-16-109A	PIPE-M.PU-PIP-D3/N3	PE	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QPM1572	QCC-04-PUR-16-109A	PIPE-M.PU-PIP-D3/N3	PE	Mech Valves	100.00%	0.00%	-100.00%	0.00%
T17QPWE1568	QCC-04-PUR-16-109	C&W-M.PC&W-D4/N4	PE	Mech Valves	100.00%	63.33%	-36.67%	63.33%
T17QPWE1569	QCC-04-PUR-16-109	C&W-M.PC&W-D4/N4	PE	Mech Valves	100.00%	87.16%	-12.84%	87.16%
T17QPWE1570	QCC-04-PUR-16-109	C&W-M.PC&W-D4/N4	PE	Mech Valves	100.00%	88.98%	-11.02%	88.98%
T17QPCV0545	QCC-04-INT-43-30874	CV-M.P-CV-D1/N1	PE	CV	100.00%	95.77%	-4.23%	95.77%
T17QPCV0554	QCC-04-INT-43-40446	CV-M.P-CV-D1/N1	PE	CV	100.00%	29.70%	-70.30%	29.70%
T17QPM1162	QCC-04-PUR-67-29	PIPE-M.P-PIP-D1/N1	PE	Mech Valves	100.00%	90.91%	-9.09%	90.91%
T17QPM1195	QCC-04-PUR-41-40A	PIPE-M.P-PIP-D1/N1	PE	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QPM1164	QCC-04-PUR-16-115	PIPE-M.P-PIP-D1/N1	PE	Piping	100.00%	0.00%	-100.00%	0.00%
T17QPM1609	QCC-04-PUR-95-7	PIPE-M.PU-PIP-D3/N3	PE	Mech Valves	100.00%	79.45%	-20.55%	79.45%
T17QPM10816	QCC-04-UTL-95-372	CSE.P-CSE-D2/N2	PE	Drum	100.00%	100.00%	0.00%	100.00%
T17QPWE1722	QCC-04-PUR-41-14	C&W-M.PC&W-D2/N2	PE	Piping	100.00%	84.30%	-15.70%	84.30%



TA JOB TAG WISE PROGRESS



T17QPM0841	QCC-04-UTL-95-368	CSE.P-CSE-D2/N2	PE	Tank	100.00%	84.82%	-15.18%	84.82%
T17QPM01169	QCC-04-RX1-41-1001	PIPE-M.P-PIP-D4/N4	PE	Piping	63.34%	0.00%	-63.34%	0.00%
T17QPM0284	QCC-04-RX1-41-1001	PIPE-M.P-PIP-D5/N5	PE	Piping	84.10%	31.71%	-52.39%	31.71%
T17QPM0842	QCC-04-UTL-95-377	CSE.P-CSE-D2/N2	PE	Drum	100.00%	99.40%	-0.60%	99.40%
T17QPM01194	QCC-04-INT-43-63255	PIPE-M.P-PIP-D1/N1	PE	Mech Valves	100.00%	91.84%	-8.16%	91.84%
T17QPWE1094	QCC-04-INT-43-73045	C&W-M.PC&W-D2/N2	PE	Mech Valves	100.00%	93.92%	-6.08%	93.92%
T17QPWE1089	QCC-04-FGC-95-360	C&W-M.PC&W-D2/N2	PE	Piping	100.00%	60.87%	-39.13%	60.87%
T17QPWE1091	QCC-04-FG2-95-2319	C&W-M.PU-C&W-D3/N3	PE	Piping	100.00%	94.44%	-5.56%	94.44%
T17QPWE1093	QCC-04-FG2-95-2315	C&W-M.PU-C&W-D3/N3	PE	Piping	100.00%	92.86%	-7.14%	92.86%
T17QPWE1083	QCC-04-FN1-25-1801	C&W-M.PC&W-D4/N4	PE	Piping	100.00%	47.65%	-52.35%	47.65%
T17QPWE1552	QCC-04-PUR-41-12	C&W-M.PC&W-D1/N1	PE	Piping	100.00%	24.32%	-75.68%	24.32%
T17QPWE1623	QCC-04-UTL-95-368	C&W-M.PC&W-D2/N2	PE	Mech Valves	100.00%	60.34%	-39.66%	60.34%
T17QPWE1621	QCC-04-PUR-41-7	C&W-M.PC&W-D4/N4	PE	Mech Valves	100.00%	77.98%	-22.02%	77.98%
T17QPWE1628	QCC-04-FGC-95-360	C&W-M.SP-C&W-D1/N1	PE	Piping	100.00%	95.71%	-4.29%	95.71%
T17QPWE1616	QCC-04-FGC-95-360	C&W-M.SP-C&W-D1/N1	PE	Piping	100.00%	95.00%	-5.00%	95.00%
T17QPWE1620	QCC-04-FST-35-22	C&W-M.PC&W-D4/N4	PE	Piping	100.00%	83.67%	-16.33%	83.67%
T17QPWE1617	QCC-04-FGC-95-360	C&W-M.SP-C&W-D1/N1	PE	Piping	100.00%	95.76%	-4.24%	95.76%
T17QPWE1615	QCC-04-FG2-95-2316	C&W-M.PC&W-D2/N2	PE	Piping	100.00%	94.96%	-5.04%	94.96%
T17QPWE1614	QCC-04-BUT-67-14	C&W-M.PC&W-D2/N2	PE	Piping	100.00%	96.38%	-3.62%	96.38%
T17QPWE1613	QCC-04-INT-43-66227	C&W-M.PC&W-D2/N2	PE	Piping	100.00%	88.98%	-11.02%	88.98%
T17QPWE1622	QCC-04-UTL-16-113	C&W-M.PC&W-D1/N1	PE	Piping	100.00%	87.17%	-12.83%	87.17%
T17QPCV0552	QCC-04-INT-43-63255	CV-M.P-CV-D3/N3	PE	CV	100.00%	96.38%	-3.62%	96.38%
T17QPCV0546	QCC-04-INT-43-50537	CV-M.P-CV-D3/N3	PE	CV	100.00%	38.61%	-61.39%	38.61%
T17QPCP0160		TWR-MC.TM-ME-D13/N13	PE	TWR	94.76%	51.77%	-42.99%	51.77%
T17QAOP0120-A		TWR-MC.TM-ME-D24/N24	PE	TWR	95.01%	67.09%	-27.92%	67.09%
T17QAOP0120-B		TWR-MC.TM-ME-D18/N18	PE	TWR	100.00%	85.03%	-14.97%	85.03%
T17QPWE1085	QCC-04-UTL-16-160	C&W-M.PC&W-D1/N1	PE	Mech Valves	32.99%	80.31%	47.31%	80.31%
T17QPWE1086	QCC-04-PBC-16-110A	C&W-M.PC&W-D1/N1	PE	Mech Valves	100.00%	90.19%	-9.81%	90.19%
T17QPWE1087	QCC-04-PBC-16-110B	C&W-M.PC&W-D1/N1	PE	Mech Valves	100.00%	93.56%	-6.44%	93.56%
T17QPWE1088	QCC-04-PBC-16-110C	C&W-M.PC&W-D1/N1	PE	Mech Valves	100.00%	90.74%	-9.26%	90.74%
T17QPWE1115	QCC-04-INT-43-70105	C&W-M.PC&W-D2/N2	PE	Mech Valves	100.00%	77.12%	-22.88%	77.12%
T17QHCV0912	QCC-03-INT-43-31230	CV-M.P-CV-D1/N1	HEX	CV	100.00%	100.00%	0.00%	100.00%
T17QHME0784	QCC-03-RCY-16-135	PIPE-M.HPIPE-D1/N1	HEX	Piping	100.00%	63.32%	-36.68%	63.32%
T17QHCP0006		TWR-MC.TM-ME-D14/N14	HEX	TWR	100.00%	67.00%	-33.00%	67.00%
T17QHME0197	QCC-03-INT-43-61495	PIPE-M.HPIPE-D1/N1	HEX	Piping	100.00%	100.00%	0.00%	100.00%
T17QHWE1627	QCC-03-PRV-93-302	C&W-M.HC&W-D1/N1	HEX	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QHWE1550	QCC-03-RXC-41-60	C&W-M.HC&W-D1/N1	HEX	Piping	100.00%	100.00%	0.00%	100.00%
T17QHWE1551	QCC-03-UTL-95-365	C&W-M.HC&W-D1/N1	HEX	Piping	100.00%	27.19%	72.81%	27.19%
T17QHWE1611	QCC-03-INT-43-61494	C&W-M.HC&W-D1/N1	HEX	Mech Valves	100.00%	97.37%	-2.63%	97.37%
T17QHWE1625	QCC-03-PRF-95-230	C&W-M.HC&W-D1/N1	HEX	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QHME1198	QCC-03-RX1-41-1061	PIPE-M.HPIPE-D1/N1	HEX	Mech Valves	100.00%	0.00%	-100.00%	0.00%
T17QHWE1527	QCC-03-RCY-41-35	C&W-M.HC&W-D1/N1	HEX	Mech Valves	100.00%	0.00%	-100.00%	0.00%
T17QUME0845	QCC-09-UTL-97-908	SW.USWI-D1/N1	UTL	SW Screen	83.67%	86.05%	2.39%	86.05%
T17QUME0846	QCC-09-UTL-67-2	SW.USWO-D2/N2	UTL	SW Screen	100.00%	96.78%	-3.22%	96.78%
T17QUME0282	QCC-09-UTL-67-91	PIPE-M.U-PIP-D5/N5	UTL	Mech Valves	100.00%	22.46%	-77.54%	22.46%
T17QUME1013	QCC-09-UTL-67-91	PIPE-M.U-PIP-D1/N1	UTL	Mech Valves	91.24%	41.15%	-50.09%	41.15%
T17QUME1014	QCC-09-UTL-67-91A	PIPE-M.U-PIP-D1/N1	UTL	Mech Valves	91.22%	41.23%	-49.99%	41.23%
T17QUME1015	QCC-09-UTL-67-91B	PIPE-M.U-PIP-D1/N1	UTL	Mech Valves	91.24%	38.03%	-53.20%	38.03%
T17QUME1016	QCC-09-UTL-67-91C	PIPE-M.U-PIP-D1/N1	UTL	Mech Valves	90.79%	39.98%	-50.81%	39.98%
T17QUME1017	QCC-09-UTL-67-91D	PIPE-M.U-PIP-D1/N1	UTL	Mech Valves	71.09%	38.06%	-33.03%	38.06%
T17QUME1018	QCC-09-UTL-67-91E	PIPE-M.U-PIP-D1/N1	UTL	Mech Valves	51.02%	37.69%	-13.33%	37.69%
T17QUCV0468	QCC-09-INT-43-31052	CV-M.U-CV-D1/N1	UTL	CV	67.83%	48.25%	-19.58%	48.25%
T17QUCV0469	QCC-09-INT-43-31053	CV-M.U-CV-D1/N1	UTL	CV	48.25%	48.25%	0.00%	48.25%
T17QUCV0470	QCC-09-INT-43-31054	CV-M.U-CV-D1/N1	UTL	CV	48.25%	48.25%	0.00%	48.25%
T17QUCV0471	QCC-09-INT-43-31077	CV-M.U-CV-D1/N1	UTL	CV	48.25%	48.25%	0.00%	48.25%
T17QUCV0472	QCC-09-INT-43-31078	CV-M.U-CV-D1/N1	UTL	CV	48.25%	48.25%	0.00%	48.25%
T17QUCV0473	QCC-09-INT-43-31079	CV-M.U-CV-D1/N1	UTL	CV	48.25%	48.25%	0.00%	48.25%
T17QUME1012	QCC-01-BOL-84-213	PIPE-M.U-PIP-D5/N5	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUME1706	QCC-01-BOL-07-201	PIPE-M.U-PIP-D7/N7	UTL	Piping	100.00%	0.00%	-100.00%	0.00%
T17QUME1034	QCC-01-UTL-07-381	PIPE-M.U-PIP-D5/N5	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUME1050	QCC-01-BOL-84-211	PIPE-M.U-PIP-D5/N5	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUME1064	QCC-01-INT-43-74747	PIPE-M.U-PIP-D5/N5	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUWE0980	QCC-01-BOL-07-203	C&W-M.LUC&W-D2/N2	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUWE0981	QCC-01-BOL-07-203	C&W-M.LUC&W-D2/N2	UTL	Mech Valves	98.01%	100.00%	1.99%	100.00%
T17QUWE0986	QCC-02-BFW-67-67	C&W-M.LUC&W-D2/N2	UTL	Mech Valves	0.00%	100.00%	100.00%	100.00%
T17QUWE0993	QCC-01-BOL-07-203	C&W-M.UC&W-D4/N4	UTL	Piping	93.83%	56.63%	-37.21%	56.63%
T17QUWE1588	QCC-01-BOL-61-428	C&W-M.UC&W-D3/N3	UTL	Piping	83.61%	86.96%	3.34%	86.96%
T17QUWE1591	QCC-02-INT-43-75848	C&W-M.UC&W-D3/N3	UTL	Piping	60.16%	100.00%	39.84%	100.00%
T17QUWE1707	QCC-01-BOL-84-211	C&W-M.UC&W-D4/N4	UTL	Piping	100.00%	98.89%	-1.11%	98.89%
T17QUME1573	QCC-01-BOL-84-212	PIPE-M.U-PIP-D5/N5	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUCV0479	QCC-02-INT-43-62915	CV-M.U-CV-D2/N2	UTL	CV	100.00%	77.09%	-22.91%	77.09%
T17QUCV0474	QCC-01-INT-43-60500	CV-M.U-CV-D1/N1	UTL	CV	100.00%	48.31%	-51.69%	48.31%
T17QUCV0475	QCC-01-INT-43-60500	CV-M.U-CV-D1/N1	UTL	CV	100.00%	97.19%	-2.81%	97.19%
T17QUCV0467	QCC-01-INT-43-74747	CV-M.U-CV-D1/N1	UTL	CV	100.00%	96.15%	-3.85%	96.15%
T17QUCV0500	QCC-02-INT-43-75848	CV-M.U-CV-D2/N2	UTL	CV	100.00%	96.81%	-3.19%	96.81%
T17QUCP0327		TWR-MC.TM-ME-D10/N10	UTL	TWR	98.35%	60.14%	-38.22%	60.14%
T17QACP0013		TWR-MC.TM-ME-D15/N15	UTL	TWR	100.00%	72.45%	-27.55%	72.45%
T17QUME1007	QCC-02-CON-95-352	CSE.SU-CSE-D4/N4	UTL	Vessel	100.00%	80.38%	-19.62%	80.38%
T17QUWE1033	QCC-02-CON-95-352	C&W-M.UC&W-D1/N1	UTL	Mech Valves	100.00%	96.17%	-3.83%	96.17%
T17QUCV0482	QCC-02-INT-43-52881	CV-M.U-CV-D2/N2	UTL	CV	100.00%	51.38%	-48.62%	51.38%
T17QUCV0481	QCC-02-INT-43-42883	CV-M.U-CV-D2/N2	UTL	CV	100.00%	94.85%	-5.15%	94.85%
T17QUME1009	QCC-02-BFW-95-351	CSE.U-CSE-D3/N3	UTL	Vessel	89.93%	48.40%	-41.53%	48.40%
T17QUME1055	QCC-02-BFW-95-350	CSE.U-CSE-D3/N3	UTL	Vessel	84.95%	55.15%	-29.80%	55.15%
T17QUME1066	QCC-02-AUX-67-35	PIPE-M.U-PIP-D7/N7	UTL	Mechanical	91.07%	44.75%	-46.32%	44.75%
T17QUME1051	QCC-02-BFW-67-67A	PIPE-M.U-PIP-D5/N5	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUWE1006	QCC-02-INT-43-63166	C&W-M.UC&W-D1/N1	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUWE1000	QCC-02-BFW-67-67A	C&W-M.UC&W-D3/N3	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUWE1030	QCC-02-AUX-67-35	C&W-M.UC&W-D3/N3	UTL	Piping	100.00%	52.06%	-47.94%	52.06%
T17QUCV0480	QCC-02-INT-43-32918	CV-M.U-CV-D2/N2	UTL	CV	81.77%	79.80%	-1.97%	79.80%
T17QUCV0485	QCC-09-INT-43-32022	CV-M.U-CV-D1/N1	UTL	CV	100.00%	96.84%	-3.16%	96.84%
T17QUCV0487	QCC-02-INT-43-63166	CV-M.U-CV-D2/N2	UTL	CV	100.00%	96.84%	-3.16%	96.84%
T17QUCV0476	QCC-01-INT-43-70508	CV-M.U-CV-D1/N1	UTL	CV	100.00%	56.84%	-43.16%	56.84%
T17QUCV0477	QCC-01-INT-43-70509	CV-M.U-CV-D1/N1	UTL	CV	100.00%	96.84%	-3.16%	96.84%
T17QUOP0325		TWR-MC.TM-IE-D1/N1	UTL	TWR	100.00%	95.11%	-4.89%	95.11%
T17QUME1010	QCC-02-CON-95-2	CSE.U-CSE-D2/N2	UTL	Tank	100.00%	20.74%	-79.26%	20.74%
T17QUME1011	QCC-02-AUX-41-79	PIPE-M.U-PIP-D5/N5	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUME1067	QCC-02-INT-43-48540	PIPE-M.U-PIP-D5/N5	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUWE1574	QCC-02-CON-95-2	PIPE-M.EU-PIPE-D3/N3	UTL	Piping	50.00%	100.00%	50.00%	100.00%
T17QUCV0478	QCC-02-INT-43-52912	CV-M.U-CV-D2/N2	UTL	CV	100.00%	18.87%	-81.13%	18.87%
T17QUCV0465	QCC-02-INT-43-48558	CV-M.U-CV-D2/N2	UTL	CV	100.00%	48.21%	-51.79%	48.21%
T17QUOP0138		TWR-MC.TM-ME-D15/N15	UTL	TWR	100.00%	77.32%	-22.68%	77.32%
T17QUME1035	QCC-01-AUX-95-301	PIPE-M.U-PIP-D6/N6	UTL	Piping	100.00%	0.00%	-100.00%	0.00%
T17QUME1057	QCC-01-AUX-95-301	PIPE-M.U-PIP-D6/N6	UTL	Mech Valves	100.00%	84.55%	-15.45%	84.55%



TA JOB TAG WISE PROGRESS



T17QUME1061	QCC-01-AUX-95-301	PIPE-M.U-PIP-D6/N6	UTL	Mech Valves	100.00%	48.33%	-51.67%	48.33%
T17QUWE0994	QCC-01-AUX-95-301	PIPE-M.U-PIP-D6/N6	UTL	Piping	100.00%	100.00%	0.00%	100.00%
T17QUOP0135		TWR-MC.TM-ME-D14/N14	UTL	TWR	100.00%	83.33%	-16.67%	83.33%
T17QEOP1529-D		TWR-MC.TM-ME-D17/N17	UTL	TWR	100.00%	75.32%	-24.68%	75.32%
T17QUME1056	QCC-09-UTL-95-421	CSE.U-CSE-D2/N2	UTL	Vessel	76.94%	100.00%	23.06%	100.00%
T17QUME1004	QCC-01-UTL-16-151A	PIPE-M.U-PIP-D5/N5	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUME1028	QCC-09-INT-43-42025	PIPE-M.U-PIP-D9/N9	UTL	Mech Valves	100.00%	61.94%	-38.06%	61.94%
T17QUME1019	QCC-09-UTL-67-92	PIPE-M.U-PIP-D4/N4	UTL	Mech Valves	100.00%	88.86%	-11.14%	88.86%
T17QUME1020	QCC-09-UTL-67-92A	PIPE-M.U-PIP-D4/N4	UTL	Mech Valves	100.00%	86.86%	-13.14%	86.86%
T17QUME1021	QCC-09-UTL-67-92B	PIPE-M.U-PIP-D4/N4	UTL	Mech Valves	100.00%	86.86%	-13.14%	86.86%
T17QUME1022	QCC-09-UTL-67-92C	PIPE-M.U-PIP-D4/N4	UTL	Mech Valves	92.07%	76.54%	-15.53%	76.54%
T17QUME1023	QCC-09-UTL-67-92D	PIPE-M.U-PIP-D9/N9	UTL	Mech Valves	100.00%	62.70%	-37.30%	62.70%
T17QUME0281	QCC-09-UTL-41-51	PIPE-M.U-PIP-D9/N9	UTL	Mech Valves	81.28%	50.89%	-30.39%	50.89%
T17QUME1037	QCC-09-UTL-41-51A	PIPE-M.U-PIP-D2/N2	UTL	Mech Valves	100.00%	56.88%	-43.12%	56.88%
T17QUME1038	QCC-09-UTL-41-51B	PIPE-M.U-PIP-D2/N2	UTL	Mech Valves	100.00%	55.92%	-44.08%	55.92%
T17QUME1039	QCC-09-UTL-41-51C	PIPE-M.U-PIP-D2/N2	UTL	Mech Valves	100.00%	55.92%	-44.08%	55.92%
T17QUME1040	QCC-09-UTL-41-51D	PIPE-M.U-PIP-D2/N2	UTL	Mech Valves	100.00%	55.92%	-44.08%	55.92%
T17QUME1041	QCC-09-UTL-41-51E	PIPE-M.U-PIP-D2/N2	UTL	Mech Valves	90.70%	52.36%	-38.35%	52.36%
T17QUME1042	QCC-09-UTL-41-51F	PIPE-M.U-PIP-D2/N2	UTL	Mech Valves	79.26%	53.14%	-26.12%	53.14%
T17QUME1043	QCC-09-UTL-41-51G	PIPE-M.U-PIP-D3/N3	UTL	Mech Valves	100.00%	56.50%	-43.50%	56.50%
T17QUME1045	QCC-02-CAU-67-60	PIPE-M.U-PIP-D3/N3	UTL	Mech Valves	100.00%	56.00%	-44.00%	56.00%
T17QUME1044	QCC-09-UTL-41-51J	PIPE-M.U-PIP-D3/N3	UTL	Mech Valves	100.00%	55.95%	-44.05%	55.95%
T17QUME1046	QCC-09-UTL-41-51K	PIPE-M.U-PIP-D3/N3	UTL	Mech Valves	100.00%	55.95%	-44.05%	55.95%
T17QUME1047	QCC-09-UTL-41-51L	PIPE-M.U-PIP-D3/N3	UTL	Mech Valves	90.17%	55.95%	-34.22%	55.95%
T17QUME1048	QCC-09-UTL-41-51M	PIPE-M.U-PIP-D3/N3	UTL	Mech Valves	72.69%	55.95%	-16.75%	55.95%
T17QUWE0855	QCC-02-CAU-67-60	C&W-M.UC&W-D1/N1	UTL	Piping	100.00%	94.71%	-5.29%	94.71%
T17QUCV0488	QCC-09-INT-43-42025	CV-M.U-CV-D1/N1	UTL	CV	100.00%	77.99%	-22.01%	77.99%
T17QUCV0484	QCC-09-INT-43-62018	CV-M.U-CV-D1/N1	UTL	CV	100.00%	47.42%	-52.58%	47.42%
T17QUCV0483	QCC-09-INT-43-62018	CV-M.U-CV-D1/N1	UTL	CV	100.00%	96.20%	-3.80%	96.20%
T17QUWE0995	QCC-01-UTL-61-162	PIPE-M.U-PIP-D6/N6	UTL	Piping	100.00%	100.00%	0.00%	100.00%
T17QUWE0998	QCC-01-UTL-61-162	C&W-M.UC&W-D3/N3	UTL	Piping	100.00%	100.00%	0.00%	100.00%
T17QUME1538	QCC-01-UTL-61-162	PIPE-M.U-PIP-D6/N6	UTL	Flare	100.00%	0.00%	-100.00%	0.00%
T17QUIN0504	QCC-01-UTL-61-162	FLARE.U-FLR-IN D1/N1	UTL	Instrument	100.00%	7.78%	-92.22%	7.78%
T17QUWE0997	QCC-01-UTL-61-161	C&W-M.UC&W-D3/N3	UTL	Piping	16.87%	100.00%	83.13%	100.00%
T17QUME1537	QCC-01-UTL-61-161	PIPE-M.U-PIP-D6/N6	UTL	Flare	22.07%	100.00%	77.93%	100.00%
T17QUIN0503	QCC-01-UTL-61-161	FLARE.U-FLR-IN D1/N1	UTL	Instrument	30.67%	100.00%	69.33%	100.00%
T17QUME1024	QCC-01-UTL-95-411	CSE.SU-CSE-D4/N4	UTL	Vessel	100.00%	100.00%	0.00%	100.00%
T17QUME1026	QCC-01-INT-43-34002	PIPE-M.U-PIP-D7/N7	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUWE0989	QCC-01-INT-43-34011	C&W-M.UC&W-D3/N3	UTL	Piping	100.00%	100.00%	0.00%	100.00%
T17QUWE0991	QCC-01-INT-43-34002	C&W-M.UC&W-D3/N3	UTL	Piping	100.00%	100.00%	0.00%	100.00%
T17QUCV0486	QCC-01-INT-43-34011	CV-M.U-CV-D2/N2	UTL	CV	100.00%	100.00%	0.00%	100.00%
T17QUCV0491	QCC-01-INT-43-34500	CV-M.U-CV-D2/N2	UTL	CV	100.00%	100.00%	0.00%	100.00%
T17QUCV0493	QCC-01-INT-43-34512	CV-M.U-CV-D2/N2	UTL	CV	100.00%	100.00%	0.00%	100.00%
T17QUCV0283	QCC-01-INT-43-34002	CV-M.U-CV-D2/N2	UTL	CV	100.00%	100.00%	0.00%	100.00%
T17QUOP0137		TWR-MC.TM-ME-D15/N15	UTL	TWR	100.00%	100.00%	0.00%	100.00%
T17QEOP1529-E		TWR-MC.TM-ME-D16/N16	UTL	TWR	100.00%	100.00%	0.00%	100.00%
T17QUME9542	QCC-02-CAU-95-9	CSE.U-CSE-D1/N1	UTL	Tank	58.78%	54.54%	-4.24%	54.54%
T17QUME1002	QCC-02-CAU-67-268	CSE.U-CSE-D2/N2	UTL	Sump	70.85%	12.72%	-58.13%	12.72%
T17QUME1062	QCC-02-CAU-95-9	PIPE-M.U-PIP-D5/N5	UTL	Mech Valves	100.00%	20.95%	-79.05%	20.95%
T17QUME1036	QCC-09-UTL-95-122	PIPE-M.PU-PIP-D3/N3	UTL	Mech Valves	100.00%	100.00%	0.00%	100.00%
T17QUWE0859	QCC-09-UTL-67-82	PIPE-M.PU-PIP-D3/N3	UTL	Piping	0.00%	100.00%	100.00%	100.00%
T17QUWE1526	QCC-02-INT-43-33336	C&W-M.UC&W-D1/N1	UTL	Mech Valves	62.56%	100.00%	37.44%	100.00%
T17QUCV0490	QCC-01-INT-43-32576	CV-M.U-CV-D1/N1	UTL	CV	52.78%	100.00%	47.22%	100.00%
T17QEOP1529-F		TWR-MC.TM-ME-D11/N11	UTL	TWR	52.00%	76.00%	24.00%	76.00%
T17QEOP0331-F		TWR-MC.TM-ME-D9/N9	UTL	TWR	42.96%	70.37%	27.41%	70.37%
T17QEOP1529-G		TWR-MC.TM-ME-D14/N14	UTL	TWR	100.00%	75.19%	-24.81%	75.19%
T17QEOP0331-G		TWR-MC.TM-ME-D15/N15	UTL	TWR	100.00%	100.00%	0.00%	100.00%
T17QEOP0331-H		TWR-MC.TM-ME-D17/N17	UTL	TWR	0.00%	65.83%	65.83%	65.83%
T17QEOP0331-J		TWR-MC.TM-ME-D5/N5	UTL	TWR	100.00%	100.00%	0.00%	100.00%
T17QEOP0331-K		TWR-MC.TM-ME-D17/N17	UTL	TWR	100.00%	88.69%	-11.31%	88.69%
T17QUME1049	QCC-09-UTL-67-61	PIPE-M.U-PIP-D6/N6	UTL	Mech Valves	100.00%	82.88%	-17.12%	82.88%
T17QUWE0996	QCC-01-UTL-67-65	PIPE-M.U-PIP-D8/N8	UTL	Piping	84.34%	100.00%	15.66%	100.00%
T17QLWE0448	QCC-05-B11-35-1002	C&W-M.LUC&W-D2/N2	LOG	Piping	100.00%	86.75%	-13.25%	86.75%
T17QLWE0449	QCC-05-B12-35-2001	C&W-M.LUC&W-D2/N2	LOG	Piping	100.00%	86.75%	-13.25%	86.75%
T17QLWE1581	QCC-05-B11-35-1001	C&W-M.LUC&W-D2/N2	LOG	Piping	100.00%	68.27%	-31.73%	68.27%
T17QLWE1582	QCC-05-B12-35-2002	C&W-M.LUC&W-D2/N2	LOG	Piping	100.00%	68.27%	-31.73%	68.27%
T17QLOP0131		TWR-MC.TM-ME-D19/N19	LOG	TWR	100.00%	100.00%	0.00%	100.00%
T17QLOP0131-B		TWR-MC.TM-ME-D19/N19	LOG	TWR	100.00%	100.00%	0.00%	100.00%
T17QLOP0131-C		TWR-MC.TM-ME-D19/N19	LOG	TWR	100.00%	93.93%	-6.07%	93.93%
T17QLOP0131-D		TWR-MC.TM-ME-D19/N19	LOG	TWR	100.00%	93.93%	-6.07%	93.93%
T17QLOP0162-A		TWR-MC.TM-IE-D3	LOG	TWR	100.00%	76.47%	-23.53%	76.47%
T17QLOP1495-A		TWR-MC.TM-IE-D3	LOG	TWR	100.00%	85.71%	-14.29%	85.71%
T17QLOP0162-B		TWR-MC.TM-IE-D3	LOG	TWR	0.00%	0.00%	0.00%	0.00%
T17QLOP1495-B		TWR-MC.TM-IE-D3	LOG	TWR	92.52%	85.71%	-6.80%	85.71%



QATAR CHEMICALS COMPANY LIMITED
TURNAROUND 2017
MANPOWER & EQUIPMENT DETAIL REPORT
Wednesday, February 15, 2017



MANPOWER & EQUIPMENT STATUS							EQUIPMENT						
A - DESCON INDIRECT MANPOWER							EQUIPMENT NAME		PLAN	ACTUAL			
	PLAN	DAY	PLAN	NIGHT	PLAN	TOTAL	#						
		ACT		ACT		ACT							
MANAGEMENT													
1	PROJECT MANAGER	1	1		1	1	1	CRANE 25 TON	1	1			
2	TURNAROUND MANAGER	1	1		1	1	2	CRANE 50 TON	4	4			
PLANNING													
6	PLANNING IN CHARGE	1	1		1	1	3	CRANE 100 TON	2	2			
7	LEAD PLANNING NIGHT			1	1	1	4	CRANE 120 TON					
8	FEDC ENGINEER	1	1		1	1	5	CRANE 160 TON	1	1			
9	PLANNING ENGINEER	1	1	1	1	2	6	FLAT BED TRAILER	2	2			
10	PLANNER / SCHEDULERS	4	5	3	4	7	7	LOW BED TRAILER	1	1			
11	IT OFFICER	1	1		1	1	8	BOOM TRUCK	2	3			
12	MANPOWER/EQUIPMENT SUPPLY COORDINATOR	1	1		1	1	9	FORKLIFT 10 TON					
13	QUANTITY SURVEYOR/TEST PACK COORDINATOR	1	1		1	1	10	FORKLIFT 7 TON	1	1			
14	WAREHOUSE IN CHARGE	1	1	1	1	2	11	FORKLIFT 5 TON	2	2			
15	MATERIAL CORDINATOR	1	1	1	1	2	12	AIR COMPRESSOR 825CFM					
16	MATERIAL HANDLER (Fitter)	3	3	2	1	5	13	AIR COMPRESSOR 600CFM					
17	DOCUMENT CONTROLLER	1	1		1	1	14	AIR COMPRESSOR 750CFM	6	6			
QA / QC													
18	QA / QC IN CHARGE	1	1		1	1	15	AIR COMPRESSOR 1600CFM					
19	QA / QC COORDINATOR			1	1	1	16	AIR COMPRESSOR 400CFM					
20	QC INSPECTOR MECHANICAL	3	3	2	2	5	17	POWER GENERATOR	6	6			
21	QC INSPECTOR PIPING	3	4	3	2	6	18	VACCUM TANKER	1				
22	NDT+PWHT COORDINATOR	1	1	1	1	2	19	WELDING GENERATOR (400AMP)	25	25			
23	WELDING INSPECTOR	1	1	1	1	2	20	DIESEL TANKER	1	1			
24	DOCUMENT CONTROLLER	1	1	1	1	2	21	BUNDLE PULLER					
HEALTH SAFETY AND ENVIRONMENT													
25	HSE IN CHARGE	1	1			1	22	HYDROJETTING MACHINE	2	2			
26	LEAD HSE OFFICER	1	1	1	1	2	23	DE-WATERING PUMP	9	9			
27	HSE INSPECTOR (FIELD)	9	9	6	6	15	24	SUPER SUCKER	1				
28	ENVIRONMENT COORDINATOR	1	1	1	1	2	25	TOWER LIGHT	2	3			
29	HSE TRAINERS	2	2	1	1	3		GRAND TOTAL			69	69	
30	ENVIRONMENT HELPER	2	2	2	2	4							
31	PARAMEDIC	2	2	1	1	3							
32	TRAINING COORDINATOR	1	1	1	1	2							
EXECUTION													
33	EXECUTION MANAGER	1	1	1	1	2							
34	AREA INCHARGE	3	3	3	3	6							
35	TWR INCHARGE	1	1	1	1	2							
36	SUPERINTENDENT WELDING	1	1			1							
37	INSTRUMENT / ELECTRICAL TEAM LEADER	1	1	1	1	2							
38	COORDINATOR - IPS	1	1	1	1	2							
39	RIGGER TEAM LEADER	1	1			1							
40	SUPERVISOR EQUIPMENT	8	8	6	4	14							
41	SUPERVISOR VALVES	3	4	3	3	6							
42	SUPERVISOR PIPING (CUT & REWELD)	6	6	5	4	11							
43	SUPERVISOR PIPING (TWR)	5	7	5	5	10							
44	SUPERVISOR WELDING	2	1	1	1	3							
45	SUPERVISOR HYDROJETTING	1	0	1	0	2							
46	SUPERVISOR RIGGING	4	3	4	4	8							
47	SUPERVISOR (CIVIL)	2	2	1	1	3							
48	SUPERVISOR (E & I)	2	2	1	1	3							
E&P													
49	E&P COORDINATORS	1	1	1	1	2							
50	E&P SUPERVISOR	1	2	1	1	2							
51	E&P ASSISTANTS	2	2	2	2	4							
52	MECHANIC	2	4	2	2	4							
COMMERCIAL& ACCOUNTS													
53	SUBCONTRACTS COORDINATOR	1	1			1							
54	CONTRACTS COORDINATOR	1	1			1							
STORES													
55	STORE IN CHARGE	1	1	1	1	2							
56	STORE SUPERVISOR	1	1	1	1	2							
57	STORE KEEPER DAY	2	2	2	2	4							
58	STORE HELPERS	4	0	3	0	7							
ADMINISTRATION													
60	ADMINISTRATION INCHARGE	1	1	1	1	2							
61	ADMIN SUPERVISOR	2	2	2	2	4							
62	ADMIN ASSISTANTS	2	3	2	3	4							
63	TIME KEEPERS	2	2	2	2	4							
64	GATEPASS COORDINATOR	2	2	2	2	4							
65	MANPOWER COORDINATOR	1	1	1	1	2							
66	TEA BOY	2	2	1	2	3							
67	JANITOR	5	8	4	5	9							
68	TRANSPORT COORDINATOR	1	1	1	1	2							
69	DRIVERS / OPERATORS (OWN+RENTLE)	20	27	10	17	30							
E&I													
70	INCHARGE E&I DAY	1	1			1							
71	INCHARGE E&I NIGHT			1	1	1							
TOTAL - MANPOWER													
B - DESCON DIRECT MANPOWER													
	PLAN	DAY	PLAN	NIGHT	PLAN	TOTAL							
		ACT		ACT		ACT							
1	LEAD WORKER	118	120	80	79	198							
2	FABRICATOR	36	47	24	33	60							
3	FITTER	164	267	144	204	308							
4	FITTER (E&I)	29	5	6	6	35							
5	WELDER	36	32	22	26	58							
6	HYDROJETTER	4	10	0	3	4							
7	RIGGER	42	60	20	32	62							
8	MILLWRIGHT	3	8	0	0	3							
9	FIRE WATCHER / HOLE WATCHER	48	64	20	23	68							
10	ELECTRICAL TECHNICIAN	5	10	5	3	10							
11	INSTRUMENT TECHNICIAN	6	9	4	2	10							
12	MASON	3	5	0	0	3							
13	CARPENTER	3	5	0	0	3							
14	STEEL FIXER	3	3	0	0	3							
15	HELPER	12	31	4	4	16							
16	HELPER (Cleaning)	36	39	12	14	48							
TOTAL - MANPOWER													
							548	715	341	429	889	1144	



MANPOWER & EQUIPMENT DETAIL REPORT

Wednesday, February 15, 2017

MANPOWER & EQUIPMENT STATUS						EQUIPMENT	
C - MANPOWER SUPPLY							
	DAY		NIGHT		TOTAL		
	PLAN	ACT	PLAN	ACT	PLAN	ACT	
1 FIELD COORDINATOR	6	6	5	5	11	11	
2 SUPERVISORS RIGGING	2	2	2	2	4	4	
3 TECHNICAL CLERK	4	4			4	4	
4 LEAD WORKER	91	91	52	52	143	143	
5 PIPE FITTER	102	102	71	71	173	173	
6 PIPE FITTER (E&I)	13	13	5	5	18	18	
7 INSTRUMENT TECHNICIAN	23	23			23	23	
8 ELECTRICAL TECHNICIAN	21	21			21	21	
9 ELECTRICIAN					0	0	
10 FABRICATOR	7	7	7	7	14	14	
11 WELDER	7	7	7	7	14	14	
12 RIGGER	25	25	12	12	37	37	
13 MACHINIST					0	0	
14 FIRE WATCH	4	4	4	4	8	8	
15 HOLE WATCH	3	3	3	3	6	6	
16 TECHNICAL LABOR	25	25	25	25	50	50	
17 CARPENTER					0	0	
18 TRAINER	2	2			2	2	
19 ROTARY EQPT TECHNICIAN					0	0	
20 MILLRIGHT TECHNICIAN					0	0	
21 FLAGMAN	4	4	2	2	6	6	
22 CRANE/FORKLIFT OPERATORS	7	7	6	6	13	13	
23 FORKLIFT OPERATORS WAREHOUSE					0	0	
TOTAL - MANPOWER	346	346	201	201	547	547	
D - SUBCONTRACTOR MANPOWER							
	DAY		NIGHT		TOTAL		
	PLAN	ACT	PLAN	ACT	PLAN	ACT	
1 INECO	200	135	150	51	350	186	
2 PRETECT /TRISTAR	30	6	30	7	60	13	
3 D/COTECH	50	25	30	11	80	36	
4 SIEVERT	10	8	10	8	20	16	
5 HAND SERVICES	10	6	10	0	20	6	
6 SEASHORE	5	8	5	7	10	15	
7 ALFANOUS/OTHERS	10	56	10	30	20	86	
8 EAST COAST	5		5		10	0	
TOTAL - MANPOWER	315	244	245	114	560	358	
GRAND TOTAL	1353	1461	892	851	2245	2312	

Archives from Personal Files

[illegible]

[illegible]

SN	TANO	TAG	Description	Type	LT&T	Blinding	Manways/ Covers Removal	Ventil	As Open Inspection/Int ernal Scaffolding	Remove Internals	Cleaning	Detailed Inspection/In stallation	Repair if any	Final insp.	Testing / Box up	De-blind/Bolt torqueing	Remarks
				79	76	74	74	73	72	72	72	68	65	53	47	21	
	SRU/AGRU			21	21	21	21	21	20	20	20	17	16	13	8	3	
44	T17QSME1210	QCC-08-TGT-95-114	HYDROGENATION REACTOR,WTS	Vessel	Done	Done	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A		8/20box up,
45	T17QSME1465	QCC-01-SRU-95-11	SULFUR STOR TANK	Tank	Done	Done	Done	Done	Done	Done	Done	IP					Hydro jetting in progress
46	T17QSME1470	QCC-08-AGR-35-1	INLET FILTER SEPARATOR	Drum	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done		
47	T17QSME1426	QCC-08-AGR-95-101	H2S ABSORBER	Tower	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done		
48	T17QSME1427	QCC-08-AGR-95-102	MDEA REGENERATOR	Drum	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	IP	De-blinding and bolt torque tightening in progress
49	T17QSME1475	QCC-08-AGR-95-103	CO2 ABSORBER	Tower	Done	Done	Done	Done	Done	Done	Done	Done	IP				Inspection done, Demister pad installation in progress
50	T17QSME1476	QCC-08-AGR-95-302	MDEA REGENERATOR REFLUX DRUM	Drum	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done		
51	T17QSME1477	QCC-08-AGR-95-305	MDEA SUMP TANK	Drum	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	IP	De-blinding and bolt torque tightening in progress
52	T17QSME1478	QCC-08-AGR-95-307	AMINE REGENERATOR REFLUX DRUM	Drum	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	IP	De-blinding and bolt torque tightening in progress
53	T17QSME1479	QCC-08-SRU-36-101	THERMAL REACTOR	Reactor	Done	Done	Done	Done	Done	Done	Done	Done	Done	IP			Refectory job done final inspection to be done
54	T17QSME1480	QCC-08-SRU-36-201	THERMAL REACTOR	Reactor	Done	Done	Done	Done	Done	Done	Done	IP					Refectory job is in progress by INECO
55	T17QSME1483	QCC-08-TGT-36-102	TGTU TAIL GAS HEATER,KTI	Heater	Done	Done	Done	Done	Done	Done	Done	Done	IP				Refectory job yet to be started
56	T17QSME1484	QCC-08-TGT-36-103	THERMAL INCINERATOR AND STACK - TRAIN 10	Incinerator	Done	Done	Done	Done	Done	Done	Done	Done	Done	IP			Refectory job done final inspection to be done
57	T17QSME1485	QCC-08-TGT-36-203	THML INCINERATOR AND STACK - TRAIN 200	Incinerator	Done	Done	Done	Done	Done	Done	Done		IP				Refectory job is in progress by INECO
58	T17QSME1486	QCC-08-TGT-95-115	QUENCH GAS SEPARATOR,WTS	Drum	Done	Done	Done	Done	Done	Done	Done	Done	Done	IP			New demister pad received by today Anhabib hydro jetting done cleaning required by Qchem
59	T17QSME1463	QCC-08-TGT-95-106	QUENCH TOWER,WTS	Tower	Done	Done	Done	Done	Done	Done	IP						Cleaning in progress
60	T17QSIN0678	QCC-01-INT-43-71618	LOOP,ACID GAS FLRE 61-163 PILOT #3	Flare	Done	N/A	N/A	N/A									Pulley arranging for removal of assembly
61	T17QSME1640	QCC-08-SRU-95-113	ACID GAS SEPARATOR	Vessel	Done	Done	Done	Done	Done	Done	Done	Done	Done	IP			Belzona work done final inspection to be done
62	T17QSME1641	QCC-08-SRU-95-213	ACID GAS SEPARATOR	Vessel	Done	Done	Done	Done	Done	Done	Done	Done	Done	IP			Belzona work done final inspection to be done / Nozzel welding to be done
63	T17QSME1405	QCC-08-AGR-35-6	AGRU- Amine Flash Drum (CO2 Absorber)	Column	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done		
65	T17QSME1338	Seal Legs	Seal Legs	Filters	Done	Done	Done	Done	Done	Done	IP						Seal leg shifting on yard in progress for Hydro jetting
	UTILITY			12	11	11	11	10	10	10	10	9	9	4	4	3	4/12 box up
63	T17QUME9542	QCC-02-CAU-95-9	SPNT CSTC STORAGE TANK	Tank	Done	Done	Done	Done	Done	Done	IP						Chemical Cleaning IP(Qchem)
64	T17QUME1007	QCC-02-CON-95-352	CDST FLASH DRUM	Vessel	Done	Done	Done	Done	Done	Done	Done	Done	IP				(Welding of elbow 6"&8" completed, Plate patch up remaining)
65	T17QUME1009	QCC-02-BFW-95-351	DEAERATOR	Vessel	Done	Done	Done	Done	Done	Done	Done	Done	IP				R STAMP JOB CARRIED OUT (Nozzle welding in progress)
66	T17QUME1010	QCC-02-CON-95-2	POLISHED WATER TANK	Tank	Done	Done	Done	Done	Done	Done	Done	Done	IP				Sand Blasting & painting to be started(Inspection in progress from 4 days)
67	T17QUME1055	QCC-02-BFW-95-350	DEAERATOR TANK	Vessel	Done	Done	Done	Done	Done	Done	Done	Done	IP				R STAMP JOB CARRIED OUT (Nozzle welding in progress)
68	T17QUME1056	QCC-09-UTL-95-421	COOLING WATER BUFFER DRUM	Vessel	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	
69	T17QUME0845	QCC-09-UTL-97-908	SEA WATER SCREENING SYSTEM	SW Screen	Done	Done	Done	Done	Done	Done	Done	IP	IP				
70	T17QUME1024	QCC-01-UTL-95-411	COMPRESSED AIR BUFFER DRUM	Vessel	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	
71	T17QUME1002	QCC-02-CAU-67-268	SPNT CSTC SUMP PUMP (AIR DR)	Sump	Done	Done	IP										
72	T17QUME0846	QCC-09-UTL-67-2	OUTFALL CHANNEL SAMPLE PUMP	SW Screen	Done	Done	Done	Done	Done	Done	Done	Done	Done	IP	IP		
73	T17QUME1537	QCC-01-UTL-61-161	ETHYLENE UNIT FLARE PILOT 1A	Flare	Done	Done	NR	NR	Done	Done	Done	Done	Done	Done	Done	Done	MECHANICAL WORK COMPLETED
74	T17QUME1538	QCC-01-UTL-61-162	POLYETHYLENE UNIT FLARE	Flare													Not Released Yet
	HEXENE			1		1	1	1	1	1	1	1	1	1	1	0	
75	T17QHME0784	QCC-03-RCY-16-135	ETHYLENE RECYCLE COMPRESSOR	Filter	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done	Done		
Total Equipment Done (DONE) In Progress (IP) Not Required (NR) 77 83%																	
		76	75	72	72	73	73	69	63	53	46	46	11				
		0	0	1	0	0	0	4	5	12	7	1	10				
		0	0	1	1	0	0	0	0	0	0	0	0				
		76	75	74	73	73	73	73	68	65	53	47	21				
		99%	97%	96%	95%	95%	95%	95%	88%	84%	69%	61%	27%				



VALVES SUMMARY



CONTROL VALVES SUMMARY

14-Feb-17

Total	173	173	172	88	88	88
OVERALL	TOTAL VALVES	REMOVE VALVES	SHIFTED TO W/S	SERVICES	SHIFTED TO SITE	RE-INSTALLED
ETHYLENE	49	49	48	21	21	21
POLYETHYLENE	74	74	74	43	43	43
SRU	21	21	21	11	11	11
UTILITY	28	28	28	12	12	12
HEXENE	1	1	1	1	1	1

MECHANICAL SERVICING VALVES SUMMARY

Total	265	264	254	132	130	119
OVERALL	TOTAL VALVES	REMOVED	SHIFTED TO W/S	SERVICES	SHIFTED TO SITE	RE-INSTALLED
ETHYLENE	8	8	8	0	0	0
POLYETHYLENE	133	133	123	62	61	61
SRU	12	12	12	0	0	0
UTILITY	112	111	111	70	69	58

MECHANICAL REPLACEMENT VALVES SUMMARY

Total	160	144	143	0	110	98
OVERALL	TOTAL VALVES	REMOVED	OLD VALVE SHIFTING	SERVICES	NEW VALVE SHIFTING AT SITE	RE-INSTALLED
ETHYLENE	16	10	10	NA	9	9
POLYETHYLENE	75	68	68	NA	51	40
HEXENE	2	0	0	NA	0	0
UTILITY	38	37	37	NA	27	27
SRU	29	29	28	NA	23	22

Grand Total	586					
Total Till Yesterday		494	491	132	211	201
Total Today		581	569	220	328	305
For the Day Removal		87	78	88	117	104
