

CLIENT : - Oman Refineries & Petrochemical Industries Company (ORPIC),

Mina Al Fahal Refinery - Muscat

Contract No. 151/2011 (E-1375 - STS)

Health, Safety & Environment

Key Performance Indicator	Target / day	Today	Cummulative
Fatality	0	0	
Lost Time Incident (LTI)	0	0	
Restricted Work Case (RWC)	0	0	
Medical Treatment Case (MTC)	0	0	
First Aid Case (FAC)	0	0	2
Near Miss (NM)	< 5	0	1
Vehicle Incident (VI)	0	0	
Property Damage (PD)	0	0	2
Unsafe Acts	0	1	22
Unsafe Conditions	0	0	5

Issue Date : 1-Apr-12
 Days completed : 13
 Days remaining : 12
 Cut off date : 1-Apr-12
 Cut off time : 16:00:00 Hrs

OVERALL PROGRESS

COMPL.

49.92%



BAL.

50.08%

DAILY PROGRESS REPORT

Overall progress	Previous Cumm	Today	Cummulative
Planned percentage	49.38%	6.32%	55.70%
Actual Percentage	45.70%	4.22%	49.92%
Variance Percentage	-3.68%	-2.09%	-5.78%

Manpower

Total Manpower	Today status		Cummulative Manhours Previous	Cummulative Manhours (total)
	Manpower	Manhours		
STS & Contractors	1228	14736	215,664	230,400

HSE Updates :

- safety audits and walk-around being conducted in the refinery at all areas.

Major Highlights for the day :

C-8351 Boxed up.
 C-8202 Boxed up.
 F-8201/02/03/04 Pre inspection of burner support ring completed.
 F-8201/02/03 Internal convectional tube cleaning completed.
 F-8201/02/03 spring hanger servicing and greasing done.
 C-8001 1 to 32 cleaning and inspection completed.53 to 54 cleaning in progress.
 C-8007 Cleaning 100%.
 C-8401 Cleaning 100%.
 C-8302 1 to 32 cleaning and inspection completed.
 F-8001 Convection, stack section, damper and internal cleaning in progress and IFR in progress.
 F-8002 Burner assembly and tube cleaning in progress.
 C-8240 Cleaning completed and offered for inspection.
 C-8131 Internal tray man way boxed up.
 F-8130 Internal cleaning in progress.(40%)
 F-8131 IFR in progress. (90%)
 F-8240 Burner cleaning in progress (30%) and internal scaffolding on top side in progress.

Areas of concerns :

- The reason for the negative variance in all the areas are :-
 - delayed receipt of gaskets is effecting box-up and hydrotesting of equipments.
 - Area - 3 and 5 will be having late handover for maintenance, this is also contributing to the negative variance on the individual areas and the overall progress.
 - Streamlining the requirement of gaskets so far issued and then will come up with the remaining required quantities.
 - U-8250 late handover due to operational problems.
 - prefabrication / piping works not progressed as per plan due to non-availability of free issue material which is contribution a major weightage in the individual areas and the overall progress.
 - even though inspection completed on many equipments the following IFRs / FIs are not being issued for further progress of works.
 - Awaiting decision from ORPIC with regards to awaiting of mellapax for C-8401, awaiting decision for damaged plug of E-8069A, E-8138B.
 - Awaiting for material for loading arms .
 - Awaiting anodes for channel head and floating head that is holding up hydrotest related activities.
 (PLEASE SEE THE ATTACHED LIST OF NON-AVAILABILITY OF GASKETS THAT ARE HOLDING UP BOX-UP OF EQUIPMENTS AND HYDROTEST)

Attachments

1. Percentage completion (Unit wise)
2. Overall summary of static equipments and miscellaneous equipments
3. Overall progress curve
4. Mobile equipment summary

Prepared by :

Planning Team (STS)

Distri. :

ORPIC, STS (Management), STS (Site)

AREAS OF CONCERN

AWAITING GASKETS

SIno	EQPT Tag	Gasket status	QTY	Remarks
1	E-8360	FLOATING HEAD COVER GASKET. CHANNEL GASKET. CHANNEL COVER GASKET	1EACH	30-03-2012
2	E-8209	SHELL COVER GASKET BELLOW GASKET	1EACH	30-03-2012
3	E-2104A/B	PLUG GASKET	756	30-03-2012
4	E-2105	PLUG GASKET	316	30-03-2012
5	E-2312A/B	PLUG GASKET	432	30-03-2012
6	E-2315A/B	PLUG GASKET	744	30-03-2012
7	E-8069 A/B/C	PLUG GASKET	2400	31-03-2012
8	E-8138 A/B	PLUG GASKET	936	31-03-2012
9	E-8131 A/B	PLUG GASKET	1280	31-03-2012
10	E-8241 A/B/C/D	PLUG GASKET	4384	31-03-2012
11	E-8041 A/B/C/D	PLATE AFC	8	31-03-2012
12	E-8407	PLATE AFC	2	31-03-2012
13	E-8354	NOT AVB		04/01/2012
14	E-8203	SINGE PARTICIAN COVER GASKET	1	04/01/2012
15	E-8214	COVER GASKET	1	04/01/2012
16	E-8204	ANODE		04/01/2012
17	E-8221	ANODE		04/01/2012
18	E-8222	ANODE		04/01/2012
19	E-8223	ANODE		04/01/2012
20	E-8224	ANODE		04/01/2012

Percentages (Unit Wise & Miscellaneous Works)	Wt %	Cumm. Planned %	Cumm. Actual %	Var %
OVERALL PROGRESS PERCENTAGE	100.00%	55.70%	49.92%	-5.78%
Area - 01 - (20-Mar-12 to 13-Apr-12 - 25 days)	25.82%	66.11%	58.97%	-7.15%
Unit - 8000 Crude Distillation Unit (CDU)	21.82%	66.92%	59.27%	-7.65%
Unit - 8300 Merox Unit	2.21%	75.20%	77.96%	2.77%
Unit - 8400/50 Sour Water Stripping Unit (SWS)	1.79%	36.55%	31.82%	-4.73%
Area - 02 - (20-Mar-12 to 13-Apr-12 - 25 days)	25.20%	53.19%	46.11%	-7.08%
Unit - 8200 Platformer Unit	17.09%	53.27%	47.30%	-5.96%
Unit - 8250 NGHR Unit	2.14%	61.88%	20.38%	-41.50%
Unit - 8350 Tail Gas / Depropaniser Unit (TG/DU)	1.77%	34.61%	41.90%	7.28%
Unit - 9200 Continuous Catalyst Regeneration (CCR)	4.20%	56.26%	56.08%	-0.18%
Area - 03 - (28-Mar-12 to 07-Apr-12 - 11 days)	8.48%	53.18%	43.30%	-9.88%
Unit - 8630/60 Fire Water System (FWS)	0.35%	56.45%	52.88%	-3.58%
Unit - 8680/90	0.14%	74.24%	72.73%	-1.52%
Unit - 8700/50 Utilities (UT)	3.28%	59.28%	42.66%	-16.61%
Unit - 8800/50 BFW / Condensate System	1.49%	35.17%	20.97%	-14.20%
Unit - 8900 Fuel Gas / Fuel Oil System (FG/FO)	1.54%	65.57%	52.40%	-13.17%
Unit - 8920/60 Yard Air / Instrument Air System	1.67%	43.35%	51.58%	8.23%
Area - 04 - (20-Mar-12 to 13-Apr-12 - 25 days)	34.17%	51.02%	50.56%	-0.45%
Unit - 2000 DHDS Unit	11.48%	53.38%	55.15%	1.76%
Unit - 2100 Amine Treating Unit (ATU)	2.63%	43.45%	37.18%	-6.27%
Unit - 2200 Sulphur Recovery Unit (SRU)	3.19%	46.73%	41.71%	-5.02%
Unit - 2300 Isomerisation Unit	5.86%	40.20%	39.72%	-0.48%
Unit - 8100 Naphtha Hydrotreating Unit (NHTU)	7.40%	64.96%	58.29%	-6.66%
Unit - 8240	3.62%	41.80%	55.31%	13.50%
Area - 05 - (28-Mar-12 to 07-Apr-12 - 11 days)	6.33%	51.82%	25.07%	-26.75%
Unit - 8500 Gasoline Blending Unit (GBU)	1.35%	59.19%	39.94%	-19.25%
Unit - 8550 Tank Farm (TF)	1.98%	50.11%	40.58%	-9.53%
Unit - 8600 Flare System (FS)	1.19%	49.14%	44.74%	-4.40%
Unit - 8640 Waste Water Treating (WWT)	1.81%	49.97%	13.71%	-36.26%

Static Equipment Status																		
Equipment Type	Total as per scope		Spaded	Opened (plugs / covers / manholes)	Removed internals (manways/demisters)	Pull bundle	Erected internal scaffolding	Cleaned internally (equipment / bundle)	Inspected	Repaired if any	Reinstalled (bundle	Pressure test (SHELL TEST)	Reinstalled internals (manways/demisters/ parts)	Pressure test (TUBE TEST)	Pressure test (FINAL TEST)	Dismantled internal scaffolding	Boxed up (plugs, covers / manholes)	Despaded
Column	19	nos.	19	19	19	N/A	19	16	12	0	N/A	N/A	8	N/A	N/A	8	7	0
Heat Exchanger	122	nos.	119	116	N/A	115	N/A	101	75	0	62	11	N/A	7	6	N/A	7	0
Fin Fan Cooler	39	nos.	39	39	N/A	N/A	N/A	29	14	0	N/A	N/A	N/A	N/A	4	N/A	4	4
Plate Exchanger	1	nos.	1	1	1	N/A	N/A	1			N/A				N/A	N/A		
Reactor	5	nos.	5	5	5	N/A	5	5	5	0	N/A	N/A	0	N/A	N/A	0	0	0
Furnace / Heater	15	nos.	15	15	15	N/A	15	5	1	0	N/A	N/A	0	N/A	N/A	0	0	0
Vessel	94	nos.	91	58	57	N/A	56	46	33	0	N/A	N/A	25	N/A	N/A	24	23	1
Ejector / Desuperhe	10	nos.	7	7	N/A	N/A	N/A	3	0	0	N/A	N/A	0	N/A	N/A	N/A	0	0
Tanks	7	nos.	6	6	6	N/A	6	5	5	0	N/A	N/A	4	N/A	N/A	4	4	0
Scrubber	6	nos.	6	6	N/A	N/A	N/A	6	0	0	N/A	N/A	N/A	N/A	N/A	N/A	0	0
Silencer	8	nos.	7	6	N/A	N/A	N/A	4	2	0	N/A	N/A	N/A	N/A	N/A	N/A	0	0
Miscellaneous	13	nos.	8	6	3													
Flare	2	nos.	2	2	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	2	
Flame Arrestor	4	nos.	4	4	4	N/A	N/A	2	2	0	N/A	N/A	1	N/A	N/A	N/A		
Filter	37	nos.	33	32	30	N/A	N/A	30	27	0	N/A	N/A	23	N/A	N/A	N/A	23	9
Waste Heat Boiler	2	nos.	2	2	0	N/A	0	0	0	0	N/A	N/A	0	N/A	N/A	N/A	0	0
Air Dryer	1	nos.	0	0	0	N/A	0	0	0	0	N/A	N/A	0	N/A	N/A	N/A	0	0
Loading Arm	2	nos.	0	0	0	N/A	0	0	0	0	N/A	N/A	0	N/A	N/A	N/A	0	0
Stack	1	nos.	N/A	1	N/A	N/A	1	0	0	0	N/A	N/A	N/A	N/A	N/A	0	0	N/A
Grand Total	390	nos.	364	325	140	115	102	253	176	0	62	11	61	7	10	36	70	14

Miscellaneous Equipments Status


Equipment Type	Total as per scope		Opened / removed	Transported to W/S	Overhauled / repaired	Inspected	Transported to Site	Box-up / reinstalled	Remarks
Relief Valves	293	nos.	240	208	167	167	167	133	
TE & TWs	1320	nos.	457	457	371	371	370	370	
Flow Orifice	140	nos.	118	117	78	78	78	24	
Level Instrument	260	nos.	152	151	0	0	0	0	
Control Valves	372	nos.	189	138	84	84	84	82	
Pipeline Replacement	70	nos.							
Isolation Valves	224	nos.	87	79	64	64	64	59	
Corroded Fasteners	790	nos.	64	N/A	N/A	N/A	N/A	64	
Quills	23	nos.	0	0	0	0	0	0	not identified
SW Lines	40	nos.	0	0	0	0	0	0	
CW Valves	19	nos.	0	0	0	0	0	0	
Painting of Pipelines	712	nos.	260	N/A	N/A	0	N/A	0	260 lines painted
Valve Servicing / Repacking or Replacement	141	nos.	0	0	0	0	0	0	
Rotating Equipment (Blinding & Deblinding)	34	nos.	34	N/A	N/A	N/A	N/A	0	
Electrical Works	116	nos.	0	N/A	N/A	0	N/A	N/A	
Engineering Works	4	nos.	0	N/A	N/A	0	N/A	N/A	
Static Equipment with Rotary	4	nos.	4	N/A	N/A	0	N/A	N/A	
Nitrogen Tank	3	nos.							
Inspection Work Request	130	nos.	0	N/A	N/A	0	N/A	N/A	
T-8771	1	nos.	1	1					
Grand total	4696	nos.	1606	1151	764	764	763	732	0




Special Technical Services (STS)
Oman Refineries & Petrochemical Industries Company (ORPIC)
OVERALL DAILY PROGRESS (S-Curve) - STS




	Day - 1	Day - 2	Day - 3	Day - 4	Day - 5	Day - 6	Day - 7	Day - 8	Day - 9	Day - 10	Day - 11	Day - 12	Day - 13	Day - 14	Day - 15	Day - 16	Day - 17	Day - 18	Day - 19	Day - 20	Day - 21	Day - 22	Day - 23	Day - 24	Day - 25	Day - 26
Date	20-Mar	21-Mar	22-Mar	23-Mar	24-Mar	25-Mar	26-Mar	27-Mar	28-Mar	29-Mar	30-Mar	31-Mar	1-Apr	2-Apr	3-Apr	4-Apr	5-Apr	6-Apr	7-Apr	8-Apr	9-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr
Cummulative Planned	2.33%	4.49%	6.86%	9.66%	13.60%	17.86%	22.30%	26.64%	32.36%	38.00%	43.53%	49.38%	55.70%	61.75%	67.25%	72.48%	77.54%	81.98%	85.66%	89.04%	92.41%	95.28%	97.44%	99.14%	100.00%	100.00%
Cummlative Actual	2.79%	5.45%	7.79%	10.78%	14.44%	17.97%	24.21%	27.55%	30.83%	35.12%	39.76%	45.70%	49.92%													
Daily Planned	2.33%	2.17%	2.37%	2.80%	3.94%	4.26%	4.44%	4.33%	5.72%	5.64%	5.53%	5.85%	6.32%	6.05%	5.50%	5.23%	5.05%	4.44%	3.68%	3.38%	3.38%	2.87%	2.16%	1.70%	0.86%	0.00%
Daily Actual	1.79%	2.66%	2.35%	2.98%	3.67%	3.52%	6.25%	3.34%	3.28%	4.29%	4.64%	5.94%	4.22%													

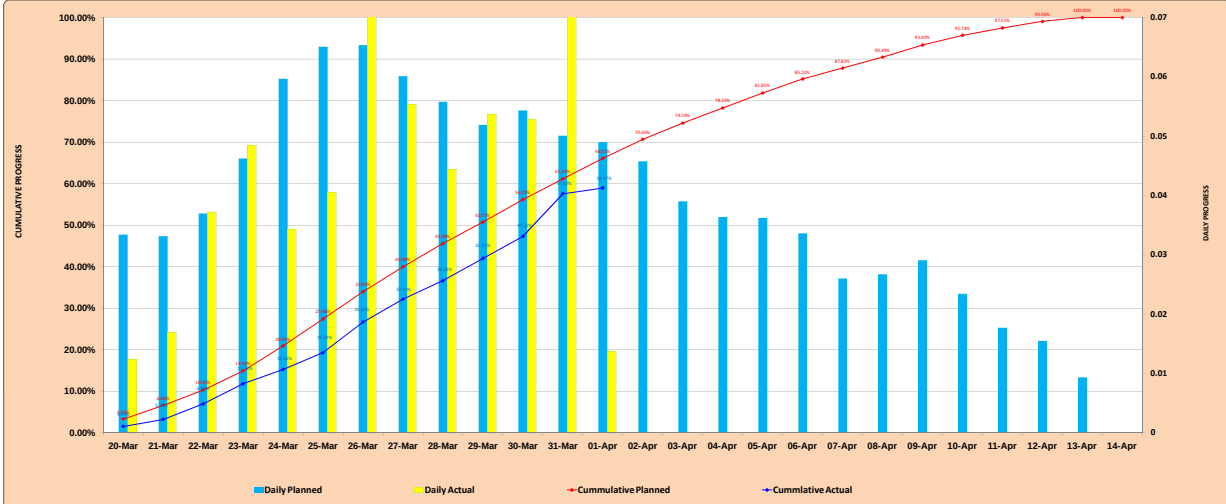

	Day -1	Day -2	Day -3	Day -4	Day -5	Day -6	Day -7	Day -8	Day -9	Day -10	Day -11	Day -12	Day -13	Day -14	Day -15	Day -16	Day -17	Day -18	Day -19	Day -20	Day -21	Day -22	Day -23	Day -24	Day -25	Day -26
Date	20-Mar	21-Mar	22-Mar	23-Mar	24-Mar	25-Mar	26-Mar	27-Mar	28-Mar	29-Mar	30-Mar	31-Mar	01-Apr	02-Apr	03-Apr	04-Apr	05-Apr	06-Apr	07-Apr	08-Apr	09-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr
Cumulative Planned	3.84%	6.56%	10.38%	14.58%	19.68%	25.28%	31.68%	38.68%	46.08%	53.68%	61.28%	68.68%	75.68%	82.08%	87.68%	92.08%	95.68%	98.08%	99.68%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%
Cumulative Actual	3.57%	6.29%	10.11%	14.31%	19.41%	25.01%	31.41%	38.41%	45.81%	53.41%	60.81%	68.01%	74.81%	81.21%	86.81%	91.21%	94.81%	97.61%	99.21%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%
Daily Planned	3.84%	2.72%	3.84%	4.20%	5.40%	5.60%	6.40%	7.00%	7.40%	7.60%	7.40%	7.20%	6.80%	6.40%	5.60%	4.80%	4.00%	3.20%	2.40%	1.60%	0.80%	0.00%	0.00%	0.00%	0.00%	0.00%
Daily Actual	3.54%	2.69%	3.72%	4.05%	5.25%	5.45%	6.25%	6.85%	7.25%	7.45%	7.25%	6.85%	6.45%	6.05%	5.25%	4.45%	3.65%	2.85%	2.05%	1.25%	0.45%	0.00%	0.00%	0.00%	0.00%	0.00%

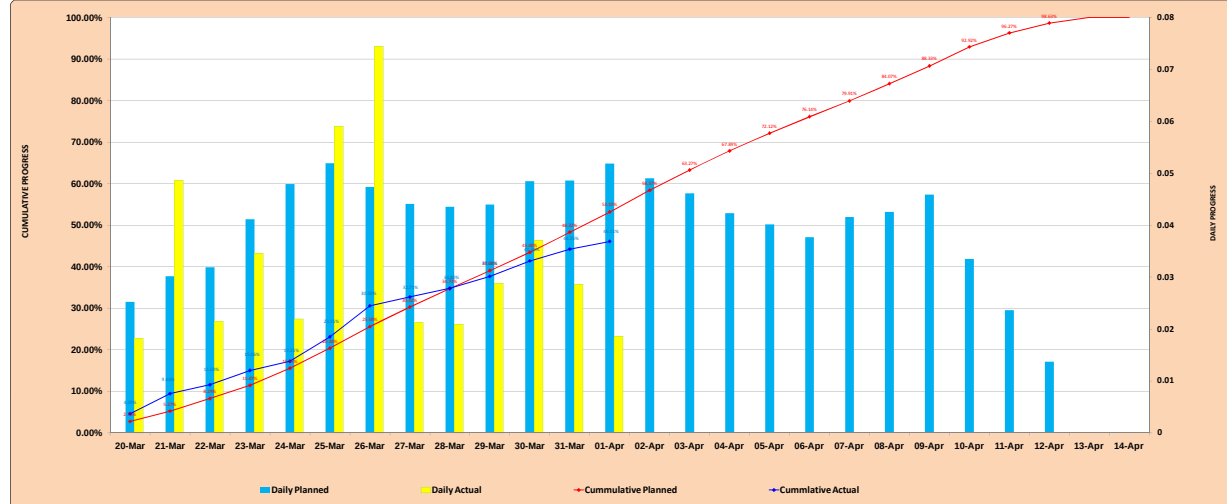


	Day -1	Day -2	Day -3	Day -4	Day -5	Day -6	Day -7	Day -8	Day -9	Day -10	Day -11	Day -12	Day -13	Day -14	Day -15	Day -16	Day -17	Day -18	Day -19	Day -20	Day -21	Day -22	Day -23	Day -24	Day -25	Day -26
Date	20-Mar	21-Mar	22-Mar	23-Mar	24-Mar	25-Mar	26-Mar	27-Mar	28-Mar	29-Mar	30-Mar	31-Mar	01-Apr	02-Apr	03-Apr	04-Apr	05-Apr	06-Apr	07-Apr	08-Apr	09-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr
Cumulative Planned	2.75%	5.27%	8.29%	11.47%	15.58%	20.38%	25.58%	30.92%	36.12%	41.72%	47.32%	52.92%	58.12%	63.32%	68.12%	72.92%	77.32%	81.72%	85.72%	89.72%	93.72%	97.72%	100.00%	100.00%	100.00%	
Cumulative Actual	4.00%	7.40%	11.40%	15.60%	20.00%	24.40%	28.80%	33.20%	37.60%	42.00%	46.40%	50.80%	55.20%	59.60%	64.00%	68.40%	72.80%	77.20%	81.60%	86.00%	90.40%	94.80%	99.20%	100.00%	100.00%	
Daily Planned	2.75%	2.52%	2.91%	3.13%	4.42%	4.70%	5.28%	5.76%	6.40%	6.80%	7.20%	7.60%	8.00%	8.40%	8.80%	9.20%	9.60%	10.00%	10.40%	10.80%	11.20%	11.60%	12.00%	12.40%		
Daily Actual	3.60%	3.80%	4.00%	4.40%	5.60%	5.60%	6.40%	6.80%	7.20%	7.60%	8.00%	8.40%	8.80%	9.20%	9.60%	10.00%	10.40%	10.80%	11.20%	11.60%	12.00%	12.40%	12.80%	13.20%		

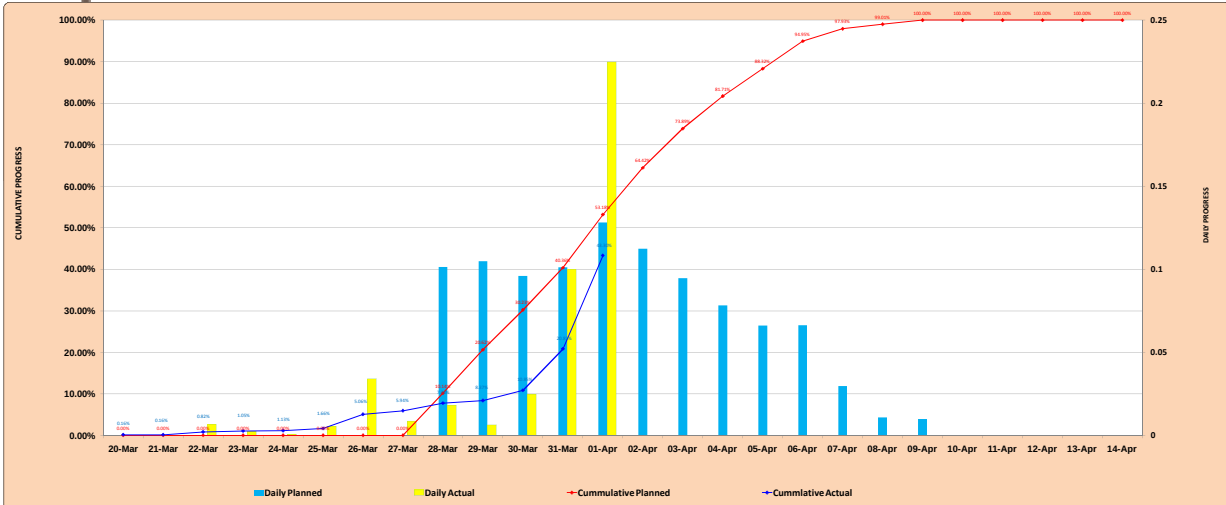

	Day -1	Day -2	Day -3	Day -4	Day -5	Day -6	Day -7	Day -8	Day -9	Day -10	Day -11	Day -12	Day -13	Day -14	Day -15	Day -16	Day -17	Day -18	Day -19	Day -20	Day -21	Day -22	Day -23	Day -24	Day -25	Day -26	
Date	20-Mar	21-Mar	22-Mar	23-Mar	24-Mar	25-Mar	26-Mar	27-Mar	28-Mar	29-Mar	30-Mar	31-Mar	01-Apr	02-Apr	03-Apr	04-Apr	05-Apr	06-Apr	07-Apr	08-Apr	09-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr	15-Apr
Cumulative Planned	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	
Cumulative Actual	0.16%	0.32%	0.48%	0.64%	0.80%	1.00%	1.16%	1.32%	1.48%	1.64%	1.80%	1.96%	2.12%	2.28%	2.44%	2.60%	2.76%	2.92%	3.08%	3.24%	3.40%	3.56%	3.72%	3.88%	4.04%	4.20%	
Daily Planned	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	
Daily Actual	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	



	Day -1	Day -2	Day -3	Day -4	Day -5	Day -6	Day -7	Day -8	Day -9	Day -10	Day -11	Day -12	Day -13	Day -14	Day -15	Day -16	Day -17	Day -18	Day -19	Day -20	Day -21	Day -22	Day -23	Day -24	Day -25	
Date	20-Mar	21-Mar	22-Mar	23-Mar	24-Mar	25-Mar	26-Mar	27-Mar	28-Mar	29-Mar	30-Mar	31-Mar	01-Apr	02-Apr	03-Apr	04-Apr	05-Apr	06-Apr	07-Apr	08-Apr	09-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr
Cumulative Planned	4.20%	8.20%	12.40%	16.40%	20.40%	24.40%	28.40%	32.40%	36.40%	40.40%	44.40%	48.40%	52.40%	56.40%	60.40%	64.40%	68.40%	72.40%	76.40%	80.40%	84.40%	88.40%	92.40%	96.40%	100.00%	
Cumulative Actual	3.90%	7.80%	10.90%	13.40%	17.00%	20.10%	23.10%	26.20%	28.90%	32.00%	35.00%	38.20%	41.20%	44.20%	47.20%	50.20%	53.20%	56.20%	59.20%	62.20%	65.20%	68.20%	71.20%	74.20%	77.20%	
Daily Planned	2.20%	1.97%	1.91%	2.35%	4.00%	4.00%	4.23%	4.60%	5.10%	5.30%	4.90%	4.90%	5.30%	5.30%	5.30%	5.30%	5.30%	5.30%	5.30%	5.30%	5.30%	5.30%	5.30%	5.30%	5.30%	
Daily Actual	2.60%	2.91%	2.29%	2.45%	6.96%	2.70%	5.13%	5.31%	4.89%	5.79%	5.80%	5.65%	5.65%	5.65%	5.65%	5.65%	5.65%	5.65%	5.65%	5.65%	5.65%	5.65%	5.65%	5.65%	5.65%	

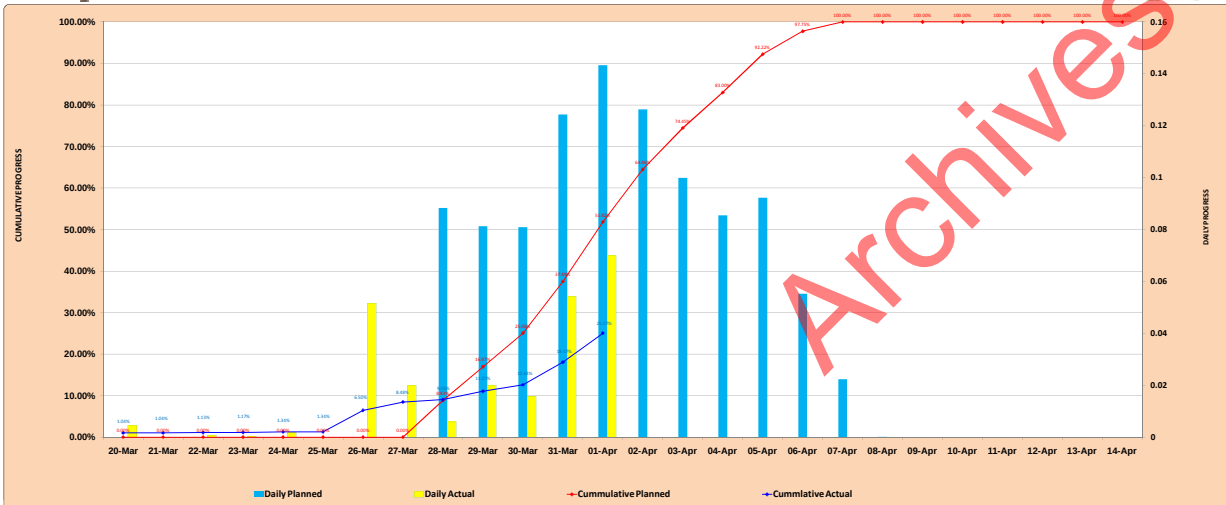

	Day -1	Day -2	Day -3	Day -4	Day -5	Day -6	Day -7	Day -8	Day -9	Day -10	Day -11	Day -12	Day -13	Day -14	Day -15	Day -16	Day -17	Day -18	Day -19	Day -20	Day -21	Day -22	Day -23	Day -24	Day -25	Day -26
Date	20-Mar	21-Mar	22-Mar	23-Mar	24-Mar	25-Mar	26-Mar	27-Mar	28-Mar	29-Mar	30-Mar	31-Mar	01-Apr	02-Apr	03-Apr	04-Apr	05-Apr	06-Apr	07-Apr	08-Apr	09-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr
Cumulative Planned	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	
Cumulative Actual	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	
Daily Planned	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	
Daily Actual	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	

Mobile Equipment Report

Equipment Details			Capacity	Planned	Actual
Total				93	101
CRANES		Mobile telescopic Crane	20-30T	1	1
		Mobile telescopic Crane	50 T	3	4
		Mobile telescopic Crane	100 T	1	1
		Mobile telescopic Crane	160T	1	1
		Mobile telescopic Crane	220 T	1	1
		Mobile telescopic Crane	800 T	1	1
		Mobile telescopic Crane	80T	1	1
LORRIES		Triler +Prime Mover	40 T	2	4
		TRUCK WITH HIAB (Inhouse)	10 T	2	3
		PLAIN TRUCK-Lorry Trk (Inhouse)	10 T	2	1
		Lorry Trk-3T- (Canter) (Inhouse)	1T	5	5
FL		FORK LIFT	3 T	1	1
		FORK LIFT	5 T	3	3
WL		Welding Machine	400 amp	10	3
		Welding Machine (Inhouse)	400 amp	9	3
CO MP.		Air Compressor	375 cfm	5	8
		Air Compressor	825 CFM	0	0
GEN'T R		Generator	110 KVA	2	2
		Generator (Inhouse)	10 KV	1	2
		Generator (Inhouse)	50 KV	0	0
JETTING/PULLING		High Pr Water Jetting Machine	15,000 PSI	7	7
		High Pr Water Jetting Machine	10,000 PSI	0	0
		High Pr Water Jetting Machine	15,000 PSI	0	0
		High Pr Water Jetting Machine	20,000 PSI	0	0
		INRO-EXRO Automatic Bundle Washing Machine (Inhouse)		1	2
		Heat Exchanger Bundle Puller (Inhouse)	40 T	1	1
		Heat Exchanger Bundle Puller (Inhouse)	45 T	1	1
TANK S		FUEL TANKER		1	1
		Water Tanker		1	1
		VACUUM TRUCK		2	2
CARS		SALOON CAR		3	4
		D/C PICK UP		1	1
		STATION WAGON(Inhouse)		1	1
		D/C PICK UP (Inhouse)		6	6
BUS		Bus	22 seat	3	2
		Bus	52 seat	13	14
		Bus (Inhouse)	22 seat	1	1

Scissor Lift

Miller Max 200 DX Welding Machines

Vacuum Unit

1

10

1
