

WEEKLY STATUS REPORT

WEEK/ YEAR – 40/2013 (5th Oct to 11th Oct 2013)

PROJECT – PURCHASE CONTRACT FOR TMMS

Contract Numbers: a)UI25688

b)UI25691

PO Numbers: a)4500033923

b)4500033927



CLIENT- QATAR SHELL GTL LTD.



**CONTRACTOR- QATAR ENGG &
CONST. CO. WLL**


PHASE- PLANNING AND PREPARATION

QCon PPT Team	Rishi Chaddha	Ahmed Nasr	11 th Oct 2013	Shell TA Team
Prepared	Checked	Approved	Date	Circulation

CONTENTS

SECTION		CONTENTS	PAGE
		INDEX	2
		PROJECT STATUS – WEEK 40 / 2013	3
		MTA-1 – CONSOLIDATED PLANNING PROGRESS CURVE	4
A		FGP BLOCK - ATTACHMENTS	
	i	Highlights	--
	ii	Schedule (Plan of Plans)	--
	iii	Progress Status	
	a	Work In Progress Table	--
	b	Progress Curve	5
	c	Equipment wise Status	6
	iv	Plan for the forthcoming week	--
B		GTL/ASU BLOCK - ATTACHMENTS	
	i	Highlights	--
	ii	Schedules (Plan of Plans)	--
	iii	Progress Status	
	a	Work In Progress Tables	--
	b	Progress Curves	7,8,9
	c	Equipment wise Status	10,11
	iv	Plan for the forthcoming week	--
C		SRU STRING OUTAGE	
	i	Highlights / Issues / Week's forecast	--
	ii	Scope / Schedule / Curve	12
	iii	Equipment wise Status	13,14
D		GENERAL – ATTACHMENTS	
	i	Highlights	--
	ii	Organization	
	a	Onboarding plan and status chart (Revised base-23rdJul)	--
	b	Updated Organogram – No Change	--
	c	Status of Interviews conducted to date	--
	iii	Documentation	
	a	Document Register Updates	--
	b	Summary of all documents	--
	iv	HSSE Section	
	a	HSSE Statistics	15
	b	SPSP Register	--
	v	Issues & Concerns (If Any)	--
	vi	Manhours (Planned / Spent / Forecast / earned) statistics	--

Note: All Progress figures being reported within this document are either Roser generated or Roser extracted. Cut off date and time is COB last day of week!

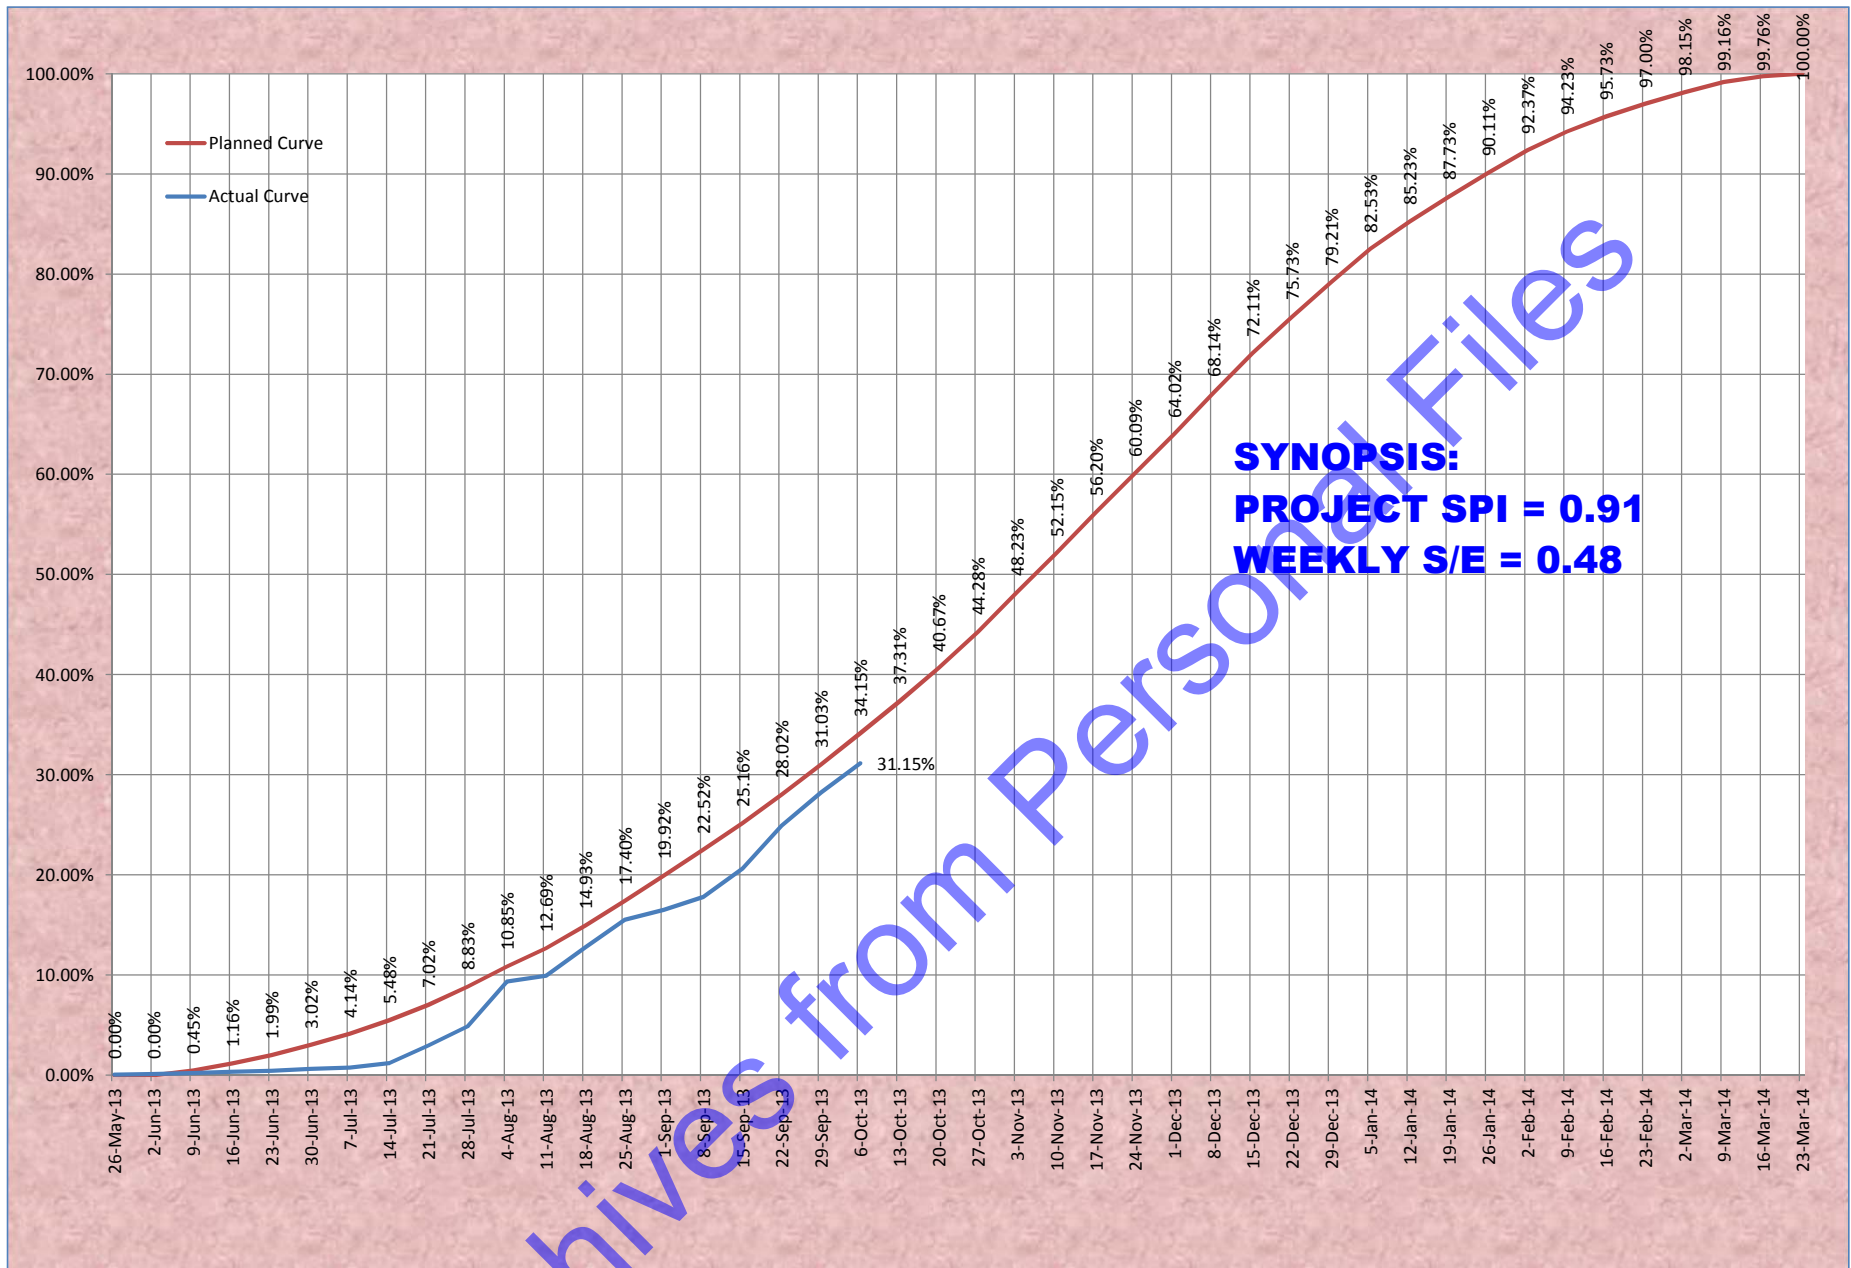

BLOCK WISE REPORT


PROGRESS CURVE / STATUS	QCON (FGP/GTL/ASU) - MTA-1						FGP BLOCK						GTL BLOCK						ASU BLOCK						GTL/ASU COMBINED						PROGRAM MAINTENANCE						
	A+B+C						A						B						C						B+C						D						
	PLAN	ACT	VAR	SPI	S/E	CPI	PLAN	ACT	VAR	SPI	S/E	CPI	PLAN	ACT	VAR	SPI	S/E	CPI	PLAN	ACT	VAR	SPI	S/E	CPI	PLAN	ACT	VAR	SPI	S/E	CPI	PLAN	ACT	VAR	SPI	S/E	CPI	
	34.15	31.15	-3.00	0.91	0.48	--	35.99	33.18	-2.81	0.92	0.56	--	32.43	26.48	-5.95	0.82	--	--	33.43	35.12	1.69	1.05	--	--	32.75	29.22	-3.53	0.89	0.48	--	41.75	42.07	0.32	1.01	0.35	--	
THIS WEEK	1) Regular meetings as per plan 2) Imran on Roser Study 3) New Planner Prasanth selected 4) Blind-IT pilot started in FGP 5)						1) Roser scopes=565, Started=513 2) 49 jobs Blinding Plan u/p 3) Muhanned -Blind-IT for FGP/SRU 4) Normal Workpacks and Addenda 5)						1) Roser Scopes = 425, Started = 303 2) Meeting held on Scope refine'mt 3) TIE-Ins scope surveys u/p 4) 47 jobs inserted in Blind-IT 5) Normal Workpacks and Addenda						1) Roser scopes=283, Started = 238 2) Only working on instrumentation 3) 4) 5)						1) Roser scopes=708, Started = 541 2) 318 jobs Blinding Plan u/p 3) 4) 5)						1) Roser scopes=112, Started = 83 2) Blind list - about 150 planned 3) Blind-IT training for Mehul 4) Working on TSOs, RVs & FVP 5) Regular daily meetings						
	NEXT WEEK	1) Misc. Internal Interviews 2) Roser exam for Imran - GTL PI 3) Yogesh - piping Engineer joins 4) Prashanth - planner joins 5)						1) 3 day work week 2) 3) 4) 5)						1) 3 day work week 2) 3) 4) 5)						1) This block will remain slow 2) 3) 4) 5)						1) More consentation on GTL Unit 2) 3) 4) 5)						1) E-0324 plan to commence 2) Column plan to commence 3) New items site surveys 4) 5)					
HOLDS/STOPS		1) Week 41 progress will drop due to lesser number of working days 2) 3) 4)						1) More L-2 scopes needed 2) Work forecast to slowdown in 3 weeks' time. Needs attention! 3) 4)						1) More L-2 Scopes needed 2) Resource refinement in Roser 3) Scope loading on Roser incomplete 4) 5)						1) More L-2 scopes needed 2) Resource refinement in Roser 3) Issues with Oxygen Services material booked 4) Scope loading on Roser incomplete						1) Resource refinement in Roser 2) Scope loading on Roser incomplete 3) More L-2 scopes needed 4) 5)						1) waiting for decision - TSO 2) Waiting for decision - FVP temp. 3) None L-2 scopes from integrity 4) 5)					
	ATTACHMENT	1) None 2) 3) 4) 5) OTHERS (PROGRESS CURVE)					x	1) UPDATED SCHEDULE 2) EQUIPMENT WISE STATUS 3) ONGOING WORKS LIST 4) CRITICAL LIST 5) OTHERS (PROGRESS CURVE)					x	1) UPDATED SCHEDULE 2) EQUIPMENT WISE STATUS 3) ONGOING WORKS LIST 4) CRITICAL LIST 5) OTHERS (PROGRESS CURVE)					x	1) UPDATED SCHEDULE 2) EQUIPMENT WISE STATUS 3) ONGOING WORKS LIST 4) CRITICAL LIST 5) OTHERS (PROGRESS CURVE)					x	1) UPDATED SCHEDULE 2) EQUIPMENT WISE STATUS 3) ONGOING WORKS LIST 4) CRITICAL LIST 5) OTHERS (PROGRESS CURVE)					x	1) UPDATED SCHEDULE 2) EQUIPMENT WISE STATUS 3) ONGOING WORKS LIST 4) CRITICAL LIST 5) OTHERS (PROGRESS CURVE)					x

GENERAL REPORTS

ONBOARDING STATUS CURVE	DAILY WORK PRODUCED PER BLOCK	L2-Scope receipt Status	GENERAL UPDATED ATTACHMENTS		ISSUES AND CONCERNS																																																							
<table border="1"><caption>Onboarding Status Curve Data (October)</caption><thead><tr><th>Metric</th><th>Value</th></tr></thead><tbody><tr><td>Planned Numbers</td><td>52</td></tr><tr><td>Selected / identified</td><td>64</td></tr><tr><td>Expected to Arrive</td><td>52</td></tr><tr><td>Actuals On Board</td><td>33</td></tr></tbody></table>	Metric	Value	Planned Numbers	52	Selected / identified	64	Expected to Arrive	52	Actuals On Board	33	<table border="1"><caption>Daily Work Produced Per Block Data</caption><thead><tr><th>Date</th><th>GTL/ASU</th><th>FGP</th><th>SRU</th></tr></thead><tbody><tr><td>5-Oct</td><td>115.04</td><td>73.6</td><td>87.6</td></tr><tr><td>6-Oct</td><td>89.2</td><td>57.2</td><td>45.62</td></tr><tr><td>7-Oct</td><td>129.46</td><td>140.82</td><td>62.78</td></tr><tr><td>8-Oct</td><td>141.92</td><td>83.04</td><td>26.4</td></tr><tr><td>9-Oct</td><td>113</td><td>108</td><td>27.2</td></tr><tr><td>10-Oct</td><td>105.8</td><td>67.46</td><td>28.32</td></tr></tbody></table>	Date	GTL/ASU	FGP	SRU	5-Oct	115.04	73.6	87.6	6-Oct	89.2	57.2	45.62	7-Oct	129.46	140.82	62.78	8-Oct	141.92	83.04	26.4	9-Oct	113	108	27.2	10-Oct	105.8	67.46	28.32	<table border="1"><caption>L2-Scope receipt Status Data</caption><thead><tr><th>Category</th><th>L2-received</th><th>Scopes</th></tr></thead><tbody><tr><td>SRU</td><td>0</td><td>102</td></tr><tr><td>MTA-1 Total</td><td>39</td><td>1552</td></tr><tr><td>FGP</td><td>18</td><td>619</td></tr><tr><td>ASU</td><td>4</td><td>436</td></tr><tr><td>GTL</td><td>17</td><td>497</td></tr></tbody></table>	Category	L2-received	Scopes	SRU	0	102	MTA-1 Total	39	1552	FGP	18	619	ASU	4	436	GTL	17	497	1) HSSE STATISTICS 2) DELIVERABLES REGISTER 3) SPSP REGISTER 4) MANHOURS FORECAST 5) INTERVIEW REGISTER 6) UPDATED ORGANOGRAM FLAWLESS / QUALITY SECTION Documents Submitted 1) Qcon's Qatar Factor Rev-2 2) ITP for RV Installation Meetings 1) Roser QC module alignment Currently Working 1) Assiting planners with w/packs Concerns 1) Roser access not yet given	1) AIM access for 4 people 2) Integrity to elaborate scopes 3) Access needed to shared folders 4) Miscellaneous Roser related issues are slowing progress 5) 6) 7) 8) CRITICAL ISSUES AND FORECASTS 1) Pending AIM Access 2) Integrity decisions on L-2 scopes 3) 4)
Metric	Value																																																											
Planned Numbers	52																																																											
Selected / identified	64																																																											
Expected to Arrive	52																																																											
Actuals On Board	33																																																											
Date	GTL/ASU	FGP	SRU																																																									
5-Oct	115.04	73.6	87.6																																																									
6-Oct	89.2	57.2	45.62																																																									
7-Oct	129.46	140.82	62.78																																																									
8-Oct	141.92	83.04	26.4																																																									
9-Oct	113	108	27.2																																																									
10-Oct	105.8	67.46	28.32																																																									
Category	L2-received	Scopes																																																										
SRU	0	102																																																										
MTA-1 Total	39	1552																																																										
FGP	18	619																																																										
ASU	4	436																																																										
GTL	17	497																																																										



SCOPE OF WORK				UNIT WISE SCOPE DISTRIBUTION BY COUNT														PROG BY COUNT		ADDENDA		PROGRESS BY MHRS			
Discipline	TOE	TOE Discreption	Scope_Count	00300	00600	00800	07200	10100	10200	10500	10600	10700	17700	19300	19400	19500	20600	IN ROSER	STARTED	IN ROSER	STARTED	PLANNED	EARNED		
M=Static																									
	COL	Column	7							6		1						7	7	2	2		232.7		
	EXR	Exchanger	16					1	8	1	1	5						15	15				231		
	FIL	Flow Indicator	14								4	10						5	4				23.8		
	FUR	Furnace	2							2								2	2				10.6		
	GWR	Guided Wave radar	8							4		4						8	8				58.8		
	PIP	Piping	74		1	3	1		21	9	29	9	1					70	64	8	4		1622.2		
	RLV	Relief Valve	62				1	1	3	11	29	17						62	60	13	12		669.08		
	RTD		3							1	2							3	0						
	TOP	Take Off Probe	26			2			4	5	6	9						26	25				170.4		
	UFM	Ultrasonic Flow Meter	5						1		1	3						5	5				25.7		
	VLV	Valve	53	1					10	7	35							52	50	11	11		1238.24		
	VMH	Vortex Monitoring HART	4							1		3						4	3				5.1		
	VSL	Vessel	12						3	1		6						12	12				98.4		
	ZZZ	Miscellaneous	16							4	10						2	4	2	1			30.5		
	Total		302	1	1	5	2	2	60	46	124	56	1	0	0	2	2	275	257	35	29		4416.52		
E=Elect																									
	CAB	Cabinet	17							1					12	4									
	SWB	Switchboard	12												4	8									
	XRF	Transformer	15												6	9									
	Total		44	0	0	0	0	0	0	1	0	0	0	22	21	0	0	0	0	0	0		0		
I=Instr																									
	ACT	Actuator	1							1								0	0				0		
	FLI	Flow Indicator	18							6	12							18	18	3			247.2		
	FVP	Flowserve Valve Posit'r	162		1	15	6	1	26	29	56	28						162	147	6			948		
	HWJ	Hardware Jumper	62			9	1		10	9	14	19						62	61				351.2		
	IPF		6			1		1	1	1	1	1													
	RTD		1								1														
	SOL	Solenoid Valve	1					1																	
	SSN	Speed Sensor	1								1														
	TRM	Transmitter	5					3		1	1							3	0				0		
	TRS	Trip Switch	7			1	1	1	1	1	1	1													
	ZZZ	Miscellaneous	1								1														
	Total		265	0	1	26	8	7	38	48	88	49	0	0	0	0	0	245	226	9	0		1546.4		
O=Others																									
	CAT	Catalyst related	1							1								1	1				6		
	ROT	Rotating	7							2	5														
	Total		8	0	0	0	0	0	0	3	5	0	0	0	0	0	0	1	1	0	0		6		
BLOCK TOTAL				619	1	2	31	10	9	98	98	217	105	1	22	21	2	2	521	484	44	29	6473	5968.92	
% Total Excluding Addenda																		84.17%		78.19%					
% Total Including Addenda																		91.28%		82.88%		35.99%		33.18%	

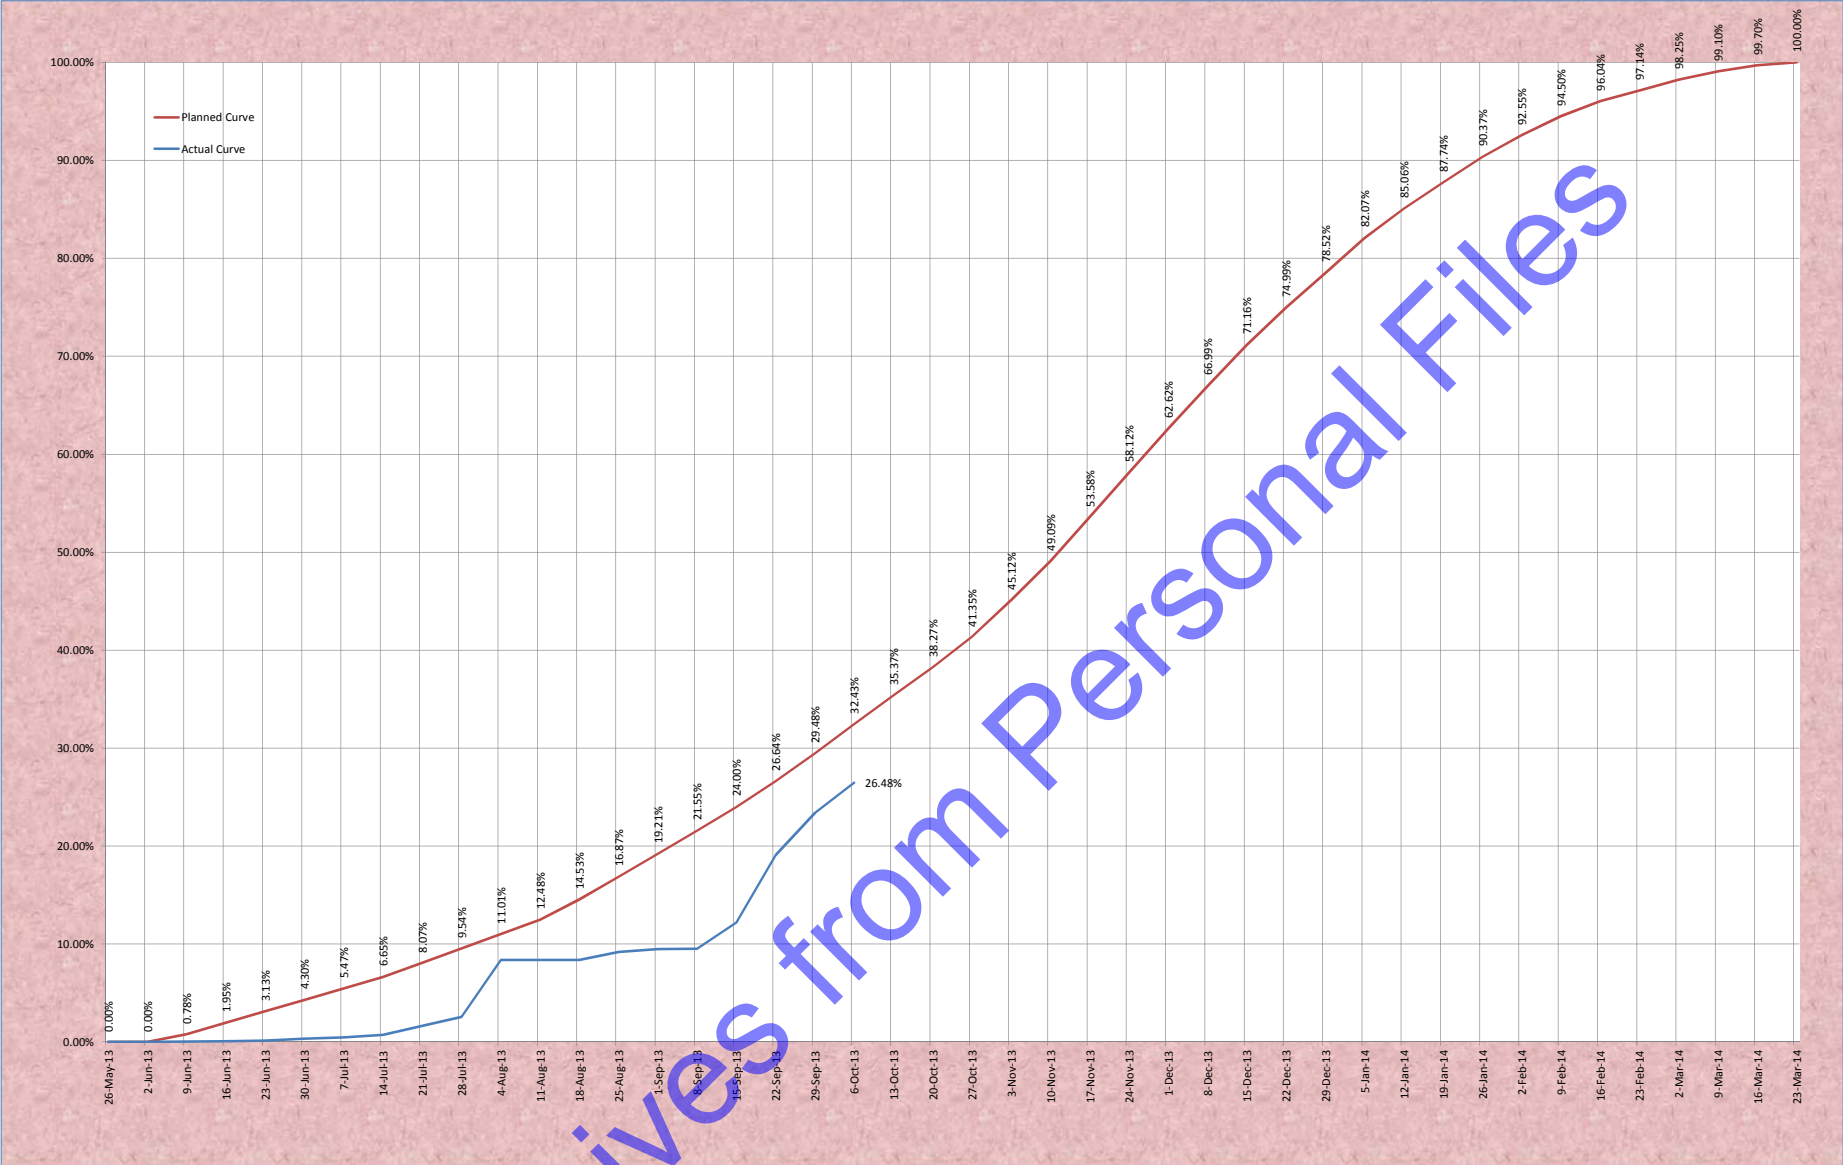






[illegible]

SCOPE OF WORK (ASU)				UNIT WISE SCOPE DISTRIBUTION BY COUNT																	CURRENT STATUS		ADDENDA		PROGRESS BY MHRS	
Discipline	TOE	TOE Discreption	Scope_Count	02000	12000	12100	12200	12300	12400	19300	19400	19800									IN ROSER	STARTED	IN ROSER	STARTED	PLANNED	EARNED
M=Static	COV	Columns & Vessels	25				4	3	8	10											10	7		3		27
	EXR	Exchanger	7						3	4											3	1				6
	PPV	piping & valves	51	1	4		7	9	16	14											9	11		4	3	77.6
	RLV	Relief Valve	194				60	37	60	37											161	172		23		2145.28
	ROT	Rotating Auxiliary	21				4	2	13	2																
	TOP	Take Off probe	1					1																		
	ZZZ	Miscellaneous	1		1																					
	Total		300	1	5	75	52	100	67	0	0	0									183	191		30	6	0
E=Elect	CAB	Cabinet	10							7	2	1														
	SWB	Switchboard	11							4	7															
	XER	Transformer	2								2															
	Total		23	0	0	0	0	0	0	11	11	1									0	0		0	0	0
I=Instr	ACT	Actuator	1		1																					
	CAB	Cabinet	1			1															0	0		1	0	
	CLV	Control valve	15		1	1			6	7																
	FLI	Flow Indicator	1						1																	
	FVP	Flowserve Valve Posit'r	70			21	14	20	15												17	25		52	16	400
	ZZZ	Miscellaneous	2			1	1		1																	
	Total		90	0	2	24	14	28	22	0	0	0									17	25		53	16	0
O=Others	ROT	Rotating	23			2	1	10	10													0				
	Total		23	0	0	2	1	10	10	0	0	0									0	0		0	0	0
UNIT TOTAL			436	1	7	101	67	138	99	11	11	1								200	216		83	22	2528	2655.88
																				% Total Excluding Addenda		45.87% 49.54%		33.43% 35.12%		
																				% Total Including Addenda		64.91% 54.59%				
BLOCK TOTAL			933																	708	541				7790.7	6952.62
																				75.88% 57.98%				32.75% 29.22%		

Archives from Personal Files

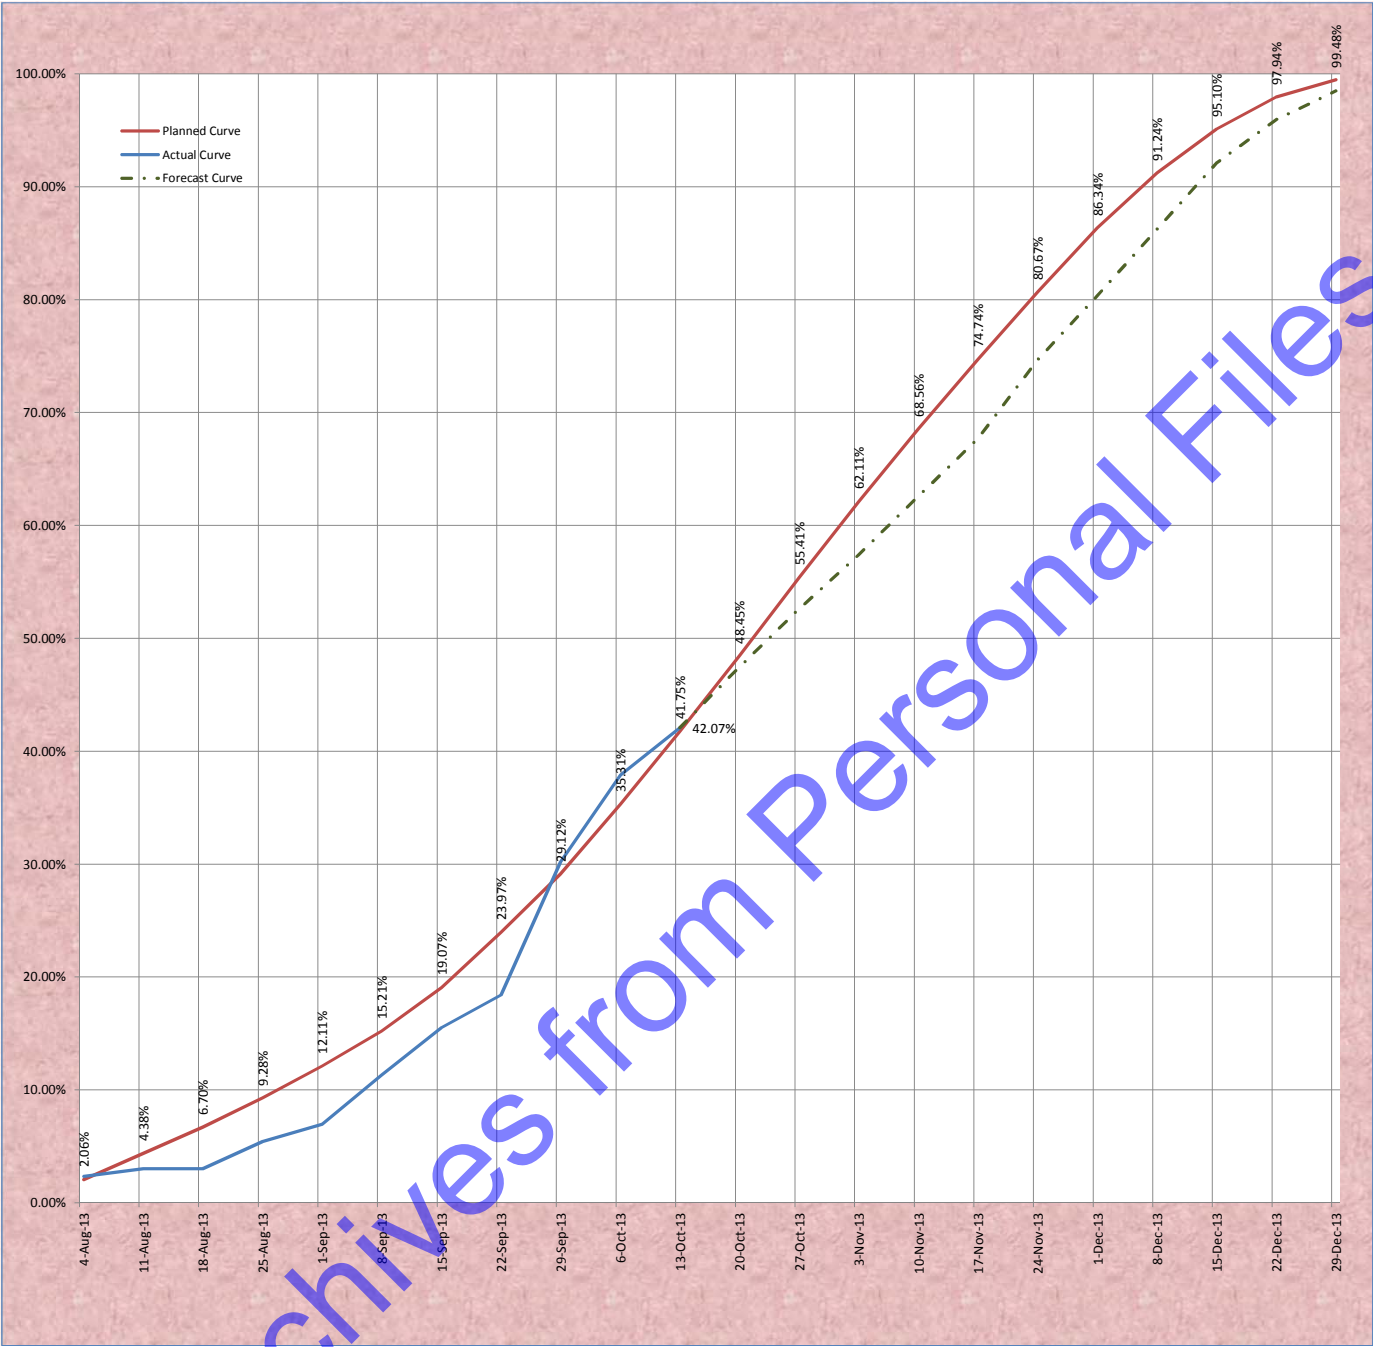

SCOPE	NR	COA	LOC	EQPT	STOP	POINT	NR	TO	HOURS	READY	WPHOLDER	% Complete
2013001	A081-0E0324				PF1300107			65		6.5		10.00%
2013002	A081-0K0421				PF1300106			30		18		60.00%
2013004	A081-004RV-21009-SV				PF1300103			16		10.88		68.00%
2013005	A081-004RV-21005-SV				PF1300102			16		10.88		68.00%
2013006	A081-004RV-21004-SV				PF1300101			16		10.88		68.00%
2013007	A081-004RV-21003-SV				PF1300100			16		10.88		68.00%
2013008	A081-004RV-21002-SV				PF1300099			16		10.88		68.00%
2013009	A081-003RV-21013-SV				PF1300098			16		10.88		68.00%
2013010	A081-003RV-21012-SV				PF1300097			16		10.88		68.00%
2013012	A081-003RV-21001-SV				PF1300096			16		10.88		68.00%
2013013	A081-003FI-21032-E				PF1300001			48		32.64		68.00%
2013014	A081-003PI-21030-TX				PF1300002			48		35.52		74.00%
2013015	A081-003PI-21046-TX				PF1300003			48		32.64		68.00%
2013016	A081-004FCA-21005-VC				PF1300006			48		4.8		10.00%
2013017	A081-004PDI-21047-TX				PF1300004			48		38.4		80.00%
2013018	A081-0C0420				PF1300014			60		6		10.00%
2013020	A081-0E0420				PF1300009			60		6		10.00%
2013025	A081-003QCA-21070-E				PF1300113			20		16		80.00%
2013026	A081-004QIA-21090-E				PF1300112			20		13.6		68.00%
2013027	A081-004QCA-21050-E				PF1300111			20		13.6		68.00%
2013028	A081-003QI-21030-E				PF1300110			20		18.4		92.00%
2013029	A081-003QI-21010-E				PF1300109			20		18.4		92.00%
2013040	A081-0F0421				PF1300010			20		2		10.00%
2013042	A081-004FC-10015-VC				PF1300079			20		16		80.00%
2013043	A081-003PCA-21096-VC				PF1300062			20		16		80.00%
2013044	A081-004PCA-21084-VC				PF1300061			20		16		80.00%
2013045	A081-004FCSA-21022-VC				PF1300060			20		16		80.00%
2013046	A081-004FCSA-21007-VC				PF1300059			20		16		80.00%
2013047	A081-004FCA-21018-VC				PF1300058			20		16		80.00%
2013048	A081-004FCA-21015-VC				PF1300057			20		16		80.00%
2013049	A081-004FCA-21003-VC				PF1300056			20		16		80.00%
2013050	A081-004FCA-21001-VC				PF1300055			20		16		80.00%
2013051	A081-004FC-21017-VC				PF1300054			20		16		80.00%
2013052	A081-004FC-21009-VC				PF1300053			20		16		80.00%
2013053	A081-004FC-21006-VC				PF1300052			20		16		80.00%
2013054	A081-003TCA-21506-VC				PF1300051			20		16		80.00%
2013055	A081-003TCA-21001-VC				PF1300050			20		16		80.00%
2013056	A081-003PDC-21023-VC				PF1300049			20		16		80.00%
2013057	A081-003FC-21001-VC				PF1300031			20		16		80.00%
2013058	A081-003FC-21004-VC				PF1300032			20		16		80.00%
2013059	A081-003FC-21008-VC				PF1300033			20		16		80.00%
2013060	A081-003FC-21013-VC				PF1300034			20		16		80.00%
2013061	A081-003FC-21028-VC				PF1300035			20		16		80.00%
2013062	A081-003FC-21030-VC				PF1300036			20		16		80.00%
2013063	A081-003FC-21031-VC				PF1300037			20		16		80.00%
2013064	A081-003FC-21049-VC				PF1300038			20		16		80.00%
2013065	A081-003FC-21069-VC				PF1300039			20		16		80.00%
2013066	A081-003FCA-21012-VC				PF1300040			20		16		80.00%
2013067	A081-003FCA-21034-VC				PF1300041			20		16		80.00%

2013068	A081-003LCA-21011-VC	PF1300042	20	16	80.00%
2013069	A081-003LCA-21013-VC	PF1300043	20	16	80.00%
2013070	A081-003LCA-21015-VC	PF1300044	20	16	80.00%
2013071	A081-003PCA-21025-VC	PF1300045	20	16	80.00%
2013072	A081-003PCA-21038B-VC	PF1300046	20	16	80.00%
2013073	A081-003PCA-21052-VC	PF1300047	20	16	80.00%
2013074	A081-003PDC-21018-VC	PF1300048	20	16	80.00%
2013075	A081-003TCA-21060-TX	PF1300114	12	9.6	80.00%
2013076	A081-0K0421	PF1300088	30	3	10.00%
2013077	A081-0P0321	PF1300087	30	27.6	92.00%
2013078	A081-0P0320B	PF1300086	30	27.6	92.00%
2013079	A081-0P0320A	PF1300085	30	27.6	92.00%
2013080	A081-0F0421	PF1300076	60	48	80.00%
2013081	A081-0F0421	PF1300108	60	48	80.00%
2013082	A081-0K0420	PF1300083	30	3	10.00%
2013083	A081-0A0420	PF1300122	120	12	10.00%
2013085	A081-0E0322	PF1300119	65	44.2	68.00%
2013086	A081-0F0320	PF1300120	120	81.6	68.00%
2013087	A081-004UZ-21209-VO	PF1300145	16	1.6	10.00%
2013088	A081-004UZ-21207-VO	PF1300144	16	1.6	10.00%
2013089	A081-004UZ-21206-VO	PF1300143	16	1.6	10.00%
2013090	A081-004UZ-21203-VO	PF1300142	16	1.6	10.00%
2013091	A081-004UZ-21201-VO	PF1300141	16	1.6	10.00%
2013092	A081-004UZ-21055-VO	PF1300140	16	1.6	10.00%
2013093	A081-004UZ-21054-VO	PF1300139	16	1.6	10.00%
2013094	A081-004UZ-21053-VO	PF1300138	16	1.6	10.00%
2013095	A081-004UZ-21051-VO	PF1300137	16	1.6	10.00%
2013096	A081-0F0421	PF1300123	105	10.5	10.00%
2013097	A081-0F0421	PF1300104	16	14.72	92.00%
2013098	A081-004PDI-21047-TX	PF1300158	8	6.4	80.00%
2013099	A081-003UZ-21152-VO	PF1300136	16	1.6	10.00%
2013100	A081-003UZ-21080-VO	PF1300135	16	1.6	10.00%
2013101	A081-003UZ-21072-VO	PF1300134	16	1.6	10.00%
2013102	A081-003UZ-21068-VO	PF1300133	16	1.6	10.00%
2013103	A081-003UZ-21067-VO	PF1300132	16	0	0.00%
2013104	A081-003UZ-21066-VO	PF1300131	16	0	0.00%
2013105	A081-003UZ-21064-VO	PF1300130	16	0	0.00%
2013106	A081-003UZ-21062-VO	PF1300129	16	0	0.00%
2013107	A081-003UZ-21059-VO	PF1300128	16	0	0.00%
2013108	A081-003UZ-21058-VO	PF1300127	16	0	0.00%
2013109	A081-003UZ-21057-VO	PF1300126	16	0	0.00%
2013110	A081-003UZ-21056-VO	PF1300125	16	0	0.00%
2013111	A081-003UZ-21054-VO	PF1300124	16	0	0.00%
2013112	A081-004LIA-21011-TX	PF1300155	4	0	0.00%
2013113	A081-004LIA-21004-TX	PF1300154	4	0	0.00%
2013114	A081-004LCA-21006-TX	PF1300153	4	0	0.00%
2013115	A081-004LCA-21002-TX	PF1300152	4	0	0.00%
2013116	A081-003LSA-21002-TX	PF1300151	4	0	0.00%
2013117	A081-003LIA-21018-TX	PF1300150	4	0	0.00%
2013118	A081-003LIA-21005-TX	PF1300149	4	0	0.00%
2013119	A081-003LCA-21015-TX	PF1300148	4	0	0.00%
2013120	A081-003LCA-21013-TX	PF1300147	4	0	0.00%
2013121	A081-003LCA-21011-TX	PF1300146	4	0	0.00%

Additional Anticipated Work

529

projected Baseline Grand Total

3000

1262.16

42.07%



QSGTL-TMMS, Contract no. UI25688 & UI25691- SGBP's
WEEKLY HSSE STATISTICS REPORT
 (04 - 10 Oct 2013)



KEY LEADING AND LAGGING INDICATORS:

1	Man-hours & Manpower Statistics:	Unit	This Week	Last Week Cumulative	Cumulative to Date
1.1	Manpower Average	Ave.	33	n/a	n/a
1.2	Man hours worked	No.	1,558 **	22,331	23,889
1.3	Total Number of Kilometers Driven	No.	5,660	107,206	112,866

2	Injuries/ Incidents/ Damages:				
2.1	Number of Near Misses	No.	0	0	0
2.2	Number of Potential Incidents (Unsafe acts and conditions)	No.	0	0	0
2.3	Number of Asset Damages	No.	0	0	0
2.4	Number of Vehicles Accidents	No.	0	0	1
2.5	Number of First Aid Cases (FAC)	No.	0	0	0

3	Recordable case injury (MTC/LTI/PTD/Fatality etc)				
3.1	Number of Cases requiring Medical Treatment(MTC)	No.	0	0	0
3.2	Number of Cases resulting in Restricted Work (RWC)	No.	0	0	0
3.3	Number of Cases resulting in Lost Time Injury (LTI)	No.	0	0	0
3.4	Number of Cases resulting in Permanent Total Disability (PTD)	No.	0	0	0
3.5	Number of Cases resulting in fatality	No.	0	0	0
3.6	Number of Occupational illness & Heat stress incidents	No.	0	0	0
3.7	Total Reportable Cases (Total no. of Fatality+PTD+LTI+RWC+MTC)	No.	0	0	0

4	LSR Violations, Environmental incidents and Spills as per QSGTL Fountain reports				
4.1	Number of Fountain Reports (FIM)	No.	0	0	0
4.2	Number of Life Saving Rule Violations	No.	0	0	0
4.3	Number of Asset Rule Violations	No.	0	0	0
4.4	Number of Spills	No.	0	0	0
4.5	Number of Environment Incident	No.	0	0	0
4.6	Number of Grievance Complaints	No.	0	0	0

5	HSSE Communications				
5.1	Number of site walk (Example- SPSP)	No.	6	118	124
5.2	Number of PTSW Inspections/Audits	No.	0	0	0
5.3	Number of HSSE Inspections	No.	0	0	0
5.4	Number of 3 What's Observation Cards	No.	0	0	0
5.5	Number of Internal Audits	No.	0	0	0
5.6	Number of QSGTL Road Safety Audits/Appraisals	No.	0	0	0
5.7	Number of Driver Forum	No.	0	0	0
5.8	Number of Safety tool box talks	No.	1	23	24

HSSE Highlights for this Week: (Note: All personnel are off during Friday)
1. This week's QCon internal TA Toolbox talk topic was: "What is MSDS, why is it important?". This topic was taken up as it is vital for the planning and preparation stage/ phase wherein all Planners will be needing an information of any chemicals to be used during MTA2015. A list or register of FGP Asset MSDS has been disseminated to all planners and other work team to use as references. They may find the attached link that directs to the MSDS main document to see what are the potential hazards associated and the safety precautionary measures to be followed when handling such chemicals/ compounds. 2. A team of QCon TA Core Group has conducted SPSP at GTL-1 (Phase-1) where Mourik crew conducting a hydro-jetting works to unblocked some tubing's on the Reactor (IR-3029). SPSP team members were: Vilfredo Nucom, Rama Rao and Englebert. One more SPSP report conducted by Mahmoud Helmy on same date. And on Wednesday, 09-Oct, Zia Ahmed and Rajesh as conducted the same at GTL. Total SPSP (6) nos. 3. Weekly HSSE meeting with QSGTL HSSE Advisor was attended and/or presided by Englebert, the meeting consisting of QSGTL and Madina HSSE Representatives and discussed various issues and concerning to MTA2015 preparation phase. 4. Daily toolbox topics for the MTA2015 has been discussed with Madina and Mourik, where each of the HSSE LEAD's designated numbers to be prepared and what topics to be delivered before January 2014. Some of the toolbox topics shall be used for the String-1 Outage Project in 2014 Q1.

HSSE Plans for next Week:
1. Initiate a Core Team meeting on the Total Technical Scope of Work risk classification/ identification process that was scheduled to initially conduct on 14-October 2013. This is to make segregation of High/ Medium Risk to Low risk jobs. As discussed previously with TA HSSE Advisor, Low Risk Jobs shall bear any JSA to be part of the work package/method statement for the MTA2015. 2. Carry out interview for another HSSE Coordinator candidate as backup for the MTA2015 where it defined on Fatigue Management. However, (3) HSSE Coordinators as of this moment been confirmed and selected and awaits their mobilization. 3. Complete the String-1 Outage HSSE Plan (inputs) before 31-October 2013.

Prepared by:

Englebert Tungol
 HSSE Manager/ Sr. HSSE Lead-TMMS

**** INCLUDES DRIVERS**

CC: Rishi Chaddha-Planning Manager

Noted by:

Ahmed Nasr
 Site Manager-TMMS
