

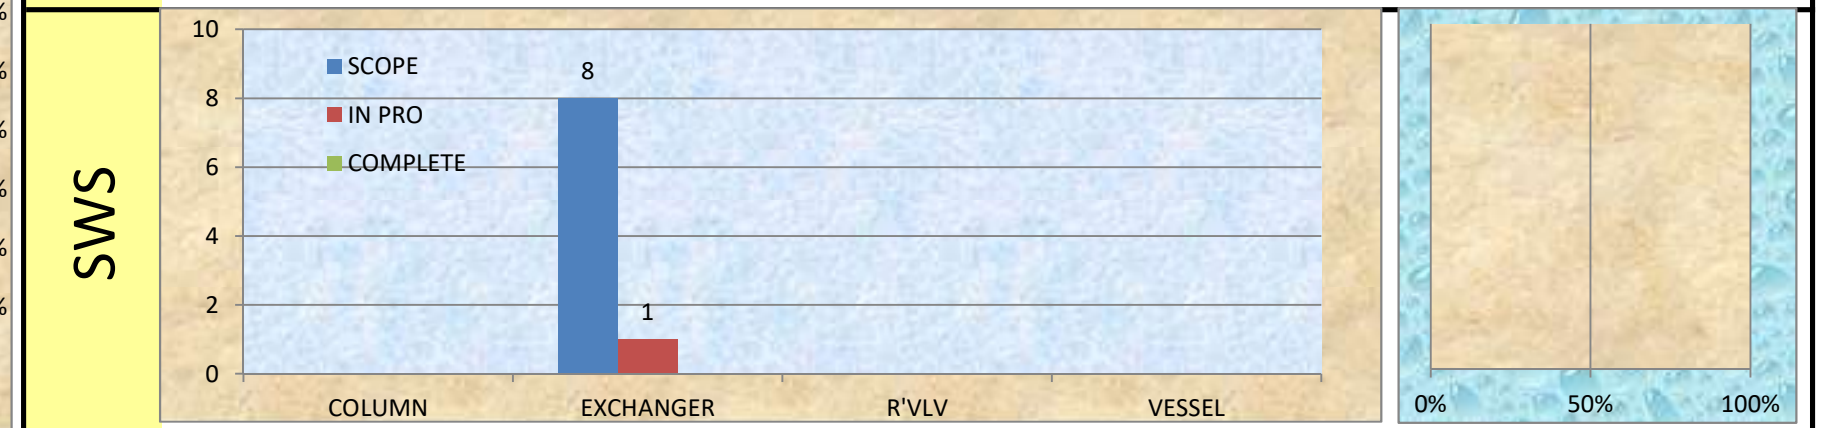
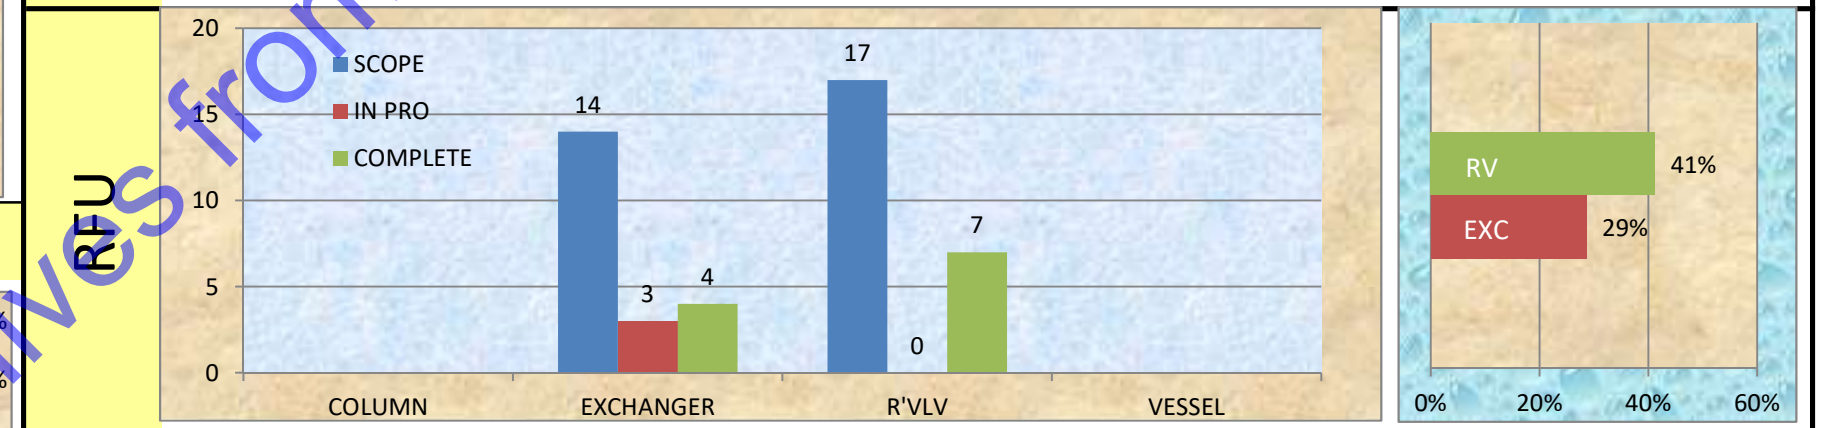
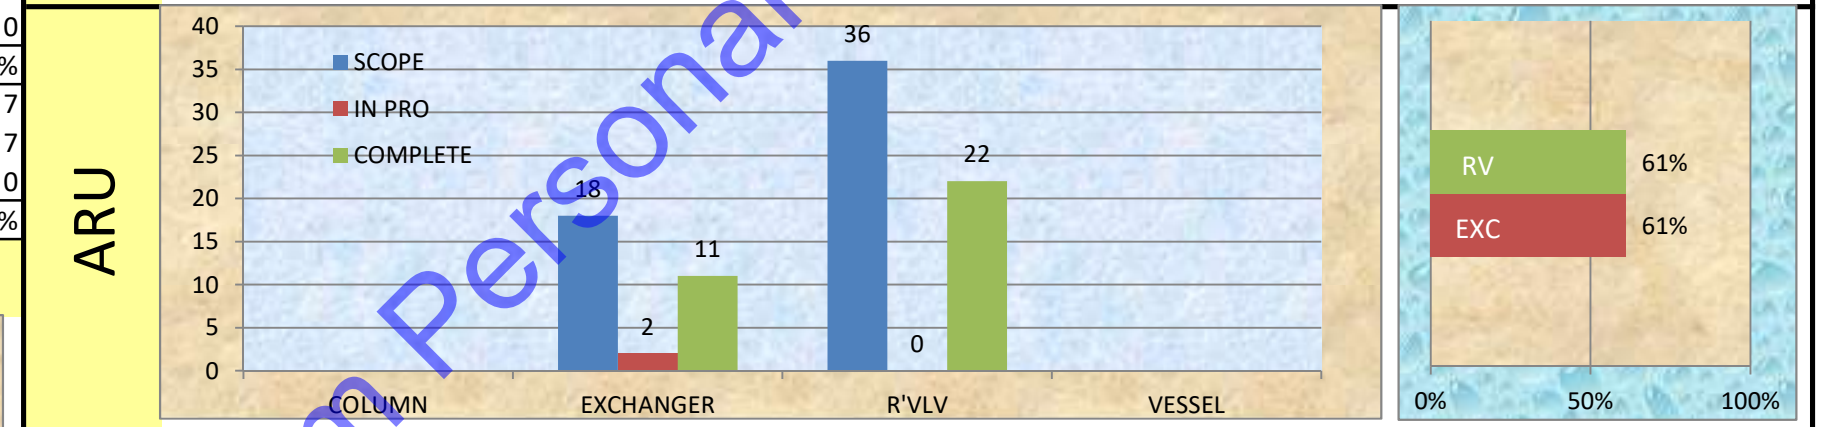
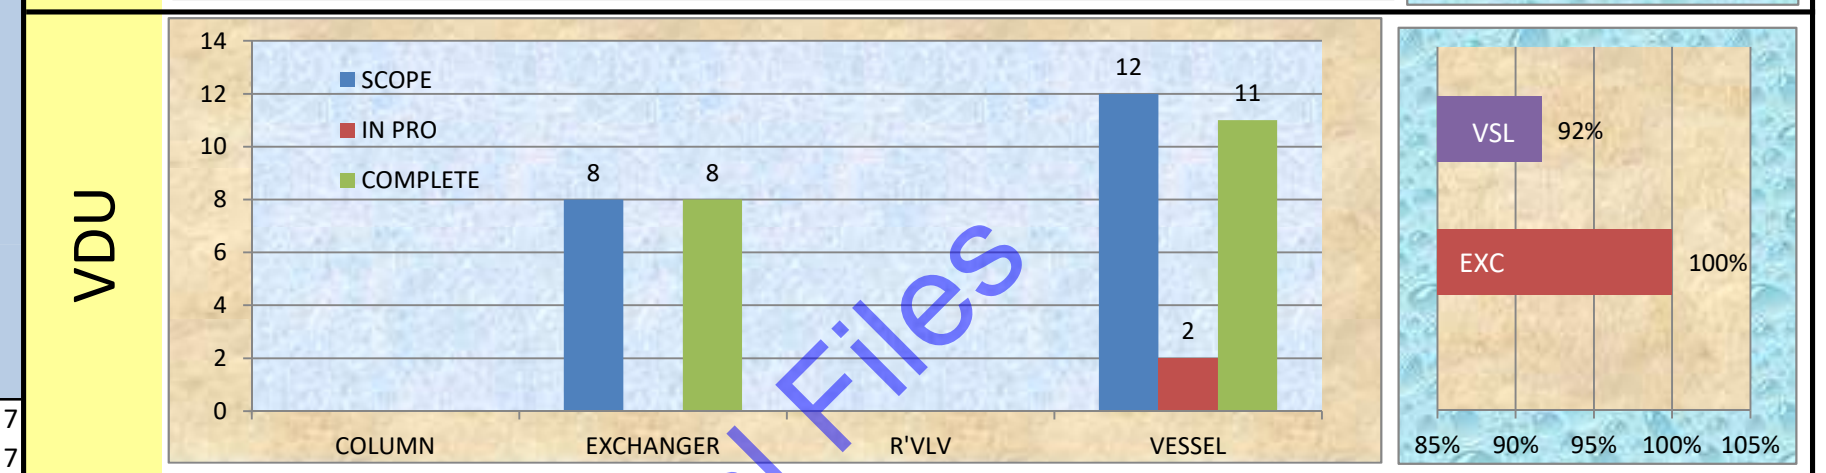


BPCL PRESHUTDOWN WORKS STATUS BY COUNT (20th MAY 2019)

UNIT	PRESHUTDOWN	COLUMN	EXCHANGER	R'VLV	VESSEL	MOC
CDU-4	SCOPE	1	21	363	25	
	IN PRO	0	2	5	7	
	COMPLETE		9	223	16	
	% Complete	0%	43%	61%	64%	
VDU-4	SCOPE		8		12	
	IN PRO				2	
	COMPLETE		8		11	
	% Complete		100%		92%	
ARU	SCOPE		18	36		
	IN PRO		2	0		
	COMPLETE		11	22		
	% Complete		61%	61%		
RFU	SCOPE		14	17		
	IN PRO		3	0		
	COMPLETE		4	7		
	% Complete		29%	41%		
SWS-4	SCOPE		8			
	IN PRO		1			
	COMPLETE					
	% Complete		0%			
DELTA - NEW SCOPES	NEW SCOPE		3	15	1	7
	IN PRO		1	1		7
	COMPLETE		2	14	1	0
	% Complete		67%	93%	100%	0%
TOTAL	SCOPE	1	72	431	38	7
	IN PRO	0	9	6	9	7
	COMPLETE	0	34	266	28	0
	% Complete	0%	47%	62%	74%	0%

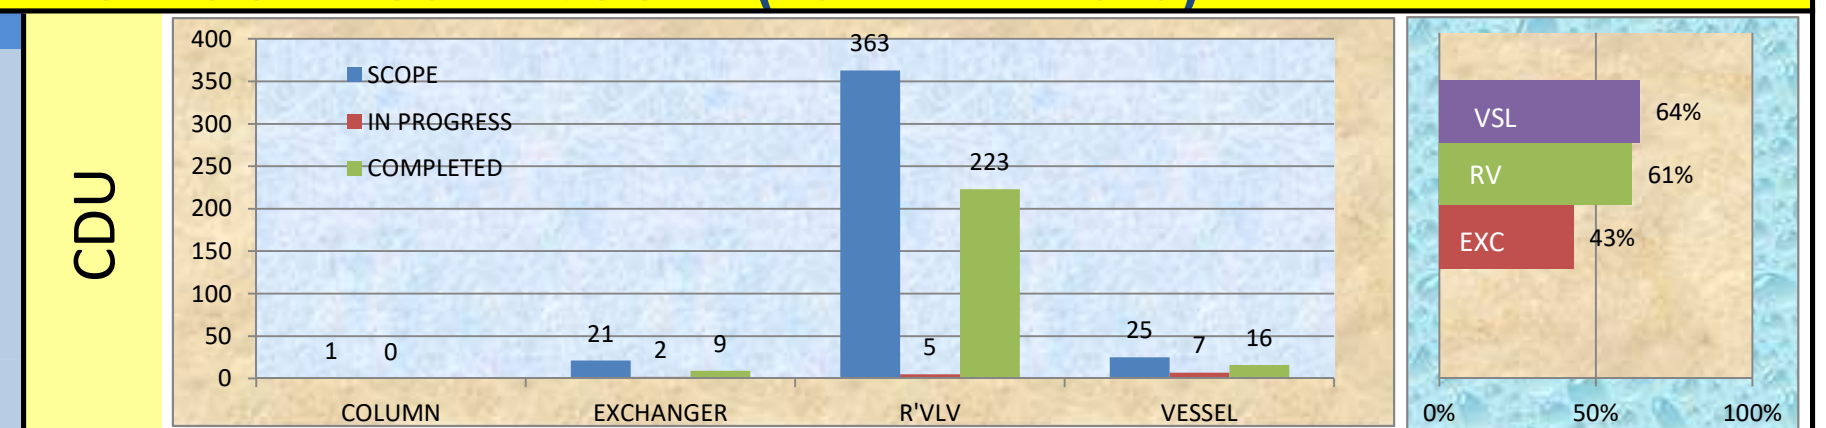

ADDITIONAL SCOPES

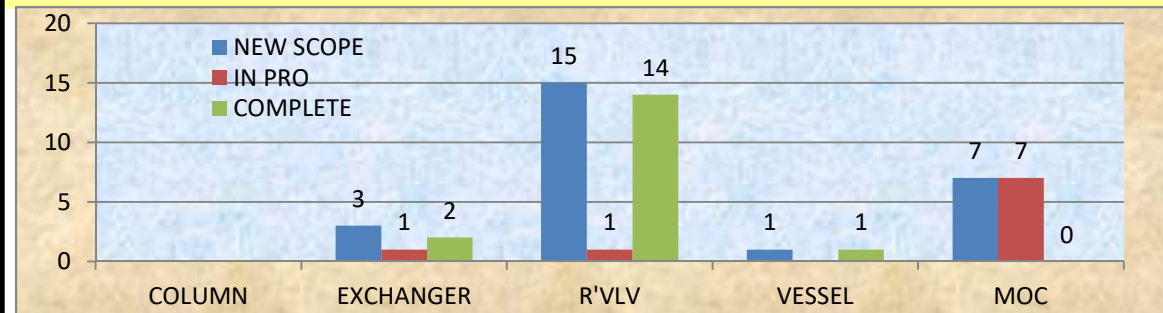

OVERALL - PRESHUTDOWN

