



Home Page

Date	1-Mar-26	Shift	Day	Night	Report No	14D	Day	15	To Go	22

NAVIGATION PAGE



Overall Progress Curve

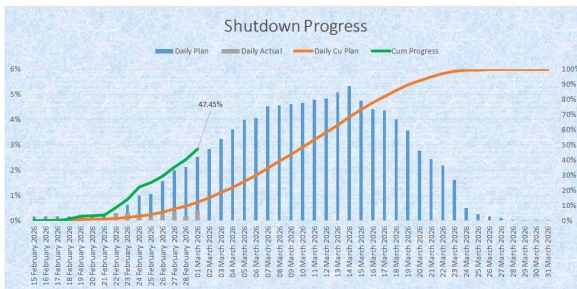

Area Wise PROGRESS FOR SHUTDOWN ACTIVITIES

Equipment	Progress to Date
SynGas Turbine	17.04%
MP Stripper	27.67%
CO2 Pipe Replacement	85.93%
Venturi	46.11%
Air Turbine	23.01%
SynGas Compressor LPC	70.76%
SynGas Compressor HPC	88.22%
AEC 102 COILS	66.22%

Equipment Wise PROGRESS

MAJOR ERECTION MILESTONES OF THE PROJECT


Planned Date	EQUIPMENT	Erection	Dismantling	Remarks
15 FEB	PUMPS 1302 A/B	✓		Completed P&ID
17 FEB	Air Turbine	✓	✓	Completed 16/02 NS
18 FEB	ASV Cooler	✓		Completed 20/02 DS
19 FEB	Skid for SynGas	✓		Completed P&ID
20-24 FEB	Coils for AEC-102	✓	✓	Completed 24/02 NS
20-24 FEB	Coils for AEC-102	✓		Started 26/02 DS
22 FEB	Dismantle Old ASV Cooler	✓		Completed 23/02 DS
22 FEB	Bundles for SynGas Compressor	✓	✓	Completed 15/02 NS
22 FEB	Bundles for SynGas Compressor	✓		Completed 26/02 DS
24 FEB	Old SynGas Turbine	✓	✓	Completed 19/02 DS
24 FEB	New SynGas Turbine	✓		
25-27 FEB	8 Exchangers for MP Stripper	✓		Completed 22/02 DS
26 FEB	New Air Turbine	✓		Completed 22/02 NS
27 FEB	MP Stripper	✓		Completed 23/02 DS
22-28 FEB	Regenerator Dome Strip Lining	✓		Welding of Old Plates
3-6 MAR	Five Platforms for MP Stripper Structure	✓		Started 15/02 DS
4 MAR	PUMPS 1710 A/B	✓		Completed 25/02 DS
20 FEB	Full CO2 Line (Old)	✓	✓	Completed 23/02 DS
22 FEB	Full CO2 Line (New)	✓		Completed 23/02 DS
22 FEB	Full Venturi Line (Old)	✓	✓	Completed 23/02 DS
1 MAR	Full Venturi Line (New)	✓		Started 28/02 DS
	Spools erection for new ASV Cooler Inlet / Outlet connections	✓		Started on 24/02 NS

Piping Erection & Welding PROGRESS to DATE

A) Field Welding Area Wise Punchlist

Date	ASV Cool	CO2	EC102	MP Stripper	T&C	Venturi	Lube Oil	IBR	Others	Total	by Achieved ID
25-Feb	283	48	146	841	1532	50	824	72	850	4646	
26-Feb	283	0	134	719	1431	50	740.5	72	850	4279.5	
27-Feb	256	0	110	603.5	1429	50	700.5	48	850	4047	
28-Feb	244	0	82	511.5	1355	20	637.5	18	850	3728	
1-Mar	196	0	74	467.5	1205	20	587	18	850	3417.5	
2-Mar											
3-Mar											
4-Mar											
5-Mar											
6-Mar											
7-Mar											
8-Mar											
9-Mar											
10-Mar											

Balance (Field Piping)



B) Critical Connections Focus - Monitoring of Work Balance

Line No	4"-4026	3"-3896	1.5"-3898	6"-4022	6"-4023	6"-4024	6"-4028	4019	12"-4030	12"-3821	8"-4032	12"-4031
Scope (ID)	270	186	103	121	262	363	118	174	230	93	259	376
Comp (ID)	218	156	89	94	224	225	87	132	141	43	172	280
Balance Field Welding Inch Dia												
21-Feb	52	30	14	27	38	138	31	42	89	50	87	99
22-Feb	52	30	14	27	38	138	31	42	89	50	87	96
23-Feb	52	15	14	27	38	138	31	42	89	50	87	96
24-Feb	52	0	6.5	27	38	126	31	36	79	50	87	96
25-Feb	52	0	6.5	27	38	126	31	36	79	50	87	96
26-Feb	52	0	6.5	27	38	126	31	36	79	50	87	96
27-Feb	48	0	6.5	27	38	94	31	36	79	50	87	72
28-Feb	48	0	6.5	27	38	94	31	12	79	50	87	36
1-Mar	48	0	6.5	27	38	94	31	0	79	50	87	30
2-Mar												
3-Mar												
4-Mar												
5-Mar												

Critical Lines Completion Trends



C) Total Welding Consolidated Summary

Area	Welding Details				Testing Details				
	Scope	Shop	Field	Total	Balance	UT	RT	PAUT	Hydro
CO2	2060	1530	530	2060	0				
EC102	650	504	72	576	74				
Stripper	4643	3627	548.5	4175.5	467.5				
Venturi	296	246	30	276					
Trimming & Compressor	6358	3608	1527	5135	1223				
ASV Cooler	1271	886	189	1075	196				
Lube Oil	3854	2448	819	3267	587				
Others*	1100		250	250	850				
					3417.5				
