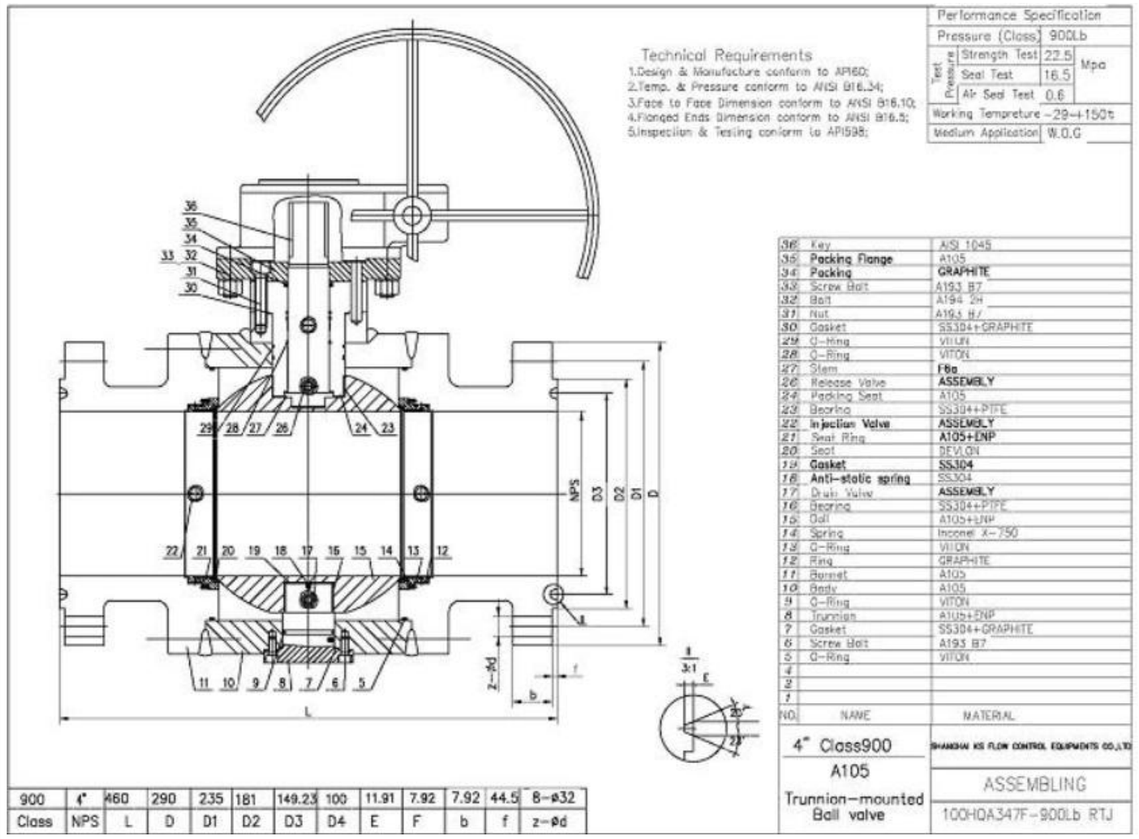


JOINT VALVE ROUTINE & SHUTDOWN MAINTENANCE FRAGNET

OPENING


- **Preparation**
  - **LOTO**
    - Depressurize
    - Isolate
  - **Inspect as found**
    - TAG
    - Inspect Body
    - Ispect Bonnet
  - **Functional Check**
    - Manual Operation
    - Check for Open/Close
- **Removal & Dissassemble**
  - **Drop the Valve**
    - Scaffold
    - Drop
    - Move to shop

REFURBISHMENT


- **Shop Activities**
  - **Dismantle Valve**
  - **Clean**
    - Remove Dirt
    - Remove Scale
    - Remove product
  - **Lubricate as recommended**
    - Lubricate stem
    - Lubricate gearboxes
    - Lubticator actuator links
  - **Seal & packing**
    - Replace valve gaskets
    - Replace valve packing
    - Replace O-rings
    - Replace seals
  - **Machining if needed**
    - Machine worn out parts
    - Machine gasket seats
    - Machine stem to free
  - **Reassemble**
    - Boxup Valve
    - Connect Body to Bonnet
    - Boltup end connections
  - **Valve testing**
    - Leak Test
    - Pressure test in shop
  - **Painting**
  - **Final Visual Inspection**

REFIXING

- **Valve return & refix**
  - **Rig Back**
    - Fix in location
    - Check direction and angle
  - **Bolting**
    - Clean mating flange surfaces
    - Replace gaskets
    - Boxup in location
    - Torque to appropriate value
  - **Reinsulate for HOT & Cold Services**
  - **Deblind**
  - **Descaffold**

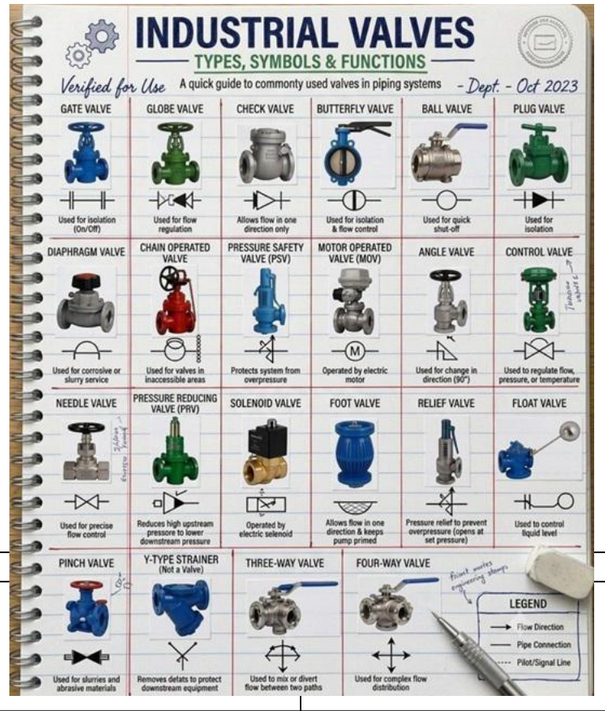

T17QPME1203: Replace Filling, I/L & O/L VLVs(95-207)		548	22-Jan-17 08:00	14-Feb-17 04:00								
Pre Shutdown		3	22-Jan-17 08:00	22-Jan-17 11:00								
R4T-5010	Erect Scaffolding/Firebox	2	22-Jan-17 08:00	22-Jan-17 10:00								
R4T-5015	Remove Insulation	1	22-Jan-17 10:00	22-Jan-17 11:00								
Shutdown		253	02-Feb-17 17:00	13-Feb-17 06:00								
R4T-5020	Verify LT&T and Obtain PTW	2	02-Feb-17 17:00	02-Feb-17 19:00								
R4T-5025	Mechanical Isolation & Blinding	16	02-Feb-17 19:00	03-Feb-17 11:00								
R4T-5030	Replace 6" Ball Valves (4 nos)	24	03-Feb-17 11:00	04-Feb-17 11:00								
R4T-5035	Cut & Weld 1" Globe Valves (2 nos)	12	07-Feb-17 01:00	07-Feb-17 13:00								
R4T-5040	Inspection as per R4T Sheet	6	07-Feb-17 13:00	07-Feb-17 19:00								
R4T-5045	Hydro Test	12	08-Feb-17 14:00	09-Feb-17 02:00								
R4T-5050	Paint Weld Joints	4	09-Feb-17 02:00	09-Feb-17 06:00								
R4T-5055	Carry out De-Blinding	16	12-Feb-17 13:00	13-Feb-17 05:00								
R4T-5060	Housekeeping & Close PTW	1	13-Feb-17 05:00	13-Feb-17 06:00								
R4T-5065	Mechanical Completion	0		13-Feb-17 06:00								
Post Shutdown		22	13-Feb-17 06:00	14-Feb-17 04:00								
R4T-5070	Fix Back Insulation	4	13-Feb-17 06:00	13-Feb-17 10:00								
R4T-5075	Remove Scaffolding/Firebox	2	14-Feb-17 02:00	14-Feb-17 04:00								

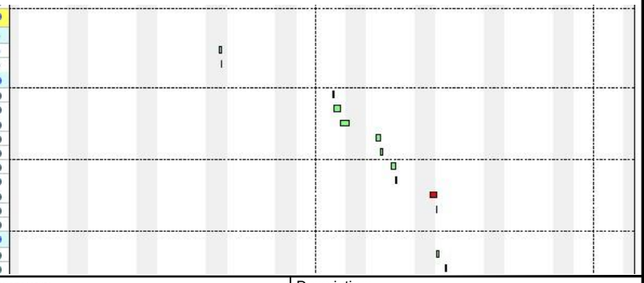

Drw Purpose Code :- R01- Educational

Status of Approval :- 01

Dimentions as Mentioned: NA

Drawing Scale :- NTS

Engg Code :- 99

Backup Info Code :- 04

Angle of Projection: NA

Sheet Size: A3

Statutory Note:
This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!

Drw electronic code

rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614

Legal Owner

QR CODE: NA

Description: BALL VALVES - FRAGNET

Drawn By:	Drawn Date
DFT-01	20260804
Checked Approved by	Checked Approved Date
rPlan-01	20260814

Drawing Number	Sheet	Rev
As Barcoaded	1 of 1	00
