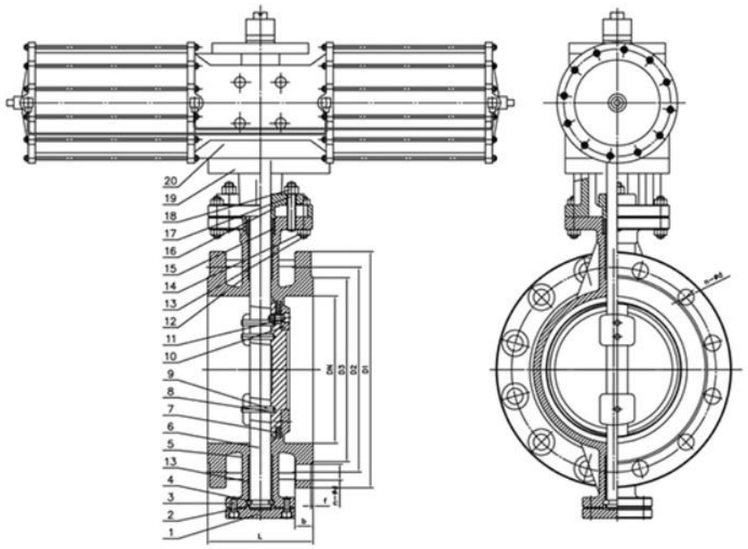


11	Socket Bolt	A193 B8M			
10	Pressure Plate	A182 F316			
9	Pin	316SS	20	Pneumatic device	Assem.
8	Disc	A351 CF3M	19	Yoke	WCB
7	Seal Ring	304+ Graphite	18	Nut	A194 2H
6	Stem	ANSI 410	17	Stud	A193 B7
5	Body	A216 WCB+13Cr	16	Packing Flange	A216 WCB
4	Split Ring	ANSI 410	15	Packing	Flexible Graphite
3	Socket Bolt	A193 B7	14	Nut	A194 2H
2	Gasket	Flexible graphite+304	13	Stud	A193 B7
1	Under Cover	A105	12	Composite Bearing	316
No.	Name	Material	No.	Name	Material

JOINT VALVE ROUTINE & SHUTDOWN MAINTENANCE FRAGNET

OPENING

- **Preparation**
  - **LOTO**
    - Depressurize
    - Isolate
  - **Inspect as found**
    - TAG
    - Inspect Body
    - Ispect Bonnet
  - **Functional Check**
    - Manual Operation
    - Check for Open/Close
- **Removal & Dissassemble**
  - **Drop the Valve**
    - Scaffold
    - Drop
    - Move to shop

REFURBISHMENT


- **Shop Activities**
  - **Dismantle Valve**
  - **Clean**
    - Remove Dirt
    - Remove Scale
    - Remove product
  - **Lubricate as recommended**
    - Lubricate stem
    - Lubricate gearboxes
    - Lubticator actuator links
  - **Seal & packing**
    - Replace valve gaskets
    - Replace valve packing
    - Replace O-rings
    - Replace seals
  - **Machining if needed**
    - Machine worn out parts
    - Machine gasket seats
    - Machine stem to free
  - **Reassemble**
    - Boxup Valve
    - Connect Body to Bonnet
    - Boltup end connections
  - **Valve testing**
    - Leak Test
    - Pressure test in shop
  - **Painting**
  - **Final Visual Inspection**

REFIXING

- **Valve return & refix**
  - **Rig Back**
    - Fix in location
    - Check direction and angle
  - **Bolting**
    - Clean mating flange surfaces
    - Replace gaskets
    - Boxup in location
    - Torque to appropriate value
  - **Reinsulate for HOT & Cold Services**
  - **Deblind**
  - **Descaffold**



T17QSME1349: Replace Blower Discharge B/V(05-101A)		939	16-Jan-17 06:00	24-Feb-17 09:00
Pre Shutdown		6	16-Jan-17 06:00	16-Jan-17 12:00
SRU1-6510	Erect Scaffolding	4	16-Jan-17 06:00	16-Jan-17 10:00
SRU1-6515	Remove Insulation	2	16-Jan-17 10:00	16-Jan-17 12:00
Shutdown		22	04-Feb-17 13:00	05-Feb-17 11:00
SRU1-6520	Verify LT&T and Obtain PTW	2	04-Feb-17 13:00	04-Feb-17 15:00
SRU1-6525	Replace 14" Butterfly Valve	16	04-Feb-17 15:00	05-Feb-17 07:00
SRU1-6530	Inspection by ERG	2	05-Feb-17 07:00	05-Feb-17 09:00
SRU1-6535	Housekeeping & Close PTW	2	05-Feb-17 09:00	05-Feb-17 11:00
SRU1-6540	Mechanical Completion	0		05-Feb-17 11:00
Post Shutdown		454	05-Feb-17 11:00	24-Feb-17 09:00
SRU1-6545	Fix Back Insulation	4	05-Feb-17 11:00	05-Feb-17 15:00
SRU1-6550	Remove Scaffolding	2	24-Feb-17 07:00	24-Feb-17 09:00
T17QSME1350: Replace Blower Discharge B/V(05-101)		937	16-Jan-17 10:00	24-Feb-17 11:00
Pre Shutdown		6	16-Jan-17 10:00	16-Jan-17 16:00
SRU1-6610	Erect Scaffolding	4	16-Jan-17 10:00	16-Jan-17 14:00
SRU1-6615	Remove Insulation	2	16-Jan-17 14:00	16-Jan-17 16:00
Shutdown		22	05-Feb-17 11:00	06-Feb-17 09:00
SRU1-6620	Verify LT&T and Obtain PTW	2	05-Feb-17 11:00	05-Feb-17 13:00
SRU1-6625	Replace 14" Butterfly Valve	16	05-Feb-17 13:00	06-Feb-17 05:00
SRU1-6630	Inspection by ERG	2	06-Feb-17 05:00	06-Feb-17 07:00
SRU1-6635	Housekeeping & Close PTW	2	06-Feb-17 07:00	06-Feb-17 09:00
SRU1-6640	Mechanical Completion	0		06-Feb-17 09:00
Post Shutdown		434	06-Feb-17 09:00	24-Feb-17 11:00
SRU1-6645	Fix Back Insulation	4	06-Feb-17 09:00	06-Feb-17 13:00
SRU1-6650	Remove Scaffolding	2	24-Feb-17 09:00	24-Feb-17 11:00

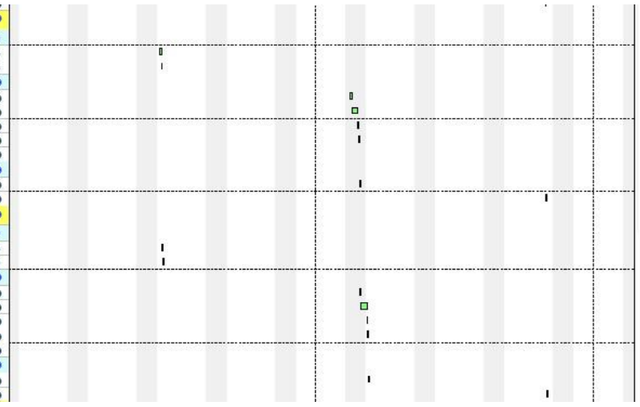

Drw Purpose Code :- R01- Educational

Status of Approval :- 01

Dimentions as Mentioned: NA

Drawing Scale :- NTS

Engg Code :- 99

Backup Info Code :- 04

Angle of Projection: NA

Sheet Size: A3

Statutory Note:
This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!

Drw electronic code

rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614

Legal Owner

QR CODE: NA

Description: Butterfly VALVES - FRAGNET

Drawn By: DFT-01

Drawn Date: 20260804

Checked Approved by: rPlan-01

Checked Approved Date: 20260814

Drawing Number: As Barcoaded

Sheet: 1 of 1

Rev: 00
