
Activity ID	Activity Name	Original Duration	Planned Start	Planned Finish	Actual Start	Actual Finish
- Area - 02 (Residue Fluid Catalytic Reaction)						
ORPC Related						
Entire Reactor Regen System						
R2001 0010	Start of TA	0.00h	06-Feb-10		06-Feb-10	
R2001 0020	Feed Pull Out	24.00h	06-Feb-10	07-Feb-10	06-Feb-10	07-Feb-10
R2001 0030	Cooling down	48.00h	07-Feb-10	09-Feb-10	07-Feb-10	
R2001 0040	Catalyst removal from the reactor	36.00h	09-Feb-10	10-Feb-10	08-Feb-10	
R2001 0050	Open Rx/Rg Manways	8.00h	10-Feb-10	10-Feb-10		
R2001 0055	Other preparation activities	72.00h	10-Feb-10	13-Feb-10		
R2001 0060	Cooling Completed and Reactor han...	8.00h	13-Feb-10	14-Feb-10		
Reactor-R2001						
Main Reactor R2001						
R2001 1010	Access top Manway for start	0.00h	14-Feb-10			
R2001 1020	Inside Scaffold all portions inside R2...	72.00h	14-Feb-10	17-Feb-10		
R2001 1030	Build Temporary Platform around top...	8.00h	17-Feb-10	17-Feb-10		
R2001 1031	As found inspection by Reliability	4.00h	17-Feb-10	17-Feb-10		
R2001 1038	Grind / remove cotter pins/ remove Fl...	48.00h	22-Feb-10	24-Feb-10		
R2001 1040	Manual removal of any residue catalyst	12.00h	17-Feb-10	18-Feb-10		
R2001 1041	Internal Coke Cleaning inside the she...	96.00h	18-Feb-10	22-Feb-10		
R2001 1042	Access Slip Joint & inspect	8.00h	17-Feb-10	18-Feb-10		
R2001 1043	Repairs around slip joint if any	72.00h	18-Feb-10	21-Feb-10		
R2001 1046	Reliability Inspection of outer cyclone...	24.00h	21-Feb-10	22-Feb-10		
R2001 1050	Refractory Repairs on inner Reactor ...	72.00h	22-Feb-10	25-Feb-10		
R2001 1086	Access Stripper Baffles using Rope L...	48.00h	26-Feb-10	28-Feb-10		
R2001 1087	Cleaning of stripper Baffles/ clamp re...	48.00h	26-Feb-10	28-Feb-10		
R2001 1088	Buildup / repairs of erosion if any	24.00h	28-Feb-10	01-Mar-10		
R2001 1112	Coke cleaning in stripper and nozzles	48.00h	22-Feb-10	24-Feb-10		
R2001 1113	Coke Cleaning of steam rings	8.00h	24-Feb-10	24-Feb-10		
Main Reactor Plenum Chamber/Ducts						
R2001 1032	Coke Cleaning of Plenum Inside	120.00h	17-Feb-10	22-Feb-10		
R2001 1045	Reliability inspection	2.00h	22-Feb-10	22-Feb-10		
R2001 1055	Cut open / access (2nos) plenum to c...	18.00h	22-Feb-10	23-Feb-10		
Main Reactor Cyclones						

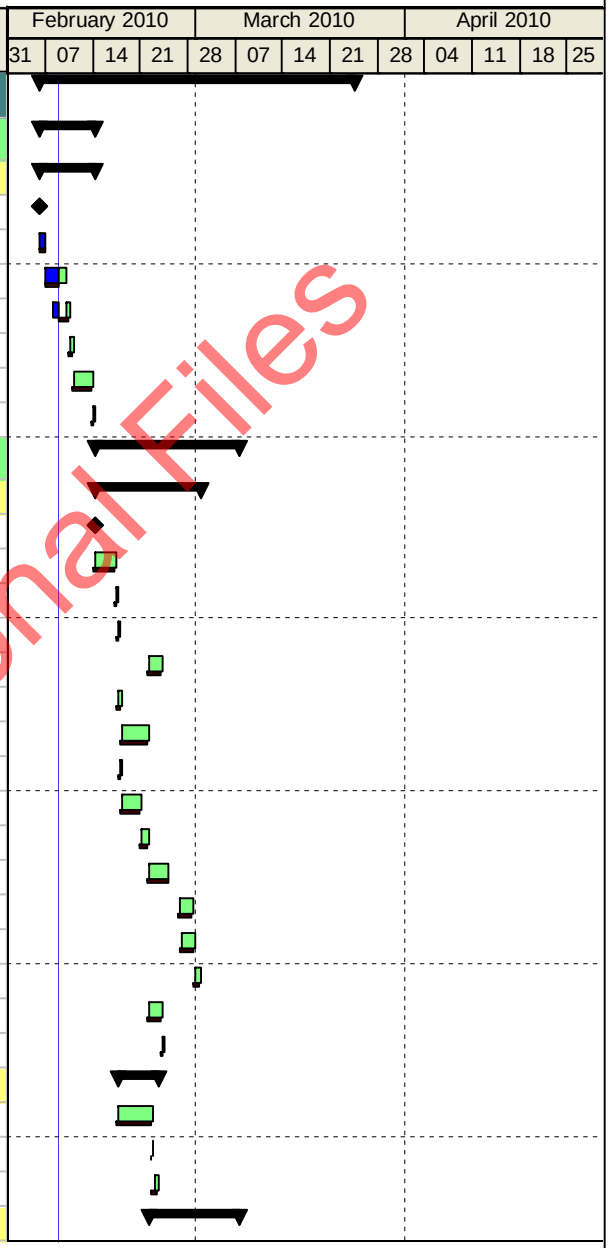

Project Baseline Bar
Actual Work
Remaining Work
Critical Remaining W...


STATIC EQUIPMENT TURNAROUND - TA2010

CRITICAL SCHEDULE - REACTOR REGENERATOR SYSTEM

Date	Revision	Checked	Approved
30-Jan-10	As commented on 30th Jan		


Archives from Personal Files

Activity ID	Activity Name	Original Duration	Planned Start	Planned Finish	Actual Start	Actual Finish
R2001 1068	Preliminary inspection inside cyclone...	8.00h	22-Feb-10	22-Feb-10		
R2001 1071	Full Scaffold inside all cyclones	48.00h	22-Feb-10	24-Feb-10		
R2001 1072	Coke Cleaning inside all Cyclones	48.00h	22-Feb-10	24-Feb-10		
R2001 1073	Patch Welding ducts if advised by Re...	72.00h	27-Feb-10	02-Mar-10		
R2001 1074	Reliability inspection inside all cyclones	48.00h	25-Feb-10	27-Feb-10		
R2001 1075	Refractory repairs inside first 4 cyclon...	48.00h	25-Feb-10	27-Feb-10		
R2001 1076	Refractory repairs inside next 4 cyclo...	48.00h	27-Feb-10	01-Mar-10		
R2001 1079	Refractory repairs inside last 4 cyclons	48.00h	01-Mar-10	03-Mar-10		
R2001 1080	Descaffold all Cyclones	96.00h	03-Mar-10	07-Mar-10		
R2001 1082	Service Flapper Valve if needed	48.00h	24-Feb-10	26-Feb-10		
R2001 1084	Fix Back Flapper Valves if removed	48.00h	24-Feb-10	26-Feb-10		
R2001 1085	Load Test Flapper valves	12.00h	26-Feb-10	27-Feb-10		
Sections associated with VSS						
R2001 1090	Cut Open / Access top of riser (VSS ...	72.00h	22-Feb-10	25-Feb-10		
R2001 1092	Provide access scaffold inside VSS s...	12.00h	25-Feb-10	26-Feb-10		
R2001 1110	Internal coke cleaning of VSS Chamber	48.00h	26-Feb-10	28-Feb-10		
R2001 1115	Relibility inspection inside VSS	8.00h	28-Feb-10	28-Feb-10		
R2001 1160	Close top openings of riser- VSS	48.00h	03-Mar-10	05-Mar-10		
Main Reactor Riser Pipe						
R2001 1091	Drop Riser Wye Distributor	8.00h	14-Feb-10	14-Feb-10		
R2001 1093	Remova any catalyst at bottom of riser	24.00h	14-Feb-10	15-Feb-10		
R2001 1100	Scaffold the Reactor Riser from Botto...	144.00h	15-Feb-10	21-Feb-10		
R2001 1101	Inspect / Remove Feed Nozzles	48.00h	21-Feb-10	23-Feb-10		
R2001 1120	Reliability inspection across riser inside	12.00h	21-Feb-10	22-Feb-10		
R2001 1130	Refractory repairs inside riser if any	144.00h	22-Feb-10	28-Feb-10		
R2001 1131	Repair riser disengaging arms	48.00h	28-Feb-10	02-Mar-10		
R2001 1132	Fix Back/ replace Feed Nozzles	48.00h	28-Feb-10	02-Mar-10		
R2001 1134	Change Nozzles if required	24.00h	23-Feb-10	24-Feb-10		
R2001 1140	Final Reliability inspection inside Riser	12.00h	28-Feb-10	28-Feb-10		
R2001 1150	Descaffold complete riser	72.00h	28-Feb-10	03-Mar-10		
R2001 1170	Fix Back Riser Wye Distributor	8.00h	03-Mar-10	03-Mar-10		
Main Reactor Stand Pipes and Exp. Joints						
R2001 5160	Bridge and access Expansion joint E...	24.00h	17-Feb-10	18-Feb-10		
R2001 5170	Inspect Spent catalyst Stand Pipe by ...	8.00h	18-Feb-10	18-Feb-10		
R2001 5172	Provision for repairs if any by others	24.00h	18-Feb-10	19-Feb-10		
R2001 5174	Remove Slide valve gate	8.00h	19-Feb-10	19-Feb-10		
R2001 5176	Refurbishment of Gate and reinstallat...	48.00h	19-Feb-10	21-Feb-10		

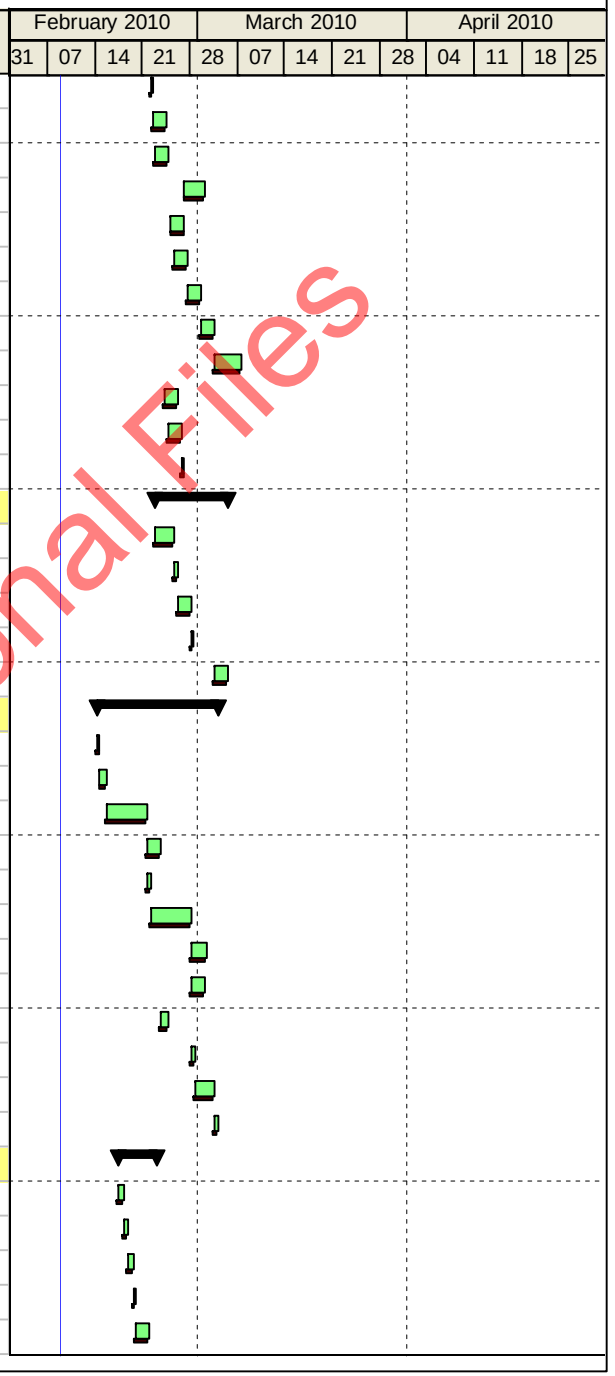


Archives from Personal Files

Activity ID	Activity Name	Original Duration	Planned Start	Planned Finish	Actual Start	Actual Finish
R2001 5180	Access EJ2002	24.00h	18-Feb-10	19-Feb-10		
R2001 5190	Inspect / repairs on EJ2002	24.00h	19-Feb-10	20-Feb-10		
R2001 5200	Any Other repairs if any	48.00h	20-Feb-10	22-Feb-10		
R2001 5210	Descaffold EJ2001 / 2002	12.00h	22-Feb-10	23-Feb-10		
Regenerator						
Regenerator -1						
R2002 1010	Access top manway in Regen-1	0.00h	14-Feb-10			
R2002 1012	Access bottom manway of Regen-1	8.00h	14-Feb-10	14-Feb-10		
R2002 1020	Complete scaffold inside Regen 1	96.00h	14-Feb-10	18-Feb-10		
R2002 1021	Build Temp Platform at Cyclone inlet ...	24.00h	18-Feb-10	19-Feb-10		
R2002 1023	Remove any residual catalyst inside r...	12.00h	19-Feb-10	19-Feb-10		
R2002 1024	Remove Cat Screen	4.00h	19-Feb-10	19-Feb-10		
R2002 1030	Wrap Gunny Bags over Trickle Valve...	8.00h	19-Feb-10	20-Feb-10		
R2002 1040	Reach bottom, scaffold and cover air ...	8.00h	20-Feb-10	20-Feb-10		
R2002 1042	Relibility inspection of outer cyclones	12.00h	20-Feb-10	20-Feb-10		
R2002 1080	Refractory repairs on inner Regen-1 ...	144.00h	18-Feb-10	24-Feb-10		
R2002 1083	Remove torch oil nozzles	72.00h	14-Feb-10	17-Feb-10		
R2002 1089	Remove cladding sheet for replacem...	12.00h	25-Feb-10	25-Feb-10		
R2002 1099	Remove Insulation Blanket	24.00h	25-Feb-10	26-Feb-10		
R2002 1109	Clean the surface, offer for inspection	48.00h	26-Feb-10	28-Feb-10		
R2002 1119	Weld new anchors if needed	48.00h	28-Feb-10	02-Mar-10		
R2002 1129	Install new fabric sheet	24.00h	02-Mar-10	03-Mar-10		
R2002 1139	Replace cladding and close	24.00h	03-Mar-10	04-Mar-10		
R2002 1149	Inspect & repair vent pipes	48.00h	04-Mar-10	07-Mar-10		
Regen-1 Plenum						
R2002 1159	Access Plenum Chamber	8.00h	18-Feb-10	18-Feb-10		
R2002 1169	Scaffold Plenum Chamber	8.00h	18-Feb-10	18-Feb-10		
R2002 1179	Chip existing refractory	96.00h	22-Feb-10	27-Feb-10		
R2002 1189	Inspect / repair welds and anchors	24.00h	27-Feb-10	28-Feb-10		
R2002 1199	Apply new refractory	120.00h	28-Feb-10	06-Mar-10		
R2002 1209	Inspect, dry & descaffold	24.00h	06-Mar-10	07-Mar-10		
Regen-1 Cyclones						
R2002 1050	Reliability inspection of outer cyclones	12.00h	20-Feb-10	20-Feb-10		
R2002 1060	Rope ladders / inspection inside Cycl...	12.00h	20-Feb-10	21-Feb-10		
R2002 1061	Scaffold inside Cyclones (1-7)	24.00h	21-Feb-10	22-Feb-10		
R2002 1062	Refractory repairs inside / outside Cy...	72.00h	22-Feb-10	25-Feb-10		
R2002 1063	Lower rope ladders/inspect inside Cy...	12.00h	25-Feb-10	25-Feb-10		

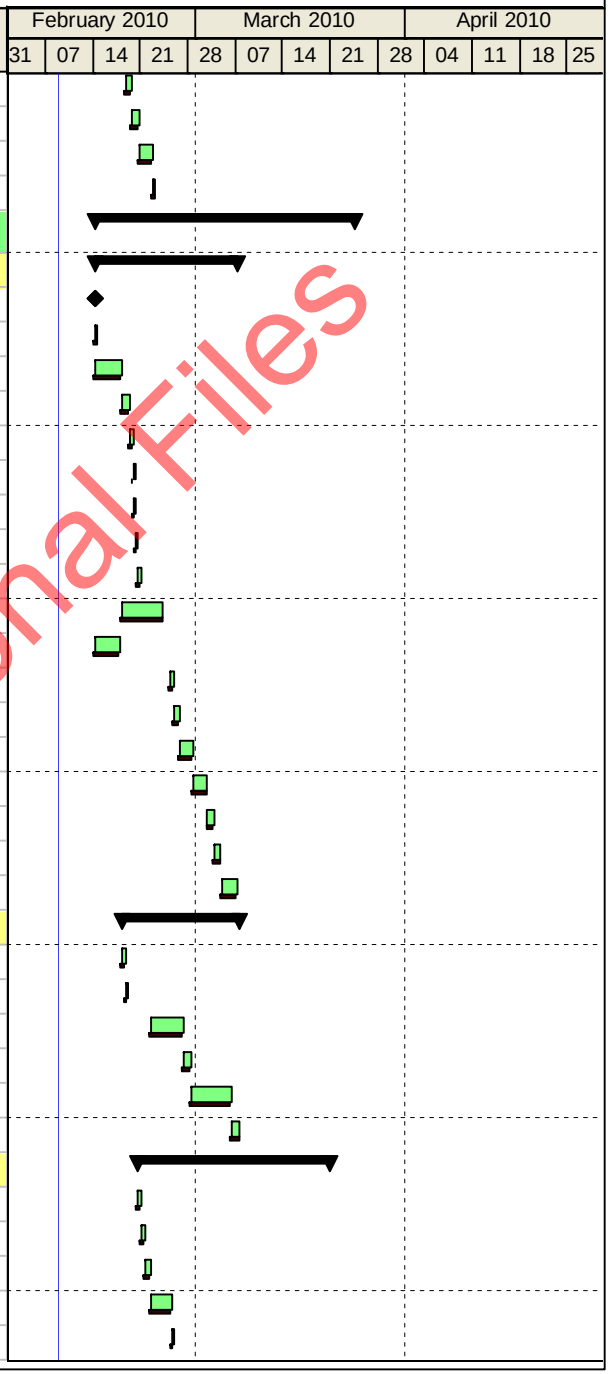

Archives from Personal Files

Activity ID	Activity Name	Original Duration	Planned Start	Planned Finish	Actual Start	Actual Finish
R2002 1064	Scaffold inside Cyclones (8-14)	24.00h	25-Feb-10	26-Feb-10		
R2002 1065	Refractory repairs inside / outside Cy...	72.00h	26-Feb-10	01-Mar-10		
R2002 1066	Lower rope ladders/inspect inside Cy...	12.00h	01-Mar-10	02-Mar-10		
R2002 1067	Scaffold inside Cyclones (15-21)	24.00h	02-Mar-10	03-Mar-10		
R2002 1068	Refractory repairs inside / outside Cy...	72.00h	03-Mar-10	06-Mar-10		
R2002 1069	Lower rope ladders/inspect inside Cy...	12.00h	06-Mar-10	06-Mar-10		
R2002 1070	Scaffold inside Cyclones (22-28)	24.00h	06-Mar-10	07-Mar-10		
R2002 1071	Refractory repairs inside / outside Cy...	72.00h	07-Mar-10	10-Mar-10		
R2002 1072	Lower rope ladders/inspect inside Cy...	12.00h	10-Mar-10	11-Mar-10		
R2002 1073	Scaffold inside Cyclones (29-35)	24.00h	11-Mar-10	12-Mar-10		
R2002 1074	Refractory repairs inside / outside Cy...	72.00h	12-Mar-10	15-Mar-10		
R2002 1075	Lower rope ladders/inspect inside Cy...	12.00h	15-Mar-10	15-Mar-10		
R2002 1076	Scaffold inside Cyclones (36-44)	24.00h	15-Mar-10	16-Mar-10		
R2002 1077	Refractory repairs inside / outside Cy...	72.00h	16-Mar-10	19-Mar-10		
R2002 1078	Descaffold all Cyclones	240.00h	10-Mar-10	20-Mar-10		
R2002 1088	Repairs of Cyclone Bracings	48.00h	05-Mar-10	07-Mar-10		
R2002 1098	repair / Replacement of cyclone braci...	74.00h	07-Mar-10	10-Mar-10		
Cat Cooler Pipes and Exp. Joints						
R2002 1025	Cut Cat Cooler Air Pipe	8.00h	22-Feb-10	23-Feb-10		
R2002 1082	Repair and install Cat Cooler Air Pipe	24.00h	24-Feb-10	25-Feb-10		
Regenerator -2						
R2002 1090	Access Regen-2	0.00h	18-Feb-10			
R2002 1100	Complete scaffold around Regen-2 s...	96.00h	18-Feb-10	22-Feb-10		
R2002 1110	Remove catalyst residue from below i...	48.00h	22-Feb-10	24-Feb-10		
R2002 1115	Access scaffold below air grid	8.00h	24-Feb-10	24-Feb-10		
R2002 1120	Reliability inspection of internals	12.00h	24-Feb-10	25-Feb-10		
R2002 1140	Demolish refractory inside the shell	144.00h	25-Feb-10	03-Mar-10		
R2002 1150	Grind flush the anchor spots if neces...	24.00h	03-Mar-10	04-Mar-10		
R2002 1160	Shell inspection by Reliability	24.00h	04-Mar-10	05-Mar-10		
R2002 1170	Reweld new anchors if any	48.00h	05-Mar-10	07-Mar-10		
R2002 1180	New Refractory gunniting on the shell...	240.00h	07-Mar-10	17-Mar-10		
R2002 1183	Final Reliability inspection- roof & shell	24.00h	17-Mar-10	18-Mar-10		
R2002 1184	Dry, set and final inspect refractory	24.00h	18-Mar-10	19-Mar-10		
R2002 1185	descaffold inside shell	48.00h	19-Mar-10	21-Mar-10		
R2002 1186	Chip existing refractory or air grid, re...	96.00h	19-Mar-10	23-Mar-10		
R2002 1187	Weld new anchors	48.00h	21-Mar-10	23-Mar-10		
R2002 1188	Refractory application including repai...	48.00h	21-Mar-10	23-Mar-10		

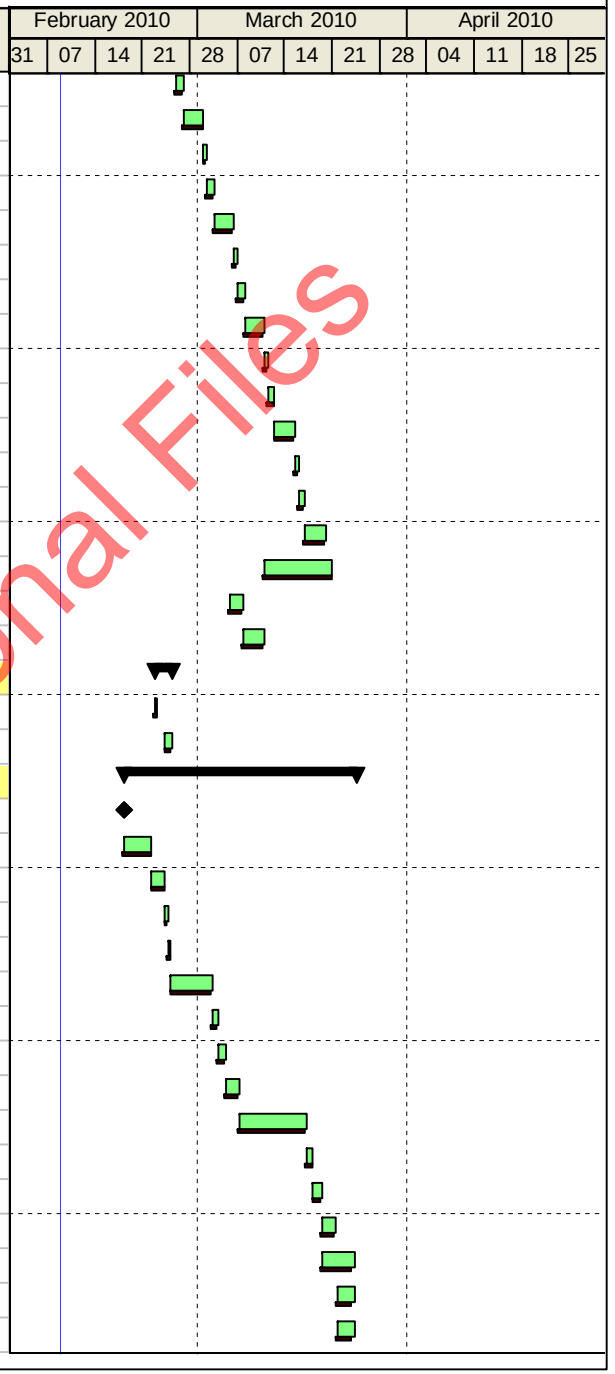


Archives from Personal Files

Activity ID	Activity Name	Original Duration	Planned Start	Planned Finish	Actual Start	Actual Finish
R2002 1195	Final inspection of air grid refractory	8.00h	23-Mar-10	24-Mar-10		
R2002 1205	Torch oil Nozzles - pull out, clean, re...	72.00h	17-Mar-10	20-Mar-10		
Recirculation Stand Pipe Regen1 to Regen2						
R2002 1190	Bridge/ scaffold inside Stand Pipe bet...	8.00h	22-Feb-10	22-Feb-10		
R2002 1200	Inspect Stand pipe internals	8.00h	22-Feb-10	22-Feb-10		
R2002 1210	repairs inside by pass if any	48.00h	22-Feb-10	24-Feb-10		
R2002 1220	Provide scaffold / access to SV2004/...	12.00h	24-Feb-10	25-Feb-10		
R2002 1230	Inspect and repair if any	24.00h	25-Feb-10	26-Feb-10		
R2002 1240	Replacement braided hose	48.00h	26-Feb-10	28-Feb-10		
Orifice Chamber V-2302						
No ReacRegenSection						
V2302 1010	Access O/C for Start of Work	0.00h	14-Feb-10			
V2302 1020	Enter Manways and inspect	8.00h	14-Feb-10	14-Feb-10		
V2302 1030	Internal Scaffold if needed	48.00h	14-Feb-10	16-Feb-10		
V2302 1040	Reliability to mark repair spots	48.00h	16-Feb-10	18-Feb-10		
V2302 1050	refractory repairs inside O/C	120.00h	18-Feb-10	23-Feb-10		
V2302 1052	Refractory Repairs below the FG Slid...	120.00h	18-Feb-10	23-Feb-10		
V2302 1060	Scaffold. Access Flue gas Duct	12.00h	23-Feb-10	24-Feb-10		
V2302 1070	Reliability to mark repair spots on FG...	12.00h	24-Feb-10	24-Feb-10		
V2302 1080	Refractory repair on Duct Spots	48.00h	24-Feb-10	26-Feb-10		
V2302 1090	Access / scaffold to TPSV	24.00h	26-Feb-10	27-Feb-10		
V2302 1100	Inspect / Repair Internal portion of TP...	48.00h	27-Feb-10	01-Mar-10		
Vapour Line						
Bottom Horizontal Portion of VPL						
R2001 5010	Access Vapour Line for start of work	0.00h	13-Feb-10			
R2001 5015	Engineering to complete cold cutting	72.00h	13-Feb-10	16-Feb-10		
R2001 5040	Access Bottom Manway	4.00h	17-Feb-10	17-Feb-10		
R2001 5060	Manual & BJV cleaning of bottom por...	144.00h	17-Feb-10	23-Feb-10		
R2001 5070	Removal and discharge of bottom coke	12.00h	24-Feb-10	24-Feb-10		
R2001 5080	Reliability inspection of horizontal pipe	8.00h	24-Feb-10	24-Feb-10		
R2001 5120	Minor scaffold from bottom if required	8.00h	09-Mar-10	09-Mar-10		
R2001 5150	Release to Engg for welding the 24"...	0.00h		12-Mar-10		
Top Vertical Portion of VPL						
R2001 5020	Open Top Manway	4.00h	16-Feb-10	16-Feb-10		
R2001 5030	Build temporary platform inside top m...	16.00h	16-Feb-10	17-Feb-10		
R2001 5090	Insert Camera / reveiw the condition ...	16.00h	24-Feb-10	25-Feb-10		



Archives from Personal Files

Activity ID	Activity Name	Original Duration	Planned Start	Planned Finish	Actual Start	Actual Finish
R2001 5100	Preparations to lower the jetting mac...	48.00h	25-Feb-10	27-Feb-10		
R2001 5110	Hydrojet / clean Vertical pipe	240.00h	27-Feb-10	09-Mar-10		
R2001 5130	Final reliability inspection of Vertical ...	48.00h	09-Mar-10	11-Mar-10		
Middle Horizontal + Vertical Portion of VPL						
R2001 5050	Scaffold Bottom Vertical Portion	12.00h	17-Feb-10	17-Feb-10		
R2001 5062	Coke Cleaning of small Vertical and ...	8.00h	23-Feb-10	24-Feb-10		
R2001 5140	Decalffold VPL completely	24.00h	11-Mar-10	12-Mar-10		
Heater F-2001						
No ReacRegenSection						
R2002 2010	Access heater for Start of Work	0.00h	22-Feb-10			
R2002 2020	Scaffold if needed	16.00h	22-Feb-10	22-Feb-10		
R2002 2030	Attend Refractory at Burners / Manway	96.00h	22-Feb-10	26-Feb-10		
R2002 2040	Scaffold DFAH outlet to regen 2	48.00h	26-Feb-10	28-Feb-10		
R2002 2050	Refractory Repairs in Outlet Duct	48.00h	28-Feb-10	02-Mar-10		
CO Boiler						
No ReacRegenSection						
V2302 3010	Access CO Boiler for start of work	0.00h	16-Feb-10			
V2302 3020	Inspection of internal Brick Lining	8.00h	16-Feb-10	16-Feb-10		
V2302 3030	Reliability to mark repair / replaceme...	12.00h	16-Feb-10	17-Feb-10		
V2302 3040	Approx 140sqm replacement on roof	240.00h	17-Feb-10	27-Feb-10		
V2302 3050	Replacement of bottom lifted portion	48.00h	27-Feb-10	01-Mar-10		
V2302 3060	Repair of spots on Viewport nozzles	48.00h	01-Mar-10	03-Mar-10		
V2302 3070	Repair of damages on manway openi...	24.00h	03-Mar-10	04-Mar-10		
V2302 3080	Repair of cracks on east side walls	144.00h	04-Mar-10	10-Mar-10		
V2302 3090	Arrest leakage on identified loactions ...	36.00h	10-Mar-10	11-Mar-10		
V2302 3100	Repair of expansion joint on inner St...	24.00h	11-Mar-10	12-Mar-10		
Orifice Chamber Stack						
No ReacRegenSection						
V2302 2010	Access O/C stack for Start of Work	0.00h	16-Feb-10			
V2302 2020	Scaffold inside O/c stack if needed	12.00h	16-Feb-10	17-Feb-10		
V2302 2030	Reliability to mark repair spots	12.00h	17-Feb-10	17-Feb-10		
V2302 2040	Refractory repairs on repair spots	48.00h	17-Feb-10	19-Feb-10		

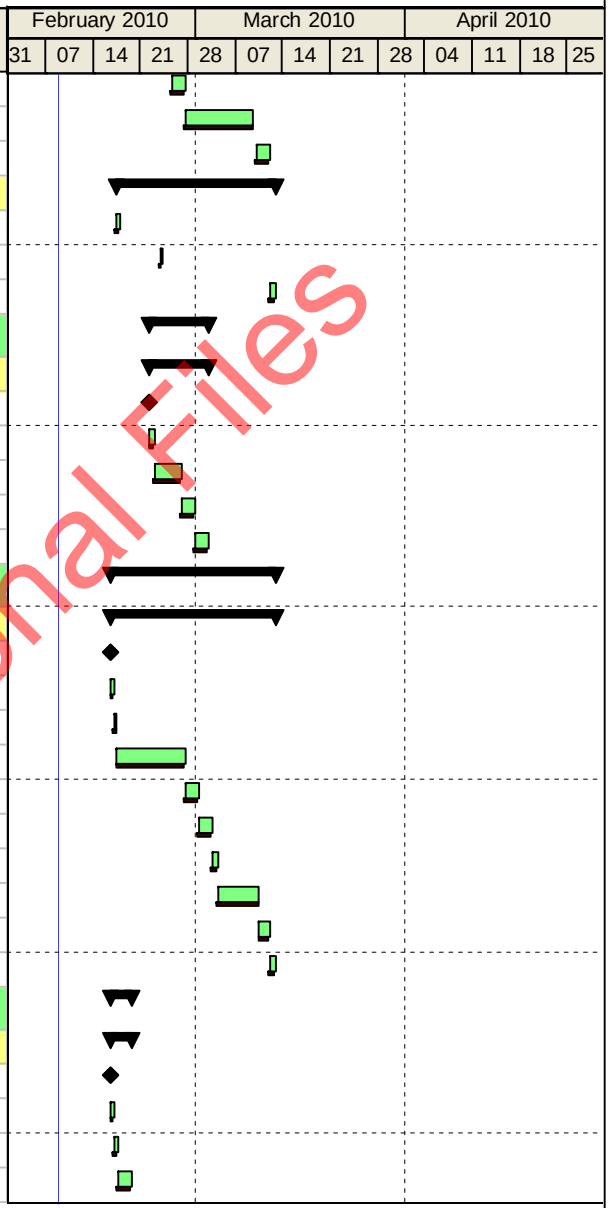

Archives from Personal Files
