






AFC		271	08-Oct-26 16:00	20-Oct-26 23:00	
704-AFC-3002A	TGCU LEAN SOLVENT COOLER	256	08-Oct-26 16:00	20-Oct-26 07:00	
704-AFC-3002A100	Obtain work permit	1	08-Oct-26 16:00	08-Oct-26 17:00	
704-AFC-3002A100	Carry out Blinding (Total 7 Blinds 4" x 4nos 2" x 3nos)	7	08-Oct-26 17:00	09-Oct-26 00:00	
704-AFC-3002A100	Erect scaffolding as required	10	09-Oct-26 01:00	09-Oct-26 11:00	
704-AFC-3002A100	Carry out the removal of 20% / as required plug in zig zag manner	9	09-Oct-26 11:00	09-Oct-26 21:00	
704-AFC-3002A100	Offer as found inspection	2	09-Oct-26 21:00	09-Oct-26 23:00	
704-AFC-3002A100	Carry out the removal of fan side cover for tube inspection	5	09-Oct-26 23:00	10-Oct-26 05:00	
704-AFC-3002A100	Carry out the servicing of all vent / drain / coupling / plugs	24	10-Oct-26 05:00	11-Oct-26 07:00	
704-AFC-3002A100	Carry out fin cleaning by air jet	6	11-Oct-26 07:00	11-Oct-26 14:00	
704-AFC-3002A100	Carry out combing of fins as if required	7	11-Oct-26 14:00	11-Oct-26 21:00	
704-AFC-3002A100	Carry out hydro jetting & air blowing of tubes	30	11-Oct-26 21:00	13-Oct-26 06:00	
704-AFC-3002A101	Carry out NDT as if required	12	13-Oct-26 06:00	13-Oct-26 19:00	
704-AFC-3002A101	Clean the gasket area	4	13-Oct-26 19:00	13-Oct-26 23:00	
704-AFC-3002A101	Offer for Inspection	1	13-Oct-26 23:00	14-Oct-26 00:00	
704-AFC-3002A101	Fix the plug with new gasket	14	14-Oct-26 01:00	14-Oct-26 16:00	
704-AFC-3002A101	IRIS, RVI (NDT BY HPCL)	24	14-Oct-26 16:00	15-Oct-26 18:00	
704-AFC-3002A101	Torquing of Plug	6	15-Oct-26 18:00	16-Oct-26 00:00	
704-AFC-3002A101	Carry out hydrotest	12	16-Oct-26 01:00	16-Oct-26 14:00	
704-AFC-3002A101	Carry out contingency repair	24	16-Oct-26 14:00	17-Oct-26 16:00	
704-AFC-3002A101	offer inspection for contingency repair	2	17-Oct-26 16:00	17-Oct-26 18:00	
704-AFC-3002A101	Reoffer hydrotest	8	17-Oct-26 18:00	18-Oct-26 03:00	
704-AFC-3002A101	Carry out the reinstalation of fan side cover	9	18-Oct-26 03:00	18-Oct-26 12:00	
704-AFC-3002A102	Carry out the external painting as required	24	18-Oct-26 13:00	19-Oct-26 15:00	
704-AFC-3002A102	Carry out the removal of scaffolding as required	6	19-Oct-26 15:00	19-Oct-26 21:00	
704-AFC-3002A102	Carry out deblinding	7	19-Oct-26 21:00	20-Oct-26 05:00	
704-AFC-3002A102	Carry out area housekeeping & equipment handover to operation	2	20-Oct-26 05:00	20-Oct-26 07:00	

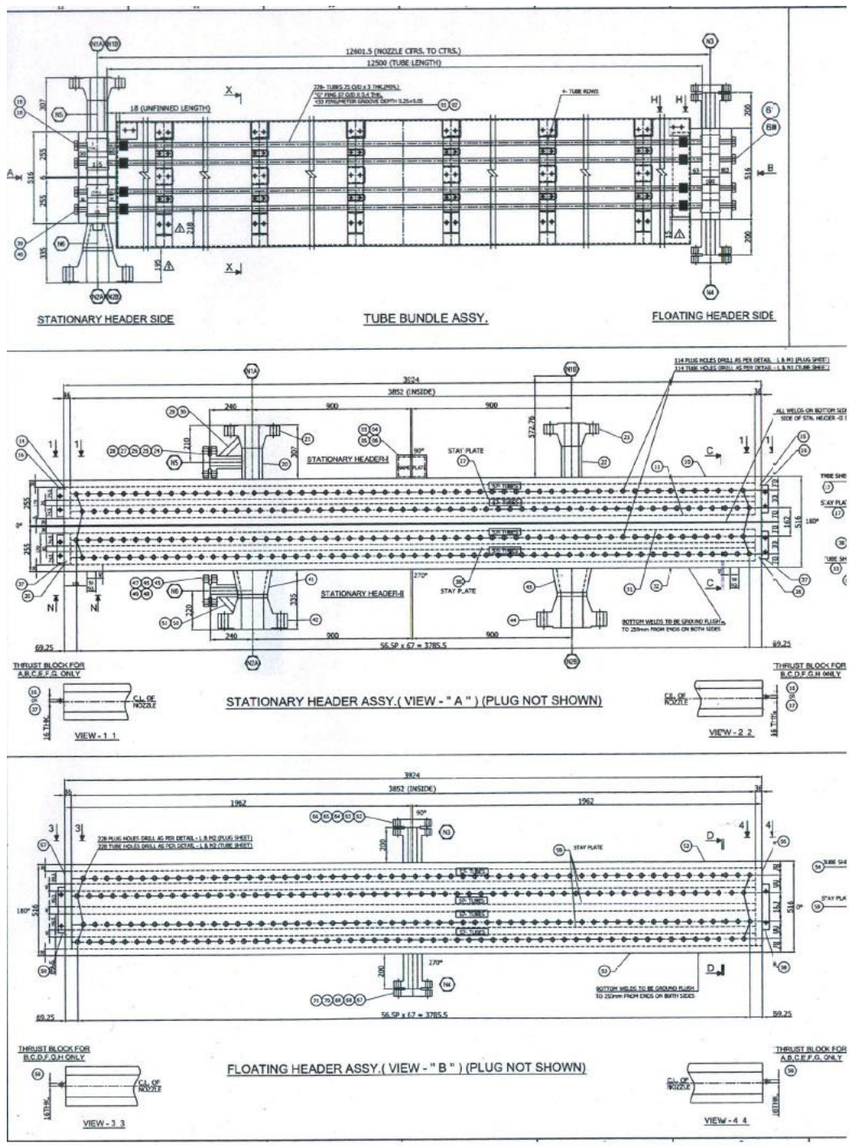

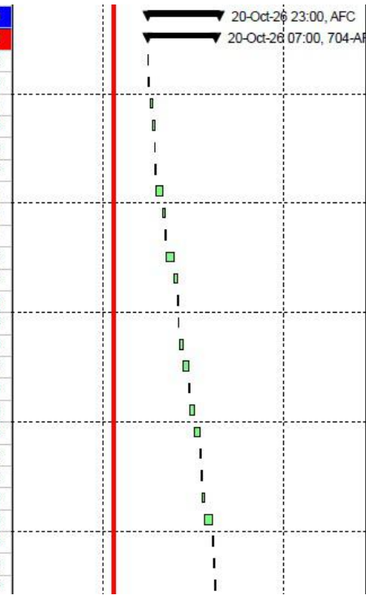

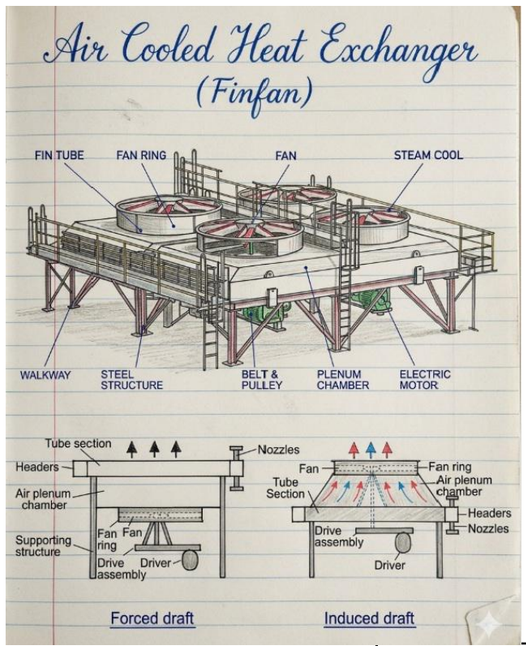

Drw Purpose Code :- 01

Status of Approval :- 01

Dimentions as Mentioned: NA

Drawing Scale :- NTS

Engg Code :- 02 | Backup Info Code :- 04

Angle of Projection: NA | Sheet Size: A3

Statutory Note:
This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!

Drw electronic code

rPlan — AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614

Legal Owner | QR CODE: NA

Description: Typical AFC FRAGNET

AFC Shutdown Works

Drawn By: DFT-01 | Drawn Date: 20260721

Checked Approved by: rPlan-01 | Checked Approved Date: 20260728

Drawing Number: As Barcoaded | Sheet: 1 of 1 | Rev: 00
