
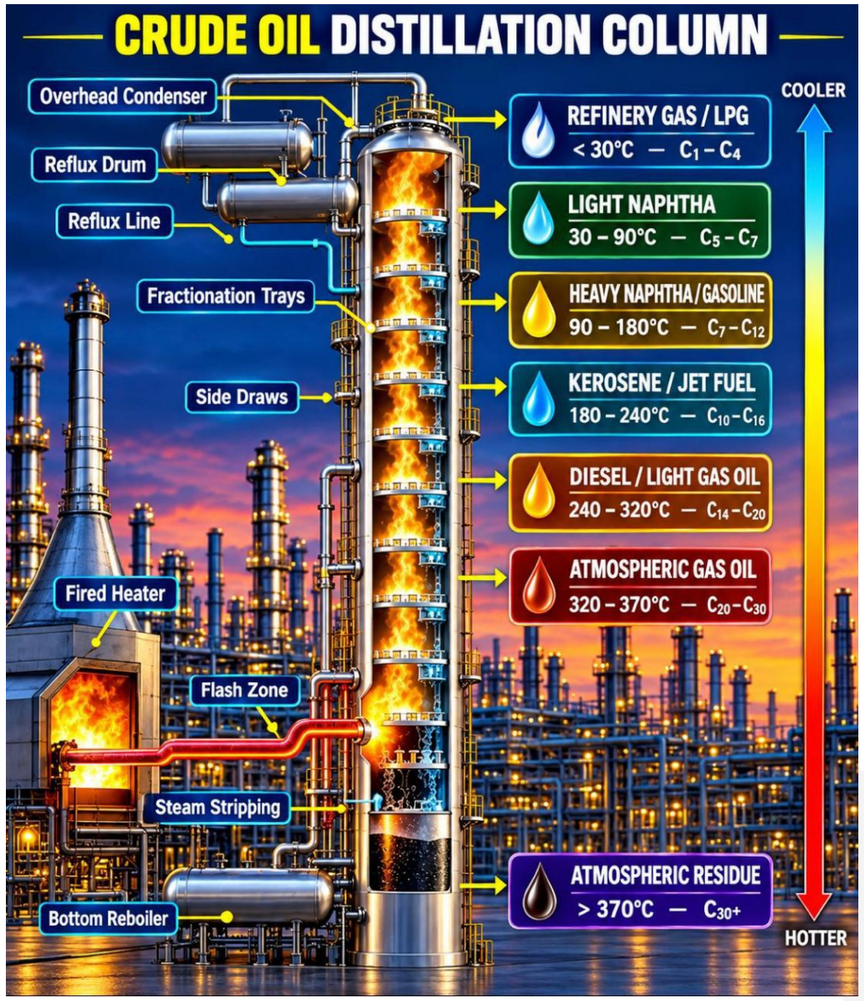


Activity ID	Activity Name	Original Duration	Start	Finish
DHDS.-B-4.PART B.1 COLUMNS		530h	17-Sep-17 16:00	09-Oct-17 18:00
DHDS.-B-4.PART B.1.120-C-01 RECYCLE GAS SCRUBBER 120-C-01		338h	20-Sep-17 00:00	04-Oct-17 02:00
120C01M	120-C-01 Handover by Operations	0h	20-Sep-17 00:00	
A1000	Carry out Spading	24h	20-Sep-17 00:00	21-Sep-17 00:00
A1005	Erect external scaffolding	12h	20-Sep-17 00:00	20-Sep-17 12:00
A3880	Open shell manways	24h	21-Sep-17 00:00	22-Sep-17 00:00
A4380	Provide lighting arrangement	8h	22-Sep-17 00:00	22-Sep-17 08:00
A5080	Enter inside the column	8h	22-Sep-17 08:00	22-Sep-17 16:00
A5100	Remove one tray section each of three trays	12h	22-Sep-17 16:00	23-Sep-17 04:00
A5110	Offer TSR for Inspection	8h	23-Sep-17 04:00	23-Sep-17 12:00
A5120	Remove all distributors,clean and check	24h	23-Sep-17 12:00	24-Sep-17 12:00
A5130	Remove and replace the demister assembly with new one	24h	24-Sep-17 12:00	25-Sep-17 12:00
A5135	Erect internal scaffolding	40h	21-Sep-17 00:00	22-Sep-17 16:00
A5140	Carry out internal cleaning	48h	22-Sep-17 16:00	24-Sep-17 16:00
A5150	offer for inspection	8h	24-Sep-17 16:00	25-Sep-17 00:00
A5160	Carry out power brushing of 3 nos weld seams internally	10h	24-Sep-17 16:00	25-Sep-17 02:00
A5170	Carry out MPI/DP	8h	25-Sep-17 02:00	25-Sep-17 10:00
A5180	Offer for Inspection	8h	25-Sep-17 10:00	25-Sep-17 18:00
A5200	Service all first isolation valves and guage glasses	28h	20-Sep-17 12:00	21-Sep-17 16:00
A5210	Clean all the nozzles	48h	20-Sep-17 12:00	22-Sep-17 12:00
A5220	Open skirt access,and provide scaffolding inside the skirt for inspection of bottom e	12h	20-Sep-17 12:00	21-Sep-17 00:00
A5230	Replace the missing tray valves	12h	25-Sep-17 18:00	26-Sep-17 06:00
A5240	Fix back all the distributors,isolation valves and gauge glass	72h	25-Sep-17 18:00	28-Sep-17 18:00
A5250	Prepare and offer seal pan test to BPCL technology	36h	28-Sep-17 18:00	30-Sep-17 06:00
A5260	Box up tray manways	16h	30-Sep-17 06:00	30-Sep-17 22:00
A5270	Remove internal scaffolding	24h	30-Sep-17 22:00	01-Oct-17 22:00
A5280	Box up all shell manways	24h	01-Oct-17 22:00	02-Oct-17 22:00
A5290	Carry out despading	16h	02-Oct-17 22:00	03-Oct-17 14:00
A5300	Remove external scaffolding except that required for hot bolting of flanges	12h	03-Oct-17 14:00	04-Oct-17 02:00

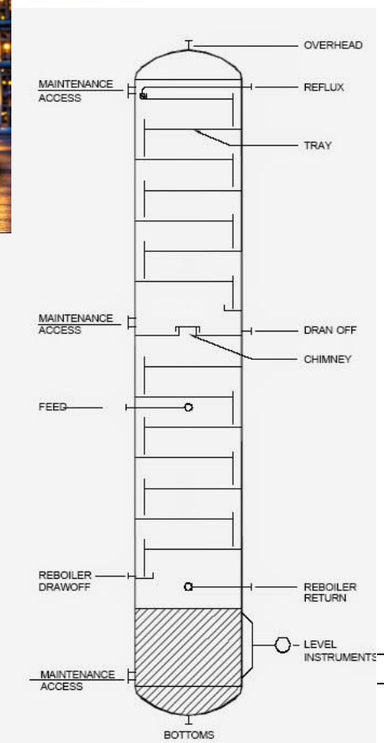

Activity ID	Activity Name	Original Duration	Activity % Complete	Planned Start	Planned Finish	Actual Start	Actual Finish
C1121 170	erect internal scaffolding	6.00h	100%	19-Feb-10	19-Feb-10	26-Feb-10	27-Feb-10
C1121 180	dismantle and remove internal scaffol...	6.00h	0%	09-Mar-10	09-Mar-10		
C1122 - De-Ethaniser							
C1122 000	spade as per the spading list - 10 nos.	12.00h	100%	15-Feb-10	16-Feb-10	14-Feb-10	15-Feb-10
C1122 010	unbolt and open manholes - 2 nos.	5.00h	100%	16-Feb-10	16-Feb-10	16-Feb-10	16-Feb-10
C1122 020	ventilate the column thoroughly	24.00h	100%	16-Feb-10	17-Feb-10	16-Feb-10	16-Feb-10
C1122 030	as found inspection at manholes	3.00h	100%	17-Feb-10	18-Feb-10	15-Feb-10	16-Feb-10
C1122 040	obtain entry permit	3.00h	100%	18-Feb-10	18-Feb-10	19-Feb-10	19-Feb-10
C1122 050	unbolt and remove manways of 30 n...	32.00h	100%	19-Feb-10	20-Feb-10	19-Feb-10	21-Feb-10
C1122 060	pre-inspection by client	6.00h	100%	20-Feb-10	21-Feb-10	21-Feb-10	21-Feb-10
C1122 070	erect internal scaffolding	6.00h	100%	21-Feb-10	21-Feb-10	27-Feb-10	28-Feb-10
C1122 080	prepare to clean the column internally	6.00h	100%	21-Feb-10	21-Feb-10	21-Feb-10	21-Feb-10
C1122 090	clean the column internally	96.00h	100%	06-Mar-10	10-Mar-10	21-Feb-10	27-Feb-10
C1122 100	inspection by client (incl. UT, PT, MT,...	16.00h	100%	11-Mar-10	11-Mar-10	28-Feb-10	28-Feb-10
C1122 110	repairs if any (incl. missing tray valves)	30.00h	100%	11-Mar-10	13-Mar-10	01-Mar-10	01-Mar-10
C1122 120	inspection by client after repairs	6.00h	100%	13-Mar-10	13-Mar-10	01-Mar-10	01-Mar-10
C1122 130	dismantle and remove internal scaffol...	6.00h	100%	13-Mar-10	13-Mar-10	01-Mar-10	01-Mar-10
C1122 140	obtain permit for box-up of tray manw...	3.00h	100%	13-Mar-10	14-Mar-10	01-Mar-10	01-Mar-10
C1122 150	reinstall and close manways of 30 no...	32.00h	18.75%	14-Mar-10	15-Mar-10	01-Mar-10	
C1122 160	obtain permit for box-up of manholes	3.00h	0%	15-Mar-10	15-Mar-10		
C1122 170	close and box-up all manholes - 2 nos.	5.00h	0%	15-Mar-10	16-Mar-10		
C1122 180	despade as per the spaded list	12.00h	0%	16-Mar-10	16-Mar-10		

C2202 - Sponge Absorber							
C2202 000	spade as per the spading list - 9 nos.	8.00h	100%	20-Feb-10	20-Feb-10	16-Feb-10	17-Feb-10
C2202 010	unbolt & open manholes - 2 nos.& du...	5.00h	100%	20-Feb-10	20-Feb-10	17-Feb-10	18-Feb-10
C2202 020	ventilate the column thoroughly	24.00h	100%	20-Feb-10	22-Feb-10	18-Feb-10	18-Feb-10
C2202 030	as found inspection by client	2.00h	100%	22-Feb-10	22-Feb-10	18-Feb-10	18-Feb-10
C2202 040	obtain entry permit	2.00h	100%	22-Feb-10	22-Feb-10	19-Feb-10	19-Feb-10
C2202 050	erect internal scaffolding at the bottom	8.00h	75%	22-Feb-10	22-Feb-10	25-Feb-10	
C2202 060	unbolt and remove the demister pad ...	4.00h	100%	22-Feb-10	22-Feb-10	20-Feb-10	20-Feb-10
C2202 070	unbolt & remove pipe & liquid distribu...	6.00h	100%	22-Feb-10	23-Feb-10	19-Feb-10	20-Feb-10
C2202 080	prepare for unloading / dumping of th...	3.00h	100%	23-Feb-10	23-Feb-10	20-Feb-10	20-Feb-10
C2202 090	unload and dump the packing	36.00h	100%	23-Feb-10	25-Feb-10	20-Feb-10	23-Feb-10
C2202 100	inspection by client	2.00h	0%	25-Feb-10	25-Feb-10		
C2202 110	erect internal scaffolding if require d	16.00h	0%	25-Feb-10	26-Feb-10		
C2202 120	clean the column internally	72.00h	0%	03-Mar-10	06-Mar-10		
C2202 130	clean the demister pad assy & distrib...	6.00h	0%	06-Mar-10	07-Mar-10		
C2202 140	inspection by client (incl. UT, MP, PT,...	12.00h	0%	07-Mar-10	07-Mar-10		
C2202 150	repairs if any	24.00h	0%	07-Mar-10	08-Mar-10		
C2202 160	inspection by client after repair	4.00h	0%	09-Mar-10	09-Mar-10		
C2202 170	dismantle and remove the internal sc...	16.00h	0%	09-Mar-10	09-Mar-10		
C2202 180	box-up the bottom manhole & handhole	3.00h	0%	10-Mar-10	10-Mar-10		
C2202 190	prepare to reload the packing material	3.00h	0%	10-Mar-10	10-Mar-10		
C2202 200	load packing material through the top...	24.00h	0%	10-Mar-10	11-Mar-10		
C2202 210	reinstall pipe & liquid distributor assy.	6.00h	0%	11-Mar-10	12-Mar-10		
C2202 220	reinstall the top demister pad assy.	4.00h	0%	12-Mar-10	12-Mar-10		
C2202 230	close and box-up top manhole	2.00h	0%	12-Mar-10	12-Mar-10		
C2202 240	despade as per the spaded list	8.00h	0%	12-Mar-10	12-Mar-10		

Drw Purpose Code :-
R01- Educational

Status of Approval :-
01

Dimentions as Mentioned
NA

Drawing Scale :- NTS

Engg Code :- 02

Backup Info Code :- 00

Angle of Projection
NA

Sheet Size
A3

Statutory Note:
This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!

Drw electronic code

rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614

Legal Owner

QR CODE
NA

Description:
Typical COLUMN Plan

FRAGNET for a Column SD

Drawn By: DFT-01

Drawn Date 20260711

Checked Approved by rPlan-01

Checked Approved Date 20260722

Drawing Number As Barcoaded

Sheet 1 of 1

Rev 00
