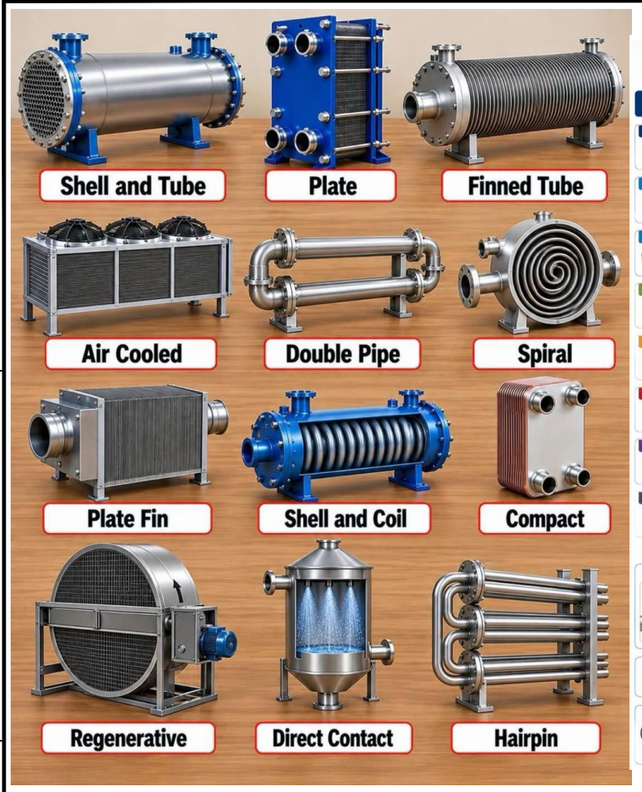
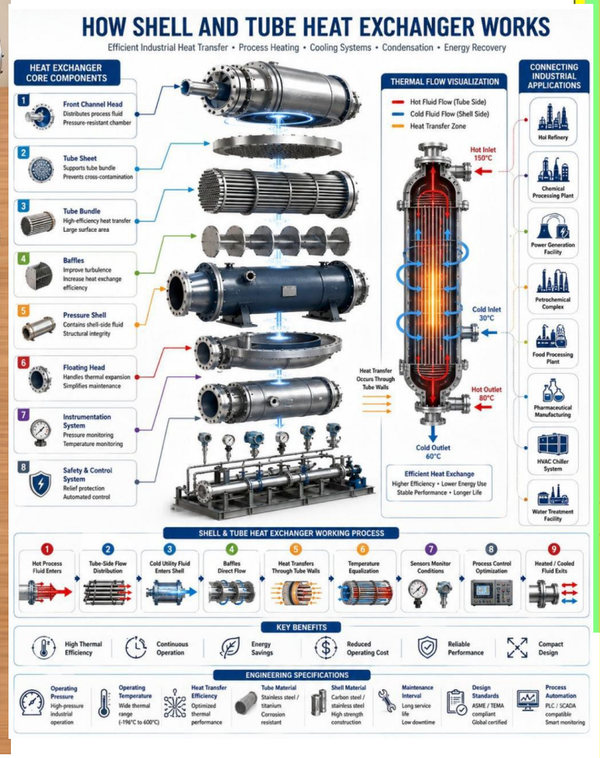





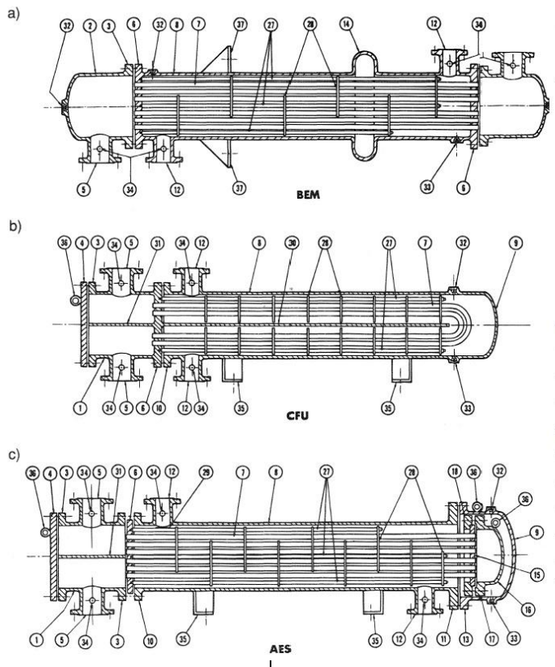


Table 1. Shell and tube geometric terminology

1	Stationary (Front) Head—Channel	20	Slip-on Backing Flange
2	Stationary (Front) Head—Bonnet	21	Floating Tubesheet Skirt
3	Stationary (Front) Head Flange	22	Floating Tubesheet Skirt
4	Channel Cover	23	Packing Box Flange
5	Stationary Head Nozzle	24	Packing
6	Stationary Tubesheet	25	Packing Follower Ring
7	Tubes	26	Lantern Ring
8	Shell	27	Tie Rods and Spacers
9	Shell Cover	28	Transverse Baffles or Support Plates
10	Shell Flange—Stationary Head End	29	Impingement Baffle or Plate
11	Shell Flange—Rear Head End	30	Longitudinal Baffle
12	Shell Nozzle	31	Pass Partition
13	Shell Cover Flange	32	Vent Connection
14	Expansion Joint	33	Drain Connection
15	Floating Tubesheet	34	Instrument Connection
16	Floating Head Cover	35	Support Saddle
17	Floating Head Flange	36	Lifting Lug
18	Floating Head Backing Device	37	Support Bracket
19	Split Shear Ring		

Activity ID	Activity Name	Original Duration	Activity % Complete	BL Project Early Start	BL Project Early Finish	Actual Start	Actual Finish	Total Float
HEAT EXCHANGERS		599h		15-Sep-17 00:00	09-Oct-17 23:00	15-Sep-17 00:00		1h
PART A		599h		15-Sep-17 00:00	09-Oct-17 23:00	15-Sep-17 00:00		1h
STRIPPER BOTTOM FEED EXCHANGER 120-E-01		71h		16-Sep-17 16:00	19-Sep-17 23:00			475h
120E01M	120-E-01 Handover by Operations	0h	0%		16-Sep-17 16:00			475h
HEX1000	Spading	4h	0%	17-Sep-17 00:00	17-Sep-17 04:00			475h
HEX1010	Opening of CB, Shell cover	10h	0%	17-Sep-17 04:00	17-Sep-17 14:00			475h
HEX1030	Removal of tube bundle	4h	0%	17-Sep-17 14:00	17-Sep-17 18:00			475h
HEX1040	Tube bundle cleaning	6h	0%	17-Sep-17 18:00	18-Sep-17 00:00			522h
HEX1045	Inspection of tube bundle	2h	0%	17-Sep-17 18:00	17-Sep-17 20:00			526h
HEX1050	Cleaning of shell & Cover	4h	0%	17-Sep-17 18:00	17-Sep-17 22:00			475h
HEX1055	UT Gauging	2h	0%	17-Sep-17 22:00	18-Sep-17 00:00			475h
HEX1060	Insertion of tube bundle	6h	0%	18-Sep-17 00:00	18-Sep-17 06:00			475h
HEX1070	Assembly of testrings	4h	0%	18-Sep-17 06:00	18-Sep-17 10:00			475h
HEX1080	Shell Test	6h	0%	18-Sep-17 10:00	18-Sep-17 16:00			475h
HEX1085	Shell test witness	1h	0%	18-Sep-17 16:00	18-Sep-17 17:00			475h
HEX1090	Removal of testrings	1h	0%	18-Sep-17 17:00	18-Sep-17 18:00			475h
HEX1100	Assembly of float head coverchannel box	8h	0%	18-Sep-17 18:00	19-Sep-17 02:00			475h
HEX1120	Tube test	8h	0%	19-Sep-17 02:00	19-Sep-17 10:00			475h
HEX1125	Tube test witness	1h	0%	19-Sep-17 10:00	19-Sep-17 11:00			475h
HEX1130	Assembly of shell cover	6h	0%	19-Sep-17 11:00	19-Sep-17 17:00			475h
HEX1140	Despading	6h	0%	19-Sep-17 17:00	19-Sep-17 23:00			475h
HOT COMBINED FEED EXCHANGER 120-E-02A		452h		21-Sep-17 00:00	09-Oct-17 20:00			4h
120E02M	120-E-02A/B/C/D Handover by Operation	0h	0%		21-Sep-17 00:00			1h
HEX245(	Spading	32h	0%	21-Sep-17 00:00	22-Sep-17 08:00			1h
HEX245(	Opening of CB	48h	0%	22-Sep-17 08:00	24-Sep-17 08:00			1h
HEX245(	Removal of tube bundle	24h	0%	24-Sep-17 08:00	25-Sep-17 08:00			1h
HEX245(	Cleaning of shell	24h	0%	25-Sep-17 08:00	26-Sep-17 08:00			4h
HEX245(	UT Gauging	8h	0%	26-Sep-17 08:00	26-Sep-17 16:00			320h
HEX246(	Tube bundle cleaning	48h	0%	25-Sep-17 08:00	27-Sep-17 08:00			4h
HEX294(	Assembly of channel box	8h	0%	20-Sep-17 20:00	21-Sep-17 04:00			431h
HEX294(	Tube test	8h	0%	21-Sep-17 04:00	21-Sep-17 12:00			431h
HEX294(	Tube test witness	1h	0%	21-Sep-17 12:00	21-Sep-17 13:00			431h
HEX294(	Assembly of shell cover	6h	0%	21-Sep-17 13:00	21-Sep-17 19:00			431h
HEX294(	Despading	6h	0%	21-Sep-17 19:00	22-Sep-17 01:00			431h
PRE HEATER II 129-E-103		300h		19-Sep-17 00:00	01-Oct-17 12:00			204h
129E103	129-E-103 Handover by Operations	0h	0%	19-Sep-17 00:00				274h
HEX188(	Spading	8h	0%	27-Sep-17 16:00	28-Sep-17 00:00			66h
HEX188(	Cutting and replacing of IL & OL of channe	10h	0%	28-Sep-17 00:00	28-Sep-17 10:00			204h
HEX188(	Cleaning of tube bundle	12h	0%	28-Sep-17 10:00	28-Sep-17 22:00			204h
HEX188(	Cleaning of shell & Covers	4h	0%	28-Sep-17 22:00	29-Sep-17 02:00			204h
HEX188(	Tube bundle inspection	8h	0%	28-Sep-17 22:00	29-Sep-17 06:00			258h
HEX188(	UT Gauging	2h	0%	29-Sep-17 02:00	29-Sep-17 04:00			204h
HEX188(	Tube Sheet Strenghtening	6h	0%	29-Sep-17 04:00	29-Sep-17 10:00			204h
HEX188(	Radiography 100%	4h	0%	29-Sep-17 10:00	29-Sep-17 14:00			204h
HEX188(	Bring back the Exchanger and erection at	6h	0%	29-Sep-17 14:00	29-Sep-17 20:00			204h
HEX188(	Carry out Power brushing of weld joints	2h	0%	29-Sep-17 20:00	29-Sep-17 22:00			204h
HEX188(	Carry out MPI test of weld joints & inspecti	2h	0%	29-Sep-17 22:00	30-Sep-17 00:00			204h
HEX189(	Shell Test	6h	0%	30-Sep-17 00:00	30-Sep-17 06:00			204h
HEX189(	Shell test witness	1h	0%	30-Sep-17 06:00	30-Sep-17 07:00			204h
HEX189(	Assembly of channel covershell cover	14h	0%	30-Sep-17 07:00	30-Sep-17 21:00			204h
HEX189(	Tube test	8h	0%	30-Sep-17 21:00	01-Oct-17 05:00			204h
HEX189(	Tube test witness	1h	0%	01-Oct-17 05:00	01-Oct-17 06:00			204h
HEX189(	De spading	6h	0%	01-Oct-17 06:00	01-Oct-17 12:00			204h
PRE HEATER II 129-E-203		70h		19-Sep-17 00:00	21-Sep-17 22:00			434h
129E203	Handover by Operations	0h	0%	19-Sep-17 00:00				438h
HEX467(	Spading	4h	0%	19-Sep-17 04:00	19-Sep-17 08:00			434h
HEX467(	Opening of CB & covers	10h	0%	19-Sep-17 08:00	19-Sep-17 18:00			434h
HEX467(	Cleaning of shell & Covers	4h	0%	19-Sep-17 18:00	19-Sep-17 22:00			434h
HEX467(	UT Gauging	2h	0%	19-Sep-17 22:00	20-Sep-17 00:00			434h
HEX468(	In situ Tube bundle cleaning	8h	0%	19-Sep-17 16:00	20-Sep-17 00:00			434h
HEX468(	Inspection of tube bundle	2h	0%	19-Sep-17 22:00	20-Sep-17 00:00			434h
HEX468(	Carry out RFET for 100% of tubes	8h	0%	20-Sep-17 00:00	20-Sep-17 08:00			434h
HEX468(	Assembly of channel box	8h	0%	20-Sep-17 08:00	20-Sep-17 16:00			434h
HEX468(	Shell Test	6h	0%	20-Sep-17 16:00	20-Sep-17 22:00			434h
HEX468(	Shell test witness	1h	0%	20-Sep-17 22:00	20-Sep-17 23:00			434h
HEX468(	Assembly of channel box covershell cove	8h	0%	20-Sep-17 23:00	21-Sep-17 07:00			434h
HEX468(	Tube test	8h	0%	21-Sep-17 07:00	21-Sep-17 15:00			434h
HEX468(	Tube test witness	1h	0%	21-Sep-17 15:00	21-Sep-17 16:00			434h
HEX468(	Despading	6h	0%	21-Sep-17 16:00	21-Sep-17 22:00			434h



Drw Purpose Code :-
R01-Educational

Status of Approval :-
01

Dimentions as Mentioned
NA

Drawing Scale :- NTS

Engg Code :- 02

Backup Info Code :- 01

Angle of Projection
NA

Sheet Size
A3

Statutory Note:
This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!

Drw electronic code

rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614

Legal Owner

QR CODE

NA

Description:
Heat Exchangers

Exchangers - TYPICAL FRAGNET

Drawn By: DFT-01

Drawn Date 20260715

Checked Approved by rPlan-01

Checked Approved Date 20260820

Drawing Number As Barcoaded

Sheet 1 of 1

Rev 00
