



Pre Shutdown		**6h**	**19-Jan-2017 12:00**	**19-Jan-2017 18:00**
SIN2-5010	Erect Scaffolding	4h	19-Jan-2017 12:00	19-Jan-2017 16:00
SIN2-5020	Remove Insulation	2h	19-Jan-2017 16:00	19-Jan-2017 18:00
Shutdown		**219h**	**8-Feb-2017 11:00**	**17-Feb-2017 14:00**
SIN2-5030	Verify LT&T and Obtain PTW	1h	8-Feb-2017 11:00	8-Feb-2017 12:00
SIN2-5040	Mechanical Isolation & Blinding	16h	8-Feb-2017 12:00	9-Feb-2017 4:00
SIN2-5050	Remove Instrument Connections	4h	9-Feb-2017 4:00	9-Feb-2017 8:00
SIN2-5060	Open Manway	8h	9-Feb-2017 4:00	9-Feb-2017 12:00
SIN2-5070	Arrange Air Movers & Lights	2h	9-Feb-2017 12:00	9-Feb-2017 14:00
SIN2-5080	Air Ventilation	6h	9-Feb-2017 14:00	9-Feb-2017 20:00
SIN2-5090	Rescue Team Setup	1h	9-Feb-2017 20:00	9-Feb-2017 21:00
SIN2-5100	Obtain CSE Permit	1h	9-Feb-2017 21:00	9-Feb-2017 22:00
SIN2-5110	Erect Internal Scaffolding	10h	9-Feb-2017 22:00	10-Feb-2017 8:00
SIN2-5120	Preliminary inspection	1h	10-Feb-2017 8:00	10-Feb-2017 9:00
SIN2-5130	Internal Cleaning	6h	10-Feb-2017 9:00	10-Feb-2017 15:00
SIN2-5140	Inspection after Cleaning	2h	10-Feb-2017 15:00	10-Feb-2017 17:00
SIN2-5150	Anchor bolt welding	8h	10-Feb-2017 17:00	11-Feb-2017 1:00
SIN2-5160	Refractory Repair	48h	13-Feb-2017 1:00	15-Feb-2017 1:00
SIN2-5170	Service Main Burner Dampers (3 nos)	48h	13-Feb-2017 1:00	15-Feb-2017 1:00
SIN2-5180	Inspection after Repair	2h	15-Feb-2017 1:00	15-Feb-2017 3:00
SIN2-5190	Remove Internal Scaffolding	4h	15-Feb-2017 3:00	15-Feb-2017 7:00
SIN2-5200	Final Inspection	1h	16-Feb-2017 6:00	16-Feb-2017 7:00
SIN2-5210	Obtain Box up Clearance Certificate	1h	16-Feb-2017 7:00	16-Feb-2017 8:00
SIN2-5220	Remove Air Movers & Lights	1h	16-Feb-2017 8:00	16-Feb-2017 9:00
SIN2-5230	Box up Manway	8h	16-Feb-2017 9:00	16-Feb-2017 17:00
SIN2-5240	Remove Insulation For CUI	8h	9-Feb-2017 12:00	9-Feb-2017 20:00
SIN2-5250	External Inspection	6h	9-Feb-2017 20:00	10-Feb-2017 2:00
SIN2-5260	Fix Back Insulation after CUI	12h	10-Feb-2017 2:00	10-Feb-2017 14:00
SIN2-5270	Fix Back Instrument Connections	4h	16-Feb-2017 17:00	16-Feb-2017 21:00
SIN2-5280	Carry out De-Blinding	16h	16-Feb-2017 21:00	17-Feb-2017 13:00
SIN2-5300	Housekeeping & Close PTW	1h	17-Feb-2017 13:00	17-Feb-2017 14:00
SIN2-5310	Mechanical Completion	0h		17-Feb-2017 14:00
Post Shutdown		**132h**	**17-Feb-2017 14:00**	**23-Feb-2017 2:00**
SIN2-5320	Fix Back Insulation	4h	17-Feb-2017 14:00	17-Feb-2017 18:00
SIN2-5330	Remove Scaffolding	2h	23-Feb-2017 0:00	23-Feb-2017 2:00

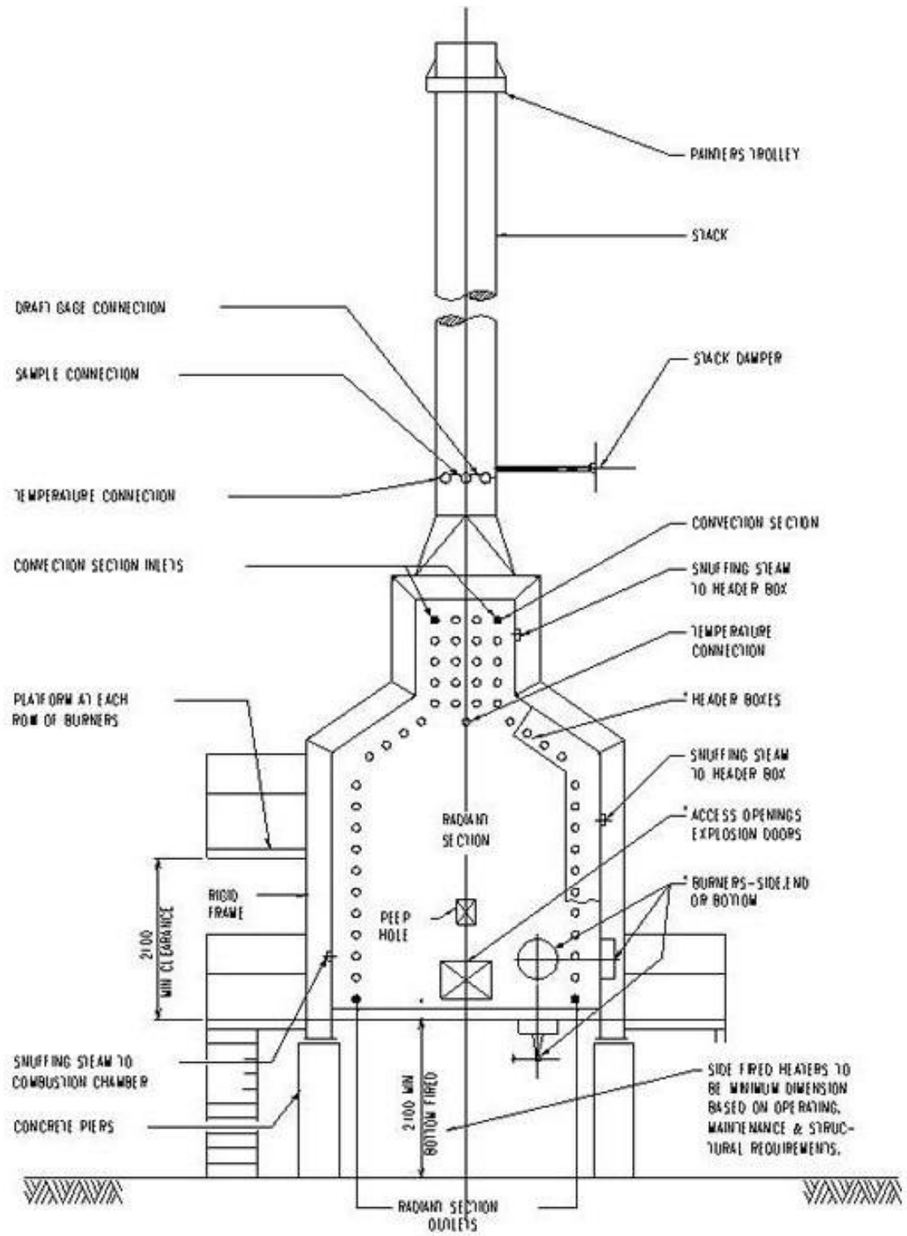

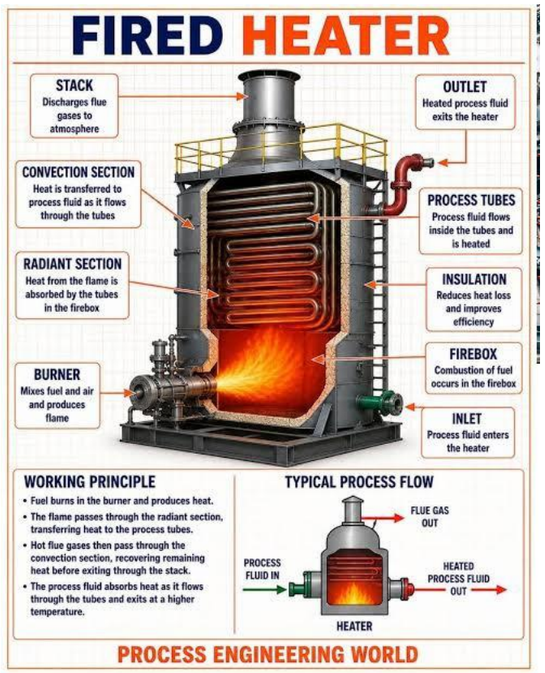

Drw Purpose Code :- R01-Educational	**Statutory Note:** This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!	Description: Typical HEATERS PLAN FURNACES TYP FRAGNET	
Status of Approval :- 01			
Dimentions as Mentioned NA	Drw electronic code		
Drawing Scale :-NTS	rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614	Drawn By: DFT-01	Drawn Date 20260713
Engg Code :- 02 / Backup Info Code :- 01	Legal Owner / QR CODE	Checked Approved by rPlan-01	Checked Approved Date 20260719
Angle of Projection NA / Sheet Size A3	NA	Drawing Number As Barcoaded / Sheet 1 of 1 / Rev 00	
