




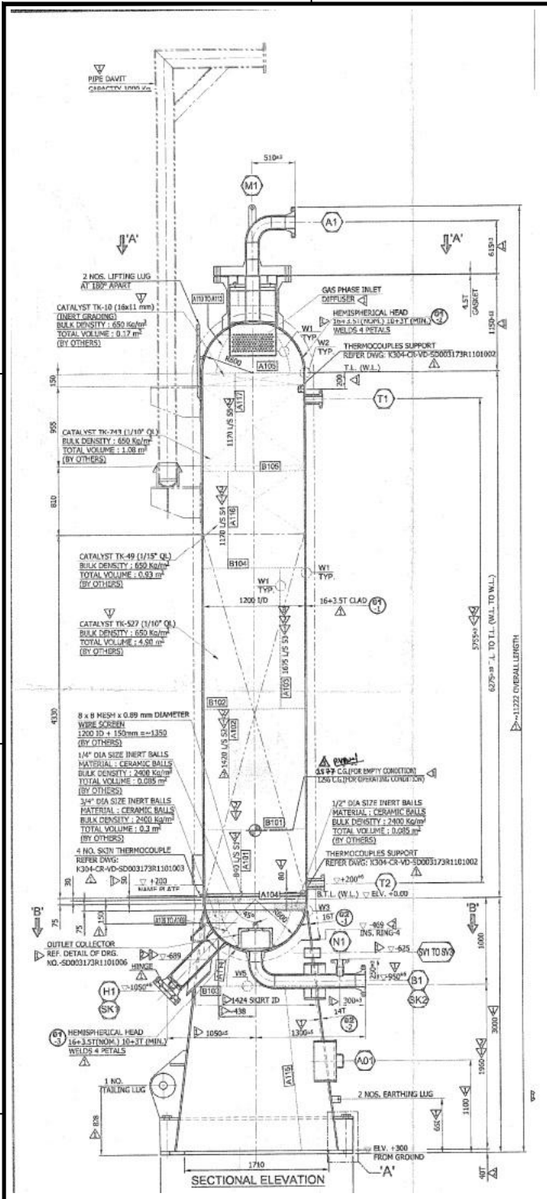

2640-D-016-Reactor#1		324			23-Jan-20 11:00	30-Jan-20 20:00	23-Jan-20 11:00 A	01-Feb-20 23:00	
R#1-1000	Cleaning of plug Distributor, Inner and Outer screen by manually & h	140	CR	100%	23-Jan-20 11:00	29-Jan-20 07:00	23-Jan-20 11:00 A	26-Jan-20 10:00	
Inner Screen		271			25-Jan-20 16:00	29-Jan-20 22:00	25-Jan-20 10:00 A	01-Feb-20 23:00	
R#1-1010	Carryout inspection of inner screen by ADNOC & UOP	4	ADNOC	100%	25-Jan-20 16:00	25-Jan-20 20:00	25-Jan-20 10:00 A	25-Jan-20 14:00	
R#1-1020	Recommendation by ADNOC & UOP	4	ADNOC	100%	25-Jan-20 20:00	26-Jan-20 00:00	25-Jan-20 14:00 A	25-Jan-20 17:00	
R#1-1030	Perforated louver cutting and removal	8	Johnson Screen	100%	26-Jan-20 01:00	26-Jan-20 09:00	25-Jan-20 22:00 A	26-Jan-20 07:00	
R#1-1040	Carryout welding repair	12	Johnson Screen	100%	26-Jan-20 09:00	26-Jan-20 21:00	26-Jan-20 07:00 A	26-Jan-20 20:00	
R#1-1050	NDT inspection by ADNOC & UOP	6	ADNOC	100%	28-Jan-20 07:00	28-Jan-20 13:00	28-Jan-20 07:00 A	28-Jan-20 13:00	
R#1-1060	Reactor inlet elbow thread tapping	6	CR	100%	28-Jan-20 14:00	28-Jan-20 20:00	28-Jan-20 14:00 A	29-Jan-20 10:00	
R#1-1070	Reactor inlet elbow damaged nuts replacement & welding	8	CR	100%	29-Jan-20 10:00	29-Jan-20 18:00	29-Jan-20 07:00 A	29-Jan-20 15:00	
R#1-1080	NDT inspection by ADNOC & UOP	2	ADNOC	100%	29-Jan-20 18:00	29-Jan-20 20:00	29-Jan-20 15:00 A	29-Jan-20 17:00	
R#1-1095	Reactor louvers repair as per IML	120	Johnson Screen	100%			31-Jan-20 22:00 A	01-Feb-20 21:00	IML Recieved 31st Jan 3pm
R#1-1096	Despatch for installation	2	CR	100%	29-Jan-20 20:00	29-Jan-20 22:00	01-Feb-20 21:00 A	01-Feb-20 23:00	
Outer Screen		111			26-Jan-20 01:00	30-Jan-20 20:00	26-Jan-20 10:00 A	30-Jan-20 04:00	
R#1-1100	Recommendation by ADNOC & UOP	4	ADNOC	100%	26-Jan-20 01:00	26-Jan-20 05:00	26-Jan-20 10:00 A	26-Jan-20 15:00	
R#1-1110	Repair welding between channel rod & blank off	12	Johnson Screen	100%	29-Jan-20 05:00	29-Jan-20 17:00	28-Jan-20 07:00 A	29-Jan-20 13:00	
R#1-1120	NDT inspection by ADNOC & UOP	4	ADNOC	100%	29-Jan-20 18:00	29-Jan-20 22:00	29-Jan-20 18:00 A	29-Jan-20 22:00	
R#1-1130	Support base bolt replacement & welding	12	CR	100%	29-Jan-20 22:00	30-Jan-20 10:00	29-Jan-20 18:00 A	30-Jan-20 00:00	
R#1-1135	Support base plate nuts tapping	6	CR	100%	30-Jan-20 10:00	30-Jan-20 16:00	30-Jan-20 00:00 A	30-Jan-20 02:00	
R#1-1140	NDT inspection by ADNOC & UOP	2	ADNOC	100%	30-Jan-20 16:00	30-Jan-20 18:00	30-Jan-20 03:00 A	30-Jan-20 04:00	
R#1-1150	Despatch for installation	2	CR	100%	30-Jan-20 18:00	30-Jan-20 20:00	30-Jan-20 03:00 A	30-Jan-20 04:00	
2640-D-017-Reactor#2		176			23-Jan-20 18:00	31-Jan-20 02:00	23-Jan-20 18:00 A	30-Jan-20 23:00	
R#2-1060	Cleaning of plug Distributor, Inner and Outer screen by manually & h	140	CR	100%	23-Jan-20 18:00	29-Jan-20 14:00	23-Jan-20 18:00 A	27-Jan-20 03:00	
Inner Screen		123			25-Jan-20 23:00	31-Jan-20 02:00	25-Jan-20 10:00 A	30-Jan-20 23:00	
R#2-1000	Carryout inspection of inner screen by ADNOC & UOP	4	ADNOC	100%	25-Jan-20 23:00	26-Jan-20 03:00	25-Jan-20 10:00 A	25-Jan-20 14:00	
R#2-1010	Recommendation by ADNOC & UOP	4	ADNOC	100%	26-Jan-20 05:00	26-Jan-20 09:00	25-Jan-20 14:00 A	25-Jan-20 18:00	
R#2-1020	Perforated louver cutting and removal	8	Johnson Screen	100%	26-Jan-20 09:00	26-Jan-20 17:00	27-Jan-20 07:00 A	27-Jan-20 14:00	
R#2-1030	Carryout welding repair	22	Johnson Screen	100%	29-Jan-20 03:00	30-Jan-20 01:00	27-Jan-20 14:00 A	28-Jan-20 03:00	
R#2-1040	NDT inspection by ADNOC & UOP	6	ADNOC	100%	28-Jan-20 11:00	28-Jan-20 17:00	28-Jan-20 11:00 A	29-Jan-20 10:00	
R#2-1050	Reactor inlet elbow thread tapping	8	CR	100%	30-Jan-20 18:00	31-Jan-20 02:00	28-Jan-20 18:00 A	29-Jan-20 14:00	
R#2-1070	Reactor inlet elbow damaged nuts replacement & welding	4	CR	100%	29-Jan-20 18:00	29-Jan-20 22:00	30-Jan-20 15:00 A	30-Jan-20 19:00	
R#2-1080	NDT inspection by ADNOC & UOP	2	ADNOC	100%	29-Jan-20 22:00	30-Jan-20 00:00	30-Jan-20 19:00 A	30-Jan-20 21:00	
R#2-1090	Despatch for installation	2	CR	100%	30-Jan-20 00:00	30-Jan-20 02:00	30-Jan-20 21:00 A	30-Jan-20 23:00	
Outer Screen		96			26-Jan-20 09:00	30-Jan-20 07:00	27-Jan-20 09:00 A	30-Jan-20 09:00	
R#2-1100	Recommendation by ADNOC & UOP	4	ADNOC	100%	26-Jan-20 09:00	26-Jan-20 13:00	27-Jan-20 09:00 A	27-Jan-20 13:00	
R#2-1110	Repair welding between channel rod & blank off	12	Johnson Screen	100%	28-Jan-20 07:00	28-Jan-20 19:00	28-Jan-20 07:00 A	28-Jan-20 20:00	
R#2-1120	NDT inspection by ADNOC & UOP	4	ADNOC	100%	29-Jan-20 07:00	29-Jan-20 11:00	29-Jan-20 07:00 A	29-Jan-20 11:00	
R#2-1130	Support base bolt replacement & welding	12	CR	100%	29-Jan-20 11:00	29-Jan-20 23:00	29-Jan-20 11:00 A	29-Jan-20 23:00	
R#2-1135	Support base plate nuts tapping	4	CR	100%	29-Jan-20 23:00	30-Jan-20 03:00	29-Jan-20 19:00 A	29-Jan-20 23:00	

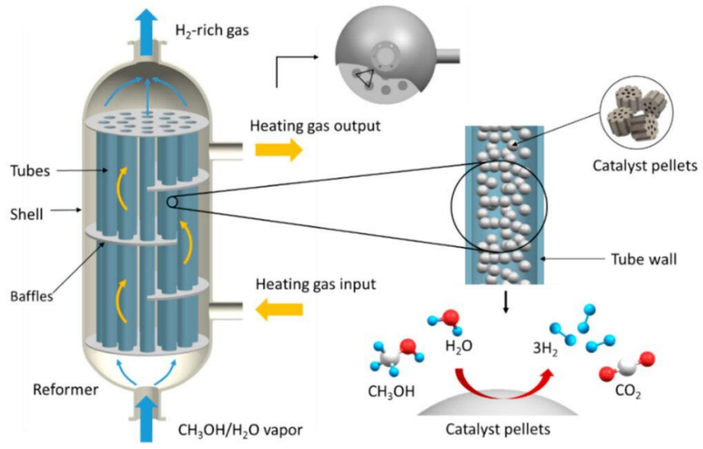

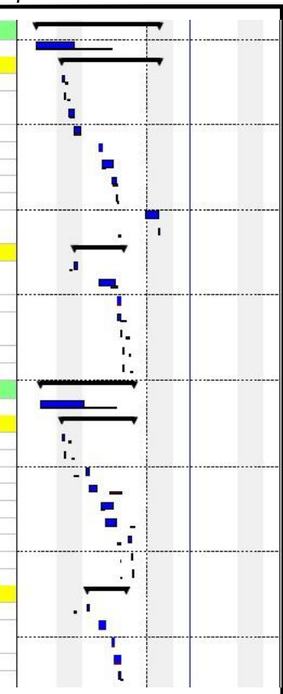

Drw Purpose Code :-
R01-Educational

Status of Approval :-
01

Dimentions as Mentioned
NA

Drawing Scale :- NTS

Engg Code :- 02

Backup Info Code :- 04

Angle of Projection
NA

Sheet Size
A3

Statutory Note:
This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!

Drw electronic code

rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614

Legal Owner

QR CODE
NA

Description:
Typical Reactors FRAGNET

REACTORS S/D

Drawn By: DFT-01

Drawn Date 20260717

Checked Approved by rPlan-01

Checked Approved Date 20260801

Drawing Number As Barcoaded

Sheet 1 of 1

Rev 00
