





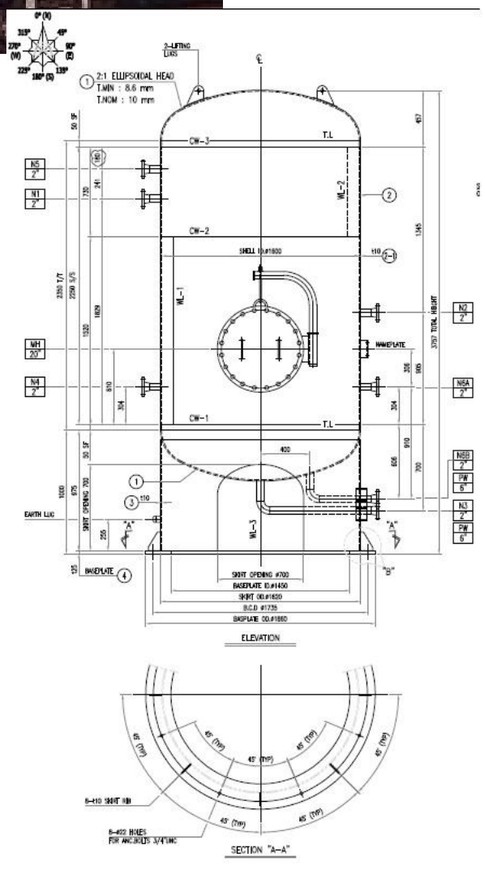

Activity ID	Activity Name	Original Duration	Activity % Complete	BL Project Early Start	BL Project Early Finish	Actual Start	Actual Finish	Total Float
VESSELS		494h		15-Sep-17 00:00	06-Oct-17 08:00	15-Sep-17 16:00		90h
PART A		494h		15-Sep-17 00:00	06-Oct-17 08:00	15-Sep-17 16:00		90h
FEED COALESCER & SURGE DRUM 120-V-01		107h		21-Sep-17 00:00	25-Sep-17 11:00			349h
120V01M	120-V-01 Handover by Operations	0h	0%	21-Sep-17 00:00				349h
HEXx19	Spading	4h	0%	21-Sep-17 00:00	21-Sep-17 04:00			349h
HEXx19	open manhole cover	4h	0%	21-Sep-17 04:00	21-Sep-17 08:00			349h
HEXx19	erect internal scaffolding	8h	0%	21-Sep-17 08:00	21-Sep-17 16:00			349h
HEXx19	manually clean the vessel internally	48h	0%	21-Sep-17 16:00	23-Sep-17 16:00			349h
HEXx19	Internal Inspection	4h	0%	23-Sep-17 16:00	23-Sep-17 20:00			349h
HEXx19	Internal UT Guaging	4h	0%	23-Sep-17 20:00	24-Sep-17 00:00			353h
HEXx19	Power Brushing of weld Joints	4h	0%	23-Sep-17 20:00	24-Sep-17 00:00			349h
HEXx19	Carry out MPI testing	4h	0%	24-Sep-17 00:00	24-Sep-17 04:00			349h
HEXx19	Servicing of Guage glass	6h	0%	21-Sep-17 04:00	21-Sep-17 10:00			421h
HEXx19	dismantle & remove internal scaffolding	6h	0%	24-Sep-17 04:00	24-Sep-17 10:00			349h
HEXx19	Box up & prepare vessel for hydrotest	6h	0%	24-Sep-17 10:00	24-Sep-17 16:00			349h
HEXx19	Carry out Hydrotest	6h	0%	24-Sep-17 16:00	24-Sep-17 22:00			349h
HEXx19	Depressurise	1h	0%	24-Sep-17 22:00	24-Sep-17 23:00			349h
HEXx19	Despade	12h	0%	24-Sep-17 23:00	25-Sep-17 11:00			349h
SEPARATOR 120-V-02		103h		21-Sep-17 00:00	25-Sep-17 11:00	16-Sep-17 12:00		439h
120V02M	120-V-02 Handover by Operations	0h	100%	21-Sep-17 00:00		16-Sep-17 12:00		
Z5950	Spading	4h	2%	21-Sep-17 00:00	21-Sep-17 04:00	16-Sep-17 12:00		439h
Z5960	open manhole cover	4h	0%	21-Sep-17 04:00	21-Sep-17 08:00			439h
Z5970	erect internal scaffolding	8h	0%	21-Sep-17 08:00	21-Sep-17 16:00			439h
Z5980	manually clean the vessel internally	48h	0%	21-Sep-17 16:00	23-Sep-17 16:00			439h
Z5990	Servicing of Guage glass	6h	0%	21-Sep-17 04:00	21-Sep-17 10:00			511h
Z6000	Internal Inspection	4h	0%	23-Sep-17 16:00	23-Sep-17 20:00			439h
Z6010	dismantle & remove internal scaffolding	6h	0%	24-Sep-17 04:00	24-Sep-17 10:00			439h
Z6020	Box up & prepare vessel for hydrotest	6h	0%	24-Sep-17 10:00	24-Sep-17 16:00			439h
Z6030	Carry out Hydrotest	6h	0%	24-Sep-17 16:00	24-Sep-17 22:00			439h
Z6040	Depressurise	1h	0%	24-Sep-17 22:00	24-Sep-17 23:00			439h
Z6050	Power Brushing of weld Joints	4h	0%	23-Sep-17 20:00	24-Sep-17 00:00			439h
Z6060	Internal UT Guaging	4h	0%	23-Sep-17 20:00	24-Sep-17 00:00			443h
Z6070	Despade	12h	0%	24-Sep-17 23:00	25-Sep-17 11:00			439h
Z6080	Carry out MPI testing	4h	0%	24-Sep-17 00:00	24-Sep-17 04:00			439h
RECYCLE GAS SCRUBBER KOD 120-V-03		94h		19-Sep-17 16:00	23-Sep-17 14:00			394h
120V03M	120-V-03 Handover by Operations	0h	0%	19-Sep-17 16:00				394h
HEXx22	Spading	4h	0%	19-Sep-17 16:00	19-Sep-17 20:00			394h
HEXx22	open manhole cover	4h	0%	19-Sep-17 20:00	20-Sep-17 00:00			394h
HEXx22	erect internal scaffolding	8h	0%	20-Sep-17 00:00	20-Sep-17 08:00			394h
HEXx22	Remove demister	8h	0%	20-Sep-17 08:00	20-Sep-17 16:00			394h
HEXx22	manually clean the vessel internally	15h	0%	20-Sep-17 16:00	21-Sep-17 07:00			394h

Pre Shutdown		4h	14-Jan-2017 10:00	14-Jan-2017 14:00
SAST-5010	Erect Scaffolding	4h	14-Jan-2017 10:00	14-Jan-2017 14:00
Shutdown		172h	7-Feb-2017 15:00	14-Feb-2017 19:00
SAST-5030	Verify LT&T and Obtain PTW	1h	7-Feb-2017 15:00	7-Feb-2017 16:00
SAST-5040	Remove Sump Covers	4h	7-Feb-2017 16:00	7-Feb-2017 20:00
SAST-5050	Mechanical Isolation & Blinding	8h	7-Feb-2017 20:00	8-Feb-2017 4:00
SAST-5060	Open Manway & Nozzles	6h	8-Feb-2017 4:00	8-Feb-2017 10:00
SAST-5070	Arrange Air Movers & Lights	1h	8-Feb-2017 10:00	8-Feb-2017 11:00
SAST-5080	Air Ventilation	6h	8-Feb-2017 11:00	8-Feb-2017 17:00
SAST-5090	Rescue Team Setup	1h	8-Feb-2017 17:00	8-Feb-2017 18:00
SAST-5100	Obtain CSE Permit	2h	8-Feb-2017 18:00	8-Feb-2017 20:00
SAST-5110	Erect Internal Scaffolding	4h	8-Feb-2017 20:00	9-Feb-2017 0:00
SAST-5120	Preliminary inspection	2h	9-Feb-2017 0:00	9-Feb-2017 2:00
SAST-5130	Internal Cleaning	8h	9-Feb-2017 2:00	9-Feb-2017 10:00
SAST-5140	Inspection after Cleaning	4h	9-Feb-2017 10:00	9-Feb-2017 14:00
SAST-5150	Repair if any	12h	9-Feb-2017 14:00	10-Feb-2017 2:00
SAST-5160	Inspection after Repair	4h	10-Feb-2017 2:00	10-Feb-2017 6:00
SAST-5170	Remove Internal Scaffolding	2h	10-Feb-2017 6:00	10-Feb-2017 8:00
SAST-5180	Final Inspection	1h	13-Feb-2017 18:00	13-Feb-2017 19:00
SAST-5190	Obtain Box up Clearance Certificate	1h	13-Feb-2017 19:00	13-Feb-2017 20:00
SAST-5200	Remove Air Movers & Lights	2h	13-Feb-2017 20:00	13-Feb-2017 22:00
SAST-5210	Box up Manway & Nozzles	8h	13-Feb-2017 22:00	14-Feb-2017 6:00
SAST-5220	Carry out De-Blinding	8h	14-Feb-2017 6:00	14-Feb-2017 14:00
SAST-5245	Fix Back Sump Covers	4h	14-Feb-2017 14:00	14-Feb-2017 18:00
SAST-5250	Housekeeping & Close PTW	1h	14-Feb-2017 18:00	14-Feb-2017 19:00
SAST-5260	Mechanical Completion	0h		14-Feb-2017 19:00
Post Shutdown		2h	21-Feb-2017 0:00	21-Feb-2017 2:00
SAST-5280	Remove Scaffolding	2h	21-Feb-2017 0:00	21-Feb-2017 2:00

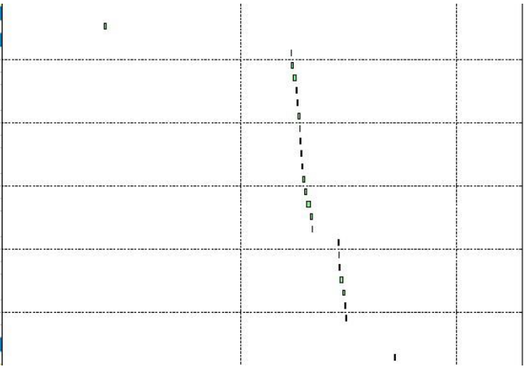

Drw Purpose Code :-
R01-Educational

Status of Approval :-
01

Dimentions as Mentioned
NA

Drawing Scale :- NTS

Engg Code :- 02

Backup Info Code :- 00

Angle of Projection: NA

Sheet Size: A3

Statutory Note:
This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!

Drw electronic code

rPlan
AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614

Legal Owner

QR CODE: NA

Description:
Typical Vessels FRAGNET

Vessels / Drums / Tanks

Drawn By: DFT-01

Drawn Date: 20260717

Checked Approved by: rPlan-01

Checked Approved Date: 20260726

Drawing Number: As Barcoaded

Sheet: 1 of 1

Rev: 00
