
الشركة العمانية للمصافي والبتروكيماويات
Oman Refineries and Petrochemicals Company

STATIC EQUIPMENT TURNAROUND-TA2010
SOHAR REFINERY & PETROCHEMICALS COMPANY
CONTRACTOR - SPECIAL TECHNICAL SERVICES LLC.
PRESHUTDOWN PREPARATIONS PROGRESS REPORT DT. 4TH FEBRUARY 2010
PERIOD OF PERFORMANCE - 29TH JANUARY TO 4TH FEBRUARY 2010

STS
SPECIAL TECHNICAL SERVICES

SECTION 10 — MANPOWER MOBILIZATION PROGRESS CURVE

Crew (Contractor / Sub-Contractor)	Planned	Achieved
All Crews (Cumulative Plan)	2173	
Actual Mubilization (Crew Wise):		1694
OCC (subcontractor)	1505	1276
STS (Muscat)	178	136
STS (Piping & Hotworks)	130	65
Plantech (subcontractor)	33	29
Cape (Scaffolding)	104	88
Nafal (Insulation)	50	17
Refractory & Painting Sub Con.	50	0
Tanks & Pit Cleaning Sub-Con.	85	21
Others	38	62
Legend: Planned Curve / Actual Curve		

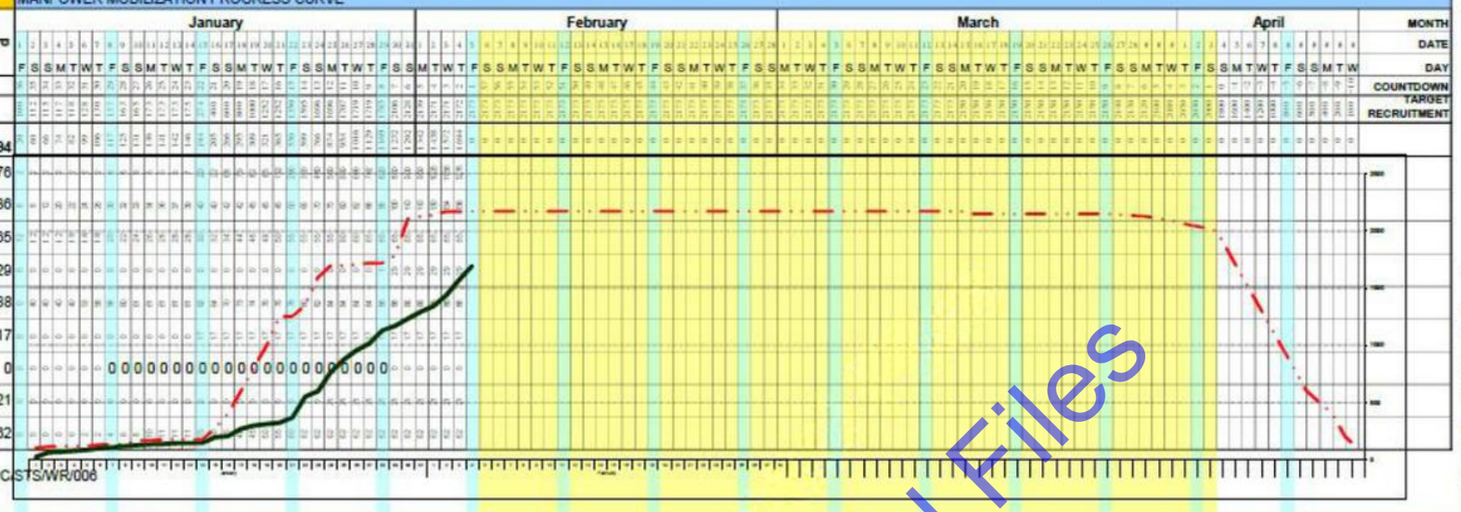

SECTION 11 — MACHINERY MOBILIZATION PROGRESS CURVE

Crew	Planned	Achieved
All Crews (Cumulative Plan)	229	
Actual Mubilization (Crew Wise):		37
Cranes	21	2
Flat beds, lorry & trucks	21	10
Forklifts	14	5
Welding Machines, Plasma Cutters	17	2
Compressors/ Generators	50	5
Dia Pumps / Hydrotest Pumps	23	1
Water Jettres & Washing Machines	6	7
Bundle Pullers	4	4
Fuel / Vacuum Trucks	8	
Transport Vehicals	38	
Bicycles / Trycycles	25	
Other s	2	1
Legend: Planned Curve / Actual Curve		



Archives from Personal Files

Drw Purpose Code :-	R01- Educational
Status of Approval :-	01
Dimentions as Mentioned	NA
Drawing Scale :-	NTS
Engg Code :-	02
Backup Info Code :-	00
Angle of Projection	NA
Sheet Size	A3

Statutory Note:
This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!

Drw electronic code

rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614

Legal Owner

QR CODE NA

Description: Resource Mobilization Plan Typical to STOs/TAs

Drawn By:	DFT-01
Drawn Date	20261005
Checked Approved by	rPlan-01
Checked Approved Date	20261020
Drawing Number	As Barcoded
Sheet	1 of 1
Rev	00
