


NO.	PART NAME	MATERIAL	STANDARD	NO.	PART NAME	MATERIAL	STANDARD
1	BODY	CAST IRON	ASTM A126B	10	HINGE PIN	BRASS	ASTM B16 C36000
2	SEAT RING	CAST BRONZE	ASTM B62	11	GASKET	PTFE	NON ASBESTOS
3	DISC RING	CAST BONZE	ASTM B62	12	SIDE PLUG	BRASS	ASTM B16 C36000
4	DISC	CAST IRON	ASTM B126B	13	WASHER	STEEL	ASTM A307 B
5	BONNET	CAST IRON	ASTM A126B	14	SPLIT PIN	STAINLESS STEEL	ASTM 420 S42000
6	BODY GASKET	GRAPHITE	NON ASBESTOS	15	NUT	STEEL	ASTM A307 B
7	NUTS	STEEL	ASTM A307B	16	BOLT	STEEL	ASTM A307 B
8	BOLTS	STEEL	ASTM A307B	17	HINGE	DUCTILE IRON	ASTM A536
9	NAME PLATE	ALUMINUM	COMMERCIAL				

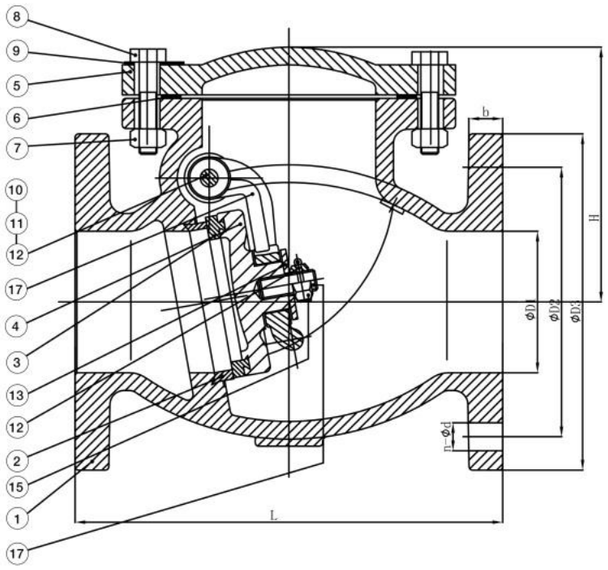


JOINT VALVE ROUTINE & SHUTDOWN MAINTENANCE FRAGNET

OPENING
Preparation
LOTO
Depressurize
Isolate
Inspect as found
TAG
Inspect Body
Ispect Bonnet
Functional Check
Manual Operation
Check for Open/Close
Removal & Dissassemble
Drop the Valve
Scaffold
Drop
Move to shop

REFURBISHMENT
Shop Activities
Dismantle Valve
Clean
Remove Dirt
Remove Scale
Remove product
Lubricate as recommended
Lubricate stem
Lubricate gearboxes
Lubticator actuator links
Seal & packing
Replace valve gaskets
Replace valve packing
Replace O-rings
Replace seals
Machining if needed
Machine worn out parts
Machine gasket seats
Machine stem to free
Reassemble
Boxup Valve
Connect Body to Bonnet
Boltup end connections
Valve testing
Leak Test
Pressure test in shop
Painting
Final Visual Inspection

REFIXING
Valve return & refix
Rig Back
Fix in location
Check direction and angle
Bolting
Clean mating flange surfaces
Replace gaskets
Boxup in location
Torque to appropriate value
Reinsulate for HOT & Cold Services
Deblind
Descaffold

T17QSME1347: Service 12" 2nos Check Valves(35-6)		644	26-Jan-17 08:00 — 22-Feb-17 04:00
Pre Shutdown		6	26-Jan-17 08:00 — 26-Jan-17 14:00
SAFD-5310	Erect Scaffolding	4	26-Jan-17 08:00 — 26-Jan-17 12:00
SAFD-5320	Remove Insulation	2	26-Jan-17 12:00 — 26-Jan-17 14:00
Shutdown		93	30-Jan-17 20:00 — 03-Feb-17 17:00
SAFD-5330	Verify LT&T and Obtain PTW	2	30-Jan-17 20:00 — 30-Jan-17 22:00
SAFD-5340	Remove 12" NRVs (2 nos) & Install Blinds	12	30-Jan-17 22:00 — 31-Jan-17 10:00
SAFD-5350	Shift NRVs to Workshop from Site	8	31-Jan-17 10:00 — 31-Jan-17 18:00
SAFD-5360	Overhaul/Service 12" NRVs (2 nos)	48	31-Jan-17 18:00 — 02-Feb-17 18:00
SAFD-5370	Inspect/Test Valve	2	02-Feb-17 18:00 — 02-Feb-17 20:00
SAFD-5380	Shift Valves From Workshop to Site	8	02-Feb-17 20:00 — 03-Feb-17 04:00
SAFD-5390	Remove Blinds & Fix Back 12" NRVs (2 nos)	12	03-Feb-17 04:00 — 03-Feb-17 16:00
SAFD-5400	Housekeeping & Close PTW	1	03-Feb-17 16:00 — 03-Feb-17 17:00
SAFD-5410	Mechanical Completion	0	03-Feb-17 17:00
Post Shutdown		443	03-Feb-17 17:00 — 22-Feb-17 04:00
SAFD-5420	Fix Back Insulation	4	03-Feb-17 17:00 — 03-Feb-17 21:00
SAFD-5430	Remove Scaffolding	2	22-Feb-17 02:00 — 22-Feb-17 04:00

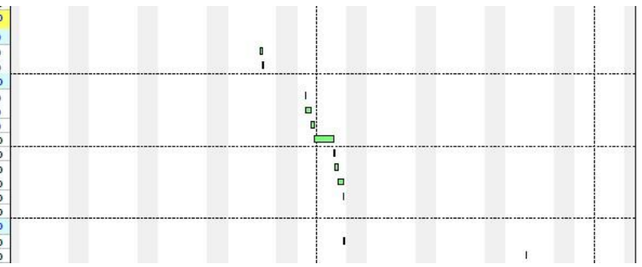

Drw Purpose Code :-
R01- Educational

Status of Approval :-
01

Dimentions as Mentioned
NA

Drawing Scale :- NTS

Engg Code :- 99

Backup Info Code :- 04

Angle of Projection
NA

Sheet Size
A3

Statutory Note:
This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!

Drw electronic code

rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614

Legal Owner

QR CODE
NA

Description:
CHECK VALVES - FRAGNET

Drawn By: DFT-01

Drawn Date: 20260804

Checked Approved by: rPlan-01

Checked Approved Date: 20260814

Drawing Number: As Barcoaded

Sheet: 1 of 1

Rev: 00
