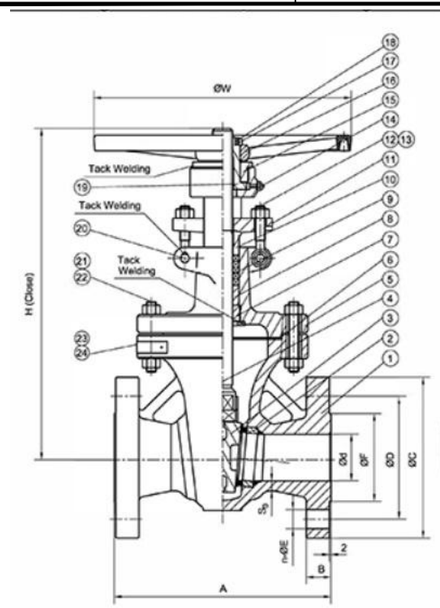


ITEM	NAME	MATERIAL
1	BODY	ASTM A216-WCB
2	SEAT	ASTM A105N+STL
3	FLEXIBLE WEDGE	ASTM A217-CA15
4	STEM	ASTM A182-F6a
5	BONNET	ASTM A216-WCB
6	GASKET	304+GRAPHITE
7	BACKSEAT	ASTM A276-420
8	PACKING SPACER	ASTM A276-410
9	PACKING	INCONEL600+GRAPHITE
10	GLAND	ASTM A276-410
11	GLAND FLANGE	ASTM A216-WCB
12	EYE BOLT	ASTM A193-B7
13	NUT	ASTM A194-2H
14	GREASE FITTING	ASTM A283 GRC
15	GLAND NUT	AISI 1025
16	HANDWHEEL	ASTM A536 60-40-18
17	HANDWHEEL NUT	AISI 1025
18	SCREW	AISI 1025
19	STEM NUT	ASTM A439 D-2
20	PIN	AISI 1035
21	BOLT	ASTM A193-B7
22	NUT	ASTM A194-2H
23	NAMEPLATE	ASTM A240-304
24	RIVET	ASTM A240-304

NOTE:

1. FLEXIBLE WEDGE
2. API 624 QUALIFIED

ITEM	FIG NO.	SIZE	UNIT	d	A	B	C	D	n	E	F	H	W	Sb	Weight(kg/lbs)
01	GT300CSF8	2"	mm	51	216	23	105	127	8	19	92.1	355	200	9.7	57/26
		2"	in	2.0	8.5	0.91	4.5	5.0	8	3/4	3.62	13.98	7.87	0.38	
02	GT300CSF8	2-1/2"	mm	64	241	26	130	149.2	8	22	104.8	371	200	11.2	77/35
		2-1/2"	in	2.5	9.5	1.02	7.5	5.88	8	7/8	4.12	14.61	7.87	0.44	

JOINT VALVE ROUTINE & SHUTDOWN MAINTENANCE FRAGNET


OPENING
Preparation
LOTO
Depressurize
Isolate
Inspect as found
TAG
Inspect Body
Ispect Bonnet
Functional Check
Manual Operation
Check for Open/Close
Removal & Dissassemble
Drop the Valve
Scaffold
Drop
Move to shop

REFURBISHMENT
Shop Activities
Dismantle Valve
Clean
Remove Dirt
Remove Scale
Remove product
Lubricate as recommended
Lubricate stem
Lubricate gearboxes
Lubticator actuator links
Seal & packing
Replace valve gaskets
Replace valve packing
Replace O-rings
Replace seals
Machining if needed
Machine worn out parts
Machine gasket seats
Machine stem to free
Reassemble
Boxup Valve
Connect Body to Bonnet
Boltup end connections
Valve testing
Leak Test
Pressure test in shop
Painting
Final Visual Inspection

REFIXING
Valve return & refix
Rig Back
Fix in location
Check direction and angle
Bolting
Clean mating flange surfaces
Replace gaskets
Boxup in location
Torque to appropriate value
Reinsulate for HOT & Cold Services
Deblind
Descaffold



T17QEME1548: Replace Suction B/V(67-5A)	999	13-Jan-17 12:00	24-Feb-17 03:00
Pre Shutdown	3	13-Jan-17 12:00	13-Jan-17 15:00
EQCT-6610 Erect Scaffolding	2	13-Jan-17 12:00	13-Jan-17 14:00
EQCT-6620 Remove Insulation	1	13-Jan-17 14:00	13-Jan-17 15:00
Shutdown	26	02-Feb-17 12:00	03-Feb-17 14:00
EQCT-6630 Verify LT&T and Obtain PTW	2	02-Feb-17 12:00	02-Feb-17 14:00
EQCT-6640 Mechanical Isolation & Blinding	4	02-Feb-17 14:00	02-Feb-17 18:00
EQCT-6650 Replace 4" Gate Valve	12	02-Feb-17 18:00	03-Feb-17 06:00
EQCT-6670 Inspection By ERG	2	03-Feb-17 06:00	03-Feb-17 08:00
EQCT-6680 Carry out De-Blinding	4	03-Feb-17 08:00	03-Feb-17 12:00
EQCT-6690 Housekeeping & Close PTW	2	03-Feb-17 12:00	03-Feb-17 14:00
EQCT-6700 Mechanical Completion	0		03-Feb-17 14:00
Post Shutdown	493	03-Feb-17 14:00	24-Feb-17 03:00
EQCT-6710 Fix Back Insulation	2	03-Feb-17 14:00	03-Feb-17 16:00
EQCT-6720 Remove Scaffolding	2	24-Feb-17 01:00	24-Feb-17 03:00



Drw Purpose Code :- R01- Educational

Status of Approval :- 01

Dimentions as Mentioned: NA

Drawing Scale :- NTS

Engg Code :- 99

Backup Info Code :- 04

Angle of Projection: NA

Sheet Size: A3

Statutory Note:
This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!

Drw electronic code

rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614

Legal Owner

QR CODE: NA

Description: GATE VALVES - FRAGNET

Drawn By:	Drawn Date
DFT-01	20260804
Checked Approved by: rPlan-01	Checked Approved Date: 20260814

Drawing Number	Sheet	Rev
As Barcoaded	1 of 1	00
