
PRESSURE SAFETY VALVES GENERAL ARRANGEMENT DRAWING

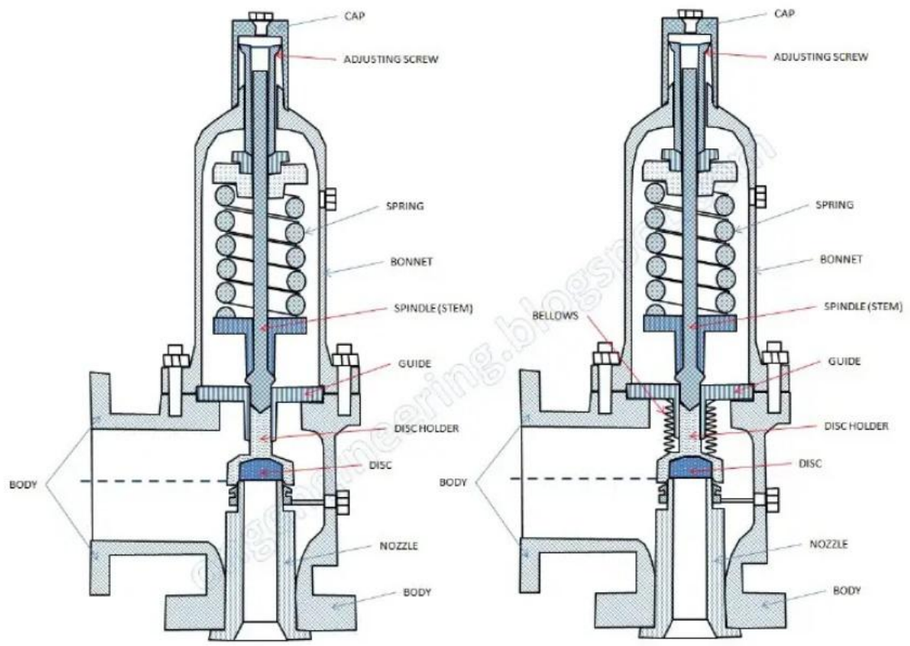

JOINT VALVE ROUTINE & SHUTDOWN MAINTENANCE FRAGNET


OPENING
Preparation
LOTO
Depressurize
Isolate
Inspect as found
TAG
Inspect Body
Ispect Bonnet
Functional Check
Manual Operation
Check for Open/Close
Removal & Dissassemble
Drop the Valve
Scaffold
Drop
Move to shop

REFURBISHMENT
Shop Activities
Dismantle Valve
Clean
Remove Dirt
Remove Scale
Remove product
Lubricate as recommended
Lubricate stem
Lubricate gearboxes
Lubticator actuator links
Seal & packing
Replace valve gaskets
Replace valve packing
Replace O-rings
Replace seals
Machining if needed
Machine worn out parts
Machine gasket seats
Machine stem to free
Reassemble
Boxup Valve
Connect Body to Bonnet
Boltup end connections
Valve testing
Leak Test
Pressure test in shop
Painting
Final Visual Inspection

REFIXING
Valve return & refix
Rig Back
Fix in location
Check direction and angle
Bolting
Clean mating flange surfaces
Replace gaskets
Boxup in location
Torque to appropriate value
Reinsulate for HOT & Cold Services
Deblind
Descaffold

T17QECV0728: Overhaul PCV 3"X300 CAT-AS(43-67731)		1075	12-Jan-17 10:00	26-Feb-17 05:00
Pre Shutdown		2	12-Jan-17 10:00	12-Jan-17 12:00
EERC-1610	Erect Scaffolding	2	12-Jan-17 10:00	12-Jan-17 12:00
Shutdown		479	02-Feb-17 02:00	22-Feb-17 01:00
EERC-1620	Verify LT&T and Obtain PTW	2	02-Feb-17 02:00	02-Feb-17 04:00
EERC-1630	Disconnect Air & 24V Connections	2	02-Feb-17 04:00	02-Feb-17 06:00
EERC-1635	Remove CV & Install End Blinds/Covers	6	02-Feb-17 06:00	02-Feb-17 12:00
EERC-1640	Shift CV From Site to Workshop	1	02-Feb-17 12:00	02-Feb-17 13:00
EERC-1645	Overhaul/Service Valve & Actuator	16	06-Feb-17 23:00	07-Feb-17 15:00
EERC-1650	Test CV as per Datasheet	2	07-Feb-17 15:00	07-Feb-17 17:00
EERC-1655	Shift CV From Workshop to Site	1	07-Feb-17 17:00	07-Feb-17 18:00
	Remove End Blinds/Covers & Install CV	6	21-Feb-17 14:00	21-Feb-17 20:00
	Re-Connect Air & 24V Connections	2	21-Feb-17 20:00	21-Feb-17 22:00
	Loop Check & Stroke test	2	21-Feb-17 22:00	22-Feb-17 00:00
	Housekeeping & Close PTW	1	22-Feb-17 00:00	22-Feb-17 01:00
	Mechanical Completion	0		22-Feb-17 01:00
		2	26-Feb-17 03:00	26-Feb-17 05:00
	Remove Scaffolding	2	26-Feb-17 03:00	26-Feb-17 05:00



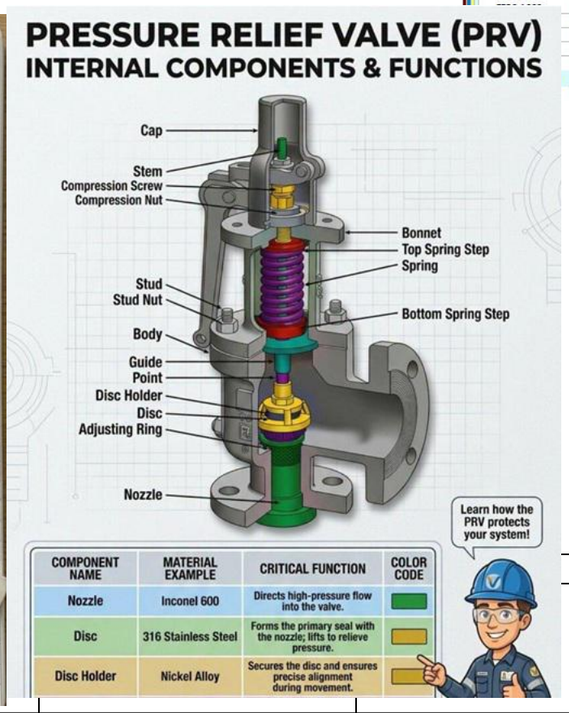

Drw Purpose Code :- R01- Educational	**Statutory Note:** This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!	Description: PRESSURE SAFETY VALVES - FRAGNET	
Status of Approval :- 01			
Dimentions as Mentioned NA	Drw electronic code	Drawn By: DFT-01	Drawn Date 20260804
Drawing Scale :- NTS	rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614	Checked Approved by rPlan-01	Checked Approved Date 20260814
Engg Code :- 99 / Backup Info Code :- 04	Legal Owner / QR CODE NA	Drawing Number As Barcoaded	Sheet 1 of 1 / Rev 00
Angle of Projection NA / Sheet Size A3			
