
EARNED VALUE MANAGEMENT
PLANNED V/S ACTUAL V/S FORECAST COMPARISONS

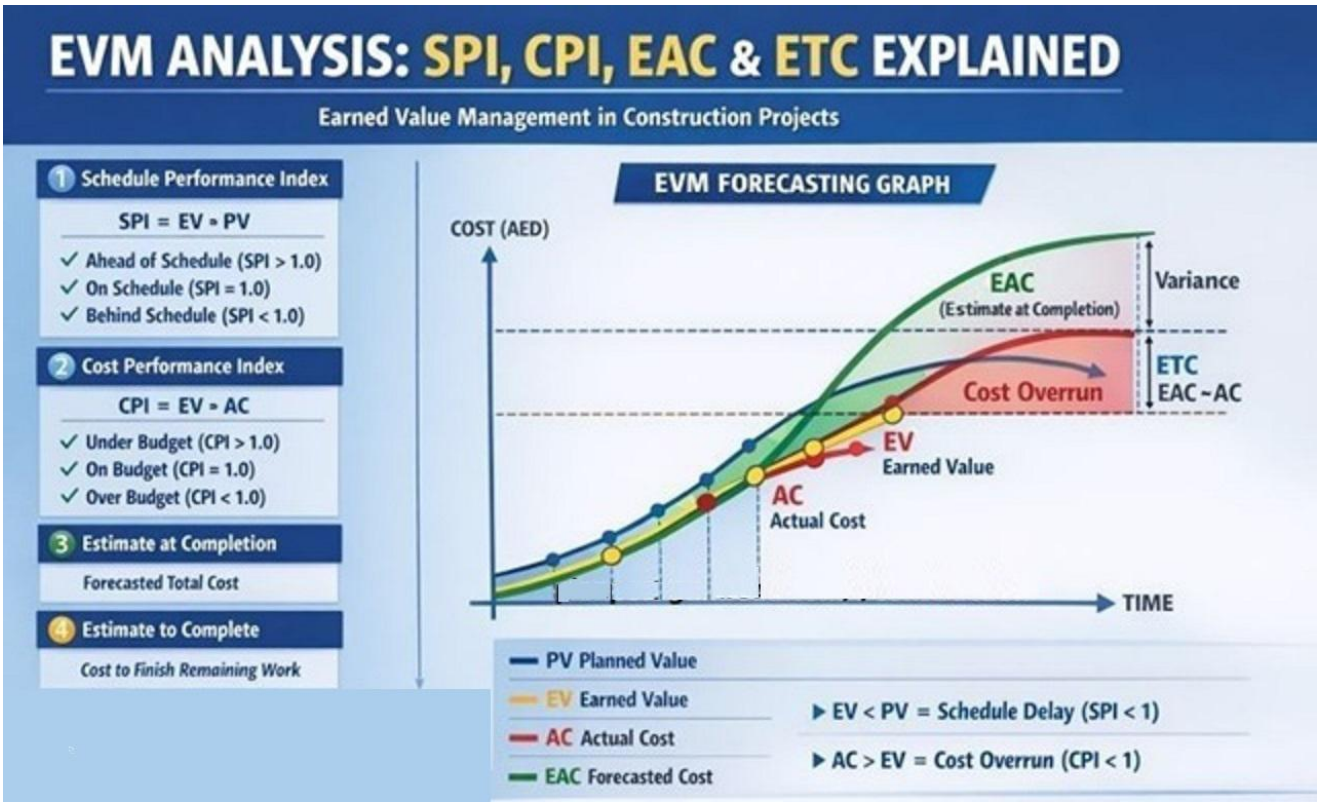

Notes:
1) Manhours can be used as accepted norms for loading each activity
2) Cumulate the weightages progressively by time period for the planned curve
3) Use delta between successive time perious for histogram heights
4) Once baselined start updating the current activities and comparing with the target curve
5) Physical progress on project site to be updated activity wise
6)Use F9 to cumulate the progress to date and allow the software to produce the comparisons
7) Make sure planned, actual and forecast curves aremonitored live to analytically assess
8) Corrective actions to be devised based on the drill down into real time delta and delays

rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614		Drw Purpose Code :- R01-Educational	**Statutory Note:** This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!
Legal Owner	QR Code	Status of Approval :- 01	
	NA	Dimentions as Mentioned NTS	
		Engg Code :- 01	
		Backup Info Code :- 01	
		Angle of Projection :- NA	Checked Approved by: rPlan-01 / Checked Approved Date: 20260902
Drw electronic code: REF DWG NO			Rev: 00 / DWG No.
Drawn By: DFT-01			
Drawn Date: 20260820		Description: EARNED VALUE MGMT Standard Concept / Curves	SCALE:- NTS / SHEET 1 of 1
