



	TOE	Scope	BL	OP	PI	CLE	NDT	REP	FIS
BLOCK-1	Columns	18	18	17	17	13	7	4	4
	Exchanger	146	146	127	127	79	58	18	18
	FinFan	170	168	167	167	159	147	144	144
	Heaters	3	3	3	3	3	3		
	Vessels	83	76	75	75	68	56	53	53
	Heater Aux	8	8	8	4	4	4		
	Ejector & De Sup	8	7	7	7	5	5	5	5
	Filter/ mixer	3	3	3	3	3	3	1	1
	Tank	14	13	13	12	12	12	12	12
	Silencer	2							
BLOCK-2	Columns	8	8	8	8	6	4	3	3
	Exchanger	84	78	78	78	66	58	18	18
	FinFan	126	126	126	126	126	126	110	96
	Heaters	7	7	7	7	6	3	3	2
	Vessels	64	64	64	64	59	45	45	45
	Heater Aux	4	4	4	2				
	Ejector & De Sup	3	3	3	3	3	3	2	2
	Filter	2	2	2	2	2	2	2	2
	Tank	10	8	8	8	8	8	8	8
	Silencer	2	2	2	1	1	1	1	1










Description	System	Remove		Overhaul		Install		Mech Completion			
		Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual		
Total Valves	81	66	60	42	29	7	17	6	6		
Total Valves	49	34	32	21	10	5	9	5	6		
CAT-AS(43-30077)	Furnace # 2	29-Jan-17 20:00	28-Jan-17 16:00	01-Feb-17 16:00	02-Feb-17 22:00	08-Feb-17 01:00	05-Feb-17 08:00	08-Feb-17 06:00			
-AS(43-60231)	Furnace # 2	30-Jan-17 06:00	28-Jan-17 12:00	02-Feb-17 14:00	30-Jan-17 12:00	07-Feb-17 01:00	31-Jan-17 13:00	07-Feb-17 06:00	01-Feb-17 06:00		
-AS(43-60226)	Furnace # 2	30-Jan-17 16:00	28-Jan-17 12:00	03-Feb-17 11:00	31-Jan-17 23:00	07-Feb-17 12:00	01-Feb-17 12:00	07-Feb-17 17:00			
CAT-AS(43-30107)	Furnace # 3	21-Jan-17 20:00	22-Jan-17 20:00	26-Jan-17 07:00	26-Jan-17 00:00	27-Jan-17 02:00	27-Jan-17 12:00	27-Jan-17 07:00	28-Jan-17 21:00		
CAT-AS(43-30167)	Furnace # 5	20-Jan-17 20:00	20-Jan-17 04:00	23-Jan-17 16:00	26-Jan-17 00:00	24-Jan-17 11:00	27-Jan-17 12:00	24-Jan-17 16:00	28-Jan-17 09:00		
-AS(43-60321)	Furnace # 5	21-Jan-17 06:00	20-Jan-17 00:00	22-Jan-17 01:00	22-Jan-17 01:00	24-Jan-17 22:00	24-Jan-17 22:00	25-Jan-17 03:00	25-Jan-17 03:00		
T-A(43-60488 B)	CGC	02-Feb-17 02:00		05-Feb-17 22:00		18-Feb-17 11:00		18-Feb-17 16:00			
T-A(43-30875)	CGC	02-Feb-17 16:00	07-Feb-17 16:00	06-Feb-17 12:00	08-Feb-17 00:00	19-Feb-17 02:00	08-Feb-17 05:00	19-Feb-17 07:00			
CAT-AS(43-40850)	CGC	03-Feb-17 04:00		06-Feb-17 12:00		19-Feb-17 15:00		19-Feb-17 20:00			
-AS(43-40904)	CGC	03-Feb-17 16:00		06-Feb-17 12:00		20-Feb-17 04:00		20-Feb-17 09:00			
T-AS(43-67525)	CGC	04-Feb-17 02:00	31-Jan-17 14:00	04-Feb-17 19:00	02-Feb-17 06:00	17-Feb-17 20:00	03-Feb-17 04:00	18-Feb-17 01:00	03-Feb-17 11:00		
T-AS(43-41745)	Propane System	05-Feb-17 09:00	06-Feb-17 02:00	08-Feb-17 17:00		11-Feb-17 10:00		11-Feb-17 15:00			
T-AS(43-41752)	Propane System	05-Feb-17 21:00	04-Feb-17 02:00	09-Feb-17 05:00		11-Feb-17 23:00		12-Feb-17 04:00			
T-AS(43-41775)	Propane System	06-Feb-17 09:00	07-Feb-17 09:00	09-Feb-17 17:00		12-Feb-17 12:00		12-Feb-17 17:00			
T-AS(43-41600)	ERC	31-Jan-17 04:00	04-Feb-17 18:00	03-Feb-17 12:00		22-Feb-17 04:00		22-Feb-17 09:00			
-AS(43-41596)	ERC	31-Jan-17 16:00	02-Feb-17 00:00	05-Feb-17 02:00		20-Feb-17 17:00		20-Feb-17 22:00			
T-AS(43-67725)	ERC	01-Feb-17 02:00	30-Jan-17 05:00	05-Feb-17 21:00	03-Feb-17 23:00	21-Feb-17 04:00		21-Feb-17 09:00			
T-AS(43-67731)	ERC	01-Feb-17 12:00	30-Jan-17 02:00	06-Feb-17 15:00	03-Feb-17 03:00	21-Feb-17 15:00	03-Feb-17 07:00	21-Feb-17 20:00	03-Feb-17 12:00		
-A(43-30793)	Quench Tower	06-Feb-17 19:00		07-Feb-17 14:00		17-Feb-17 10:00		17-Feb-17 14:00			
AS(43-31115)	Primary Dryer	01-Feb-17 04:00		05-Feb-17 08:00		14-Feb-17 13:00		14-Feb-17 18:00			
T12OFCV1748	XV Passing 20"X150 CAT-AS(43-31116)	Primary Dryer									
						09-Feb-17 00:00		14-Feb-17 23:00		15-Feb-17 04:00	
						08-Feb-17 22:00		14-Feb-17 03:00		14-Feb-17 08:00	
						08-Feb-17 00:00		13-Feb-17 05:00		13-Feb-17 10:00	
						09-Feb-17 15:00		13-Feb-17 11:00		13-Feb-17 16:00	
						10-Feb-17 10:00		13-Feb-17 15:00		13-Feb-17 19:00	
						11-Feb-17 04:00		13-Feb-17 19:00		13-Feb-17 23:00	
		06-Feb-17 16:00	06-Feb-17 04:00			20-Feb-17 04:00		20-Feb-17 09:00			
		06-Feb-17 10:00	09-Feb-17 16:00			20-Feb-17 19:00		21-Feb-17 00:00			
		07-Feb-17 19:00	13-Feb-17 04:00			21-Feb-17 10:00		21-Feb-17 15:00			
		05-Feb-17 20:00	16-Feb-17 16:00			22-Feb-17 01:00		22-Feb-17 05:00			
		06-Feb-17 06:00	09-Feb-17 20:00			15-Feb-17 07:00		15-Feb-17 12:00			
		06-Feb-17 06:00	11-Feb-17 11:00			15-Feb-17 20:00		16-Feb-17 01:00			
		06-Feb-17 04:00	13-Feb-17 02:00			16-Feb-17 09:00		16-Feb-17 14:00			
		05-Feb-17 16:00	14-Feb-17 17:00			16-Feb-17 22:00		17-Feb-17 03:00			
		06-Feb-17 04:00	16-Feb-17 08:00			17-Feb-17 09:00		17-Feb-17 14:00			
			17-Feb-17 03:00			17-Feb-17 20:00		18-Feb-17 01:00			
		05-Feb-17 14:00	17-Feb-17 21:00			18-Feb-17 07:00		18-Feb-17 12:00			
		06-Feb-17 10:00	18-Feb-17 15:00			19-Feb-17 00:00		19-Feb-17 04:00			


PROGRESS CURVE

Project Summary

Dates	Baseline	Start	15-Aug	Date	Current	23-Sep	Forecast	20-Dec
		Finish	31-Dec	Count		2961		-2834
Status by %	Baseline	Planned	35.72%	Current	35.41%	Variance	-0.31%	
Discipline / Dept wise Progress	58.11% Civil	39.44% Mech	61.42% Elec	30.59% Rotating	33.59% Instr	74.66% Procure	45.98% Manuf'g	33.28% Shutdown
Progress by Type of Equipt	36.44% AFC	73.53% Columns	73.09% Vessels	30.86% RGC	37.50% Piping	17.20% Heater	25.00% RCC Rehab	
Progress by Type ofWork	45.37% Struct	74.76% RCC	50.65% Fire Proof	71.38% Roof Sheet	57.48% E Cables	40.65% I Cables	59.76% HT Motors	67.00% LT Motors

Project S- Curve

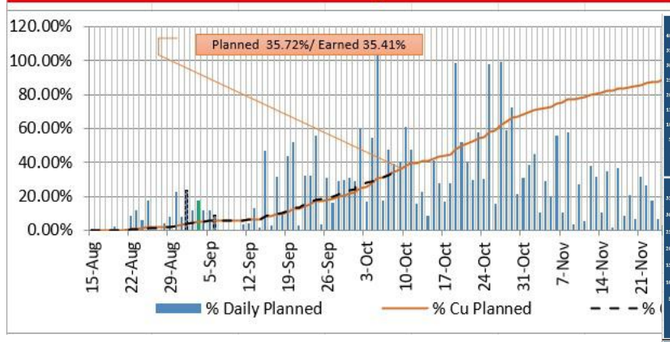

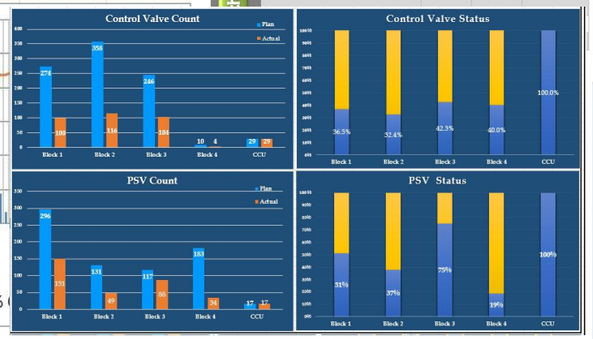


Safety	Description	Target	Cum.	On Report Date
	Lost time Incident	0.00	0.00	0.00
	Recordable Cases	0.00	0.00	0.00
	First Aid Cases	0.00	0.00	0.00
	LSR Violation	0.00	0.00	0.00
	SPSP Walks Compl/Day	1.00	74.00	1.00
	Safety Field Obvn Cards/Day	10.00	137.00	6.00

Quality	Description	Target	Cum.	On Report Date
	Weld reject rate (%)	3-5	3	3
	Flawless NCR	≤ 2	0.00	0.00
	Daily flawless surveys (No)	3.00	3.08	3.00
	Daily flawless survey score	90%	100%	100%

Other KPI	Description	Plan	Actual	Forecast
	Cost (M USD)	2.10	1.61	2.10
		Plan	Actual	Variance
	Head Counts	137.00	132.00	-5.00

Schedule Graph



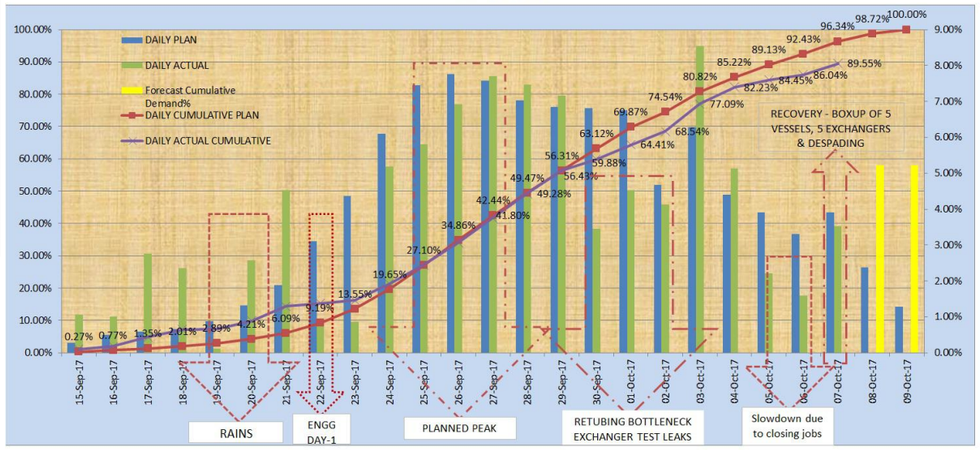

Unit	Ethylene		Sulphur		Polyethylene		Utilities		Total		Ethylene		Sulphur		Polyethylene		1-Hexene		Utilities		Total		Ethylene		Polyethylene		Total	
Total	26		19		14		8		67		41		13		7		1		1		63		5		2		137	
	Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual	Plan	Actual
Blind	25	22	15	10	12	12	4	4	56	48	36	30	11	3	7	6	1	1	0	0	55	40	5	5	2	2	118	95
Open	24	20	12	9	11	13	2	2	49	44	34	23	10	1	7	6	1	1	0	0	52	31	5	5	2	2	108	82
Clean / Hydrojet	19	15	8	1	10	10	2	1	39	27	23	19	6	0	5	2	1	1	0	0	35	22	0	0	0	0	74	49
Inspection	2	7	2	1	6	5	0	1	10	14	6	1	2	0	5	0	1	1	0	0	14	2	0	0	2	2	26	18
Hydro test	0	0	0	0	0	0	0	0	0	0	3	0	1	0	3	0	0	0	0	0	7	0	0	0	0	0	7	0
Boxup	2	7	1	1	2	5	0	0	5	13	6	1	0	0	4	0	1	1	0	0	11	2	0	0	2	2	18	17
De-Blind	2	4	1	0	2	0	0	0	5	4	0	0	0	0	4	0	1	1	0	0	5	1	0	0	0	0	10	5
Mech Completion	1	3	1	0	2	0	0	0	4	3	5	1	0	0	4	0	1	1	0	0	10	2	0	0	0	0	14	5



Drw Purpose Code :- R01-Educational

Status of Approval :- 01

Dimentions as Mentioned N/A

Drawing Scale :- PICTURE

Engg Code :- N/A

Backup Info Code :- 00

Angle of Projection N/A

Sheet Size A3

Statutory Note:
This document is prepared by rPlan and is the sole proprietory of the company.Its purpose is educational and no references within this document are for Engineering or Design corelation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website.This drw is not for duplication without company permission!

Drw electronic code

rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614

Legal Owner

QR CODE N/A

Description: Historical Analytics from Past Projects - a Pictograph

Drawn By: DFT-01

Drawn Date 20260801

Checked Approved by rPlan-01

Checked Approved Date 20260905

Drawing Number As Barcoded

Sheet 1 of 1

Rev 00
