
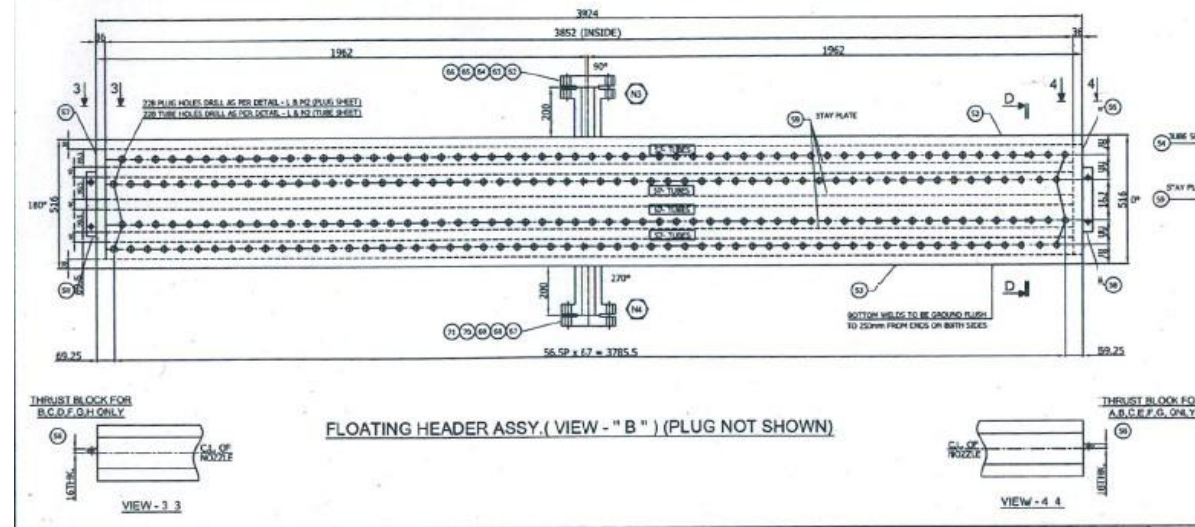
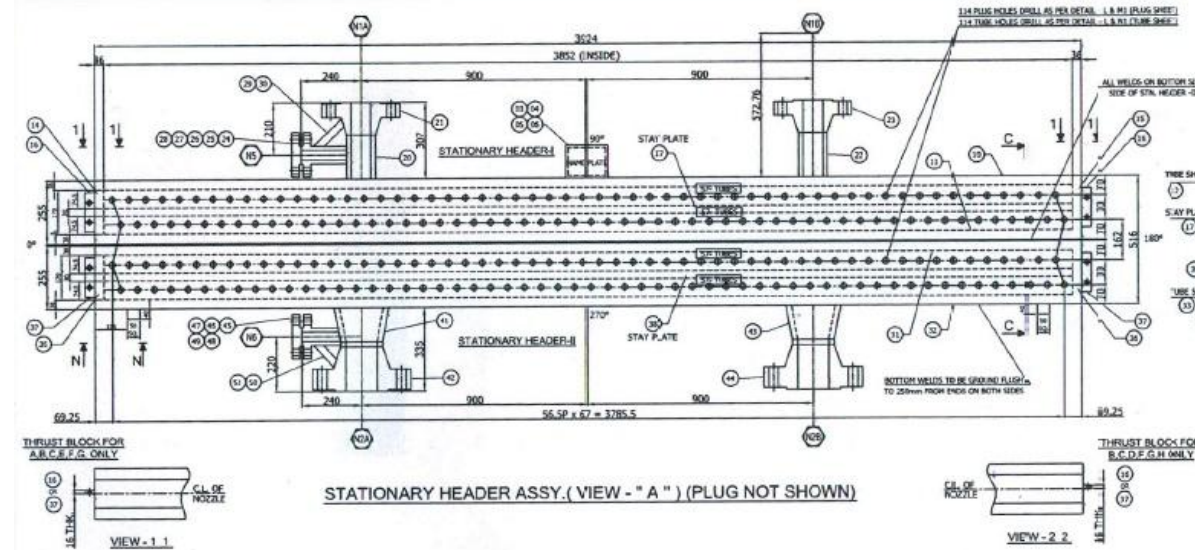


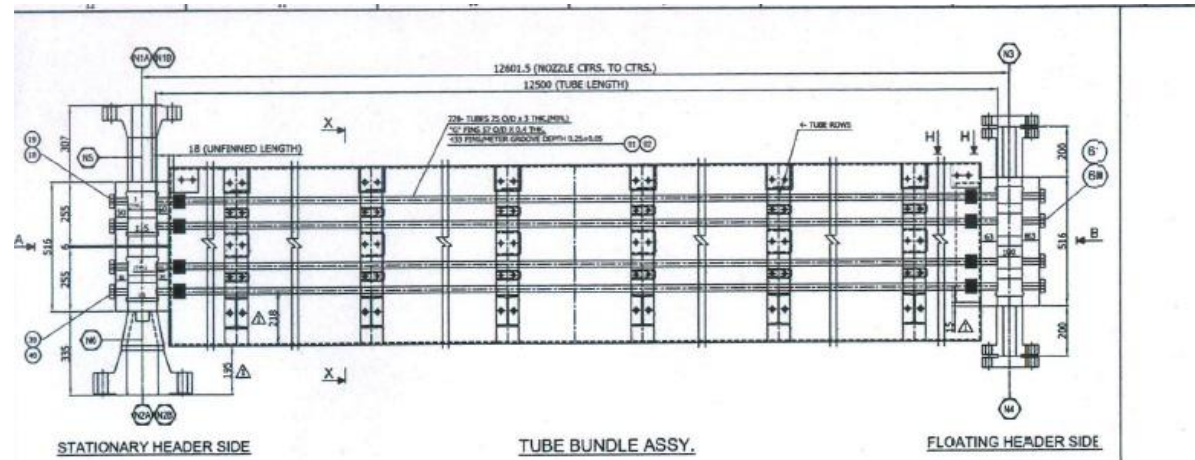

Obtain work permit	1	22-Apr-26 08:00	22-Apr-26 09:00
Carry out blinding	24	22-Apr-26 09:00	23-Apr-26 09:00
Provide access to manways	4	23-Apr-26 09:00	23-Apr-26 13:00
Open mechanical / refractory manways	12	23-Apr-26 13:00	24-Apr-26 01:00
Install air ejector / exhaust blower	4	24-Apr-26 01:00	24-Apr-26 05:00
Carry out ventilation	24	24-Apr-26 05:00	25-Apr-26 05:00
Perform gas test	2	25-Apr-26 05:00	25-Apr-26 07:00
Obtain CSE permit	1	25-Apr-26 07:00	25-Apr-26 08:00
Provide lighting arrangement	3	25-Apr-26 08:00	25-Apr-26 11:00
Offer as found inspection	2	25-Apr-26 11:00	25-Apr-26 13:00
Perform equipment related instrument job repair/testing	100	25-Apr-26 13:00	29-Apr-26 17:00
Carry out the cleaning / replacement of sight door / per	50	25-Apr-26 13:00	27-Apr-26 15:00
Drop the burner assembly and repair / testing / overha	140	25-Apr-26 13:00	01-May-26 09:00
Offer detail visual inspection of dampers / expansion jo	4	25-Apr-26 13:00	25-Apr-26 17:00
Carry out servicing / replacement of damper(s)	80	25-Apr-26 17:00	29-Apr-26 01:00
Carry out servicing / replacement of expansion joint(s)	70	25-Apr-26 17:00	28-Apr-26 15:00
Carry out servicing of air deflector	90	25-Apr-26 17:00	29-Apr-26 11:00
Remove insulation as (if) required	24	25-Apr-26 17:00	26-Apr-26 17:00
Carry out cleaning / buffing of exposed surface	24	26-Apr-26 17:00	27-Apr-26 17:00
Carry out NDT of expose surface	24	27-Apr-26 17:00	28-Apr-26 17:00
Carry out repair (mechanical / refractory) of ducts	120	28-Apr-26 17:00	03-May-26 17:00

Activity Name	Original Duration	Early Start	Early Finish	2026
Open convection header box	12	25-Apr-26 13:00	26-Apr-26 01:00	
Carry out refractory repair of header box and tube sheet	24	26-Apr-26 01:00	27-Apr-26 01:00	
Carry out cleaning / buffing of U bend	24	26-Apr-26 01:00	27-Apr-26 01:00	
Carry out NDT of U bend	12	27-Apr-26 01:00	27-Apr-26 13:00	
Carry out repair of U bend as if required	24	27-Apr-26 13:00	28-Apr-26 13:00	
Perform primary housekeeping / remove refractory deb	14	25-Apr-26 13:00	26-Apr-26 03:00	
Erect internal scaffolding as required	24	26-Apr-26 03:00	27-Apr-26 03:00	
Offer detail visual inspection of radiation / convection / i	4	27-Apr-26 03:00	27-Apr-26 07:00	
Carry out the cleaning / buffing of radiation and conve	24	27-Apr-26 07:00	28-Apr-26 07:00	
Offer cleaning inspection	3	28-Apr-26 07:00	28-Apr-26 10:00	
Perform NDT of coils	12	28-Apr-26 10:00	28-Apr-26 22:00	
Carry out contingency repair / replacement of coil etc.	30	28-Apr-26 22:00	30-Apr-26 04:00	
Offer contingency repair inspection	3	30-Apr-26 04:00	30-Apr-26 07:00	
Carry paint touch up	30	03-May-26 17:00	04-May-26 23:00	
Reinstate removed insulation	12	04-May-26 23:00	05-May-26 11:00	
Carry out refractory repair of radiation / convection / i	40	30-Apr-26 07:00	01-May-26 23:00	
Offer refractory inspection	4	01-May-26 23:00	02-May-26 03:00	
Carry out pressure test	36	02-May-26 03:00	03-May-26 15:00	
Refix convection header box panel	24	03-May-26 15:00	04-May-26 15:00	
Remove internal scaffolding	18	03-May-26 15:00	04-May-26 09:00	
Carry out floor refractory repair	24	04-May-26 09:00	05-May-26 09:00	
Offer floor refractory inspection	1	05-May-26 09:00	05-May-26 10:00	
Reinstall burner assemblies	24	05-May-26 10:00	06-May-26 10:00	
Offer alignment inspection of burner assemblies	2	06-May-26 10:00	06-May-26 12:00	
Offer final internal inspection and take box up clearanc	4	06-May-26 12:00	06-May-26 16:00	

Drw Purpose Code :- Status of Approval :- Dimentions as Mentioned Drawing Scale :- Engg Code :- Angle of Projection	Backup Info Code :- Sheet Size	Statutory Note: This document is prepared by rPlan and is the sole proprietary of the company. Its purpose is educational and no references within this document are for Engineering or Design correlation with the applicable codes. For any clarifications beyond the intended purpose viewers can always correspond to rPlan via its company website. This drw is not for duplication without company permission! Drw electronic code rPlan AT 39, MERMAID 1 CHS LTD., SEC-11, CBD-BELAPUR, NAVI MUMBAI - 400614 Legal Owner 	Description: Typical AFC FRAGNET Preliminary Doc under prep Drawn By: Drawn Date: Checked Approved by: Checked Approved Date: Drawing Number: Sheet: 1 of 1 Rev: XX
--	-----------------------------------	---	---
